

工程指示 / 要求簡箋 ENGINEER INSTRUCTIONS(E.I.)

工程指示編號:	EI- 4570	修改版本:	-
	HK- 591		
工程編號:	J 852	工程名稱:	亞皆老街中電
收件人:	生統	發件人:	Eric Liu
工程項目:	佛沙及後裝窗 後加滴水線(T1-T3)	日期:	08/04/2022

<input checked="" type="checkbox"/> 原合約工程包	<input type="checkbox"/> 原合約工程加 / 減賬 QT-	<input type="checkbox"/> 新工程報價 QT-
--	--	------------------------------------

信件批核號碼/圖紙參考編號:	批核模具圖紙編號:
客戶指示附件:	管理內部批簽署:

<input type="checkbox"/> 初步鋁料 B.M.	<input checked="" type="checkbox"/> 加工拆圖, 然後生產	<input type="checkbox"/> 尺寸表
<input type="checkbox"/> 正式鋁料 B.M.	<input type="checkbox"/> 技術上資料/指示	<input type="checkbox"/> 報價
<input type="checkbox"/> 配件 B.M.	<input type="checkbox"/> 樣辦或貨品說明書	<input type="checkbox"/> 分判合約
<input type="checkbox"/> 其他:		

內容: 請按加工圖及資料開料生產後加滴水線送地盤安裝
 (已包後裝+佛沙窗, 只做side hung窗玉位置, 梗窗及top hung窗玉不需要安裝)
 因現時窗玉關窗後, 滴水線出入數後於窗玉, 不能達至滴水線功能
 按業主要求, 現需加U槽作後加滴水線
 出貨包裝, 請分座分層及分單位, 直接打紮, 現場派料
 需有顏色: UCT806812XL-3
 共需總長907m, 謝謝

完成上列要求日期: 22/04/2022


國內

<input type="checkbox"/> 生產技術總監	<input type="checkbox"/> 連附件	<input type="checkbox"/> 技術部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 生產部	<input type="checkbox"/> 連附件
<input type="checkbox"/> 採購部	<input type="checkbox"/> 連附件	<input checked="" type="checkbox"/> 生產統籌部	<input checked="" type="checkbox"/> 連附件	<input type="checkbox"/> 報關組	<input type="checkbox"/> 連附件
<input type="checkbox"/> 質檢部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 會計部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 機械設計部	<input type="checkbox"/> 連附件
<input type="checkbox"/> 其他:					

香港

<input type="checkbox"/> 行政部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 會計部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 統籌部	<input type="checkbox"/> 連附件	<input type="checkbox"/> 工程部	<input type="checkbox"/> 連附件
<input type="checkbox"/> 採購部	<input type="checkbox"/> 連附件	<input type="checkbox"/> QS部	<input type="checkbox"/> 連附件	<input checked="" type="checkbox"/> 地盤管理	<input checked="" type="checkbox"/> 連附件	<input type="checkbox"/> 維修部	<input type="checkbox"/> 連附件

*發件人簽署:		*組別成員批核簽署:	
傳遞編號:		項目經理簽署:	

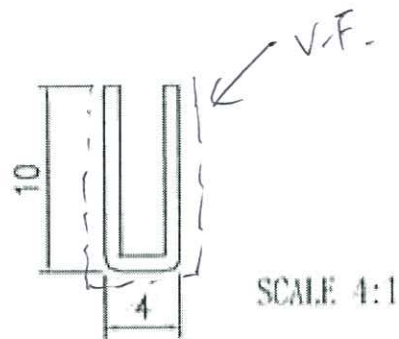

模號: 4x10mmU槽
 名稱: 隔音板用U槽
 合金狀態: 6063-T5
 重量: 0.048 KG/M
 V.F.: 0 mm

料號 = UCT 806812XL-3

總料長 = 907 m

按 5.2米一支

支需 175支

長度及數量按後頁資料

包裝出貨 = 分位
分層

分單位打裝

直接開料

不口位置補理

廠自補

窗玉滴水線

Precast

窗號	單位	Floor	加工長度 (mm)	總數量	每層數量	料總長度(m)
W3/T1B	B	1-21/F	723	36	2	26.0
W2/T1B	B	1-21/F	723	36	2	26.0
W2/T1A	A	1-21/F	723	36	2	26.0
W9/T1A	A	2-21/F	1423	17	1	24.2
W6/T1C	C	1-21/F	914	18	1	16.5
W5/T1C	C	2-21/F	1023	17	1	17.4
W4/T1C	C	1-21/F	1423	18	1	25.6
W3/T1C	C	1-21/F	1423	18	1	25.6
W7/T1B	B	2-21/F	643	34	2	21.9
22W1/T1A	A	22/F	912	2	2	1.8
22W2/T1A	A	22/F	912	2	2	1.8
22W5/T1A	A	22/F	912	2	2	1.8
22W14/T1A	A	22/F	1064	1	1	1.1
22W6/T1C	C	22/F	914	1	1	0.9
22W5/T1C	C	22/F	1023	1	1	1.0
22W4/T1C	C	22/F	1423	1	1	1.4
22W3/T1C	C	22/F	1423	1	1	1.4
22W4/T1A	A	22/F	464	1	1	0.5
23W1/T1A	A	23/F	723	2	2	1.4
23W2/T1A	A	23/F	723	2	2	1.4
23W5/T1A	A	23/F	723	2	2	1.4
23W14/T1A	A	23/F	1064	1	1	1.1
23W6/T1C	C	23/F	914	1	1	0.9
23W5/T1C	C	23/F	1023	1	1	1.0
23W4/T1C	C	23/F	1423	1	1	1.4
23W3/T1C	C	23/F	1423	1	1	1.4
23W4/T1A	A	23/F	464	1	1	0.5
			總數	254		231.7

Precast

窗號	單位	Floor	加工長度 (mm)	總數量	每層數量	料總長度(m)
W3/T2A	A	1-21/F	723	36	2	26.0
W2/T2A	A	1-21/F	723	36	2	26.0
W2/T2B	B	1-21/F	723	36	2	26.0
W3/T2B	B	1-21/F	723	36	2	26.0
W6/T2C	C	1-21/F	914	18	1	16.5
W5/T2C	C	2-21/F	1023	17	1	17.4
W4/T2C	C	1-21/F	1423	18	1	25.6
W3/T2C	C	1-21/F	1423	18	1	25.6
W7/T2A	A	2-21/F	643	34	2	21.9
W7/T2B	B	2-21/F	643	34	2	21.9
22W3/T2A	A	22/F	723	2	2	1.4
22W2/T2A	A	22/F	723	2	2	1.4
22W2/T2B	B	22/F	723	2	2	1.4
22W3/T2B	B	22/F	723	2	2	1.4
22W6/T2C	C	22/F	914	1	1	0.9
22W5/T2C	C	22/F	1023	1	1	1.0
22W4/T2C	C	22/F	1423	1	1	1.4
22W3/T2C	C	22/F	1423	1	1	1.4
22W7/T2A	A	22/F	643	2	2	1.3
22W7/T2B	B	22/F	643	2	2	1.3
23W10/T2A	A	23/F	723	2	2	1.4
23W11/T2A	A	23/F	723	2	2	1.4
23W2/T2A	A	23/F	723	2	2	1.4
23W3/T2A	A	23/F	723	2	2	1.4
23W9/T2A	A	23/F	1423	1	1	1.4
23W8/T2A	A	23/F	1264	1	1	1.3
23W5/T2A	A	23/F	634	2	2	1.3
23W4/T2A	A	23/F	1423	1	1	1.4
23W6/T2A	A	23/F	914	1	1	0.9
23W6/T2C	C	23/F	914	1	1	0.9
23W5/T2C	C	23/F	1023	1	1	1.0
23W4/T2C	C	23/F	1423	1	1	1.4
23W3/T2C	C	23/F	1423	1	1	1.4
23W15/T2A	A	23/F	464	1	1	0.5
			總數	318		263.4

Precast

窗號	單位	Floor	加工長度 (mm)	總數量	每層數量	料總長度(m)
W2/T3A	A	1-21/F	723	36	2	26.0
W2/T3B	B	1-21/F	723	36	2	26.0
W3/T3B	B	1-21/F	723	36	2	26.0
W8/T3A	A	1-21/F	1423	18	1	25.6
W9/T3A	A	2-21/F	1423	17	1	24.2
W6/T3C	C	1-21/F	914	18	1	16.5
W5/T3C	C	2-21/F	1023	17	1	17.4
W4/T3C	C	1-21/F	1423	18	1	25.6
W3/T3C	C	1-21/F	1423	18	1	25.6
W7/T3B	B	2-21/F	643	34	2	21.9
22W5/T3A	A	22/F	723	2	2	1.4
22W2/T3A	A	22/F	723	2	2	1.4
22W1/T3A	A	22/F	723	2	2	1.4
22W14/T3A	A	22/F	1064	1	1	1.1
22W6/T3C	C	22/F	914	1	1	0.9
22W5/T3C	C	22/F	1023	1	1	1.0
22W4/T3C	C	22/F	1423	1	1	1.4
22W3/T3C	C	22/F	1423	1	1	1.4
22W/T3A	A	22/F	464	1	1	0.5
23W5/T3A	A	23/F	723	2	2	1.4
23W2/T3A	A	23/F	723	2	2	1.4
23W1/T3A	A	23/F	723	2	2	1.4
23W13/T3A	A	23/F	973	1	1	1.0
23W6/T3C	C	23/F	914	1	1	0.9
23W5/T3C	C	23/F	1023	1	1	1.0
23W4/T3C	C	23/F	1423	1	1	1.4
23W3/T3C	C	23/F	1423	1	1	1.4
23W/T3A	A	23/F	464	1	1	0.5
			總數	272		256.1

窗玉滴水線

Insitu						
	Floor	單位	加工長度 (mm)	總數量	每層數量	料總長度(M)
W10/T1A	1-21/F	A	1243.2	18	1	22
W8/T2A	1-21/F	A	1274	18	1	23
W10/T3A	1-21/F	A	1234	18	1	22
W8/T1B	1-21/F	B	1274	18	1	23
W9/T2B	1-21/F	B	693.2	18	1	12
W8/T3B	1-21/F	B	1249	18	1	22
W9/T1B	1-21/F	B	693.2	18	1	12
W8/T2B	1-21/F	B	1274	18	1	23
W9/T3B	1-21/F	B	693.2	18	1	12
			總數	162		173.3

Follow-up after Meeting with Midi on 24th March 2022

Attendees: Sino – Billy Tang, Jimmy Cheung, Tony Lai, Stephen Chow, T K Poon,
Alan Chan, Jaja Wong

Midi – Garry Chan, Marco, Eric, 祥

Description	Follow up by Midi
1) Drain system is not satisfy at sliding door, and 90% bottom capping for sliding door are shortened (After adding the drain holes and tested on 25/3/22, the drain performance is accepted.)	<ul style="list-style-type: none"> - Start to proceed to add the drain holes. - Provide an L-shape capping trial before end of March 2022 for review (Outstanding)
2) Water test should complete before end of May 2022 - Midi is required to update the water test schedule on 29 March 2022 (Eric submitted on 30/3, but water test complete at late July is not accepted)	<ul style="list-style-type: none"> - Re-submit water test schedule to achieve complete at end of May 2022 (Outstanding)
3) Slow progress of gondola set up - Midi is require to speed up and complete by below target include RPE inspection, (Planned 4 nos of gondola for each tower, total 12nos of gondola to be install): <ul style="list-style-type: none"> - T1 complete on 29/3/2022 (4 nos signed on 29/3) - T3 complete on 2/4/2022 (4 nos delivered, installation not yet complete) - T2 complete on 7/4/2022 (Not yet delivery) 	<ul style="list-style-type: none"> - Speed up gondola set up for Tower 2 & 3 on time
4) Outstanding material for noise screen – It affects to sales flat and sound test completion target (Antz replied that last batch delivery at mid of May is not accepted)	<ul style="list-style-type: none"> - Outstanding noise screen should delivery before mid of April 2022
5) Catch up to reply all site inspection report issued by Meinhardt. Detail please see attached summary (Please see attached at P.3) and major statistics as below: <ul style="list-style-type: none"> - Total defects: 665nos - Nos. of defects replied by Midi: 254nos - Outstanding defects: 441nos (Included 230nos of defect at Inspection Report #46 for 5/F mock up floor) 	<ul style="list-style-type: none"> - Settle and reply all the inspection report before 15 May 2022.
6) Remedial work for rain drip at curtain wall & window still outstanding, and no material on site. (Please see attached drawing detail and photo at P.4 ~ P.5)	<ul style="list-style-type: none"> - Material should delivery before mid of April 2022

