



工程指示 / 要求簡箋(E.I.)

工程指示編號：EI / 7196 / 23

修改版次：

工程編號：J - 858

工程名稱：將軍澳日出康城 11

工程項目：顧問上廠報告 (11/9-25/12) 精華版加完整版

收件人：生統 / Doris

發件人：Paul Wong

日期：29/12/2023

要求提供 / 確認 事項：

- | | | |
|------------------------------------|-------------------------------------|-------------------------------|
| <input type="checkbox"/> 初步鋁料 B.M. | <input type="checkbox"/> 加工拆圖，然後生產 | <input type="checkbox"/> 尺寸表 |
| <input type="checkbox"/> 正式鋁料 B.M. | <input type="checkbox"/> 技術上資料 / 指示 | <input type="checkbox"/> 報價 |
| <input type="checkbox"/> 配件 B.M. | <input type="checkbox"/> 樣辦或貨品說明書 | <input type="checkbox"/> 分判合約 |
- 內容：

顧問提出改善方案，請依相中指示，影回照片後放在群組 (J858 每日生產匯報群)。

請在 2024.01.10 前完成上列要求。

附： 頁

以上項目為：

- 原合約工程包 原合約工程加 / 減賬 新工程報價

原因：-

分發東莞各部門：

- | | | | |
|---|---|--|--|
| <input type="checkbox"/> 生產技術總監 <input type="checkbox"/> 連附件 | <input checked="" type="checkbox"/> 技術部 <input checked="" type="checkbox"/> 連附件 | <input type="checkbox"/> 生產部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 機械設計部 <input type="checkbox"/> 連附件 |
| <input type="checkbox"/> 採購部 <input type="checkbox"/> 連附件 | <input checked="" type="checkbox"/> 生產統籌部 <input checked="" type="checkbox"/> 連附件 | <input checked="" type="checkbox"/> 小羅 & 清 <input checked="" type="checkbox"/> 連附件 | |
| <input checked="" type="checkbox"/> 質檢部 <input checked="" type="checkbox"/> 連附件 | <input type="checkbox"/> 會計部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 報關組 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 其他 _____ <input type="checkbox"/> 連附件 |

分發香港各部門：

- | | | | |
|---|--|---|--|
| <input type="checkbox"/> 行政部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 會計部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 統籌部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 工程部地盤科文 <input type="checkbox"/> 連附件 |
| <input type="checkbox"/> 採購部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> QS 部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 維修部 <input type="checkbox"/> 連附件 | <input type="checkbox"/> 其他 _____ <input type="checkbox"/> 連附件 |

傳遞編號：

HK 3020 / 23

發件人簽署：

項目經理簽署：

Photo 7

Location:

湖南廠




Observation

Description:

Apply structural sealant for T3 36/F to 40/F MO23

Action:

MIDI is reminded to carry out the remedial works prior products delivery and to improve workmanship for future works

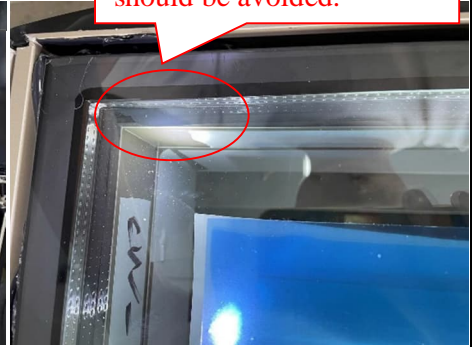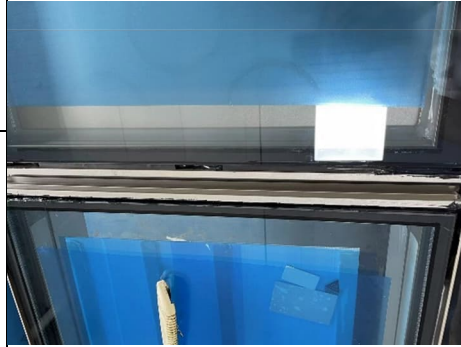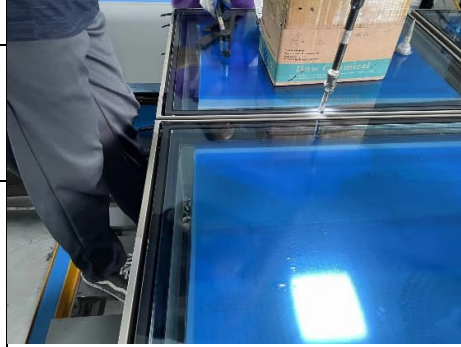

#1:
黑膠過多，影一條手工好的

Photo 8

Location:

湖南廠

Observation

Description:

Capping check and dimension check after applying structural sealant

Action:

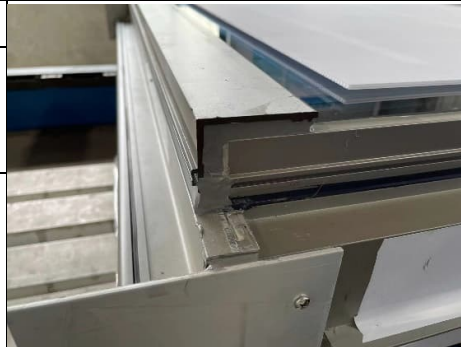


Photo 9

Location:
湖南廠

Observation

Description:
Water test for unitized panel No. AF-049 T3 38/F MO23

Action:
MIDI is reminded to find out the reason and test again.



#2:
單元件AF-049 T3 38/F MO23
漏水，俾試水報告。

Water entered the back panel.

3 COMMENT, RECOMMENDATIONS AND REMINDER

- During the assembly process, it may cause risks when crane is regularly operating because there is no protection for workers, such as safety helmet. It is recommended to strengthen the alert in the process of crane work, and improve the safety production awareness of workers. For all parties during the factory visit, please provide PPE.

#3:

吊運時，要有合適的個人防護裝備(圍欄，安全帽)。
