



工程指示 / 要求簡箋(E.I.)

工程指示編號：EI / 1575 / 20

修改版次：G

工程編號：J851

工程名稱：青衣 明翹匯

工程項目：確認模圖(後裝窗)

收件人：羅小姐

發件人：Leung Hin Wai

日期：19/05/2020

要求提供 / 確認 事項：

- | | | |
|------------------------------------|-------------------------------------|-------------------------------|
| <input type="checkbox"/> 初步鋁料 B.M. | <input type="checkbox"/> 加工拆圖，然後生產 | <input type="checkbox"/> 尺寸表 |
| <input type="checkbox"/> 正式鋁料 B.M. | <input type="checkbox"/> 技術上資料 / 指示 | <input type="checkbox"/> 報價 |
| <input type="checkbox"/> 配件 B.M. | <input type="checkbox"/> 樣辦或貨品說明書 | <input type="checkbox"/> 分判合約 |
| <input type="checkbox"/> 其他：_____ | | |

內容：

現確認附頁模圖。共1頁。

請在_____前完成上列要求。

附有關圖紙 / 文件： -

以上項目為：

- 原合約工程包 原合約工程加 / 減賬 新工程報價

原因：- _____

分發東莞各部門：

- () 生產技術總監 連附件 () 技術部 連附件 () 生產部 連附件 () 機械設計部 連附件
 () 採購部 連附件 () 生產統籌部 連附件
 () 質檢部 連附件 () 會計部 連附件 () 報關組 連附件 () 其他 _____ 連附件

分發香港各部門：

- () 行政部 連附件 () 會計部 連附件 () 統籌部 連附件 () 工程部地盤科文 連附件
 () 採購部 連附件 () QS 部 連附件 () 維修部 連附件 () 其他 _____ 連附件


傳遞編號：

HK 0870





發件人簽署：

項目經理簽署：

CUSTOMER	HONGKONG CO.	CUSTOMER APPROVAL	CUST PART NO.	X85696
			SECTION NO.	LH0091114

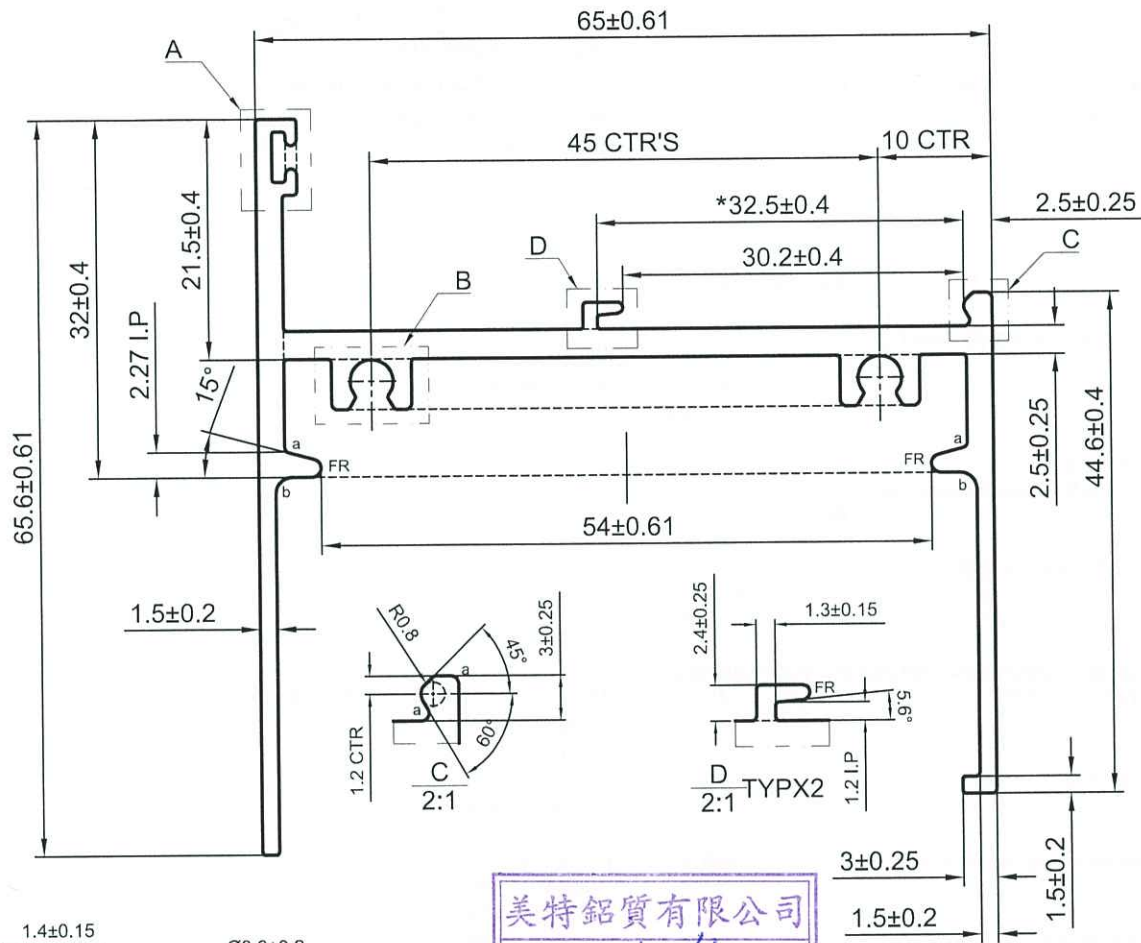

美特鋁質有限公司
承認圖面
日期 19/5-2020

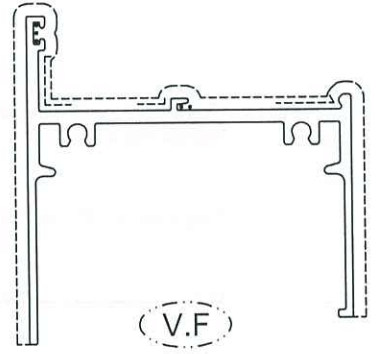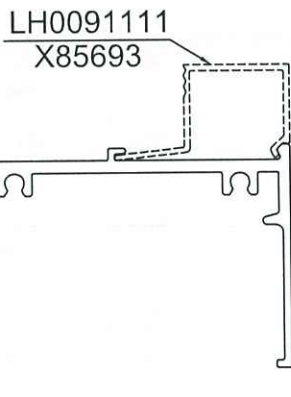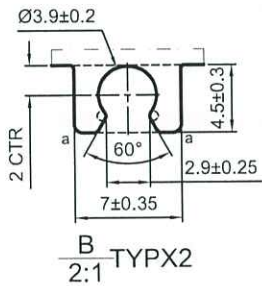

a=R0.5 b=R1.5

----- 次要裝飾面, 噴塗膜厚不足, 但不露底
----- 裝飾面
●●●●● 凹槽位置可能會有露底現象, 即膜厚不足
*配合尺寸以实物配合效果为准!

SIGNATURE GRADEING	HIGH SIGNATURE GRADEING	C.C.DIA(MM)	Ø 88.89		噴塗收費周長(mm): 215.33				
AREA (SQ MM)	409.85	UNSPECIFIED THICKNESS	2.3±0.2	PERIMETER (MM)	405.48	STANDARD	BS EN755	SCALE	1.5:1
MASS (KG/M)	1.111	UNSPECIFIED CORNERS	R 0.3	SURFACE AREA	215.33	ALLOY	6063-T6	VERSION	C
COMPANY ISSUE		B	DRAWN	陈晓舒	DATE	2020-05-18	APPELLATION	-	PAGE OF
			STANDARDIZATION		DATE				
			TO SIGN	陈国提	DATE				
			AUDITING		DATE				
MARKER	MODIFY	FILE NO	SIGNATURE	DATE	APPROV	DATE			

PANASIA ALUMINUM (CHINA) LIMITED
