



工程指示 / 要求簡箋(E.I.)

工程指示編號 : EI / 7755 / 24

修改版次 : -

工程編號 : J - 858

工程名稱 : 將軍澳日出康城 LP 11

工程項目 : 幕牆 monorail 電 Block (1 部) 地盤用

收件人 : Maggie

發件人 : Ant Yeung

日期 : 13/05/2024

□要求提供 / □確認 事項 :

- | | | |
|---------------|----------------|----------|
| () 初步鋁料 B.M. | () 加工拆圖, 然後生產 | () 尺寸表 |
| () 正式鋁料 B.M. | () 技術上資料 / 指示 | () 報價 |
| () 配件 B.M. | () 樣辦或貨品說明書 | () 分判合約 |

內容 :

因電 Block 經常壞, 業主多次要求提供備用的電 Block 現場更換用。
而華光已表示不會再提供額外的電 Block 供備用。
但在會議上, 業主不滿, 強烈要求 要有備用的電 Block。老闆已答應自行購買。

請訂購 1 部象牌 elephant, FAH 型號供 Monorail 備用
S.W.L 780 kg

請在 2024.05.17 前完成上列要求。

分發東莞各部門 :

- | | | | |
|-----------------|----------------|---------------|-------------------|
| () 生產技術總監 □連附件 | () 技術部 □連附件 | () 生產部 □連附件 | () 機械設計部 □連附件 |
| () 採購部 □連附件 | () 生產統籌部 □連附件 | () 小羅&清 □連附件 | |
| () 質檢部 □連附件 | () 會計部 □連附件 | () 報關組 □連附件 | () 其他 _____ □連附件 |

分發香港各部門 :

- | | | | |
|----------------|---------------|--------------|-----------------------|
| () 行政部 □連附件 | () 會計部 □連附件 | () 統籌部 □連附件 | (✓) 工程部地盤科文 積哥 □連附件 |
| (✓) 採購部 □連附件 | () QS 部 □連附件 | () 維修部 □連附件 | () 其他 _____ □連附件 |

傳遞編號 :

HK

/ 24

發件人簽署 :

項目經理簽署 :



LIMIT SWITCH

IP 500V 10A

LOAD CHAIN: 5A

1.1 x 2.1 Grape T

PRODUCED IN

ELEPHANT

CHAIN

MADE IN JAPAN

BLOCK CO., LTD

POWER SOURCE
LIFTING SPEED
CURRENT

50 HZ

380~415 V

7.6 m/min

4.5 A

60 HZ

380~415 V

9.1 m/min

4.8 A

SERIAL NO. FA-H 20370


現場電 Block FA-H

FAH·FB·SA

3 Phase, single speed

3 Phase, dual speed

1 phase

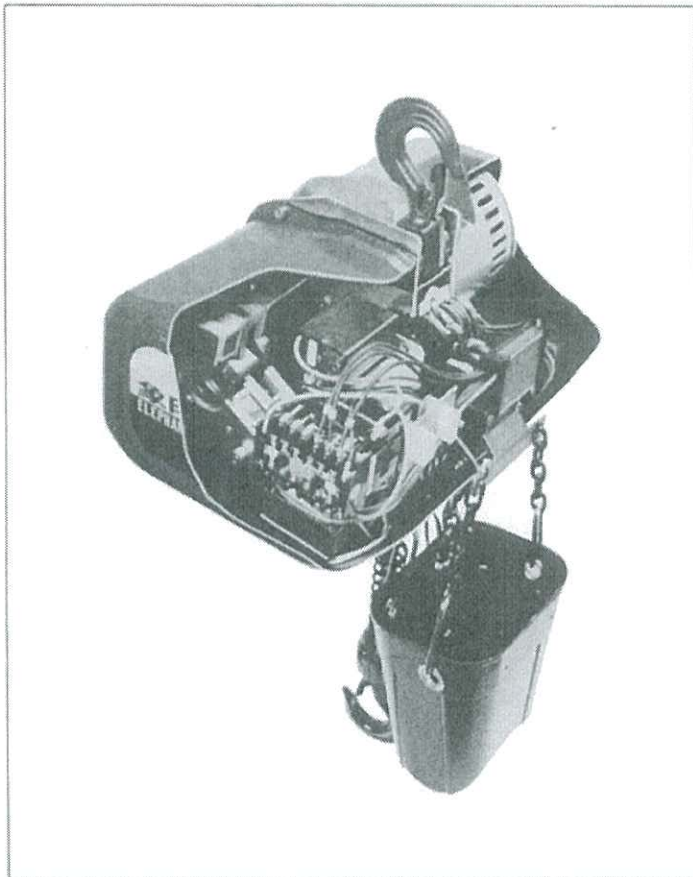

FEATURES

1. Tough, heavy-duty motor

3-phase: class E insulation

single speed FAH : 30 minutes

dual speed FB : 30 minutes (high speed)
15 minutes (low speed)

1-phase: class B insulation

single speed SA : 20minutes

2. Reliable electro-magnetic DC brake.

3. Highly durable load chain of our own manufacture.

4. Totally enclosed steel plate construction.

5. Wiring: Simple plug-in type connection of wires

6. Overload alarm hook

(In case of overloading, it gradually elongates without fracture.)

7. Chain bucket

specialy strengthened plastic bucket

Standard specifications

Power supply cable : 5m
Lifting height : 3m or 6m (0.25ton-2ton)
4m [3ton]

Option

1. Plain, geared or motorized trolley suspensions.
(motorized trolley for 3-phase model)
2. Overload protection device
3. Longer power supply cable
4. Larger lifting height (load chain and push button cord)
5. Dual speed: 1:6

50Hz ONLY

Model No.	Max working load (ton)	Manufacturer's test load (ton)	Standard lift (m)	Number of falls reeving	Load chain dia X pitch (mm)	Min. distance between hooks (mm)	Lifting speed (m/min)	Lifting motor output (kw)	Net weight (kg)	Measurement (M ³)
							[FB]High speed/Low speed			
FAH-0.5	0.5	0.63	3/6	1	6.3×19	480	7.0	0.9	43	0.067
FAH-1	1	1.25	3/6	1	7.1×21	570	7.6	1.6	56	0.082
FAH-2	2	2.5	3/6	2	7.1×21	710	3.8	1.6	64	0.100
FAH-3	3	3.5	4	3	7.1×21	810	2.5	1.6	83	0.124
FB-0.5	0.5	0.63	3/6	1	6.3×19	480	7.0/1.8	0.9/0.25	44	0.067
FB-1	1	1.25	3/6	1	7.1×21	570	6.3/1.6	1.6/0.4	57	0.082
FB-2	2	2.5	3/6	2	7.1×21	710	3.1×0.8	1.6/0.4	65	0.100
FB-3	3	3.5	4	3	7.1×21	810	2.1/0.5	1.6/0.4	84	0.124
SA-0.25	0.25	0.32	3/6	1	6.3×19	480	7.0	0.45	43	0.067
SA-0.5	0.5	0.63	3/6	1	6.3×19	480	3.5	0.45	43	0.067
SA-1	1	1.25	3/6	2	6.3×19	630	1.8	0.45	46	0.082
SA-1(S)	1	1.25	3/6	1	7.1×21	570	2.3	0.58	58	0.082



區強記機械集團有限公司

AU KEUNG KEE MACHINERY HOLDINGS LTD.

香港九龍旺角彌敦道918號地下至六樓

G/F-6/F., 918 CANTON ROAD, MONGKOK, KOWLOON, HONG KONG.

• 寫字樓 OFFICE TEL: 23889318 FAX: 23851603

• 門市部 SHOWROOM TEL: 23889118 FAX: 27825783

• 營業部 SALES DEPT. TEL: 23881903 FAX: 27708357

E-mail: admin@akc.com.hk Website: www.aukeungkee.com



ELEPHANT CHAIN BLOCK CO., LTD.
OSAKA, JAPAN

Printed in Japan 0786 3000

Specifications and figures are subject to change without notice for improvement.
