美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.

工程指示 / 要求簡箋 ENGINEER INSTRUCTIONS(E.I.)

工程指示編號:	EI- 5465/2r	**修改版本:**	-
	HK- 2240/2r		
工程編號:	J 857	**工程名稱:**	啟德6552
收件人:	生統	**發件人:**	Nero HO
工程項目:	幕牆單元件 - 地盤用收口鋁板(特式層)	**日期:**	13/12/2022

☐ 原合約工程包	☐ 原合約工程加 / 減賬 QT-	☐ 新工程報價 QT-

信件批核號碼/圖紙參考編號:	**批核模具圖紙編號:**
客戶指示附件:	**管理內部批簽署:**

☐ 初步鋁料 B.M.	☐ 加工拆圖，然後生產	☐ 尺寸表
☐ 正式鋁料 B.M.	☐ 技術上資料／指示	☐ 報價
☐ 配件 B.M.	☐ 樣辦或貨品說明書	☐ 分判合約
☐ 其他:		

內容:
按附件資料生產加工收口鋁板，送地盤。

完成上列要求日期: 30/12/2022

國內

☐ 生產技術總監	☐ 連附件	☐ 技術部	☐ 連附件	☐ 生產部	☐ 連附件
☐ 採購部	☐ 連附件	☑ 生產統籌部	☑ 連附件	☐ 報關組	☐ 連附件
☐ 質檢部	☐ 連附件	☐ 會計部	☐ 連附件	☐ 機械設計部	☐ 連附件
☐ 香港辦	☐ 連附件	☐ 其他:			

☐ 行政部	☐ 連附件	☐ 會計部	☐ 連附件	☐ 統籌部	☐ 連附件	☐ 工程部	☐ 連附件
☐ 採購部	☐ 連附件	☐ QS部	☐ 連附件	☑ 地盤管理	☑ 連附件	☐ 維修部	☐ 連附件

*發件人簽署：	*組別成員批核簽署：
傳遞編號： 4/C 2240/2r	項目經理簽署：

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
1		AC-701	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	8.991	0.415	1.659	0.415	1.659	AC-701
2		AC-702	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.336	0.800	0.800	0.800	0.800	AC-702
3		AC-703	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	5.345	0.247	0.986	0.247	0.986	AC-703
4		AC-704	3mm 铝板	AL2: ECK3M96295S-ZD1	5	0	5	6.682	0.247	1.233	0.247	1.233	AC-704
5		AC-705	3mm 铝板	AL2: ECK3M96295S-ZD1	9	0	9	15.980	0.328	2.948	0.328	2.948	AC-705
6		AC-706	3mm 铝板	AL2: ECK3M96295S-ZD1	9	0	9	13.719	0.281	2.531	0.281	2.531	AC-706
7		AC-707	3mm 铝板	AL2: ECK3M96295S-ZD1	10	0	10	17.755	0.328	3.276	0.328	3.276	AC-707
8		AC-708	3mm 铝板	AL2: ECK3M96295S-ZD1	11	0	11	16.768	0.281	3.094	0.281	3.094	AC-708
9		AC-709	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	3.860	0.356	0.712	0.356	0.712	AC-709
10		AC-710	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	5.075	0.312	0.936	0.312	0.936	AC-710
11		AC-711	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	5.075	0.312	0.936	0.312	0.936	AC-711
12		AC-712	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.071	0.567	0.567	0.567	0.567	AC-712
13		AC-713	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	6.743	0.415	1.244	0.415	1.244	AC-713
14		AC-714	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.964	0.362	0.362	0.362	0.362	AC-714
15		AC-715	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.687	0.311	0.311	0.311	0.311	AC-715
16		AC-716	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	24.933	1.150	4.600	1.150	4.600	AC-716
17		AC-717	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	21.406	0.987	3.949	0.987	3.949	AC-717
18		AC-718	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	6.233	1.150	1.150	1.150	1.150	AC-718
19		AC-719	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.351	0.987	0.987	0.987	0.987	AC-719
20		AC-720	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.393	0.811	0.811	0.811	0.811	AC-720

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
21		AC-723	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.891	0.718	0.718	0.718	0.718	AC-723
22		AC-724	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.341	0.616	0.616	0.616	0.616	AC-724
23		AC-725	3mm 铝板	鉻化	1	0	1	1.379	0.254	0.254	0.254	0.254	AC-725
24		AC-726	3mm 铝板	鉻化	1	0	1	1.184	0.218	0.218	0.218	0.218	AC-726
25		AC-727	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.477	0.826	0.826	0.826	0.826	AC-727
26		AC-728	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.843	0.709	0.709	0.709	0.709	AC-728
27		AC-729	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	6.554	1.209	1.209	1.209	1.209	AC-729
28		AC-730	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.627	1.038	1.038	1.038	1.038	AC-730
29		AC-731	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	7.904	1.458	1.458	1.458	1.458	AC-731
30		AC-732	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	12.467	1.150	2.300	1.150	2.300	AC-732
31		AC-733	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	16.054	0.987	2.962	0.987	2.962	AC-733
32		AC-734	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.023	0.742	0.742	0.742	0.742	AC-734
33		AC-735	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.691	0.866	0.866	0.866	0.866	AC-735
34		AC-736	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	6.231	0.383	1.150	0.383	1.150	AC-736
35		AC-737	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.231	0.390	0.781	0.390	0.781	AC-737
36		AC-738	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.154	0.383	0.766	0.383	0.766	AC-738
37		AC-739	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	3.860	0.356	0.712	0.356	0.712	AC-739
38		AC-740	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.116	0.390	0.390	0.390	0.390	AC-740
39		AC-741	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.406	0.259	0.259	0.259	0.259	AC-741
40		AC-742	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.734	0.689	0.689	0.689	0.689	AC-742

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
41		AC-743	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.981	0.181	0.181	0.181	0.181	AC-743
42		AC-744	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	11.481	2.118	2.118	2.118	2.118	AC-744
43		AC-801-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	11.340	2.092	2.092	2.092	2.092	AC-801
44		AC-801-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.920	2.015	2.015	2.015	2.015	AC-801
45		AC-801-3	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	21.731	2.005	4.009	2.005	4.009	AC-801
46		AC-801-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.380	0.808	0.808	0.808	0.808	AC-801
47		AC-801-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.128	1.684	1.684	1.684	1.684	AC-801
48		AC-801-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.928	2.939	2.939	2.939	2.939	AC-801
49		AC-801-7	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.241	2.812	2.812	2.812	2.812	AC-801
50		AC-801-8	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.195	2.804	2.804	2.804	2.804	AC-801
51		AC-801-9	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.558	3.239	3.239	3.239	3.239	AC-801
52		AC-801-10	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.558	3.239	3.239	3.239	3.239	AC-801
53		AC-801-11	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.195	2.804	2.804	2.804	2.804	AC-801
54		AC-801-12	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.241	2.812	2.812	2.812	2.812	AC-801
55		AC-801-13	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.077	3.704	3.704	3.704	3.704	AC-801
56		AC-801-14	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	13.366	2.466	2.466	2.466	2.466	AC-801
57		AC-802-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	20.472	1.889	3.777	1.889	3.777	AC-802
58		AC-802-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.126	0.761	0.761	0.761	0.761	AC-802
59		AC-803	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.316	0.427	0.427	0.427	0.427	AC-803
60		AC-804	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.182	0.403	0.403	0.403	0.403	AC-804

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
61		AC-805-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.498	1.568	1.568	1.568	1.568	AC-805
62		AC-806-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.128	1.684	1.684	1.684	1.684	AC-806
63		AC-807-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.050	1.485	1.485	1.485	1.485	AC-807
64		AC-808-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.050	1.485	1.485	1.485	1.485	AC-808
65		AC-809-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.498	1.568	1.568	1.568	1.568	AC-809
66		AC-810-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	20.472	1.889	3.777	1.889	3.777	AC-810
67		AC-810-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.126	0.761	0.761	0.761	0.761	AC-810
68		AC-811-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	21.731	2.005	4.009	2.005	4.009	AC-811
69		AC-811-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.380	0.808	0.808	0.808	0.808	AC-811
70		AC-812	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.182	0.403	0.403	0.403	0.403	AC-812
71		AC-813	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.316	0.427	0.427	0.427	0.427	AC-813
72		AC-814-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.459	1.745	1.745	1.745	1.745	AC-814
73		AC-815-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	12.992	2.397	2.397	2.397	2.397	AC-815
74		AC-816-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-816
75		AC-816-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.081	0.753	0.753	0.753	0.753	AC-816
76		AC-816-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-816
77		AC-817	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.158	0.398	0.398	0.398	0.398	AC-817
78		AC-818-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-818
79		AC-818-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.081	0.753	0.753	0.753	0.753	AC-818
80		AC-818-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-818

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
81		AC-819	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.158	0.398	0.398	0.398	0.398	AC-819
82		AC-820	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	14.000	2.583	2.583	2.583	2.583	AC-820
83		AC-821-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	14.210	2.622	2.622	2.622	2.622	AC-821
84		AC-822-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.056	0.564	0.564	0.564	0.564	AC-822
85		AC-822-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.981	0.550	0.550	0.550	0.550	AC-822
86		AC-822-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.972	0.548	0.548	0.548	0.548	AC-822
87		AC-822-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.434	0.634	0.634	0.634	0.634	AC-822
88		AC-822-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.434	0.634	0.634	0.634	0.634	AC-822
89		AC-822-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.972	0.548	0.548	0.548	0.548	AC-822
90		AC-822-7	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.981	0.550	0.550	0.550	0.550	AC-822
91		AC-822-8	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.851	0.711	0.711	0.711	0.711	AC-822
92		AC-823	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	19.548	3.607	3.607	3.607	3.607	AC-823
93		AC-824	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.750	0.692	0.692	0.692	0.692	AC-824
94		AC-825	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.575	3.796	3.796	3.796	3.796	AC-825
95		AC-826	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.024	0.743	0.743	0.743	0.743	AC-826
96		AC-827	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	18.183	3.355	3.355	3.355	3.355	AC-827
97		AC-828	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.556	0.656	0.656	0.656	0.656	AC-828
98		AC-829	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	18.183	3.355	3.355	3.355	3.355	AC-829
99		AC-830	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.556	0.656	0.656	0.656	0.656	AC-830
100		AC-831	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.575	3.796	3.796	3.796	3.796	AC-831

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
101		AC-832	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.024	0.743	0.743	0.743	0.743	AC-832
102		AC-833	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	23.853	4.401	4.401	4.401	4.401	AC-833
103		AC-834	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.576	0.844	0.844	0.844	0.844	AC-834
104		AC-835	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.926	0.540	0.540	0.540	0.540	AC-835
105		AC-836	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.243	0.414	0.414	0.414	0.414	AC-836
106		AC-837	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.141	0.764	0.764	0.764	0.764	AC-837
107		AC-839	1.5mm 铝板	鉻化	1	0	1	1.183	0.218	0.218	0.218	0.218	AC-839
108		AC-840	1.5mm 铝板	鉻化	1	0	1	0.957	0.177	0.177	0.177	0.177	AC-840
109		AC-841	1.5mm 铝板	鉻化	1	0	1	1.674	0.309	0.309	0.309	0.309	AC-841
110		AC-842	1.5mm 铝板	鉻化	1	0	1	1.183	0.218	0.218	0.218	0.218	AC-842
111		AC-843	1.5mm 铝板	鉻化	1	0	1	0.957	0.177	0.177	0.177	0.177	AC-843
112		AC-844	1.5mm 铝板	鉻化	1	0	1	1.674	0.309	0.309	0.309	0.309	AC-844
113		AC-845	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.178	0.955	0.955	0.955	0.955	AC-845
114		AC-846	1.5mm 铝板	鉻化	1	0	1	1.574	0.290	0.290	0.290	0.290	AC-846
115		AC-847	1.5mm 铝板	鉻化	1	0	1	4.559	0.841	0.841	0.841	0.841	AC-847
116		AC-851	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.560	0.103	0.103	0.103	0.103	AC-851
117		AC-852	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.733	0.135	0.135	0.135	0.135	AC-852
118		AC-853	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.538	0.099	0.099	0.099	0.099	AC-853
119		AC-854	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.704	0.130	0.130	0.130	0.130	AC-854
120		AC-855	3mm 铝板	鉻化	1	0	1	0.346	0.064	0.064	0.064	0.064	AC-855

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次 :		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
121		AC-856	3mm 铝板	鉻化	1	0	1	0.332	0.061	0.061	0.061	0.061	AC-856
122		AC-857	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.887	0.082	0.164	0.082	0.164	AC-857
123		AC-858	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.162	0.107	0.214	0.107	0.214	AC-858
124		AC-859-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.821	0.076	0.152	0.076	0.152	AC-859
125		AC-859-2	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.774	0.071	0.143	0.071	0.143	AC-859
126		AC-859-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.405	0.075	0.075	0.075	0.075	AC-859
127		AC-860-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.075	0.099	0.198	0.099	0.198	AC-860
128		AC-860-2	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.013	0.093	0.187	0.093	0.187	AC-860
129		AC-860-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.531	0.098	0.098	0.098	0.098	AC-860
130		AC-861	3mm 铝板	鉻化	2	0	2	0.544	0.050	0.100	0.050	0.100	AC-861
131		AC-862-1	3mm 铝板	鉻化	2	0	2	0.507	0.047	0.094	0.047	0.094	AC-862
132		AC-862-2	3mm 铝板	鉻化	2	0	2	0.475	0.044	0.088	0.044	0.088	AC-862
133		AC-862-3	3mm 铝板	鉻化	1	0	1	0.249	0.046	0.046	0.046	0.046	AC-862
134		AC-863-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.505	0.093	0.093	0.093	0.093	AC-863
135		AC-864-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.661	0.122	0.122	0.122	0.122	AC-864
136		AC-865-1	3mm 铝板	鉻化	1	0	1	0.311	0.057	0.057	0.057	0.057	AC-865
137		AC-866-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.560	0.103	0.103	0.000	0.000	AC-866
138		AC-867-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.733	0.135	0.135	0.000	0.000	AC-867
139		AC-868-1	3mm 铝板	鉻化	1	0	1	0.346	0.064	0.064	0.000	0.000	AC-868
140		AC-869-1	1.5mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.827	0.153	0.153	0.000	0.000	AC-869

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
141		AC-870-1	1.5mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.827	0.153	0.153	0.000	0.000	AC-870
142		AC-871-1	1.5mm 铝板	鉻化	1	0	1	0.352	0.065	0.065	0.000	0.000	AC-871
143		AC-901	1.5mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	34.018	2.092	6.276	0.000	0.000	AC-901
144		AC-902	1.5mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	8.161	0.502	1.506	0.000	0.000	AC-902
145		AC-903	1.5mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	16.024	2.956	2.956	0.000	0.000	AC-903
146		AC-904	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.535	0.652	0.652	0.652	0.652	AC-904
147		AC-905	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	43.751	4.036	8.072	4.036	8.072	AC-905
148		AC-906	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	10.496	0.968	1.937	0.968	1.937	AC-906
149		AC-907	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.358	3.203	3.203	3.203	3.203	AC-907
150		AC-908	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.829	0.706	0.706	0.706	0.706	AC-908
151		AC-909	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.581	1.952	1.952	1.952	1.952	AC-909
152		AC-910	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.334	0.431	0.431	0.431	0.431	AC-910
153		AC-911	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.160	2.797	2.797	2.797	2.797	AC-911
154		AC-912	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.344	0.617	0.617	0.617	0.617	AC-912
155		AC-913	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.790	0.515	0.515	0.515	0.515	AC-913
156		AC-951-1	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	4.170	0.192	0.769	0.192	0.769	AC-951
157		AC-951-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.132	0.393	0.393	0.393	0.393	AC-951
158		AC-951-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.539	0.284	0.284	0.284	0.284	AC-951
159		AC-951-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.393	0.626	0.626	0.626	0.626	AC-951
160		AC-951-5	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.727	0.252	0.503	0.252	0.503	AC-951

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	细栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
161		AC-951-6	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.585	0.423	0.846	0.423	0.846	AC-951
162		AC-951-7	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.348	0.217	0.433	0.217	0.433	AC-951
163		AC-951-8	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.791	0.165	0.331	0.165	0.331	AC-951
164		AC-951-9	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	10.464	0.644	1.931	0.644	1.931	AC-951
165		AC-951-10	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.812	0.259	0.519	0.259	0.519	AC-951
166		AC-951-11	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.600	0.295	0.295	0.295	0.295	AC-951
167		AC-951-12	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.363	0.252	0.252	0.252	0.252	AC-951
168		AC-951-13	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.811	0.334	0.334	0.334	0.334	AC-951
169		AC-951-14	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.238	0.228	0.228	0.228	0.228	AC-951
170		AC-952-1	3mm 铝板	AL2: ECK3M96295S-ZD1	8	0	8	3.754	0.087	0.693	0.087	0.693	AC-952
171		AC-952-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.045	0.193	0.193	0.193	0.193	AC-952
172		AC-952-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.175	0.217	0.217	0.217	0.217	AC-952
173		AC-952-4	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	3.475	0.160	0.641	0.160	0.641	AC-952
174		AC-952-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.999	0.184	0.184	0.184	0.184	AC-952
175		AC-952-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.943	0.174	0.174	0.174	0.174	AC-952
176		AC-953	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.877	0.900	0.900	0.900	0.900	AC-953
177		AC-954	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.889	0.349	0.349	0.349	0.349	AC-954
				總計：	282		282	1172.65	165.972	216.36	159.75	204.944	

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
1		AC-701	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	8.991	0.415	1.659	0.415	1.659	AC-701
2		AC-702	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.336	0.800	0.800	0.800	0.800	AC-702
3		AC-703	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	5.345	0.247	0.986	0.247	0.986	AC-703
4		AC-704	3mm 铝板	AL2: ECK3M96295S-ZD1	5	0	5	6.682	0.247	1.233	0.247	1.233	AC-704
5		AC-705	3mm 铝板	AL2: ECK3M96295S-ZD1	9	0	9	15.980	0.328	2.948	0.328	2.948	AC-705
6		AC-706	3mm 铝板	AL2: ECK3M96295S-ZD1	9	0	9	13.719	0.281	2.531	0.281	2.531	AC-706
7		AC-707	3mm 铝板	AL2: ECK3M96295S-ZD1	10	0	10	17.755	0.328	3.276	0.328	3.276	AC-707
8		AC-708	3mm 铝板	AL2: ECK3M96295S-ZD1	11	0	11	16.768	0.281	3.094	0.281	3.094	AC-708
9		AC-709	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	3.860	0.356	0.712	0.356	0.712	AC-709
10		AC-710	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	5.075	0.312	0.936	0.312	0.936	AC-710
11		AC-711	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	5.075	0.312	0.936	0.312	0.936	AC-711
12		AC-712	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.071	0.567	0.567	0.567	0.567	AC-712
13		AC-713	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	6.743	0.415	1.244	0.415	1.244	AC-713
14		AC-714	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.964	0.362	0.362	0.362	0.362	AC-714
15		AC-715	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.687	0.311	0.311	0.311	0.311	AC-715
16		AC-716	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	24.933	1.150	4.600	1.150	4.600	AC-716
17		AC-717	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	21.406	0.987	3.949	0.987	3.949	AC-717
18		AC-718	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	6.233	1.150	1.150	1.150	1.150	AC-718
19		AC-719	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.351	0.987	0.987	0.987	0.987	AC-719
20		AC-720	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.393	0.811	0.811	0.811	0.811	AC-720

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
21		AC-723	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.891	0.718	0.718	0.718	0.718	AC-723
22		AC-724	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.341	0.616	0.616	0.616	0.616	AC-724
23		AC-725	3mm 铝板	鉻化	1	0	1	1.379	0.254	0.254	0.254	0.254	AC-725
24		AC-726	3mm 铝板	鉻化	1	0	1	1.184	0.218	0.218	0.218	0.218	AC-726
25		AC-727	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.477	0.826	0.826	0.826	0.826	AC-727
26		AC-728	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.843	0.709	0.709	0.709	0.709	AC-728
27		AC-729	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	6.554	1.209	1.209	1.209	1.209	AC-729
28		AC-730	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.627	1.038	1.038	1.038	1.038	AC-730
29		AC-731	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	7.904	1.458	1.458	1.458	1.458	AC-731
30		AC-732	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	12.467	1.150	2.300	1.150	2.300	AC-732
31		AC-733	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	16.054	0.987	2.962	0.987	2.962	AC-733
32		AC-734	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.023	0.742	0.742	0.742	0.742	AC-734
33		AC-735	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.691	0.866	0.866	0.866	0.866	AC-735
34		AC-736	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	6.231	0.383	1.150	0.383	1.150	AC-736
35		AC-737	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.231	0.390	0.781	0.390	0.781	AC-737
36		AC-738	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.154	0.383	0.766	0.383	0.766	AC-738
37		AC-739	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	3.860	0.356	0.712	0.356	0.712	AC-739
38		AC-740	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.116	0.390	0.390	0.390	0.390	AC-740
39		AC-741	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.406	0.259	0.259	0.259	0.259	AC-741
40		AC-742	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.734	0.689	0.689	0.689	0.689	AC-742

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
41		AC-743	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.981	0.181	0.181	0.181	0.181	AC-743
42		AC-744	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	11.481	2.118	2.118	2.118	2.118	AC-744
43		AC-801-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	11.340	2.092	2.092	2.092	2.092	AC-801
44		AC-801-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.920	2.015	2.015	2.015	2.015	AC-801
45		AC-801-3	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	21.731	2.005	4.009	2.005	4.009	AC-801
46		AC-801-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.380	0.808	0.808	0.808	0.808	AC-801
47		AC-801-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.128	1.684	1.684	1.684	1.684	AC-801
48		AC-801-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.928	2.939	2.939	2.939	2.939	AC-801
49		AC-801-7	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.241	2.812	2.812	2.812	2.812	AC-801
50		AC-801-8	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.195	2.804	2.804	2.804	2.804	AC-801
51		AC-801-9	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.558	3.239	3.239	3.239	3.239	AC-801
52		AC-801-10	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.558	3.239	3.239	3.239	3.239	AC-801
53		AC-801-11	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.195	2.804	2.804	2.804	2.804	AC-801
54		AC-801-12	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.241	2.812	2.812	2.812	2.812	AC-801
55		AC-801-13	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.077	3.704	3.704	3.704	3.704	AC-801
56		AC-801-14	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	13.366	2.466	2.466	2.466	2.466	AC-801
57		AC-802-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	20.472	1.889	3.777	1.889	3.777	AC-802
58		AC-802-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.126	0.761	0.761	0.761	0.761	AC-802
59		AC-803	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.316	0.427	0.427	0.427	0.427	AC-803
60		AC-804	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.182	0.403	0.403	0.403	0.403	AC-804

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
61		AC-805-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.498	1.568	1.568	1.568	1.568	AC-805
62		AC-806-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.128	1.684	1.684	1.684	1.684	AC-806
63		AC-807-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.050	1.485	1.485	1.485	1.485	AC-807
64		AC-808-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.050	1.485	1.485	1.485	1.485	AC-808
65		AC-809-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	8.498	1.568	1.568	1.568	1.568	AC-809
66		AC-810-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	20.472	1.889	3.777	1.889	3.777	AC-810
67		AC-810-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.126	0.761	0.761	0.761	0.761	AC-810
68		AC-811-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	21.731	2.005	4.009	2.005	4.009	AC-811
69		AC-811-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.380	0.808	0.808	0.808	0.808	AC-811
70		AC-812	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.182	0.403	0.403	0.403	0.403	AC-812
71		AC-813	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.316	0.427	0.427	0.427	0.427	AC-813
72		AC-814-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	9.459	1.745	1.745	1.745	1.745	AC-814
73		AC-815-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	12.992	2.397	2.397	2.397	2.397	AC-815
74		AC-816-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-816
75		AC-816-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.081	0.753	0.753	0.753	0.753	AC-816
76		AC-816-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-816
77		AC-817	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.158	0.398	0.398	0.398	0.398	AC-817
78		AC-818-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-818
79		AC-818-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.081	0.753	0.753	0.753	0.753	AC-818
80		AC-818-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.124	1.868	1.868	1.868	1.868	AC-818

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
81		AC-819	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.158	0.398	0.398	0.398	0.398	AC-819
82		AC-820	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	14.000	2.583	2.583	2.583	2.583	AC-820
83		AC-821-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	14.210	2.622	2.622	2.622	2.622	AC-821
84		AC-822-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.056	0.564	0.564	0.564	0.564	AC-822
85		AC-822-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.981	0.550	0.550	0.550	0.550	AC-822
86		AC-822-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.972	0.548	0.548	0.548	0.548	AC-822
87		AC-822-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.434	0.634	0.634	0.634	0.634	AC-822
88		AC-822-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.434	0.634	0.634	0.634	0.634	AC-822
89		AC-822-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.972	0.548	0.548	0.548	0.548	AC-822
90		AC-822-7	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.981	0.550	0.550	0.550	0.550	AC-822
91		AC-822-8	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.851	0.711	0.711	0.711	0.711	AC-822
92		AC-823	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	19.548	3.607	3.607	3.607	3.607	AC-823
93		AC-824	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.750	0.692	0.692	0.692	0.692	AC-824
94		AC-825	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.575	3.796	3.796	3.796	3.796	AC-825
95		AC-826	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.024	0.743	0.743	0.743	0.743	AC-826
96		AC-827	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	18.183	3.355	3.355	3.355	3.355	AC-827
97		AC-828	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.556	0.656	0.656	0.656	0.656	AC-828
98		AC-829	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	18.183	3.355	3.355	3.355	3.355	AC-829
99		AC-830	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.556	0.656	0.656	0.656	0.656	AC-830
100		AC-831	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	20.575	3.796	3.796	3.796	3.796	AC-831

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次：		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
101		AC-832	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.024	0.743	0.743	0.743	0.743	AC-832
102		AC-833	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	23.853	4.401	4.401	4.401	4.401	AC-833
103		AC-834	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.576	0.844	0.844	0.844	0.844	AC-834
104		AC-835	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.926	0.540	0.540	0.540	0.540	AC-835
105		AC-836	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.243	0.414	0.414	0.414	0.414	AC-836
106		AC-837	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.141	0.764	0.764	0.764	0.764	AC-837
107		AC-839	1.5mm 铝板	鉻化	1	0	1	1.183	0.218	0.218	0.218	0.218	AC-839
108		AC-840	1.5mm 铝板	鉻化	1	0	1	0.957	0.177	0.177	0.177	0.177	AC-840
109		AC-841	1.5mm 铝板	鉻化	1	0	1	1.674	0.309	0.309	0.309	0.309	AC-841
110		AC-842	1.5mm 铝板	鉻化	1	0	1	1.183	0.218	0.218	0.218	0.218	AC-842
111		AC-843	1.5mm 铝板	鉻化	1	0	1	0.957	0.177	0.177	0.177	0.177	AC-843
112		AC-844	1.5mm 铝板	鉻化	1	0	1	1.674	0.309	0.309	0.309	0.309	AC-844
113		AC-845	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	5.178	0.955	0.955	0.955	0.955	AC-845
114		AC-846	1.5mm 铝板	鉻化	1	0	1	1.574	0.290	0.290	0.290	0.290	AC-846
115		AC-847	1.5mm 铝板	鉻化	1	0	1	4.559	0.841	0.841	0.841	0.841	AC-847
116		AC-851	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.560	0.103	0.103	0.103	0.103	AC-851
117		AC-852	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.733	0.135	0.135	0.135	0.135	AC-852
118		AC-853	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.538	0.099	0.099	0.099	0.099	AC-853
119		AC-854	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.704	0.130	0.130	0.130	0.130	AC-854
120		AC-855	3mm 铝板	鉻化	1	0	1	0.346	0.064	0.064	0.064	0.064	AC-855
121		AC-856	3mm 铝板	鉻化	1	0	1	0.332	0.061	0.061	0.061	0.061	AC-856

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:	修改版次:		A/C Code:		總面積:	216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
122		AC-857	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.887	0.082	0.164	0.082	0.164	AC-857
123		AC-858	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.162	0.107	0.214	0.107	0.214	AC-858
124		AC-859-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.821	0.076	0.152	0.076	0.152	AC-859
125		AC-859-2	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	0.774	0.071	0.143	0.071	0.143	AC-859
126		AC-859-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.405	0.075	0.075	0.075	0.075	AC-859
127		AC-860-1	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.075	0.099	0.198	0.099	0.198	AC-860
128		AC-860-2	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.013	0.093	0.187	0.093	0.187	AC-860
129		AC-860-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.531	0.098	0.098	0.098	0.098	AC-860
130		AC-861	3mm 铝板	鉻化	2	0	2	0.544	0.050	0.100	0.050	0.100	AC-861
131		AC-862-1	3mm 铝板	鉻化	2	0	2	0.507	0.047	0.094	0.047	0.094	AC-862
132		AC-862-2	3mm 铝板	鉻化	2	0	2	0.475	0.044	0.088	0.044	0.088	AC-862
133		AC-862-3	3mm 铝板	鉻化	1	0	1	0.249	0.046	0.046	0.046	0.046	AC-862
134		AC-863-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.505	0.093	0.093	0.093	0.093	AC-863
135		AC-864-1	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.661	0.122	0.122	0.122	0.122	AC-864
136		AC-865-1	3mm 铝板	鉻化	1	0	1	0.311	0.057	0.057	0.057	0.057	AC-865
137		AC-866-1	3mm 铝板	**AL2: ECK3M96295S-ZD1**	1	0	1	0.560	0.103	0.103	0.000	0.000	AC-866
138		AC-867-1	3mm 铝板	**AL2: ECK3M96295S-ZD1**	1	0	1	0.733	0.135	0.135	0.000	0.000	AC-867
139		AC-868-1	3mm 铝板	鉻化	1	0	1	0.346	0.064	0.064	0.000	0.000	AC-868
140		AC-869-1	1.5mm 铝板	**AL2: ECK3M96295S-ZD1**	1	0	1	0.827	0.153	0.153	0.000	0.000	AC-869
141		AC-870-1	1.5mm 铝板	**AL2: ECK3M96295S-ZD1**	1	0	1	0.827	0.153	0.153	0.000	0.000	AC-870

美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.		工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
		地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表		項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積:	216.355	總重量:	1172.65


序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
142		AC-871-1	1.5mm 铝板	鉻化	1	0	1	0.352	0.065	0.065	0.000	0.000	AC-871
143		AC-901	1.5mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	34.018	2.092	6.276	0.000	0.000	AC-901
144		AC-902	1.5mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	8.161	0.502	1.506	0.000	0.000	AC-902
145		AC-903	1.5mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	16.024	2.956	2.956	0.000	0.000	AC-903
146		AC-904	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.535	0.652	0.652	0.652	0.652	AC-904
147		AC-905	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	43.751	4.036	8.072	4.036	8.072	AC-905
148		AC-906	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	10.496	0.968	1.937	0.968	1.937	AC-906
149		AC-907	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	17.358	3.203	3.203	3.203	3.203	AC-907
150		AC-908	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.829	0.706	0.706	0.706	0.706	AC-908
151		AC-909	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	10.581	1.952	1.952	1.952	1.952	AC-909
152		AC-910	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.334	0.431	0.431	0.431	0.431	AC-910
153		AC-911	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	15.160	2.797	2.797	2.797	2.797	AC-911
154		AC-912	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.344	0.617	0.617	0.617	0.617	AC-912
155		AC-913	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.790	0.515	0.515	0.515	0.515	AC-913
156		AC-951-1	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	4.170	0.192	0.769	0.192	0.769	AC-951
157		AC-951-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	2.132	0.393	0.393	0.393	0.393	AC-951
158		AC-951-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.539	0.284	0.284	0.284	0.284	AC-951
159		AC-951-4	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	3.393	0.626	0.626	0.626	0.626	AC-951
160		AC-951-5	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.727	0.252	0.503	0.252	0.503	AC-951
161		AC-951-6	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	4.585	0.423	0.846	0.423	0.846	AC-951


美特鋁質 有限公司 MIDI Aluminium Fabricator Ltd.	工程號:	J-857	計算:	李傳鵬	日期:	2022.12.09	送呈:	施哥
	地盤名稱:	啟德站	核對:	練鬆文	日期:	2022.12.10	副本:	細栘
廠用鋁板B.M.表	項目類別:	單元幕牆	批准:	林仁安	日期:	2022.12.12	此BM依據大圖 計算	
BM編號:		修改版次:		A/C Code:		總面積: 216.355	總重量:	1172.65

序號	修改內容	鋁板圖號	鋁板名稱	顏色	實用	後備	總數	總重量	單件展開面積	總展開面積	單件V.F.	總V.F.	備註
									平方米		平方米		
162		AC-951-7	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.348	0.217	0.433	0.217	0.433	AC-951
163		AC-951-8	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	1.791	0.165	0.331	0.165	0.331	AC-951
164		AC-951-9	3mm 铝板	AL2: ECK3M96295S-ZD1	3	0	3	10.464	0.644	1.931	0.644	1.931	AC-951
165		AC-951-10	3mm 铝板	AL2: ECK3M96295S-ZD1	2	0	2	2.812	0.259	0.519	0.259	0.519	AC-951
166		AC-951-11	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.600	0.295	0.295	0.295	0.295	AC-951
167		AC-951-12	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.363	0.252	0.252	0.252	0.252	AC-951
168		AC-951-13	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.811	0.334	0.334	0.334	0.334	AC-951
169		AC-951-14	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.238	0.228	0.228	0.228	0.228	AC-951
170		AC-952-1	3mm 铝板	AL2: ECK3M96295S-ZD1	8	0	8	3.754	0.087	0.693	0.087	0.693	AC-952
171		AC-952-2	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.045	0.193	0.193	0.193	0.193	AC-952
172		AC-952-3	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.175	0.217	0.217	0.217	0.217	AC-952
173		AC-952-4	3mm 铝板	AL2: ECK3M96295S-ZD1	4	0	4	3.475	0.160	0.641	0.160	0.641	AC-952
174		AC-952-5	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.999	0.184	0.184	0.184	0.184	AC-952
175		AC-952-6	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	0.943	0.174	0.174	0.174	0.174	AC-952
176		AC-953	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	4.877	0.900	0.900	0.900	0.900	AC-953
177		AC-954	3mm 铝板	AL2: ECK3M96295S-ZD1	1	0	1	1.889	0.349	0.349	0.349	0.349	AC-954
				總計：	282		282	1172.65	165.972	216.36	159.75	204.944	


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-701	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	4	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

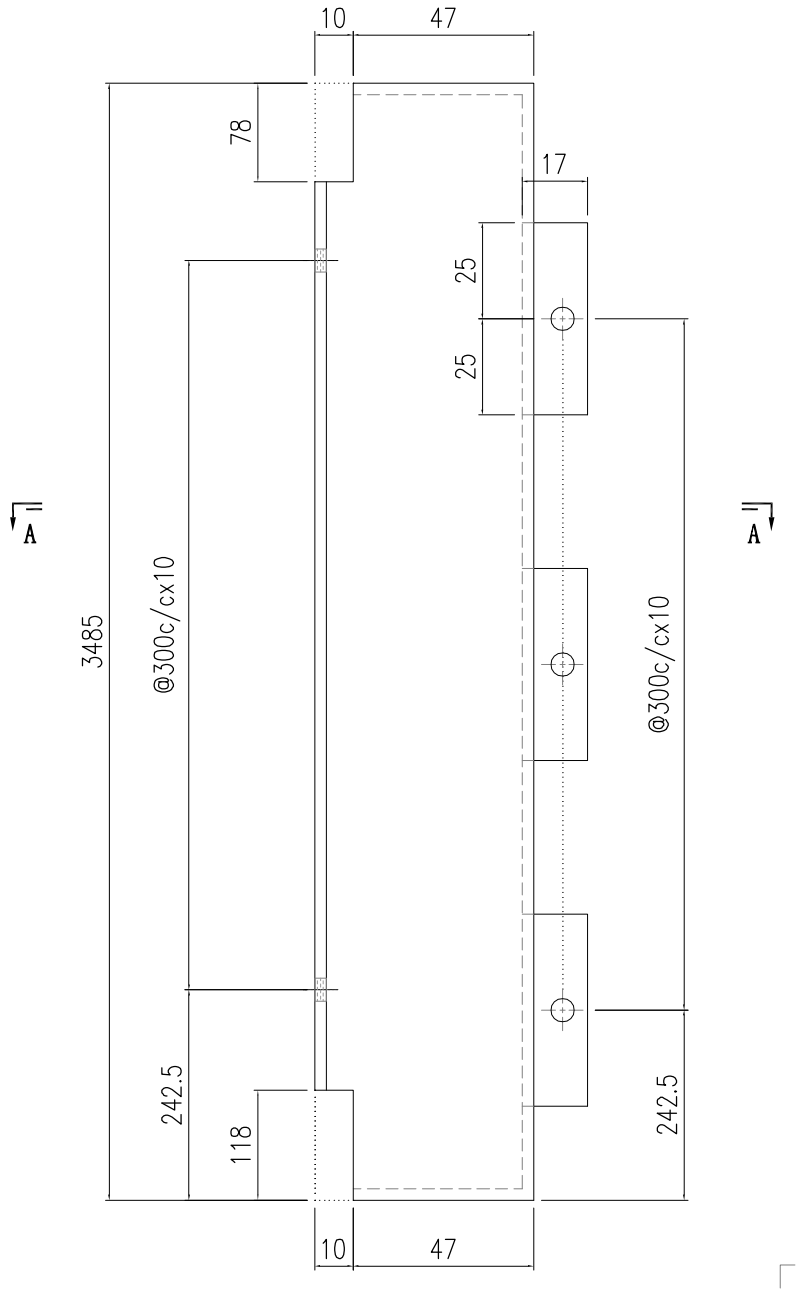


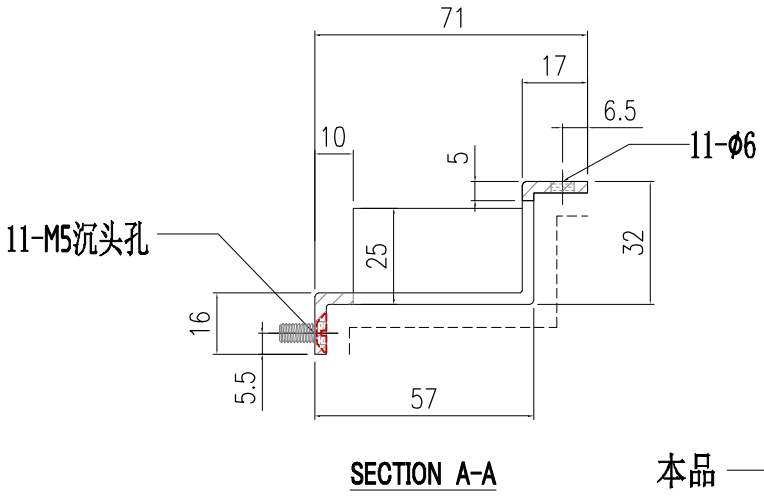


SECTION A-A

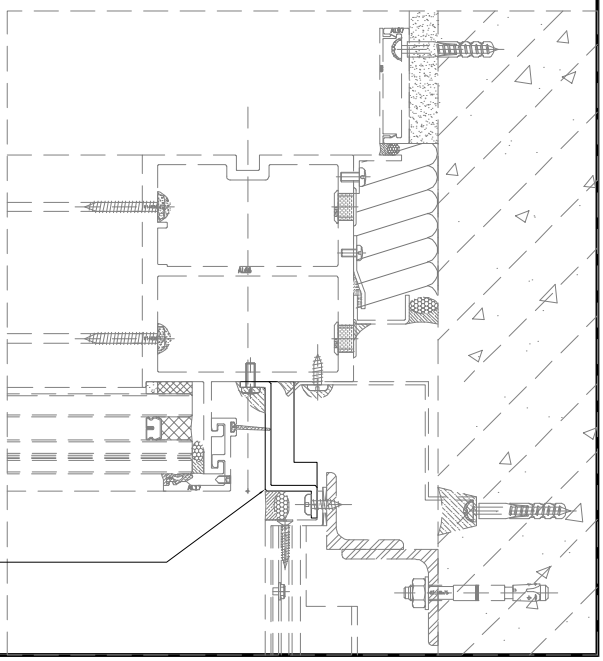


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-702	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209		數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

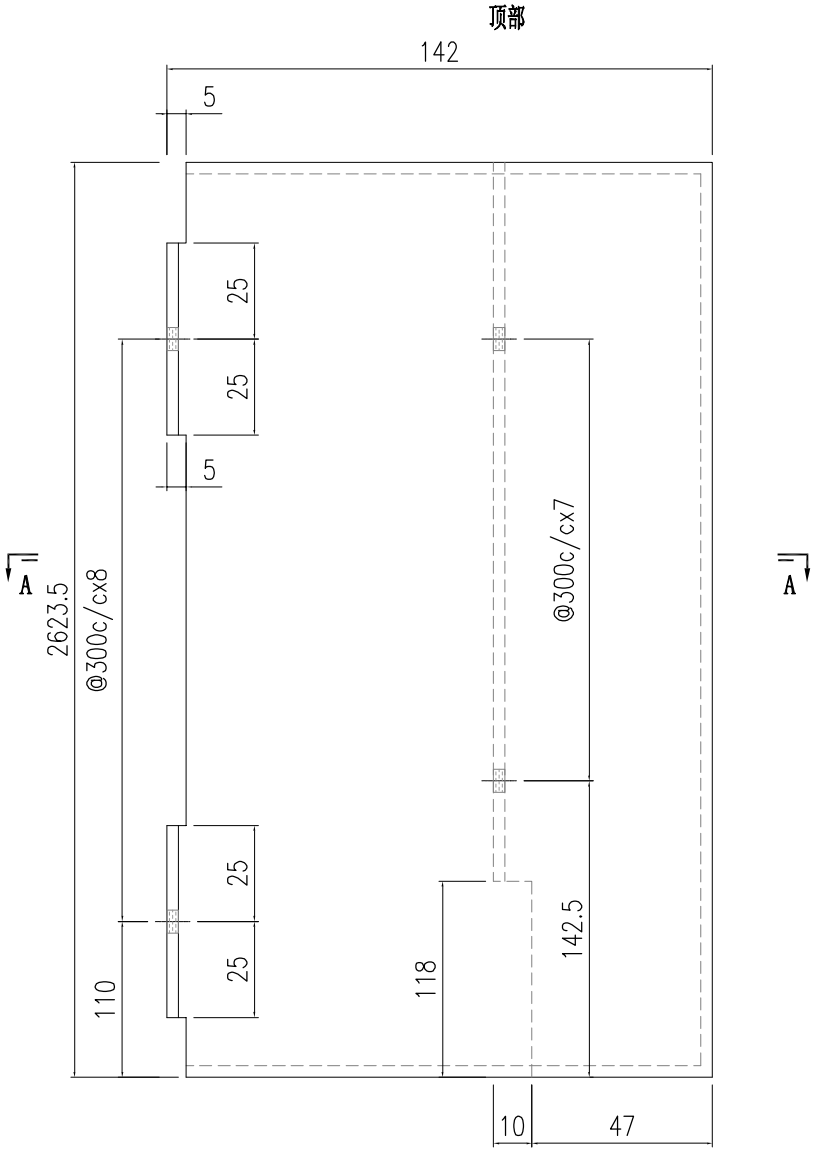

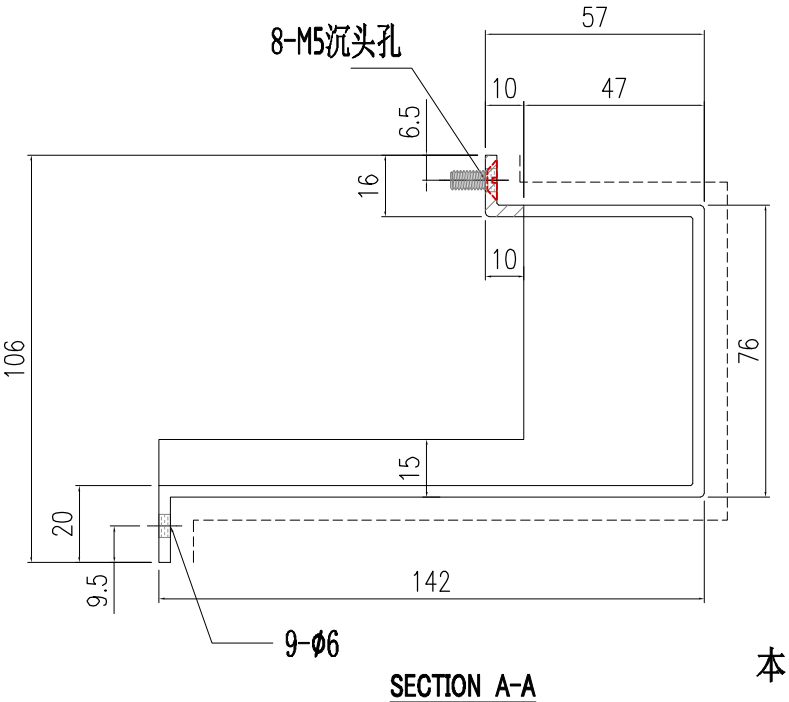



SECTION A-A

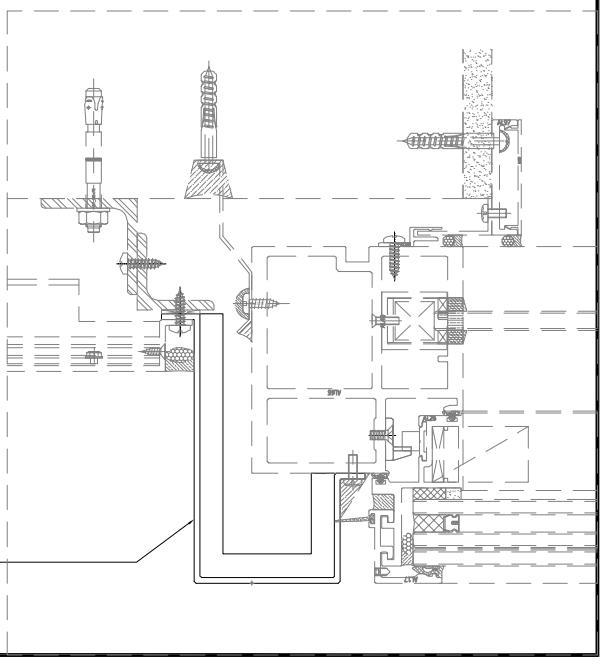


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-703
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	4
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

顶部

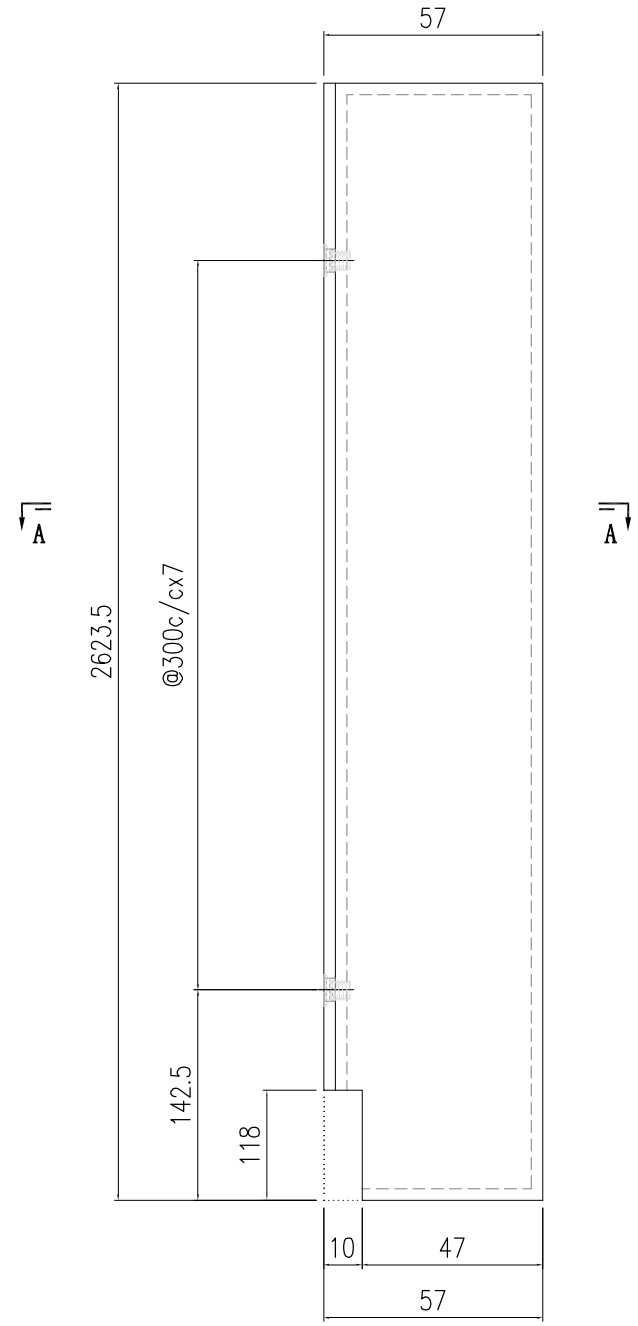

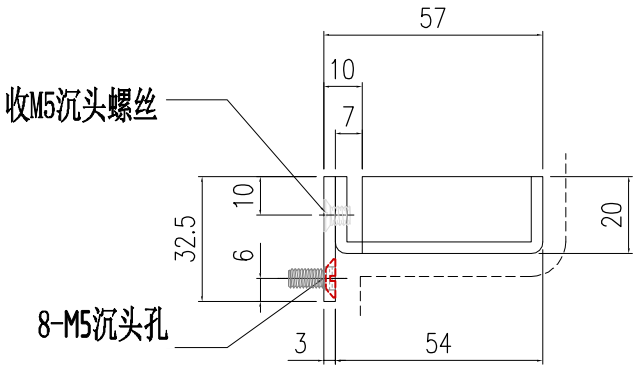



SECTION A-A

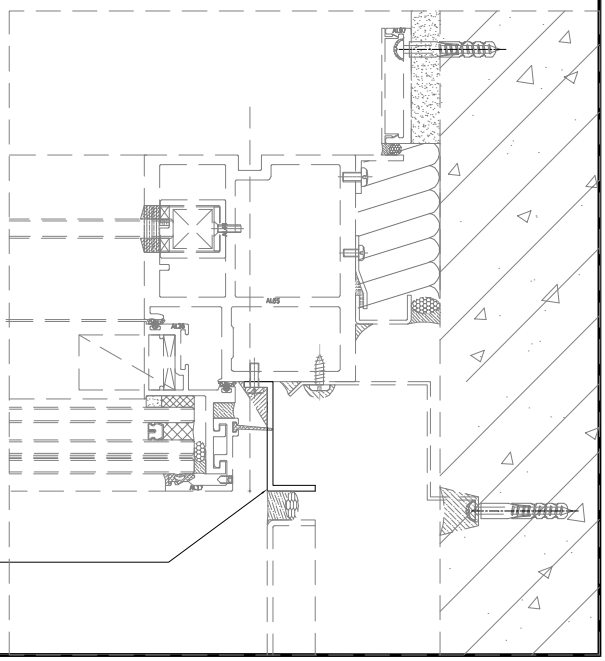


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-704	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	5	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

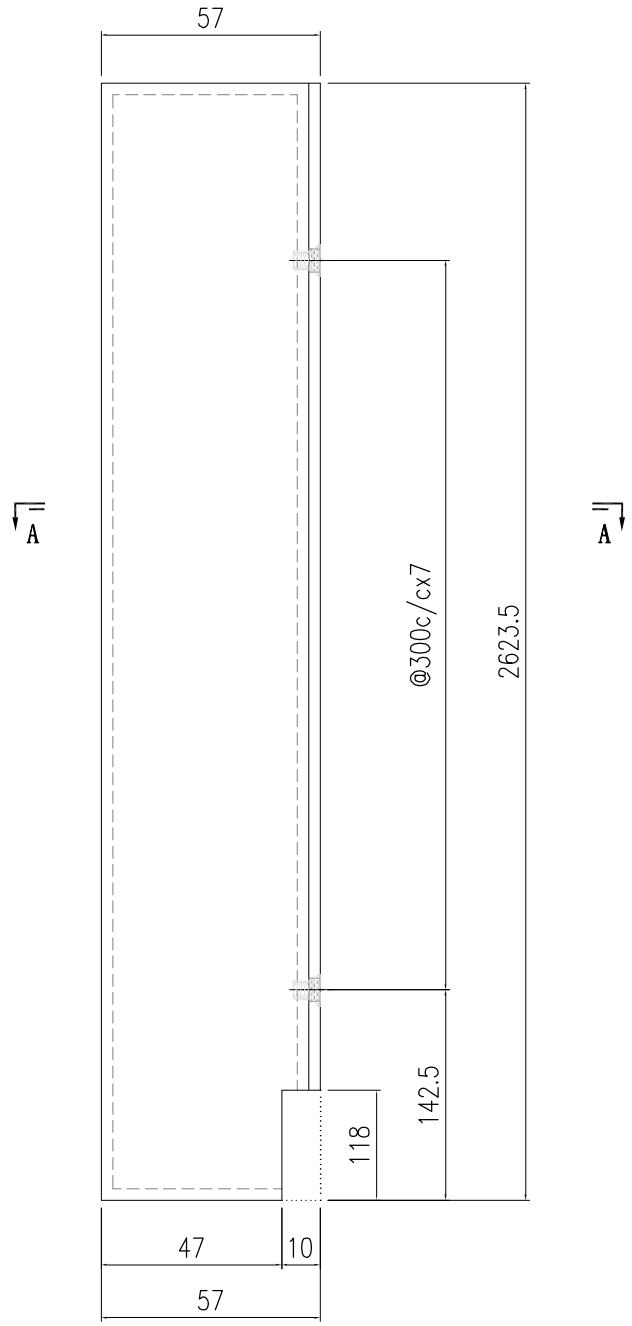

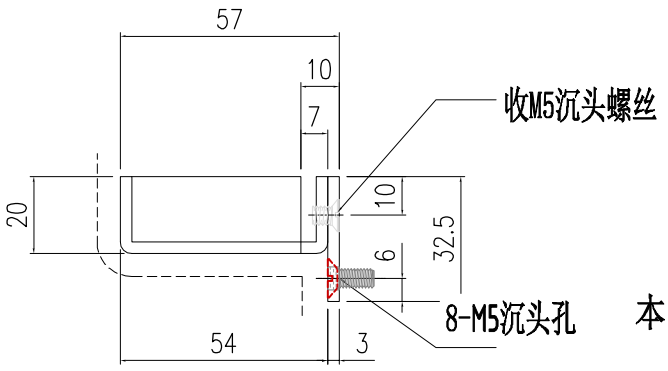



SECTION A-A

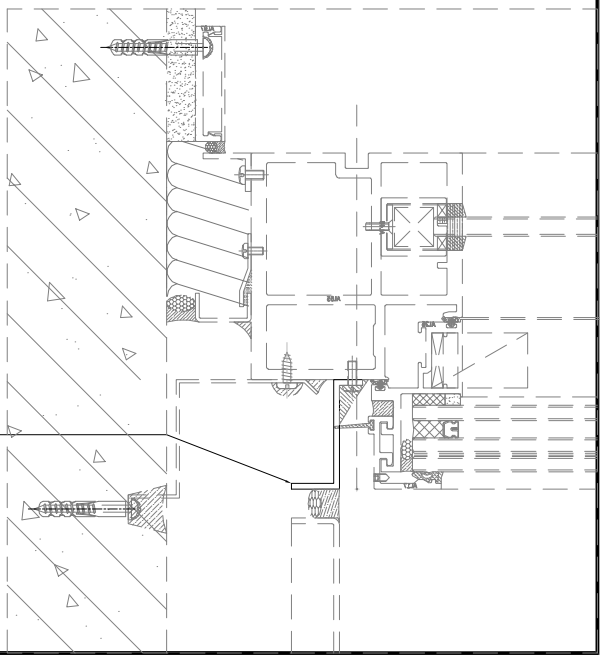


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-705
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	9
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

顶部

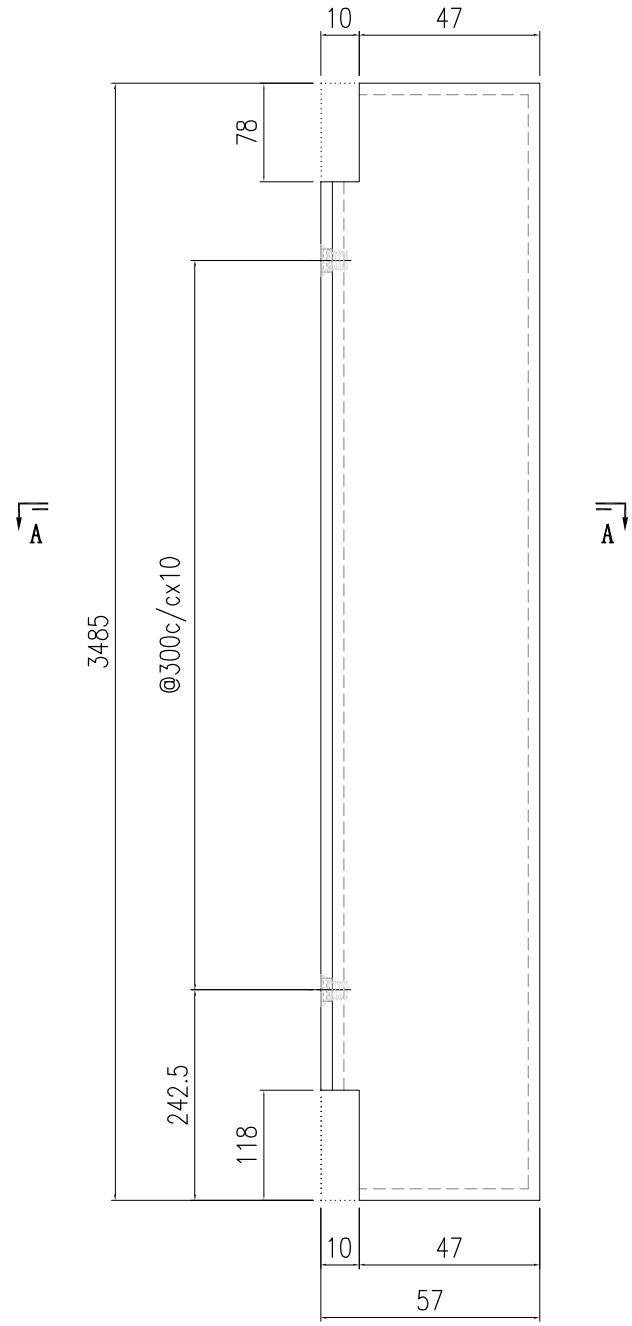


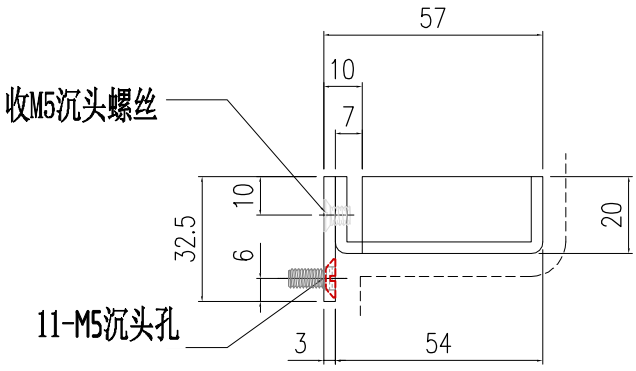


SECTION A-A

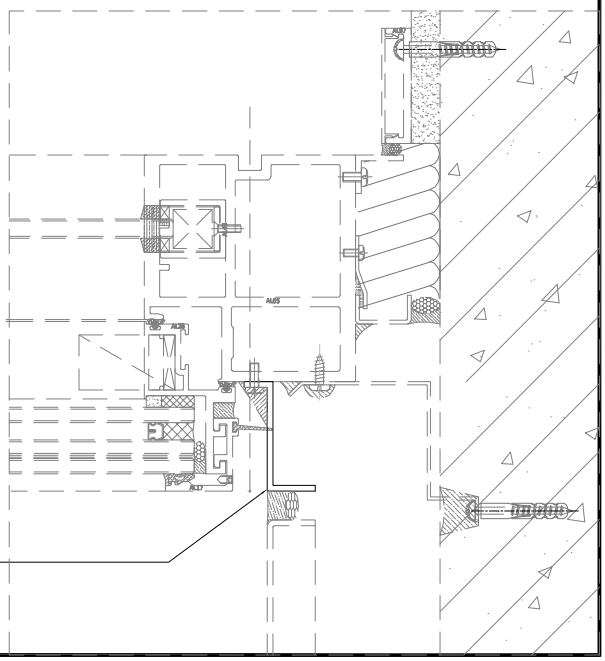


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	9	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-706	

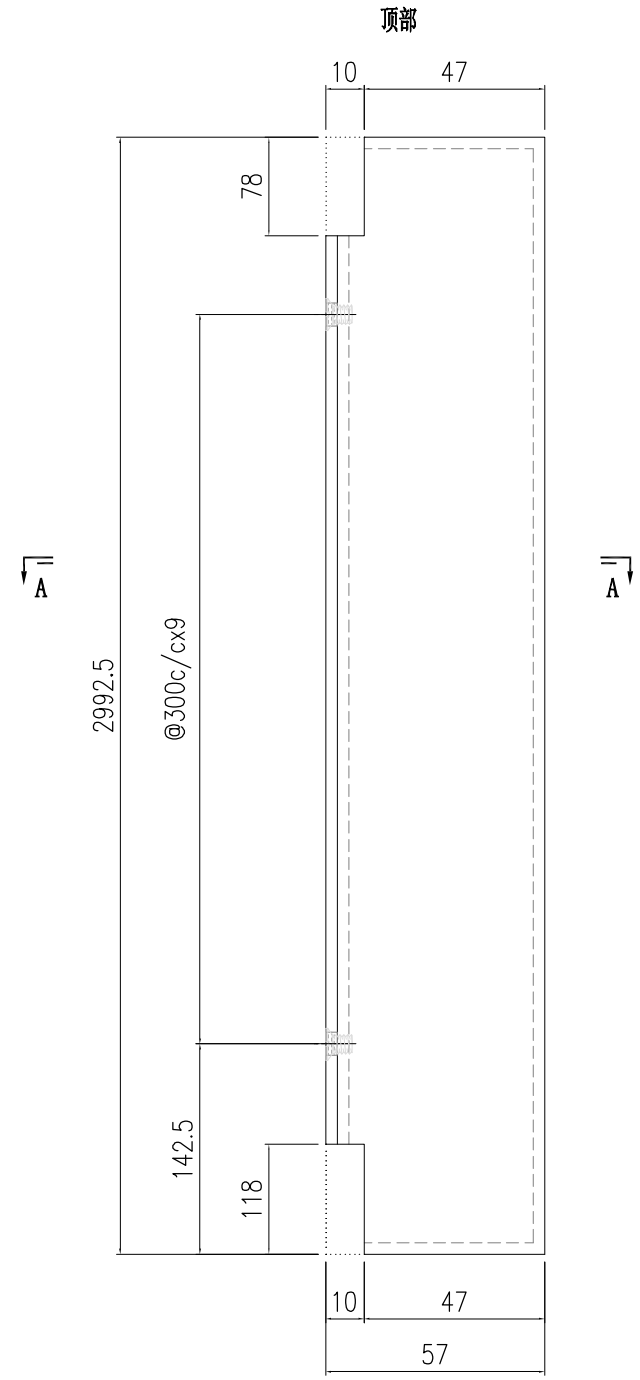


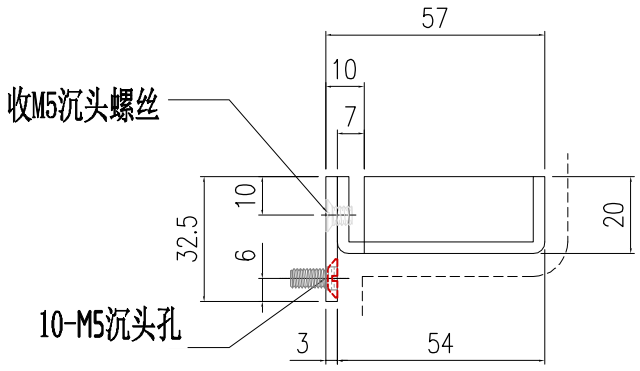


SECTION A-A

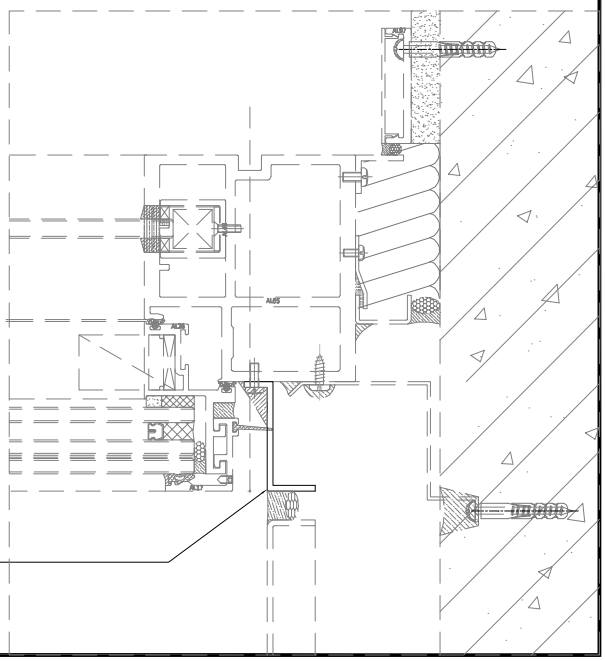


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-707	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	10	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

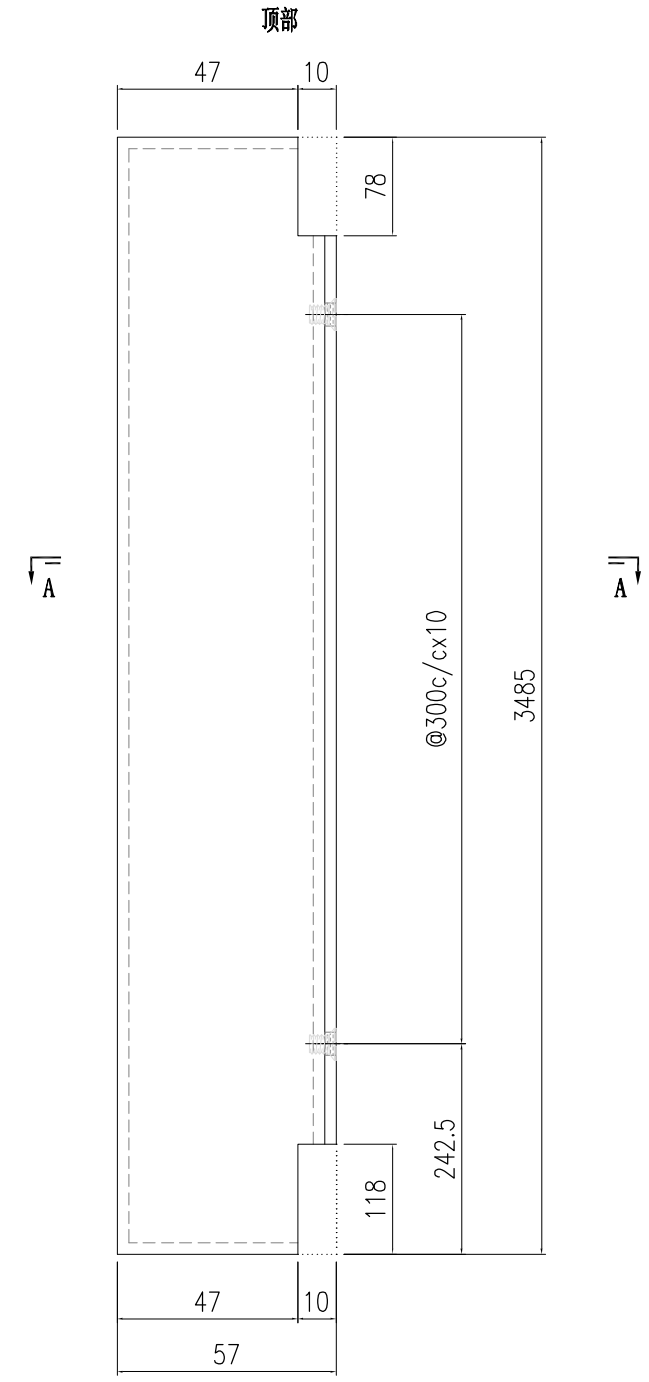

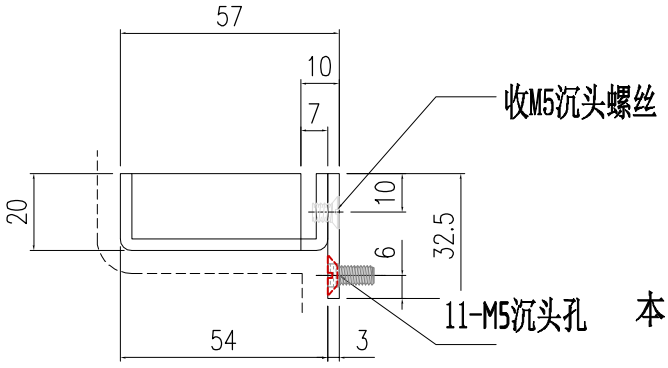



SECTION A-A

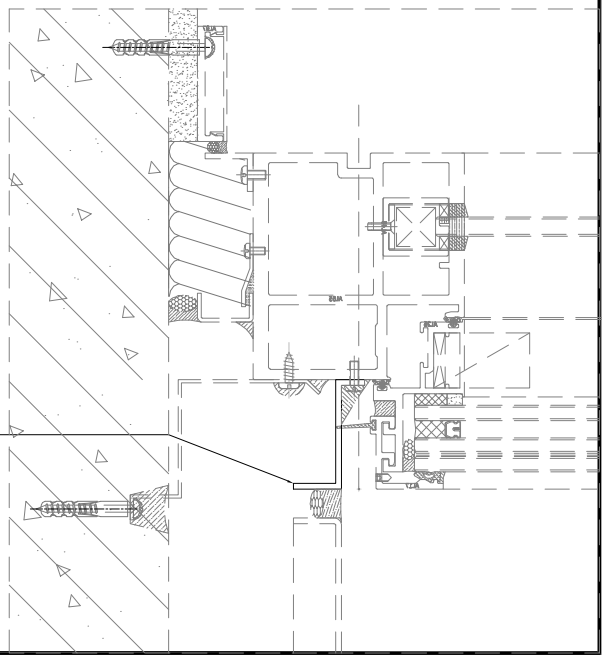


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-708	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	11	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

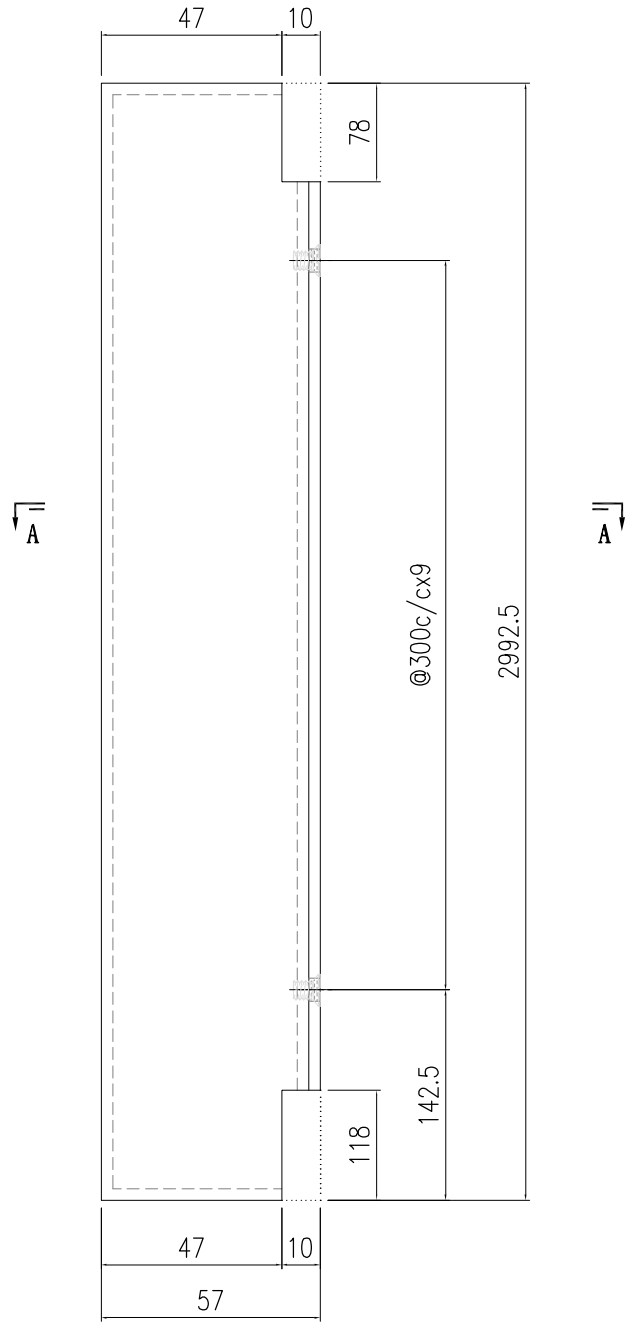

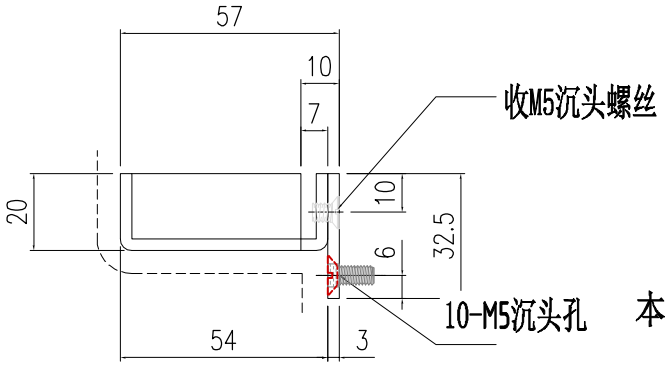



SECTION A-A

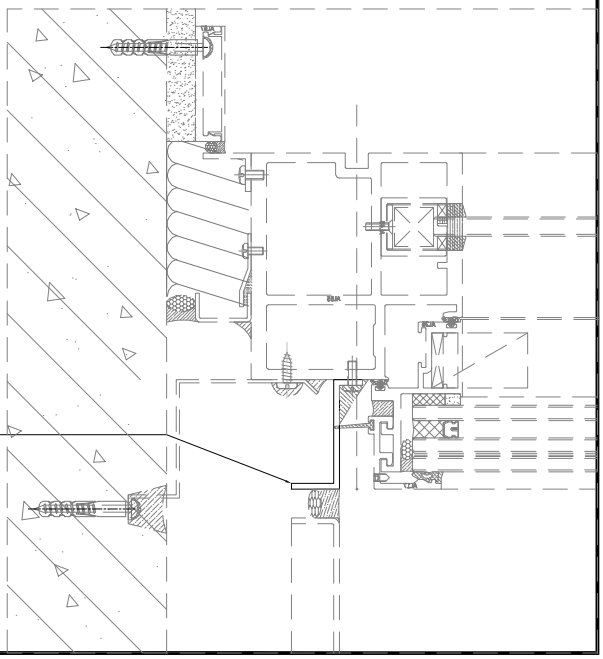


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-709	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	2	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

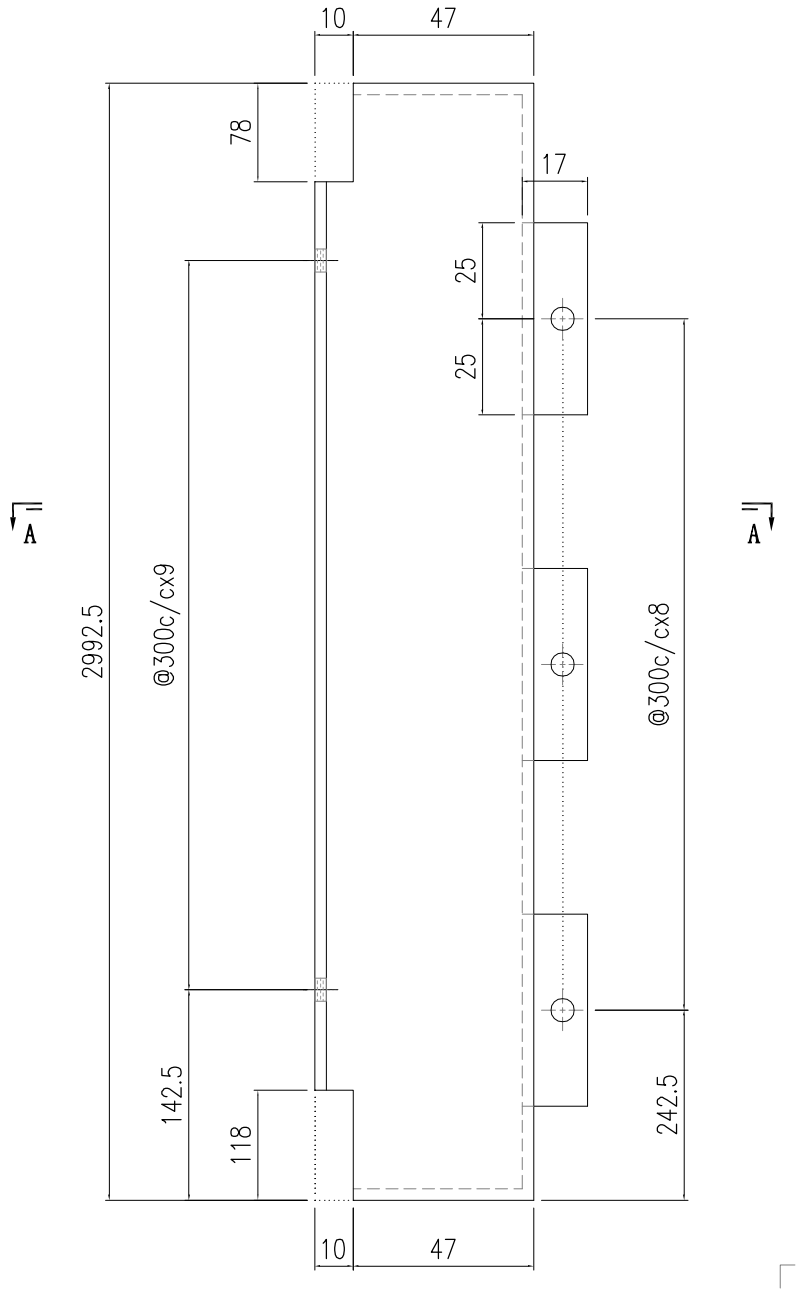

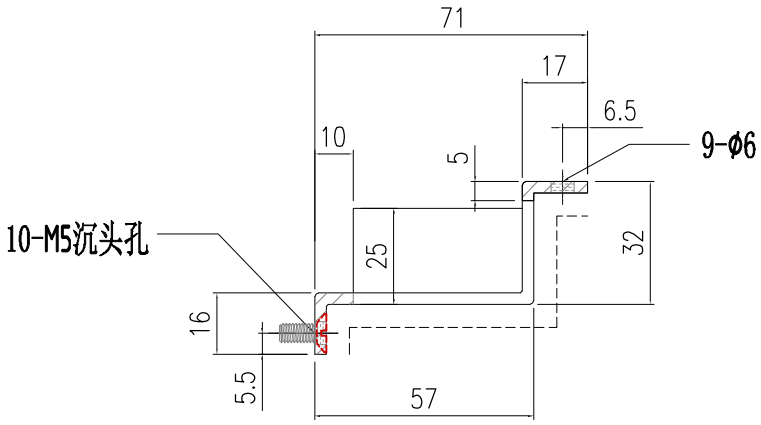



SECTION A-A

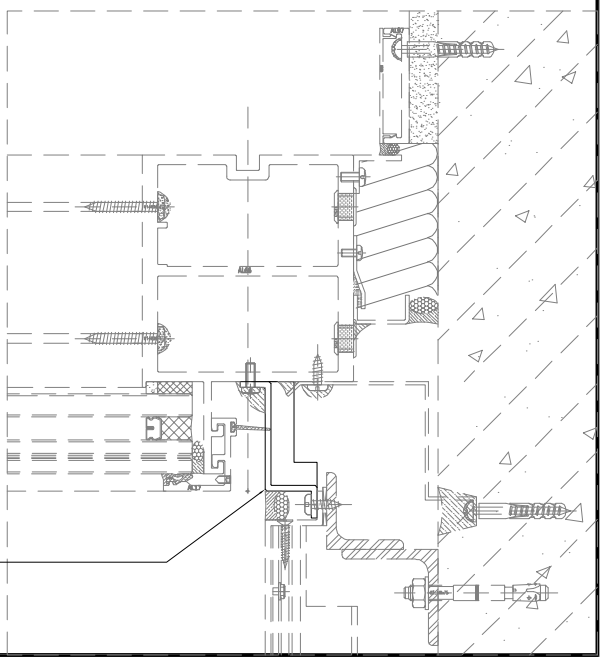


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-710	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	3	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

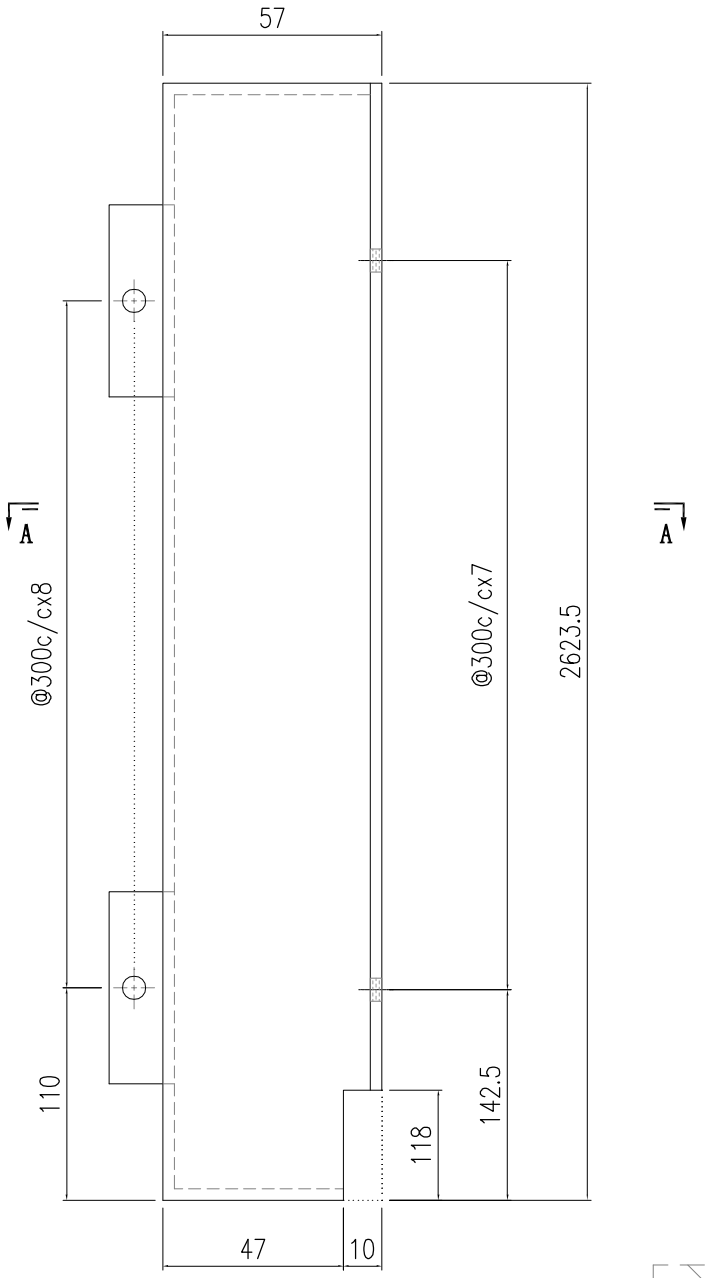

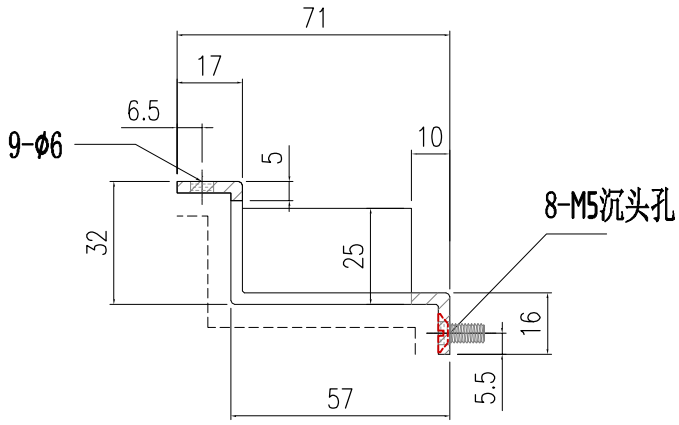



SECTION A-A

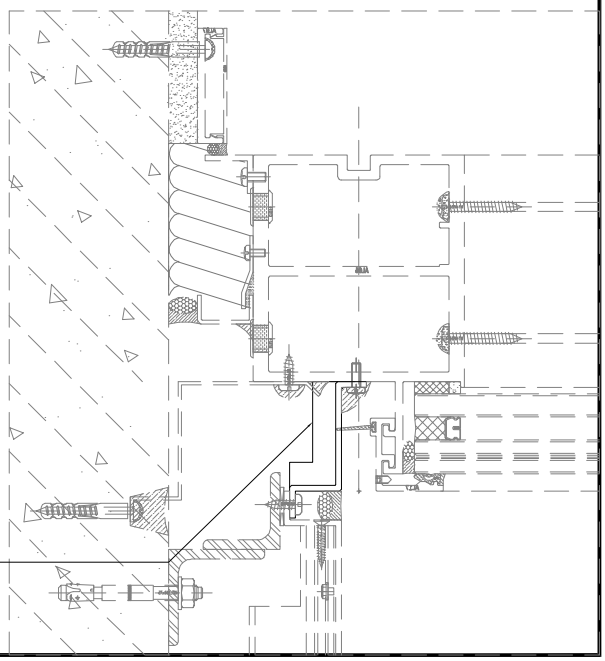


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-711	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	3	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

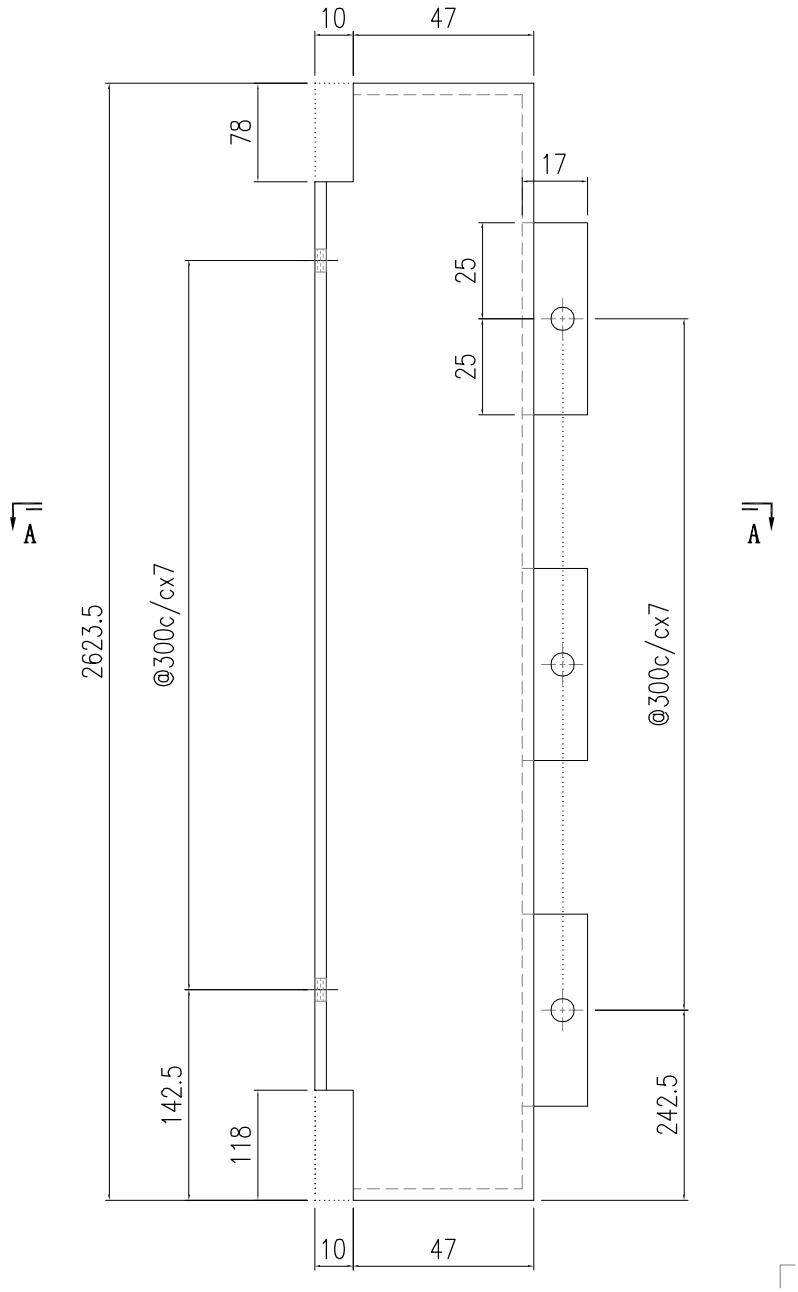

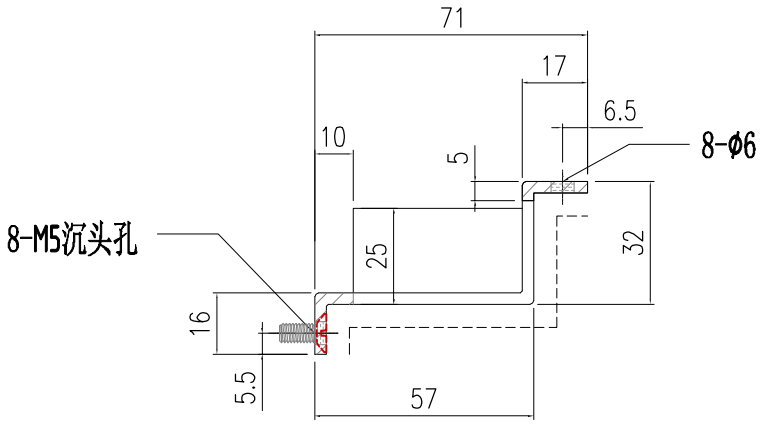



SECTION A-A

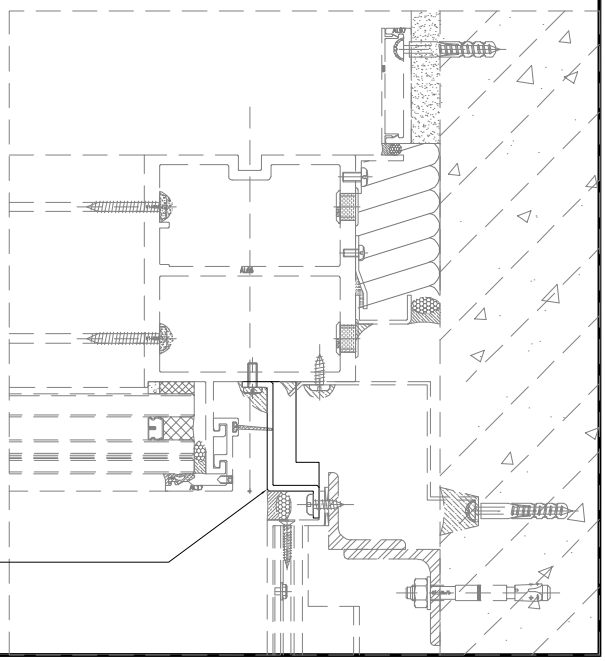


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-712	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

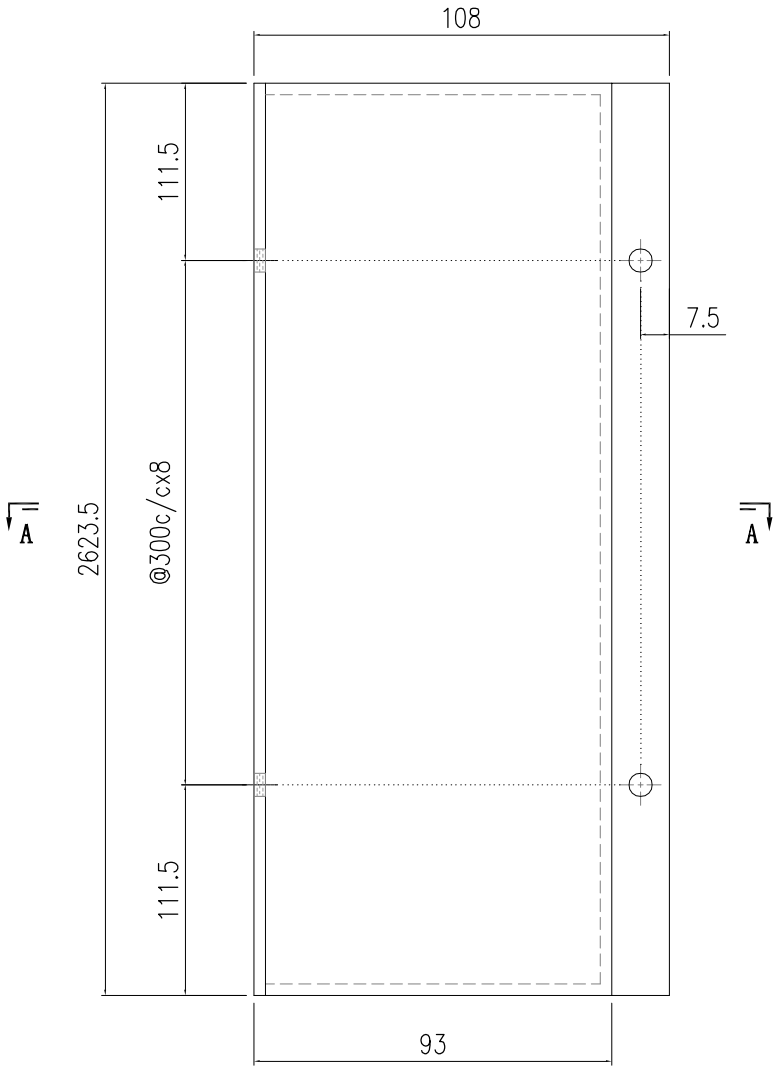

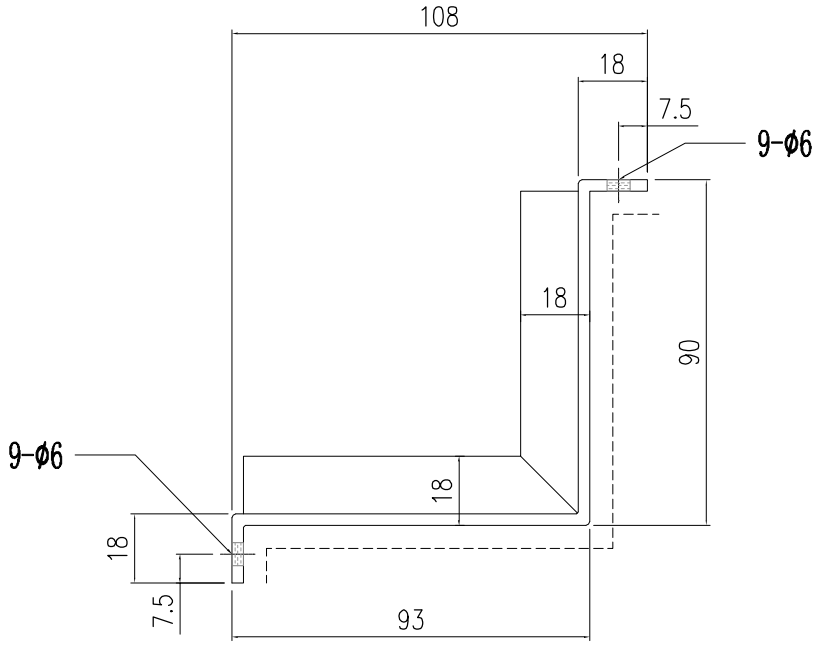


SECTION A-A

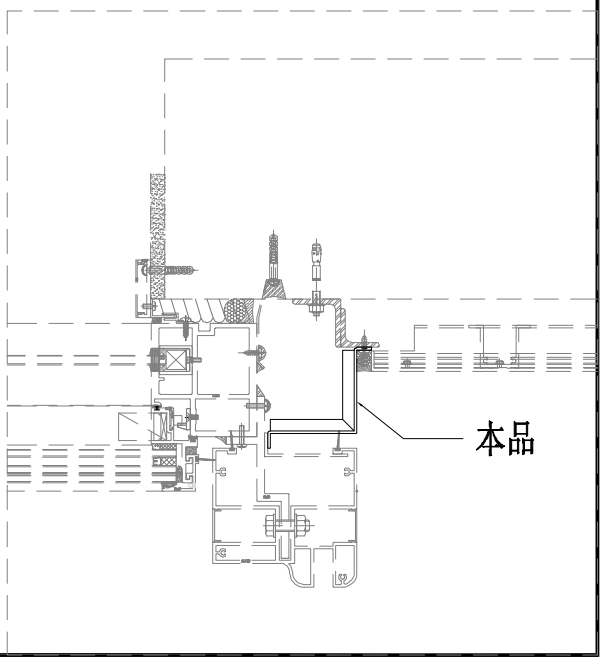


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
工程號	J857	類別		物料號	-								
地盤	啟德6552	制圖	陈梓豪	20221206	圖號	AC-713							
图纸名称	收边铝板	復核	練松文	20221209	數量	3							
材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)						


修改	A	-	-	採用	工廠	-	地盤	✓
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			

顶部

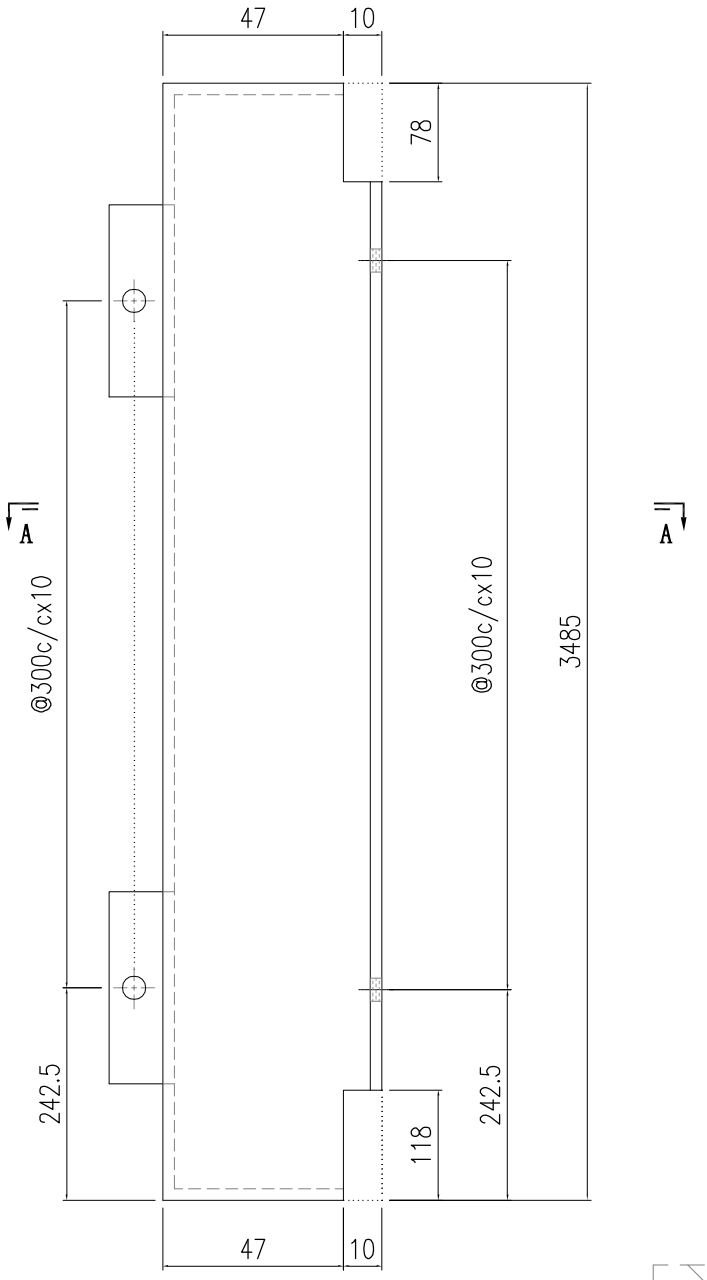


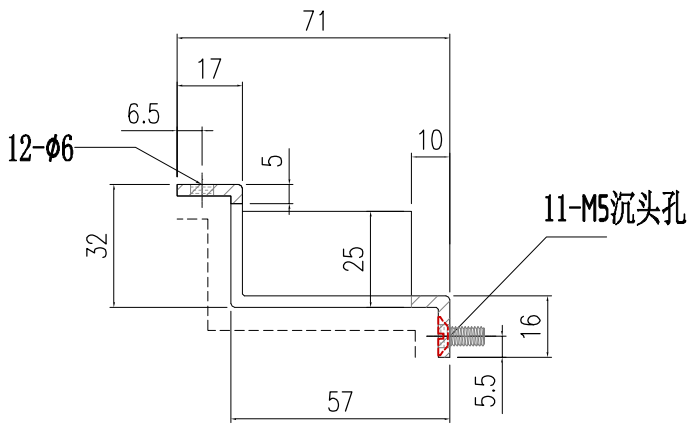


SECTION A-A

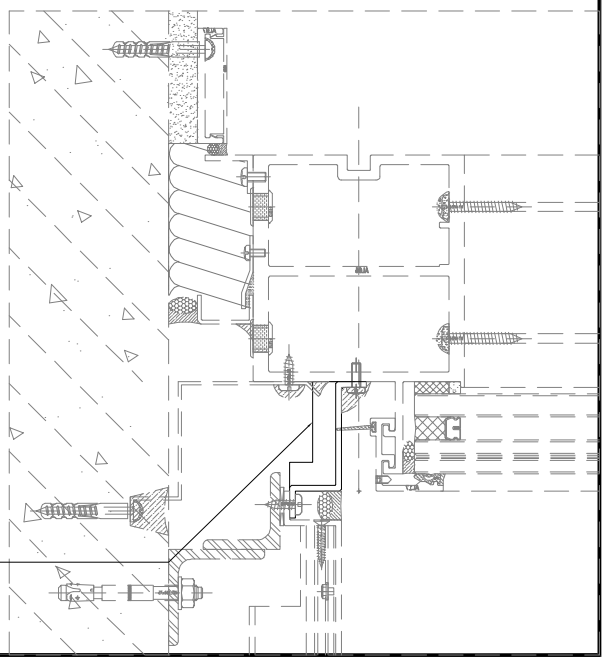


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-714	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209		數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

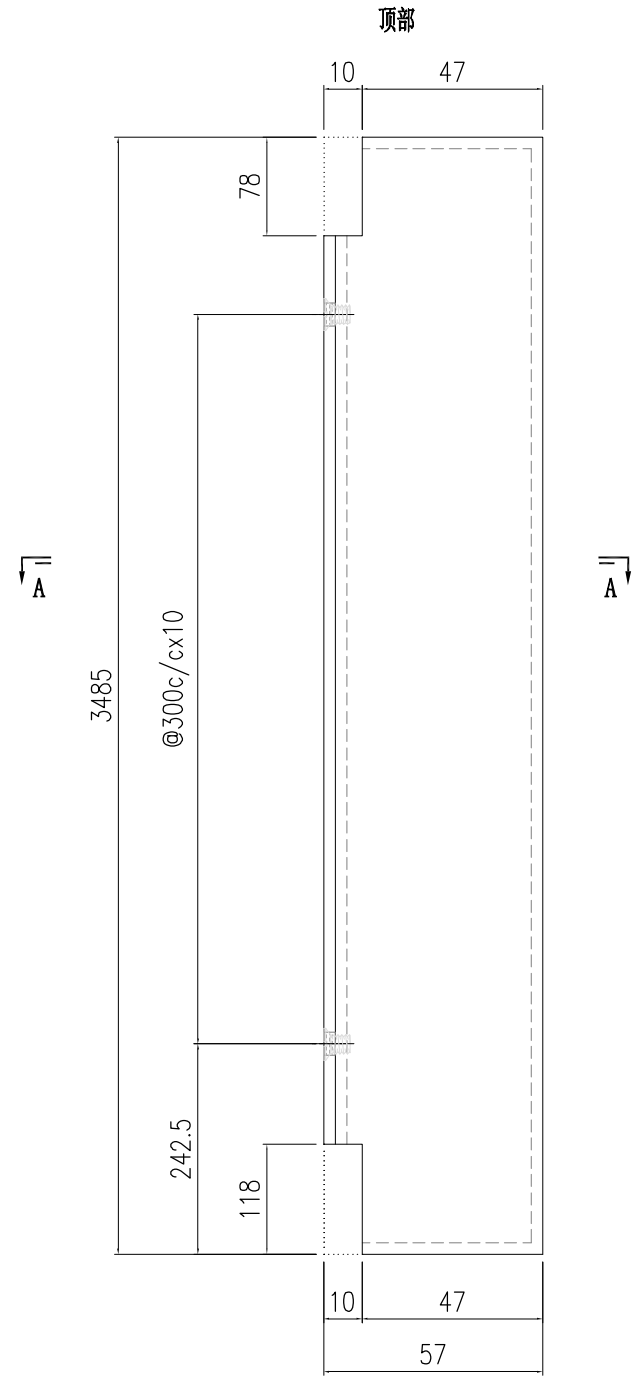

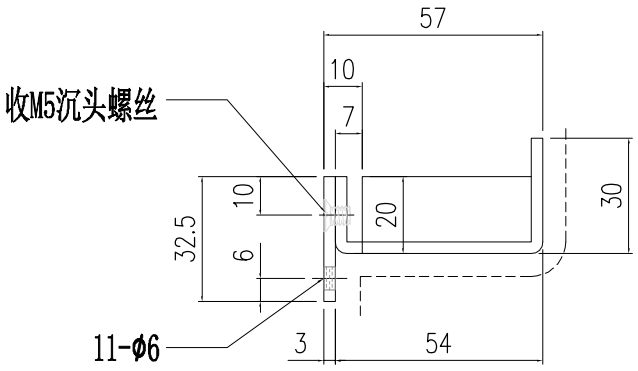



SECTION A-A

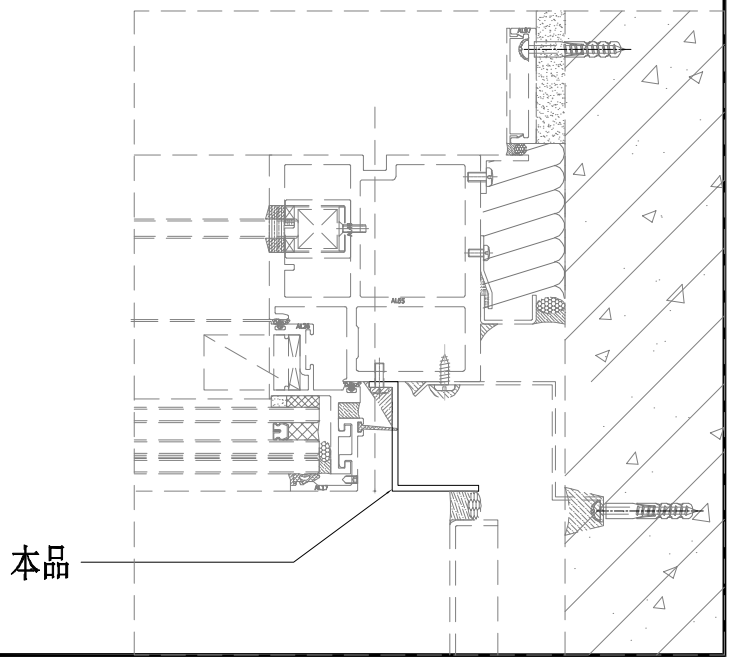


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-715	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

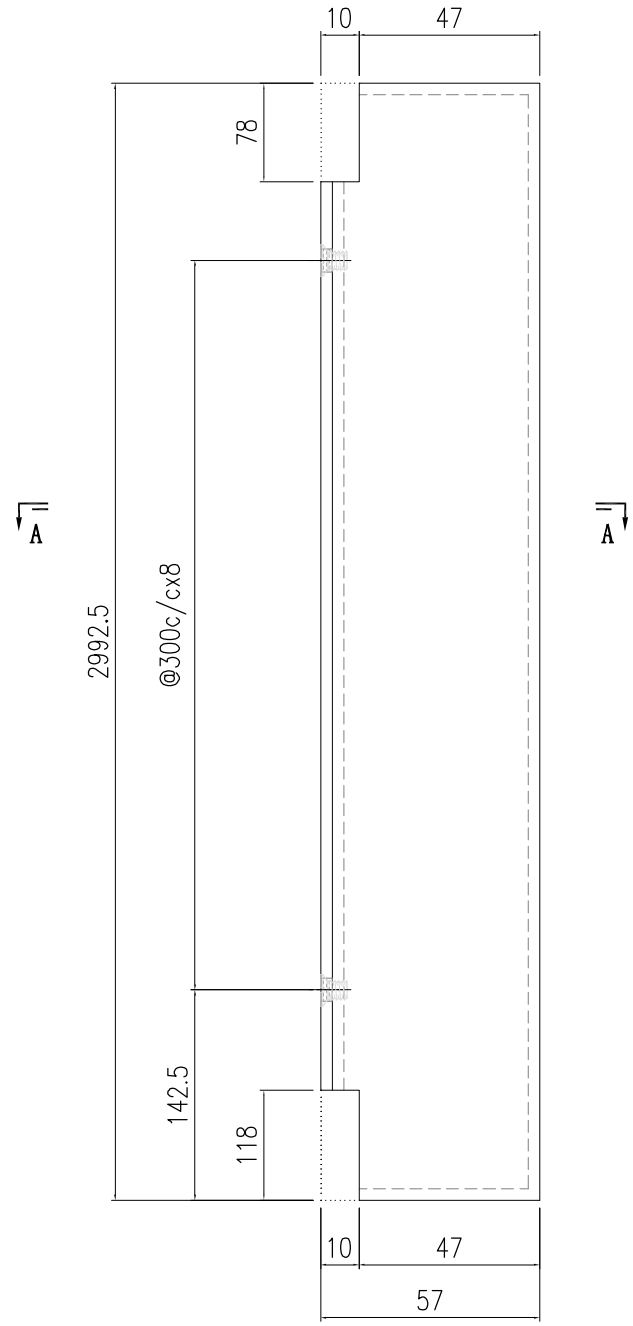


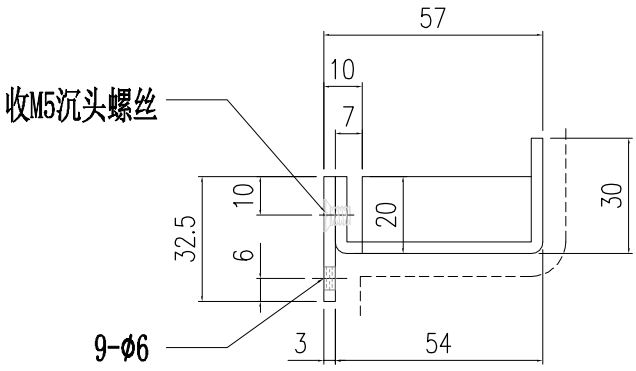



SECTION A-A

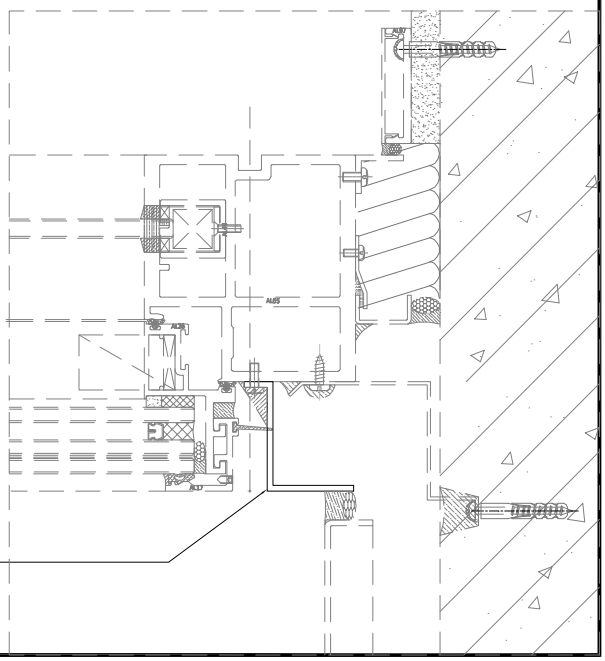

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-716	
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	4	
日期	9.21	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

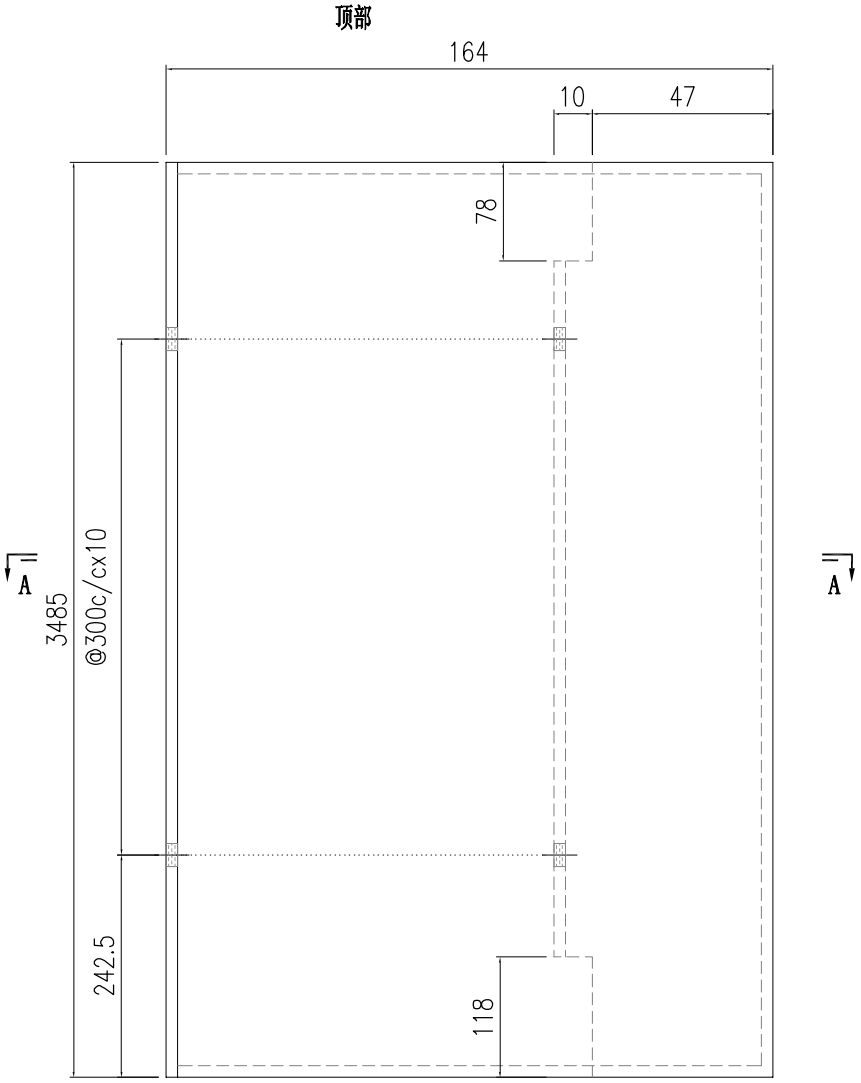


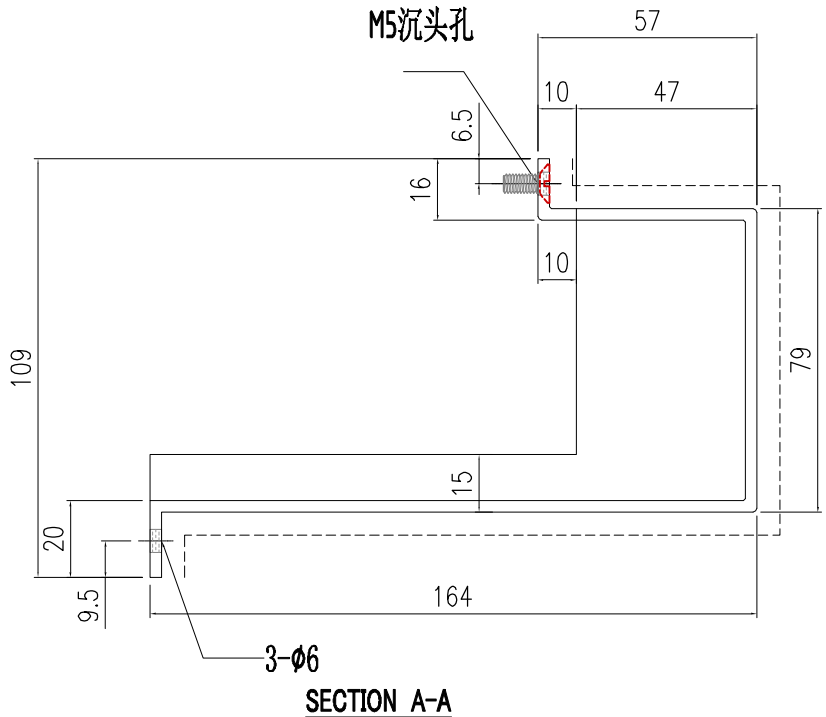


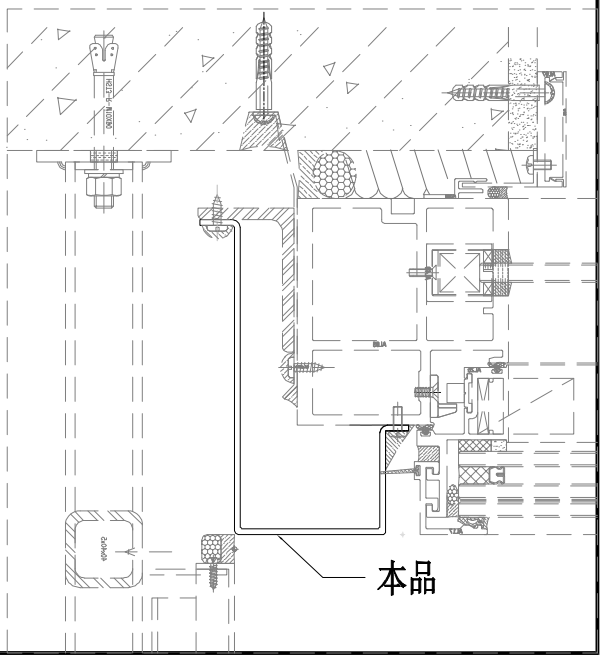


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-717	
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	4	
日期	9.21	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

頂部

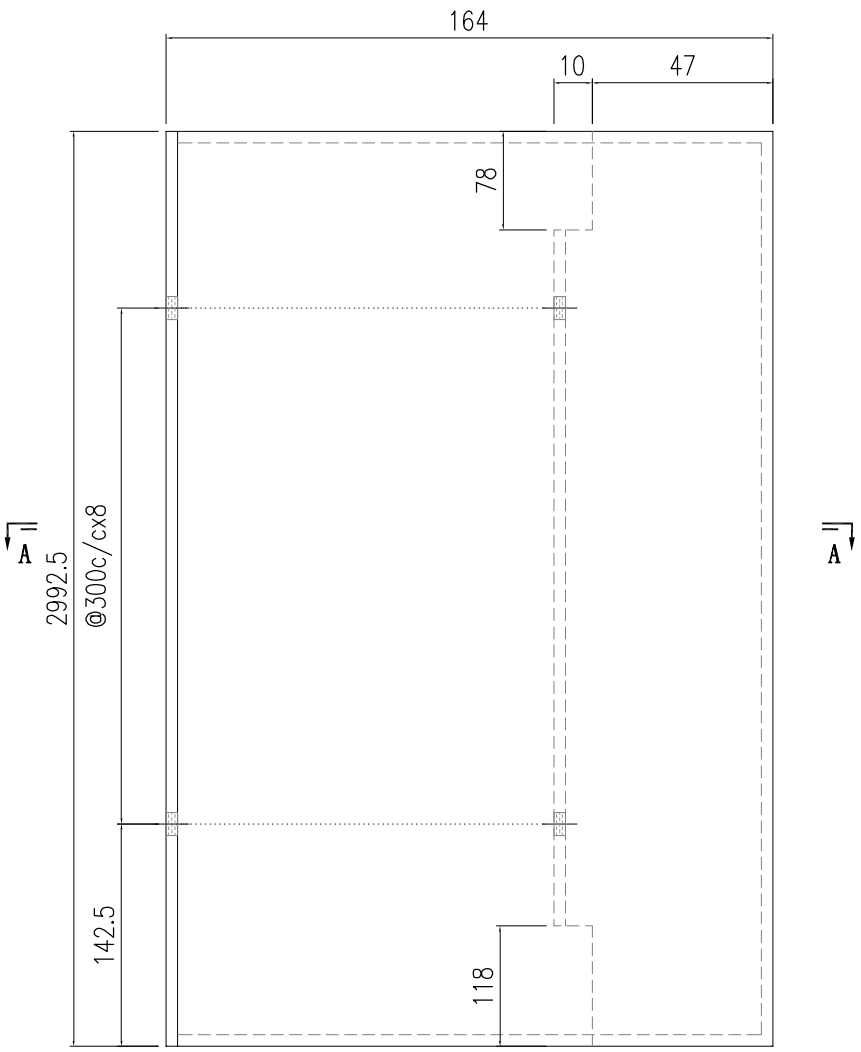


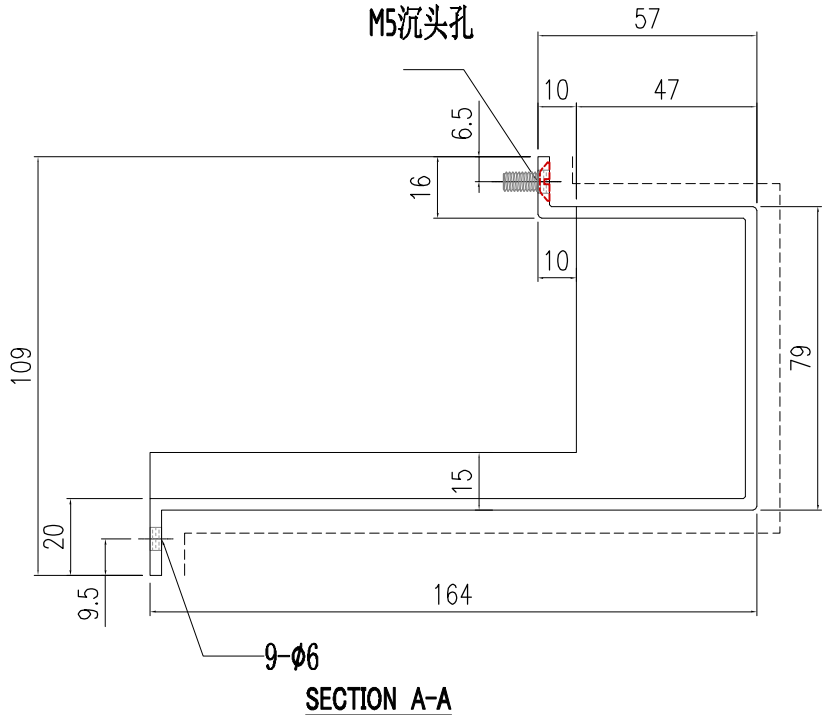


SECTION A-A

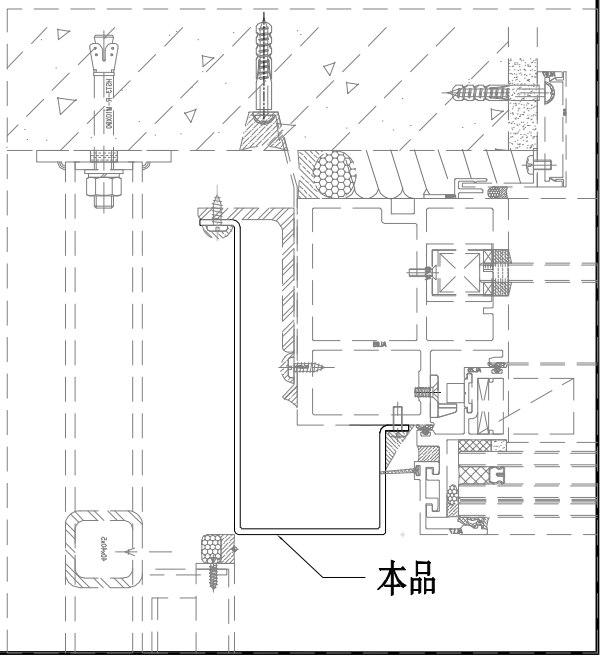


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-718
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

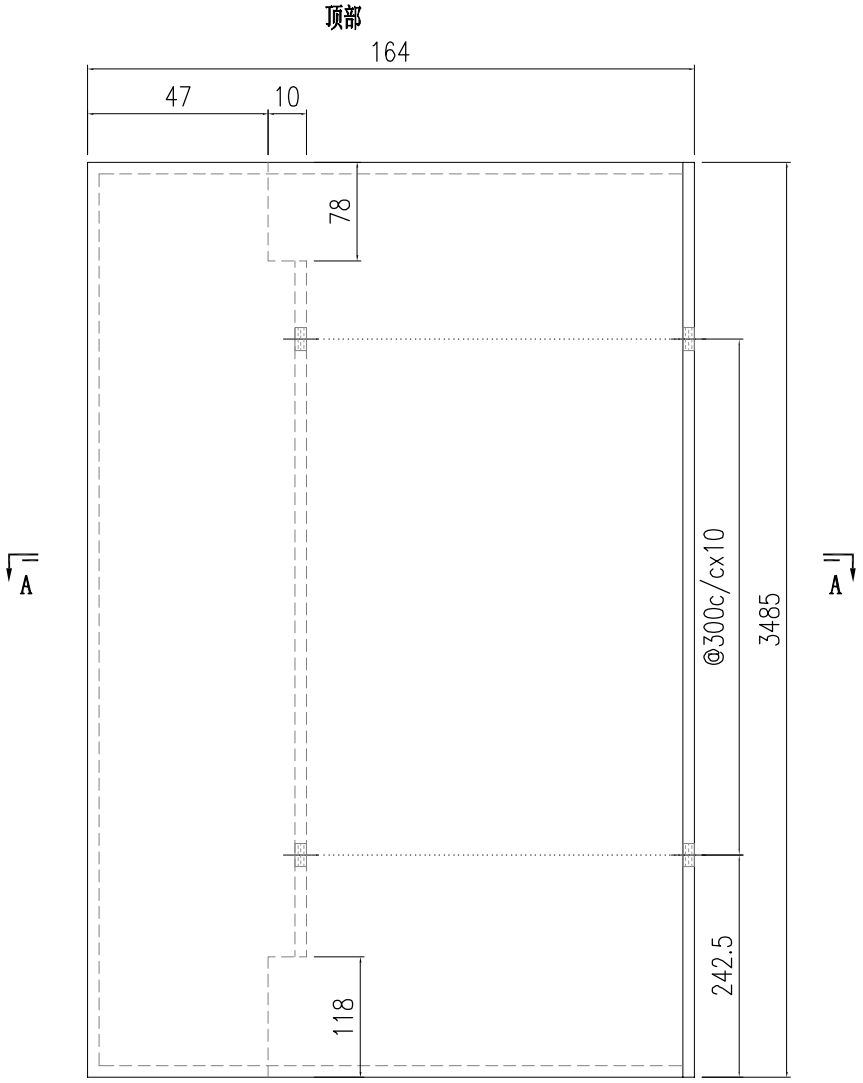


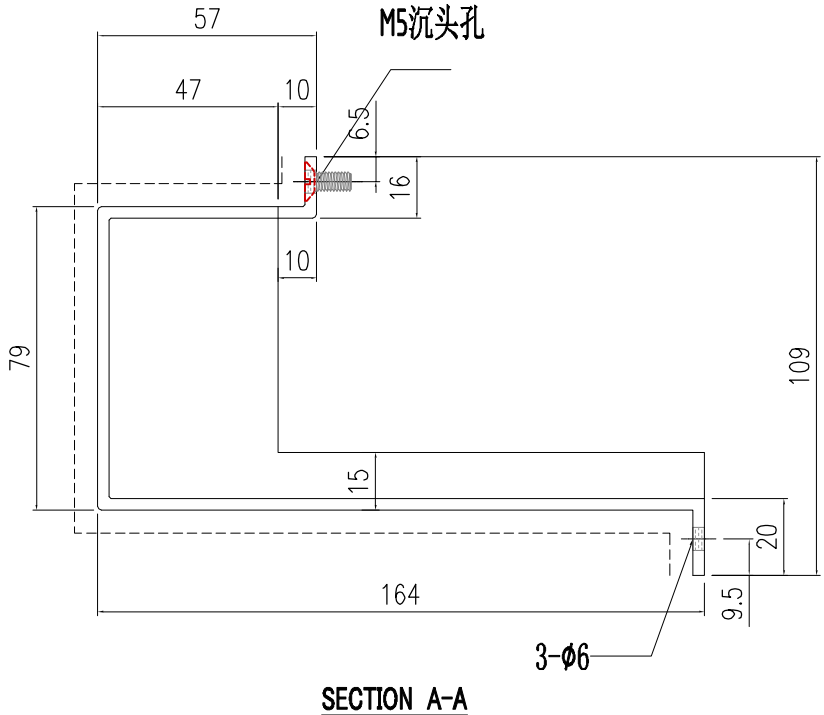


SECTION A-A

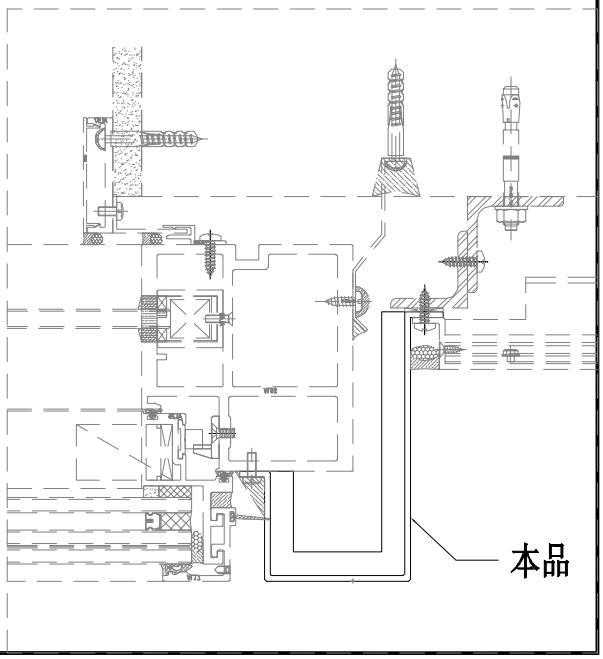


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-719	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文	20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

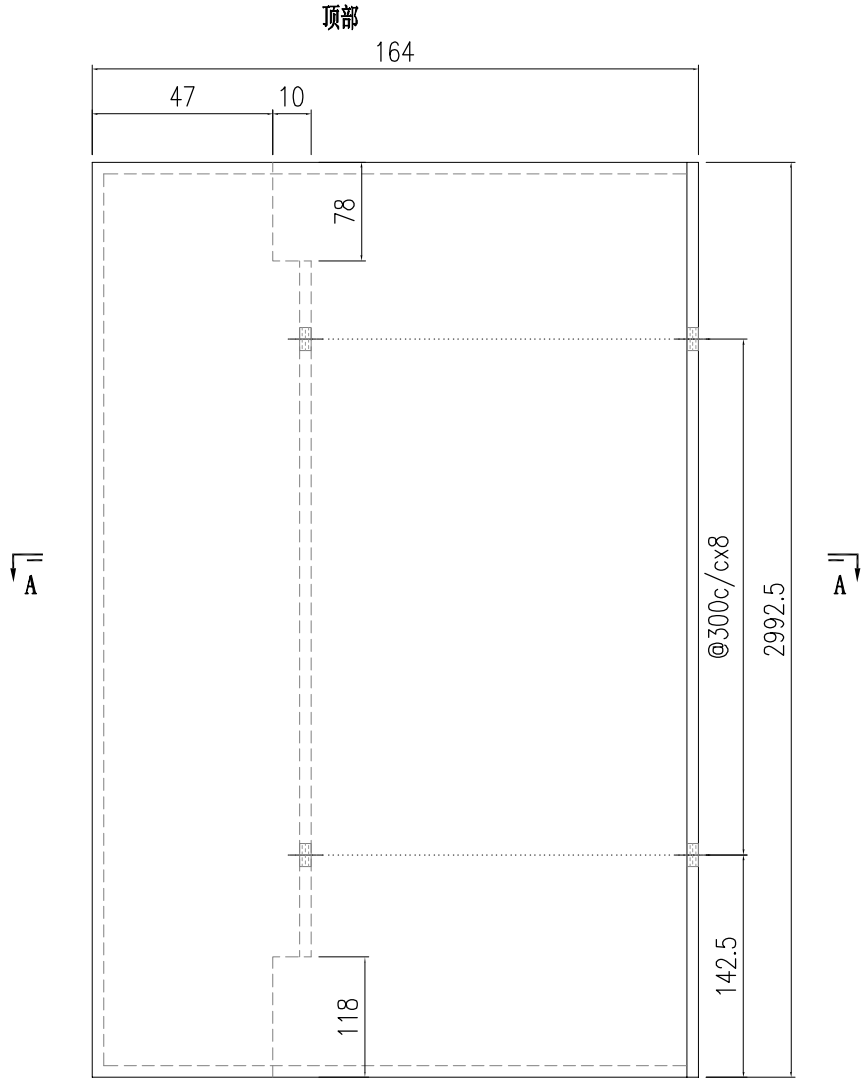

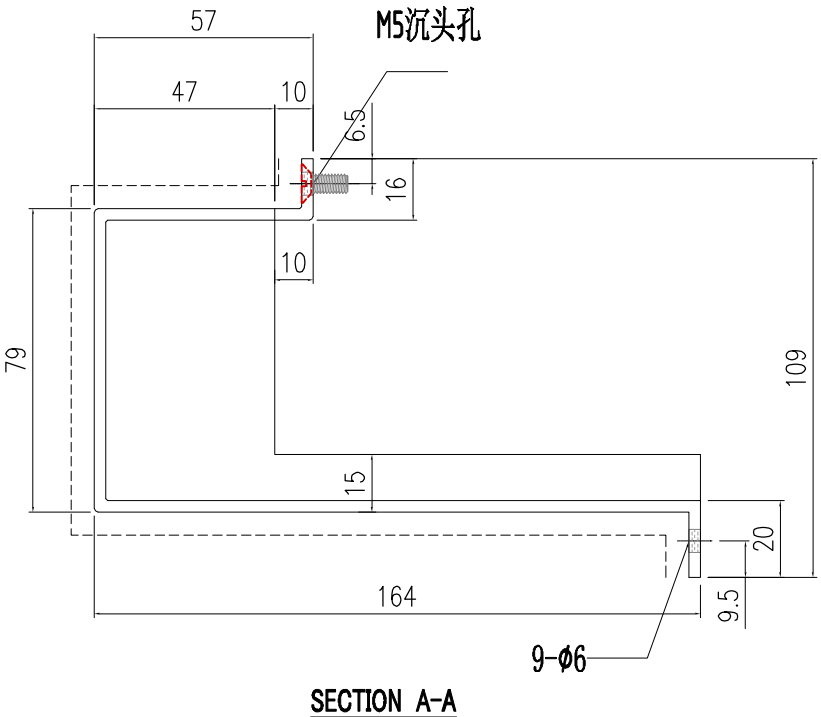



SECTION A-A

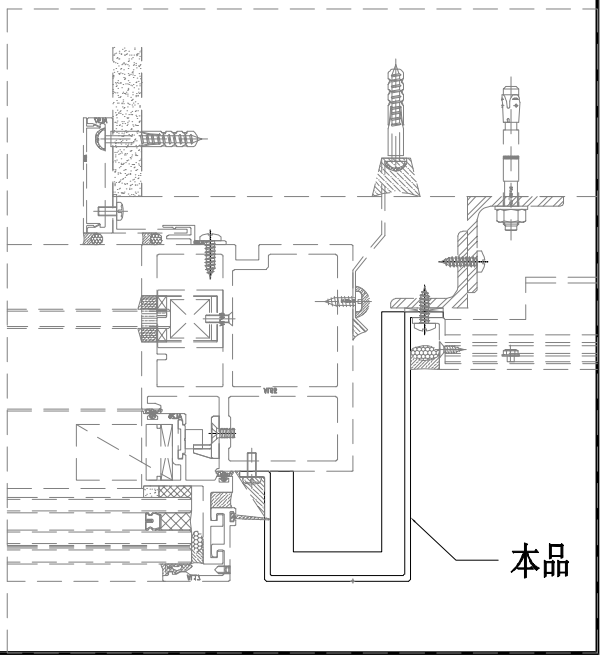


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-720	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

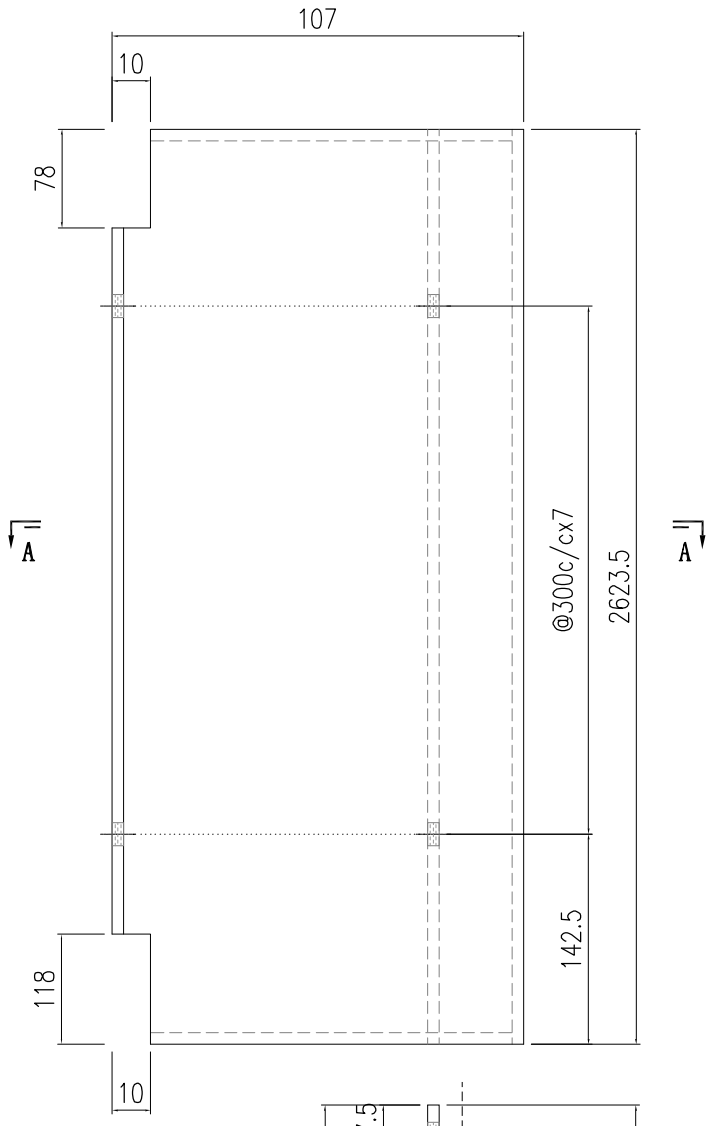


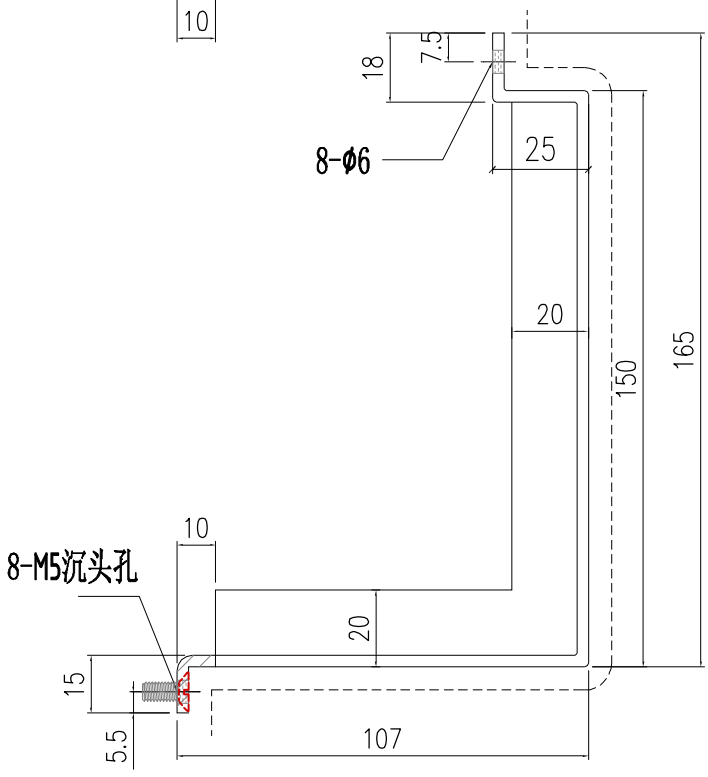


SECTION A-A

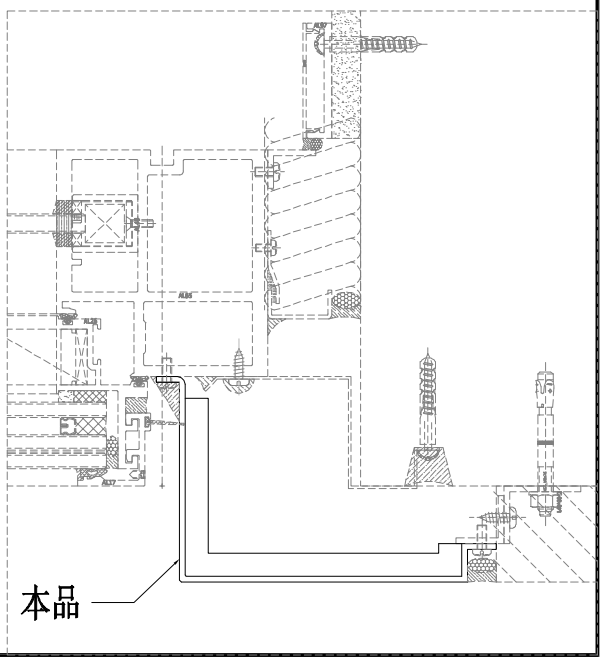


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-723
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

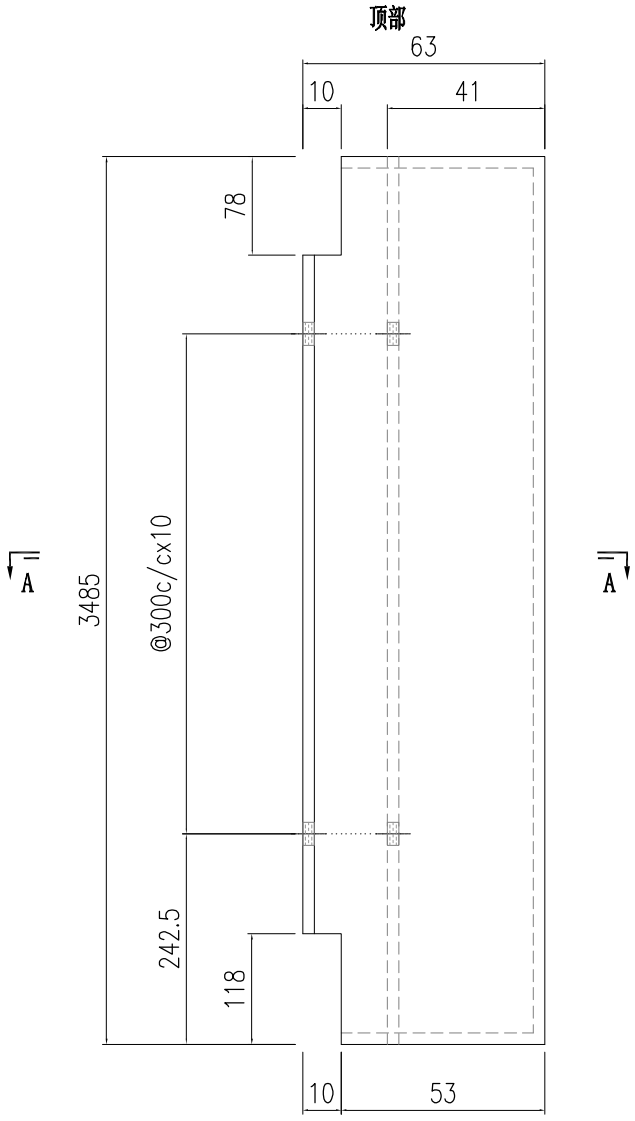


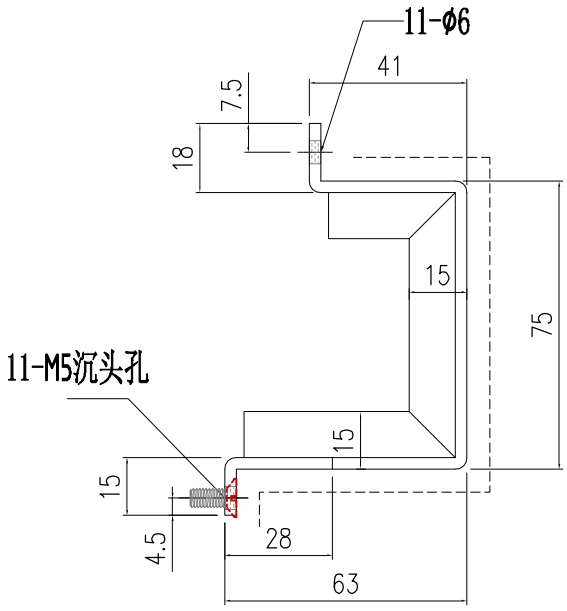


SECTION A-A

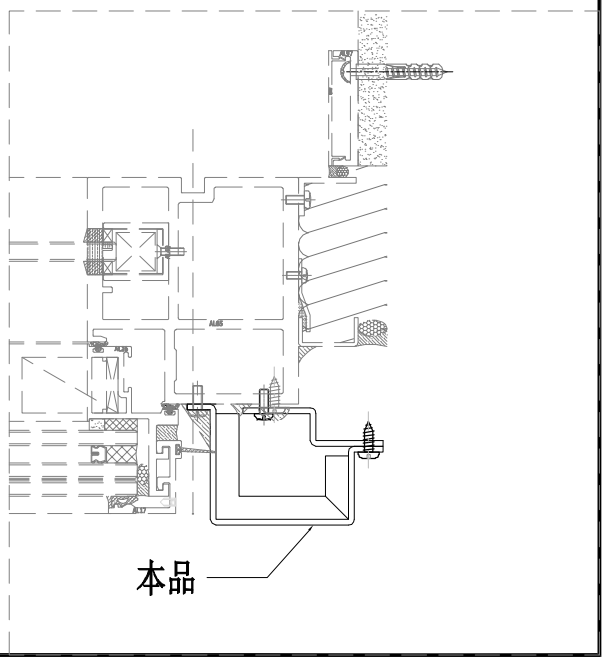


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-724	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

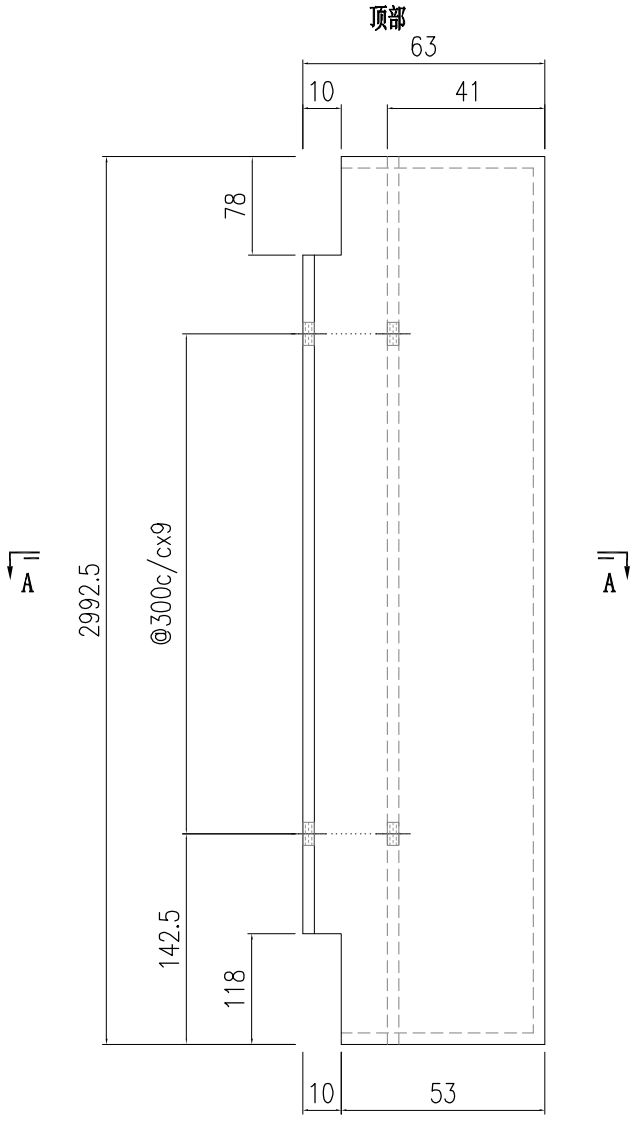

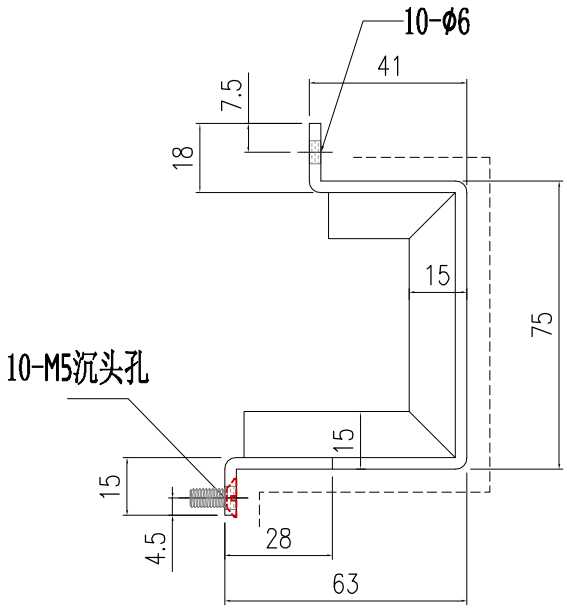



SECTION A-A

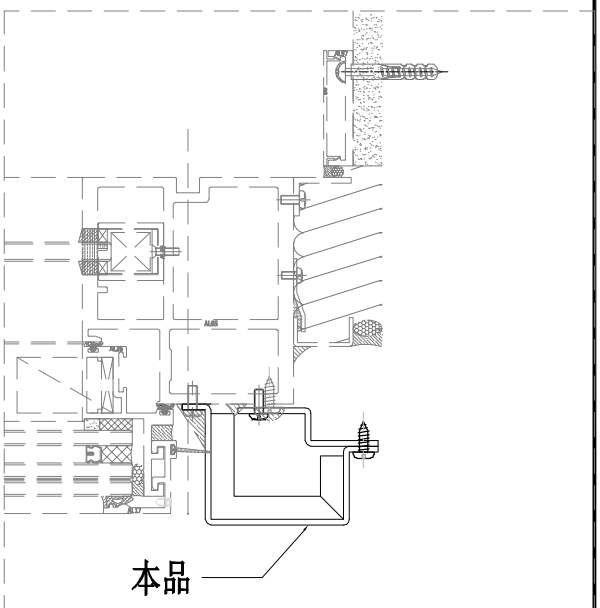


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20220915	圖號	AC-725		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20220915	數量	1		
日期	-	-	-	材料顏色	鉻化			材料	3mm 铝板	批准	林仁安 20220915	單件重量	-		(KG)

顶部

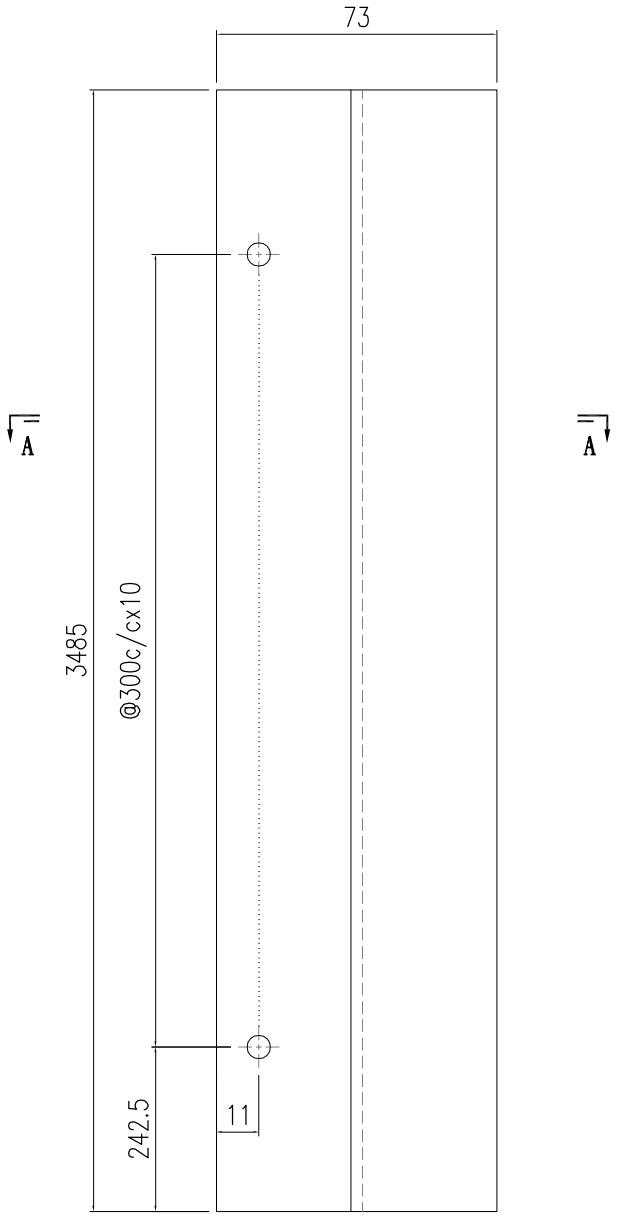

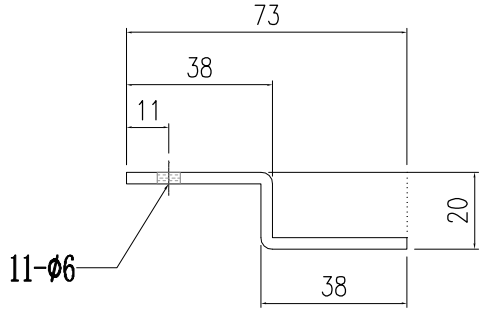



SECTION A-A

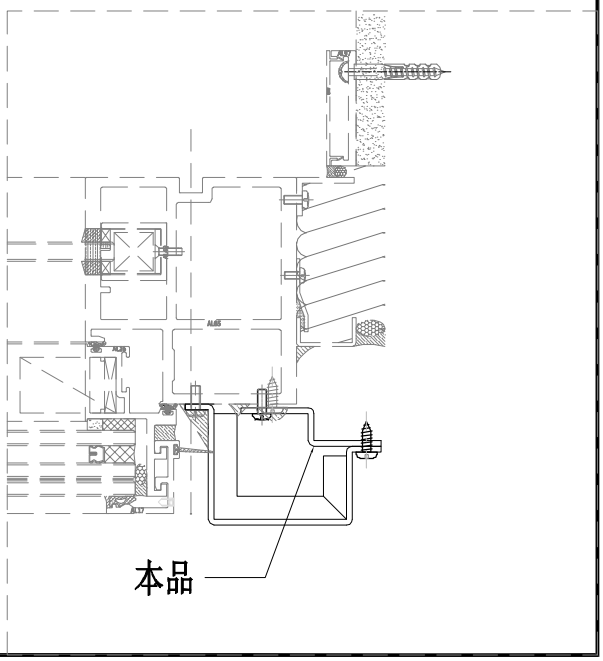


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
修改	-	-	-	採用	工廠	-	地盤	✓	工程號	J857	類別		物料號	-			
日期	-	-	-	材料顏色	鉻化				地盘	啟德6552	制圖	陈梓豪	20220915	圖號	AC-726		
									图纸名称	收边铝板	復核	練松文	20220915	數量	1		
									材料	3mm 铝板	批准	林仁安	20220915	單件重量	-		(KG)

顶部

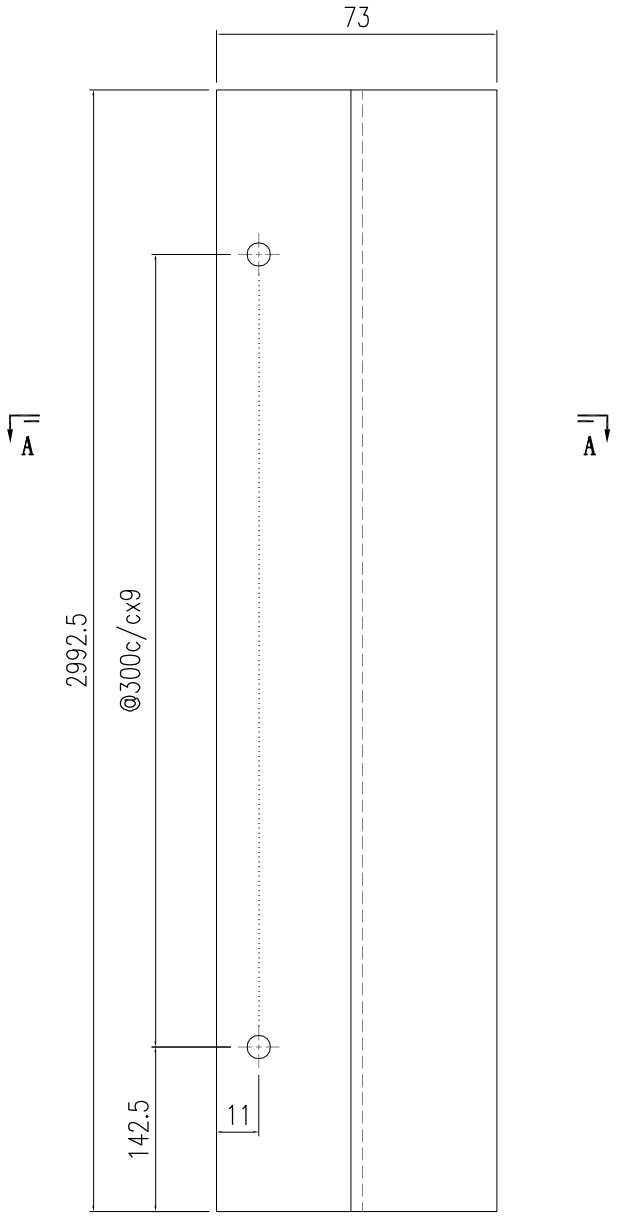


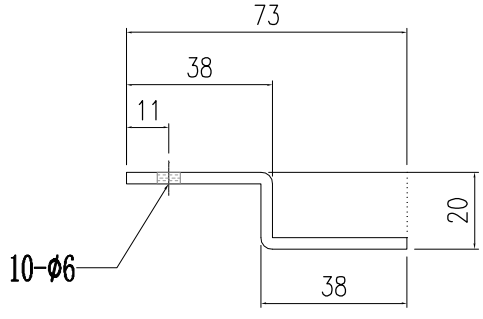


SECTION A-A

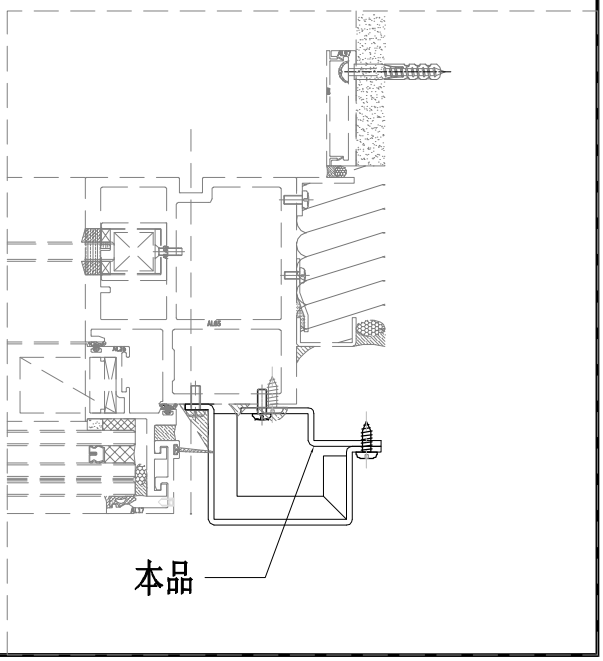


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-727	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

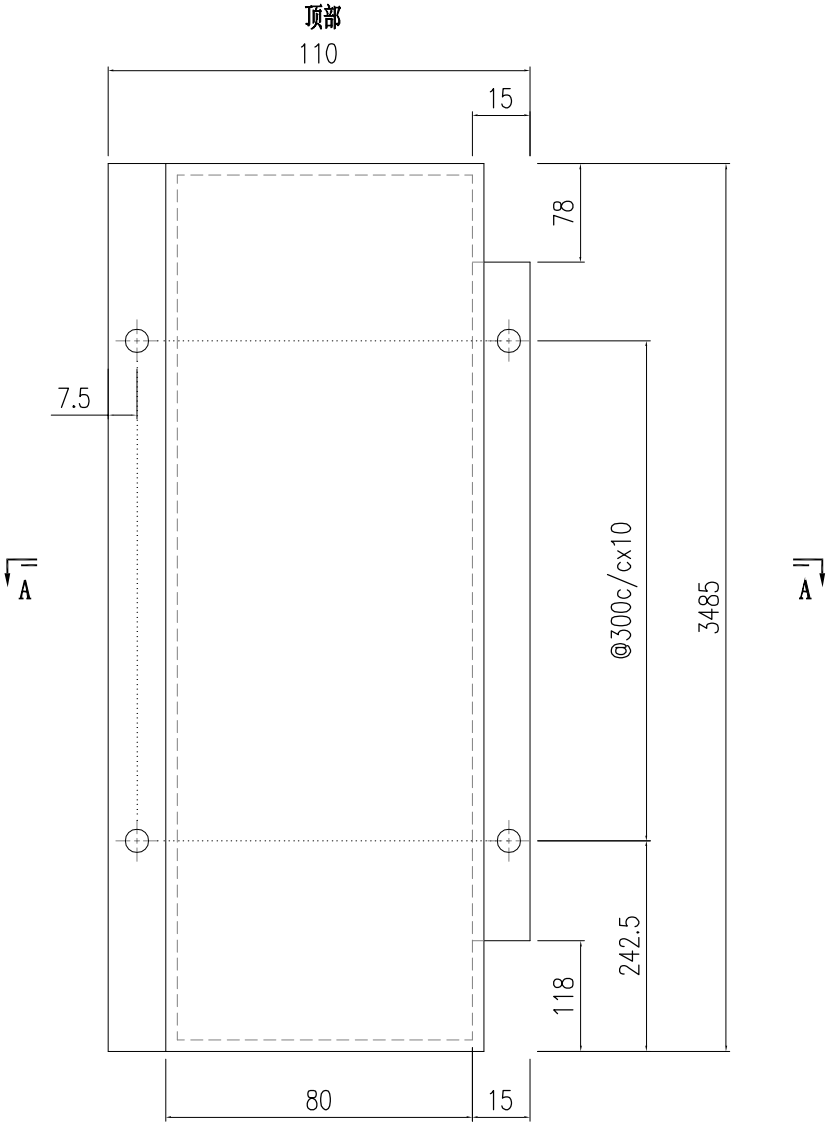

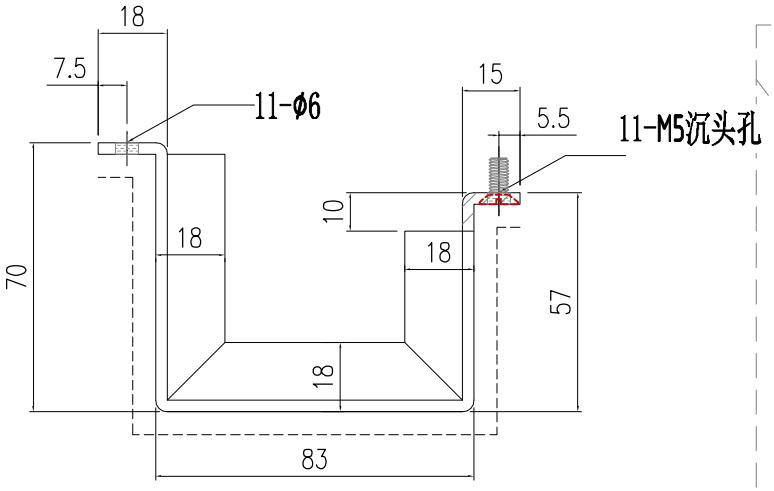



SECTION A-A

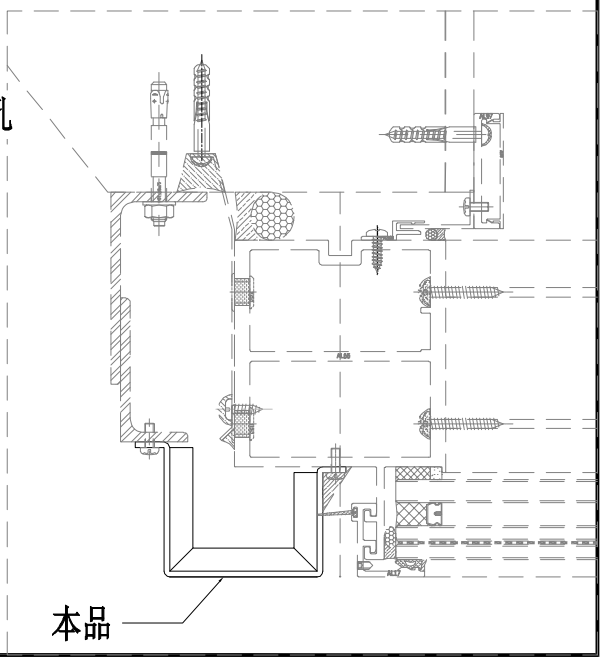


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-728	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

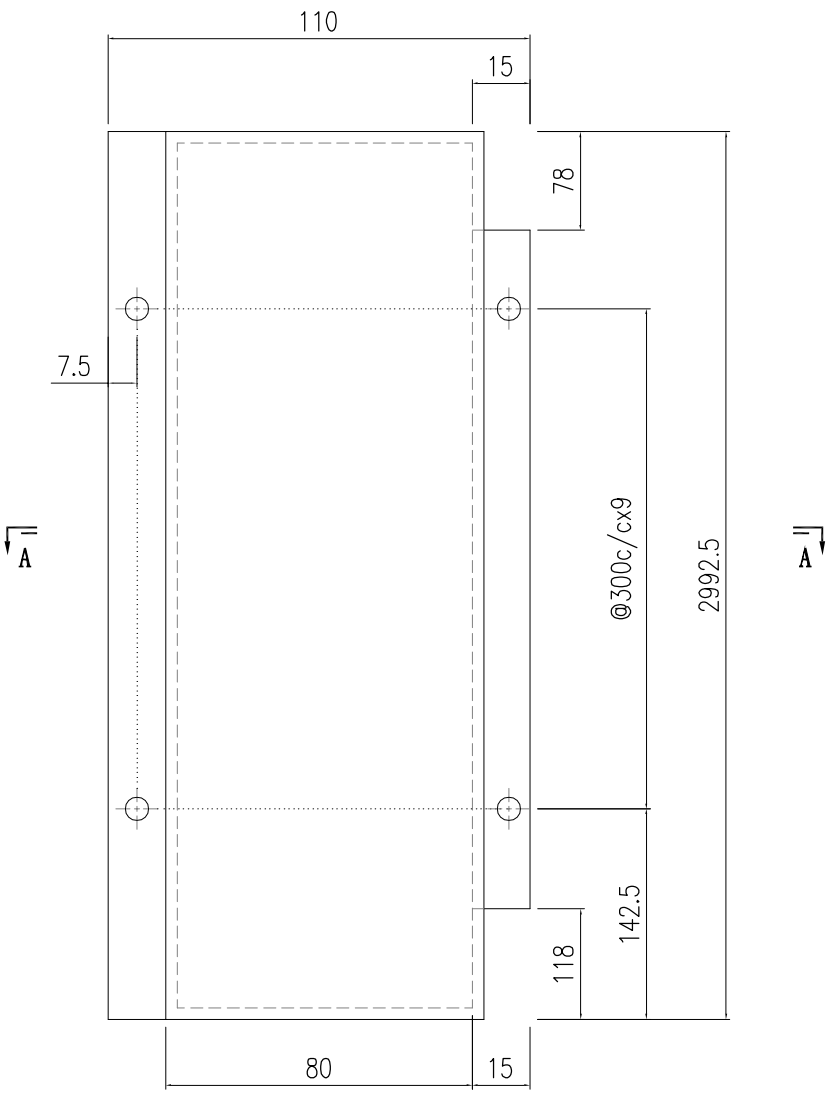

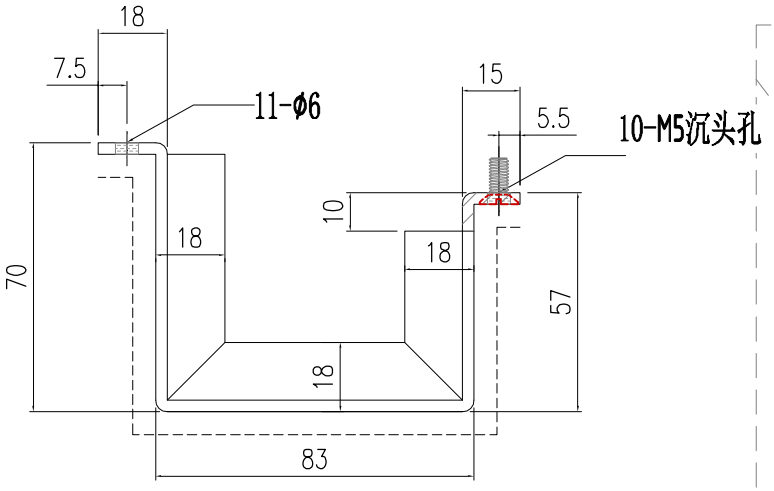



SECTION A-A

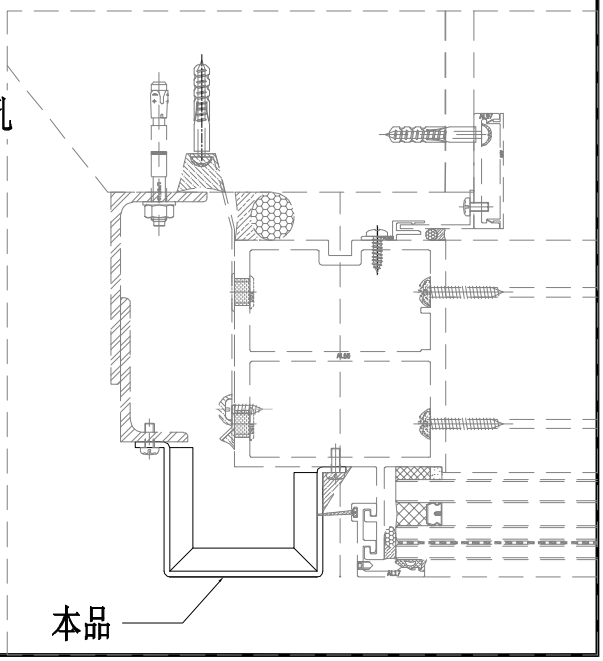


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-732	
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	2	
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

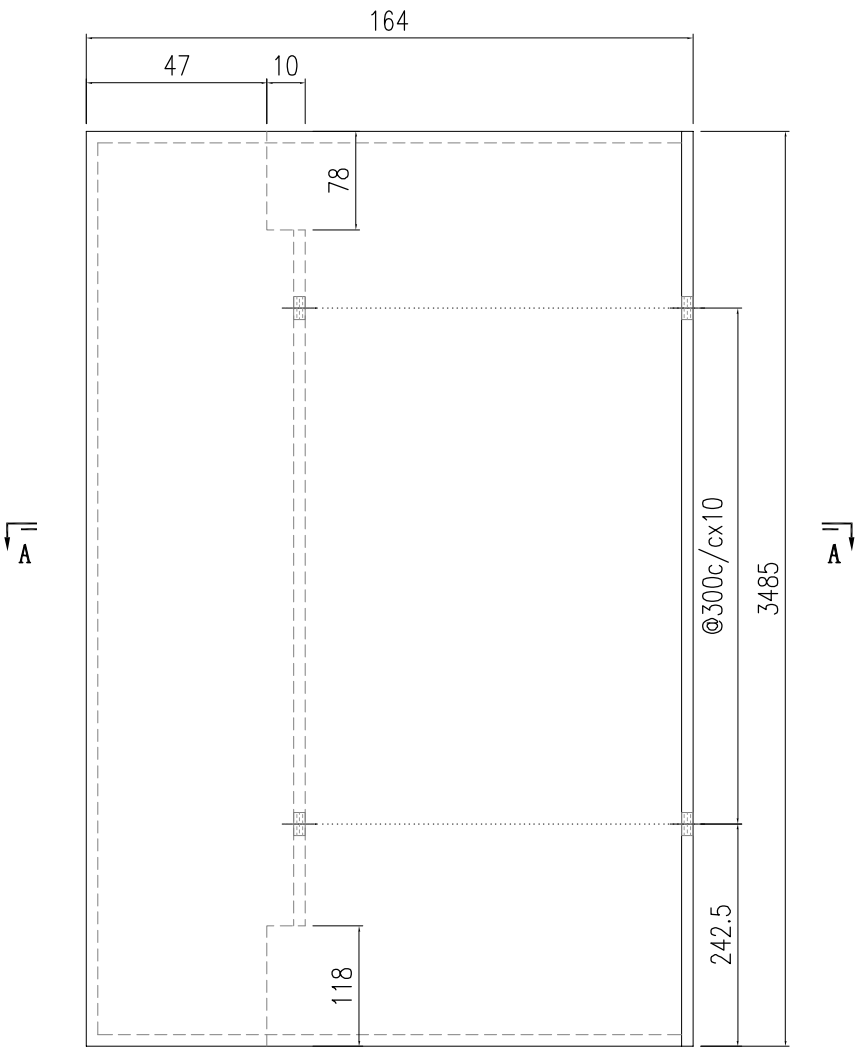

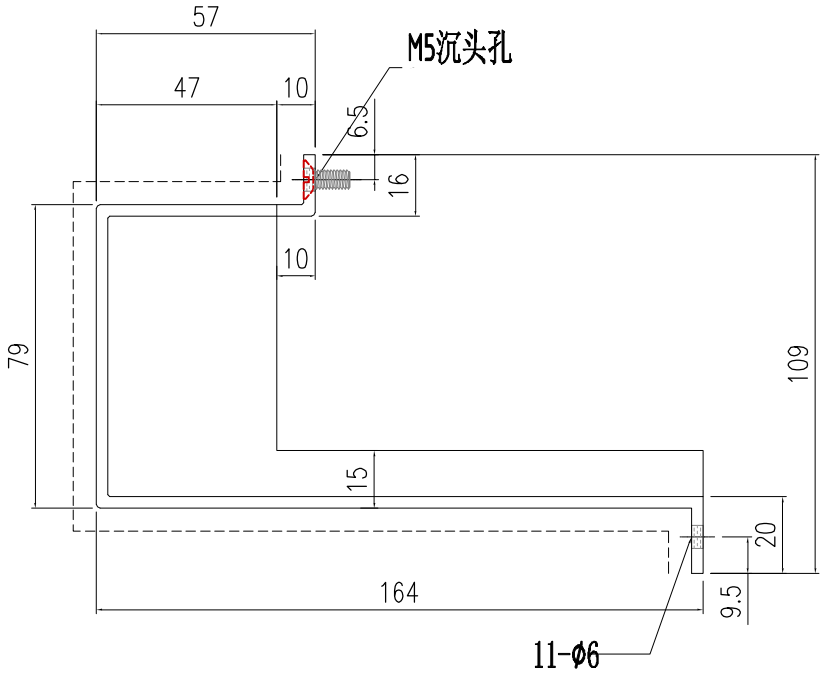



SECTION A-A

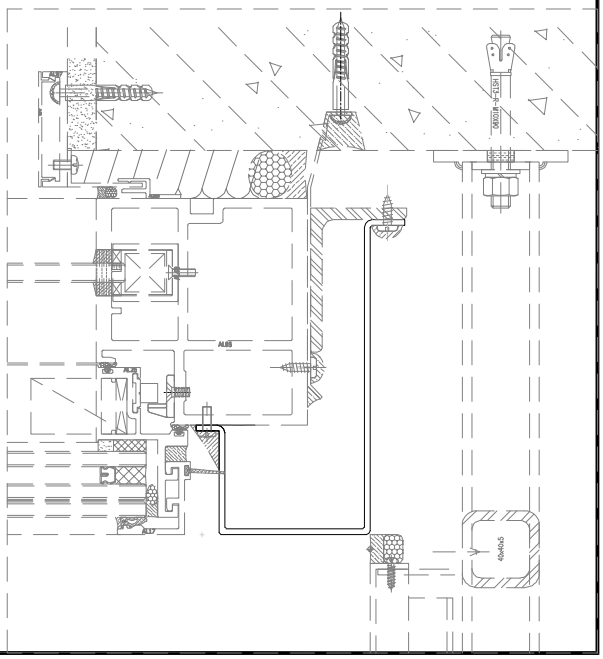


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-733	
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	3	
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

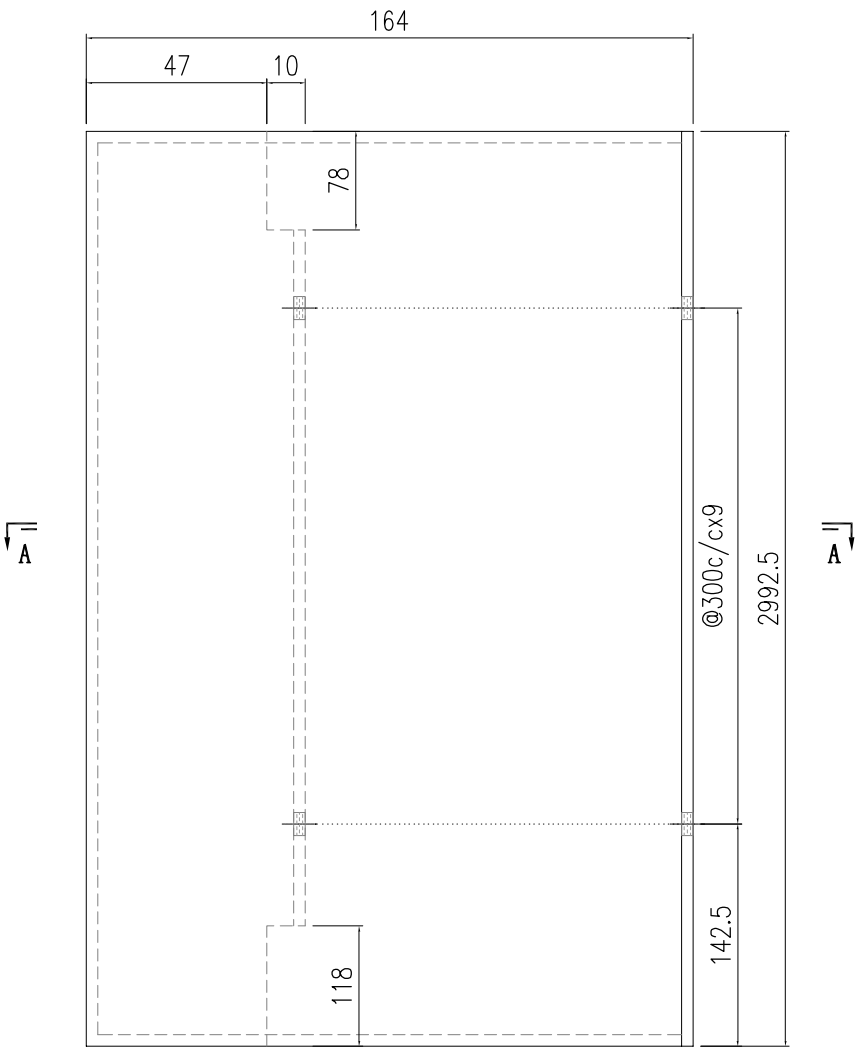

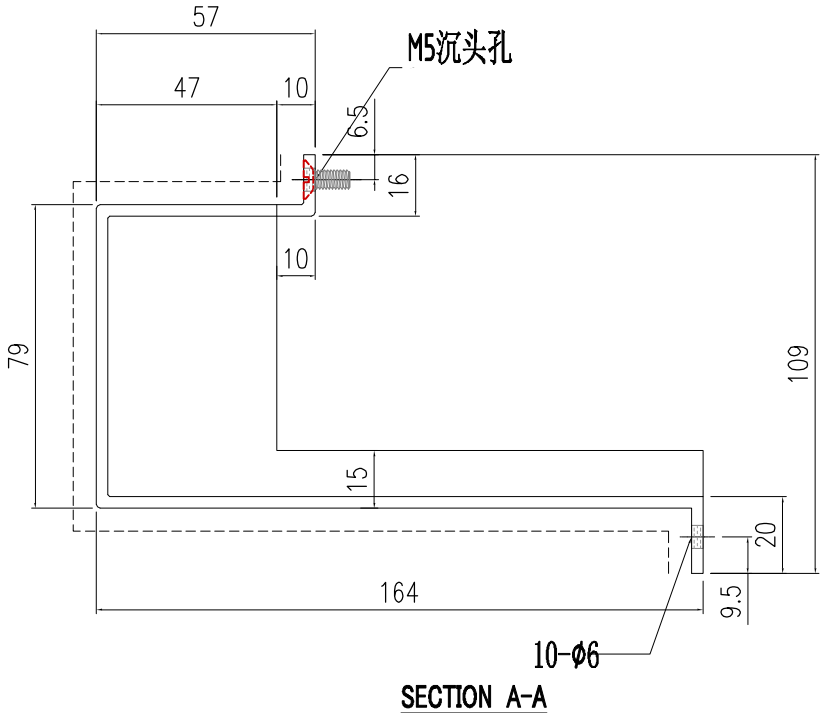



SECTION A-A

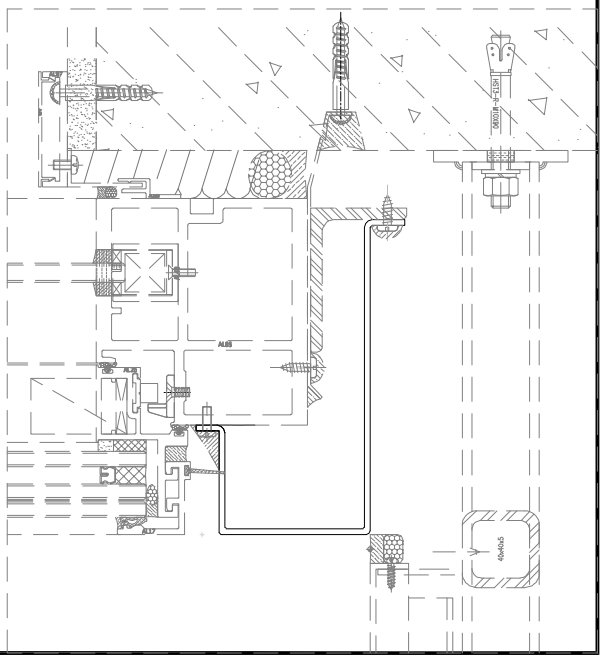


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-734	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1		材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

顶部

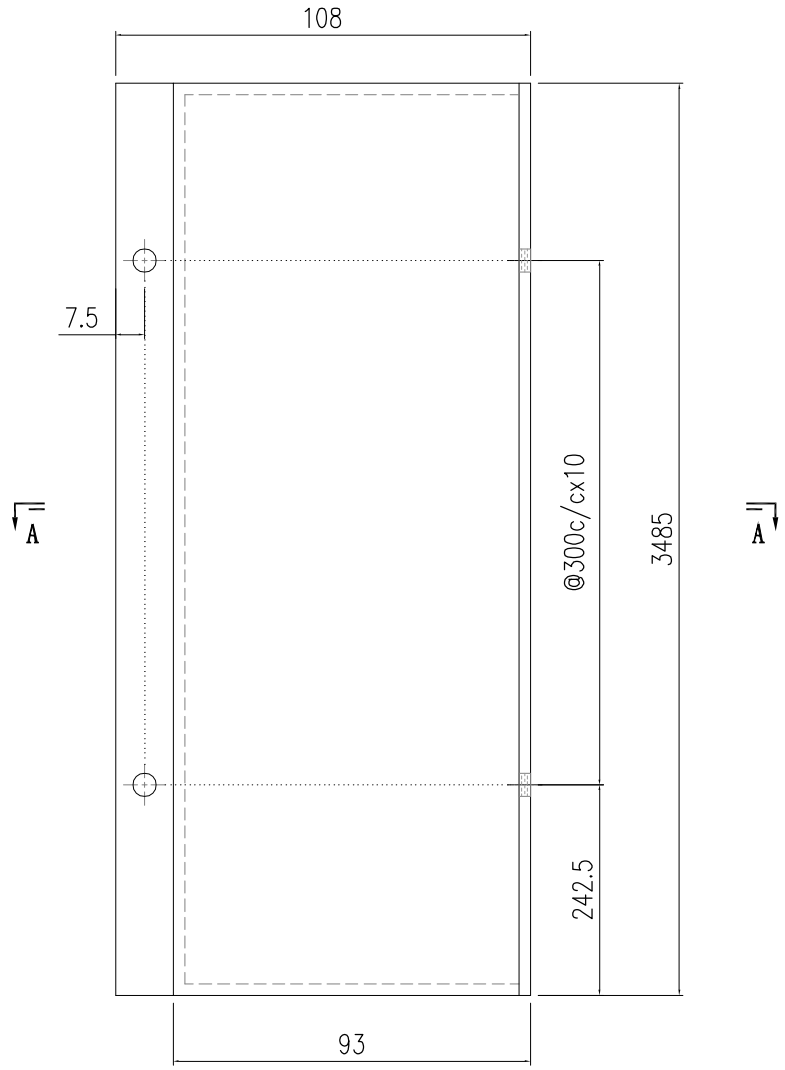

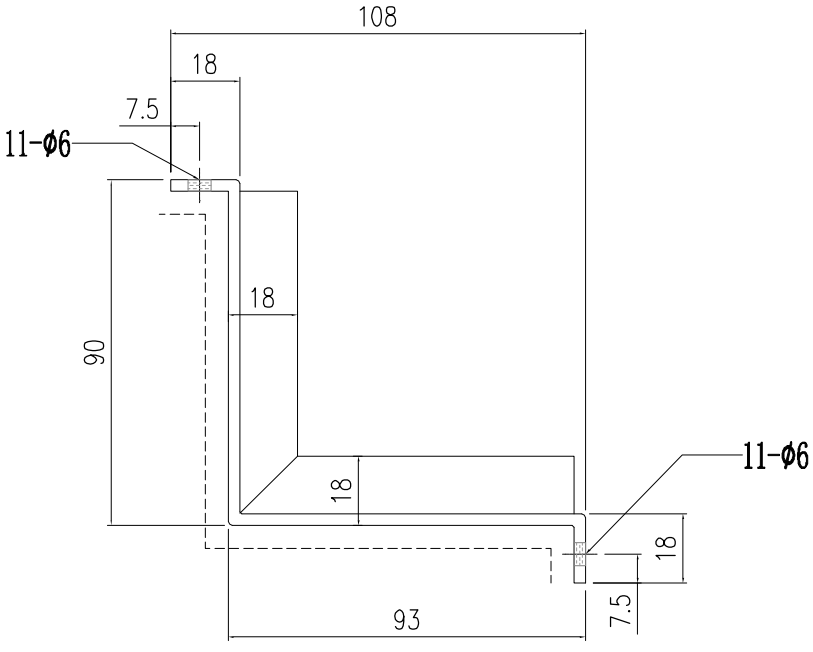



SECTION A-A

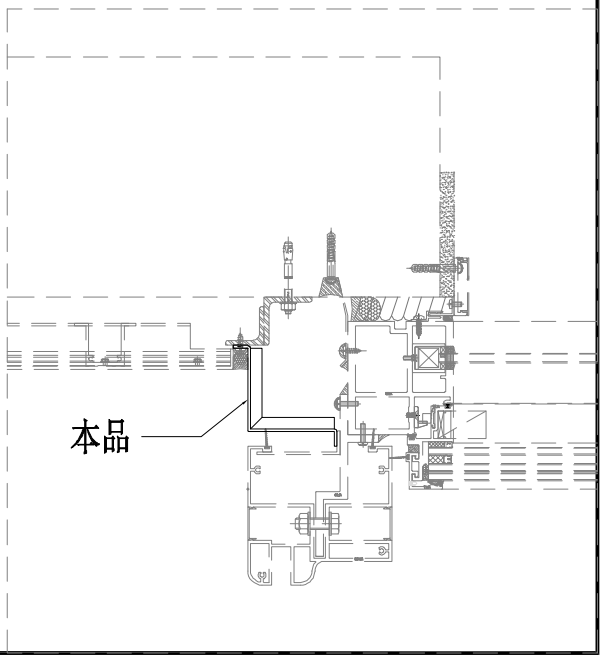


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-735	
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

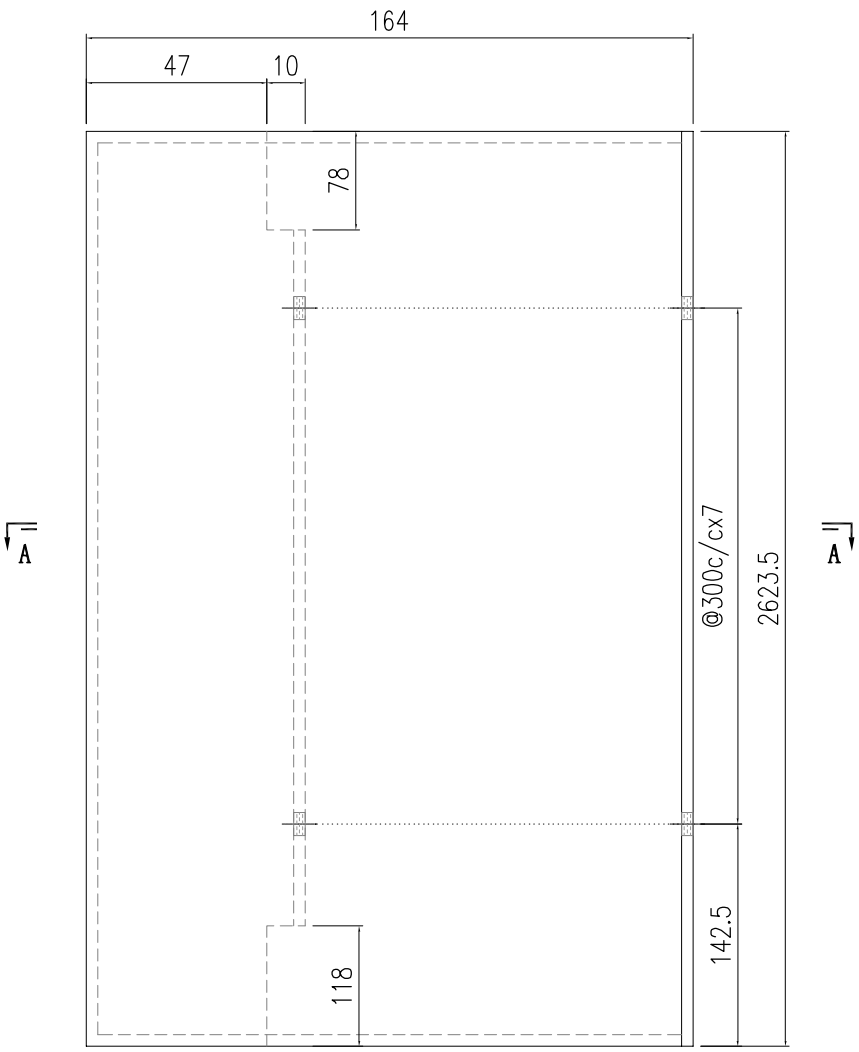

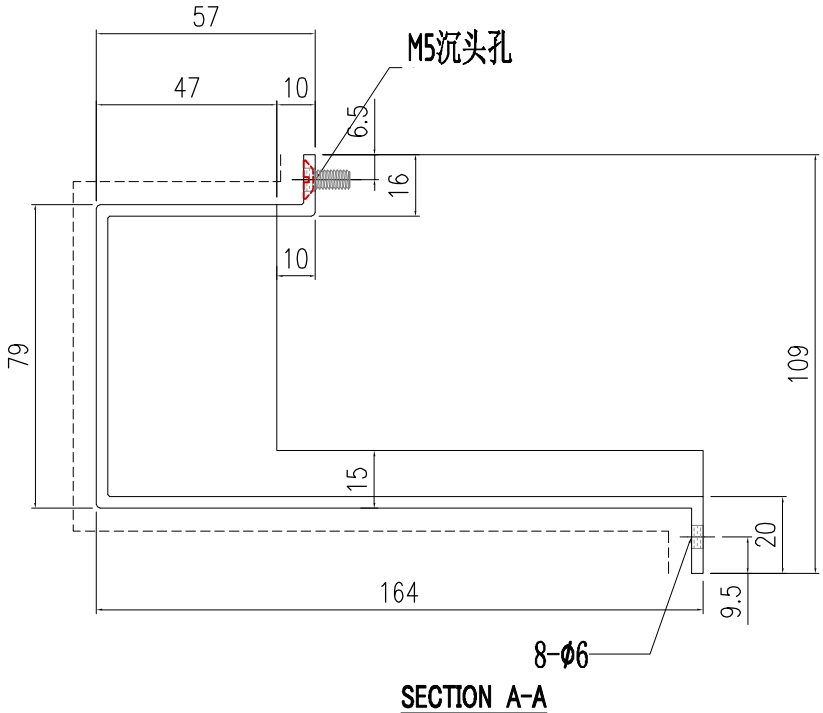



SECTION A-A

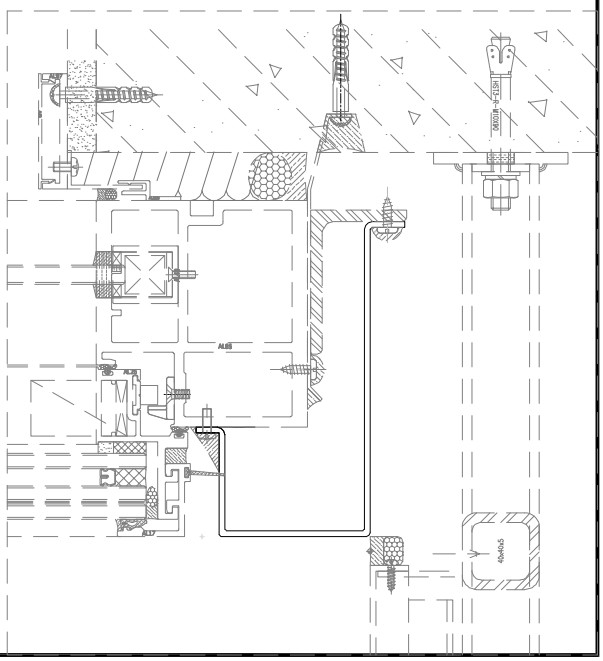


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-736	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	3	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

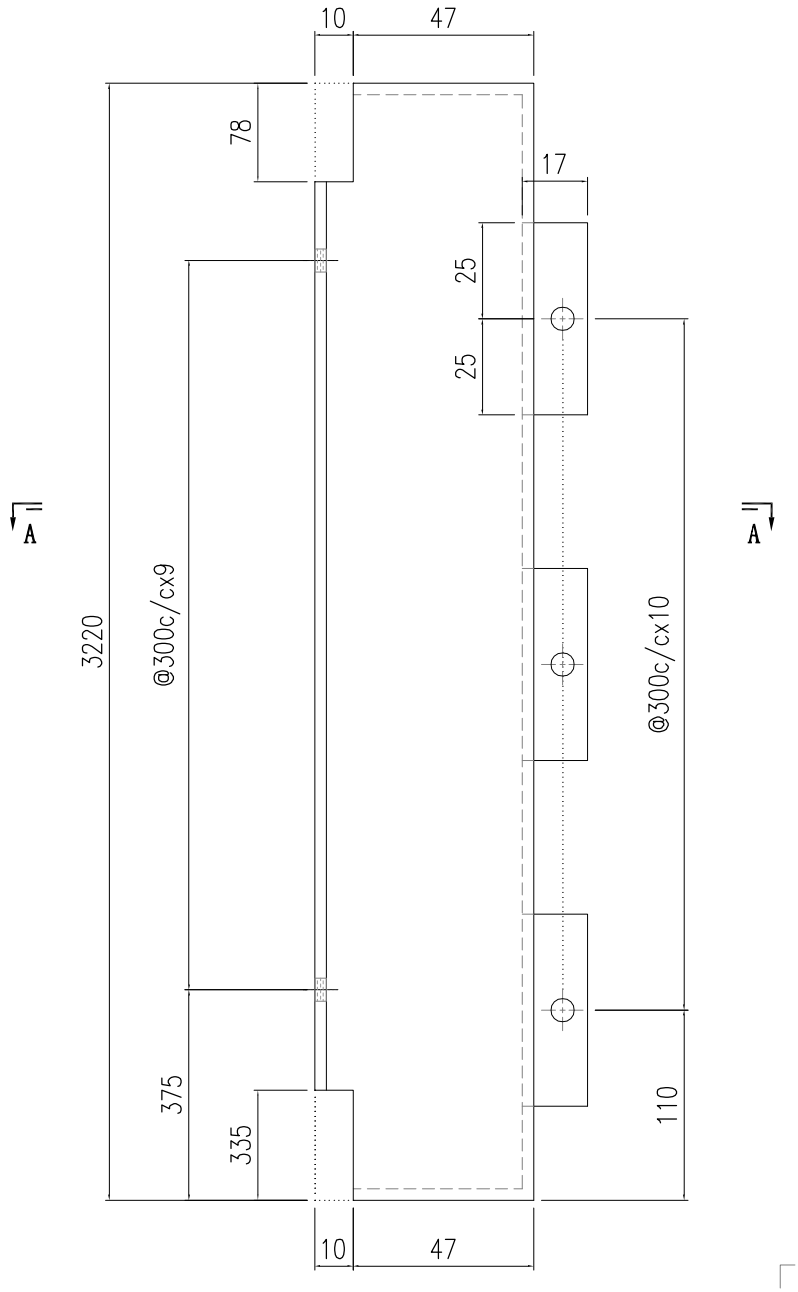

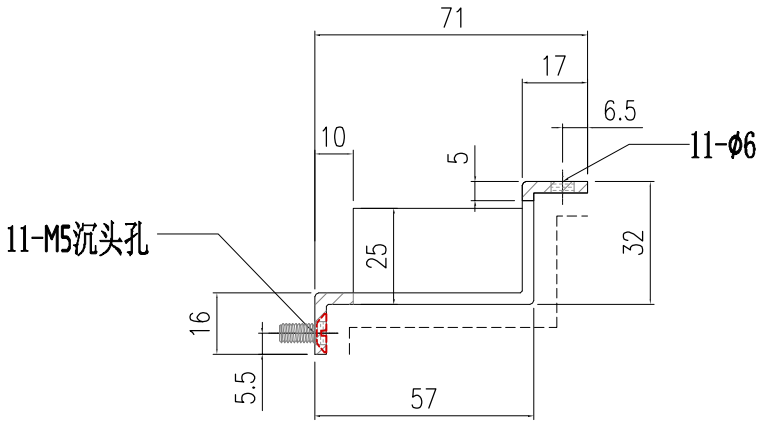



SECTION A-A

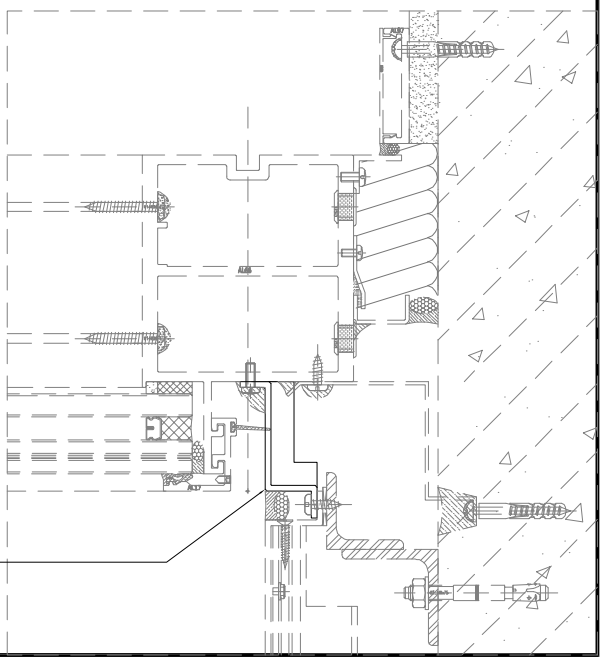


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-737	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	2	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

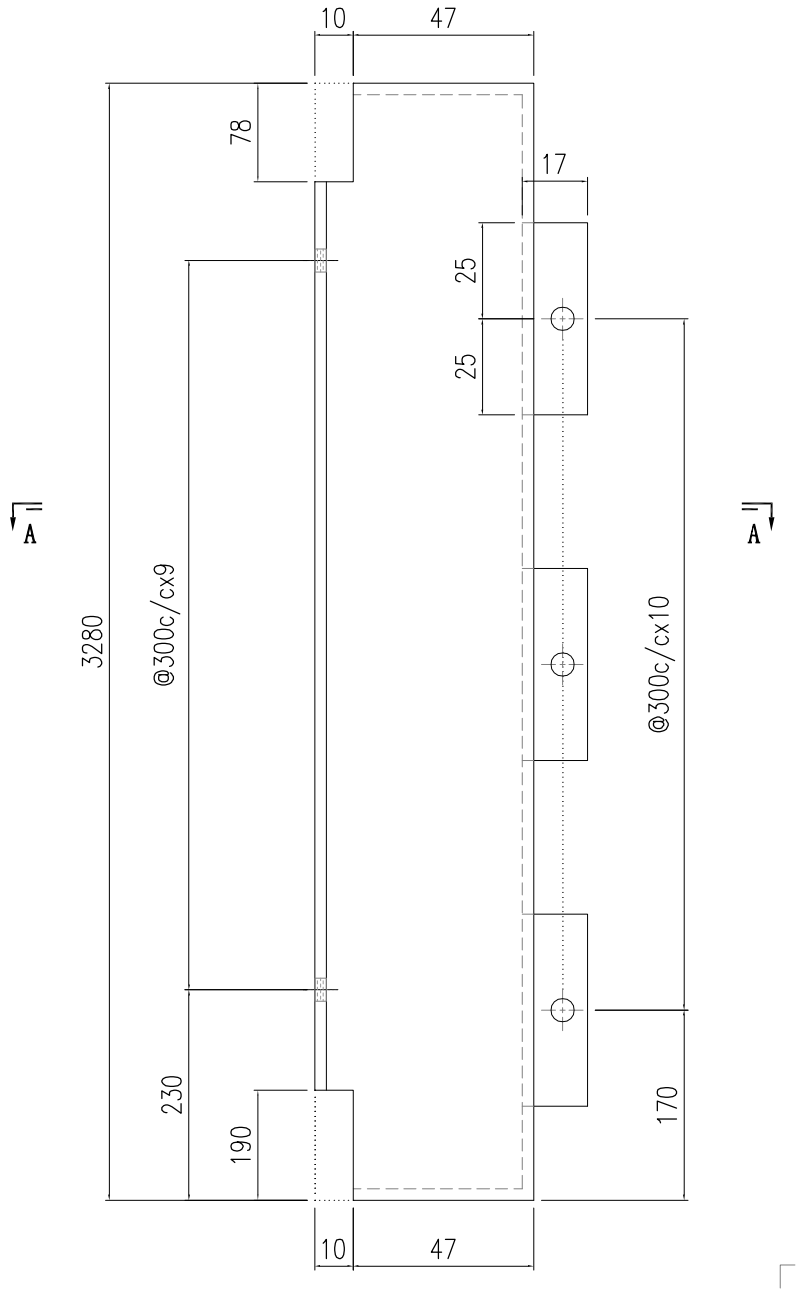


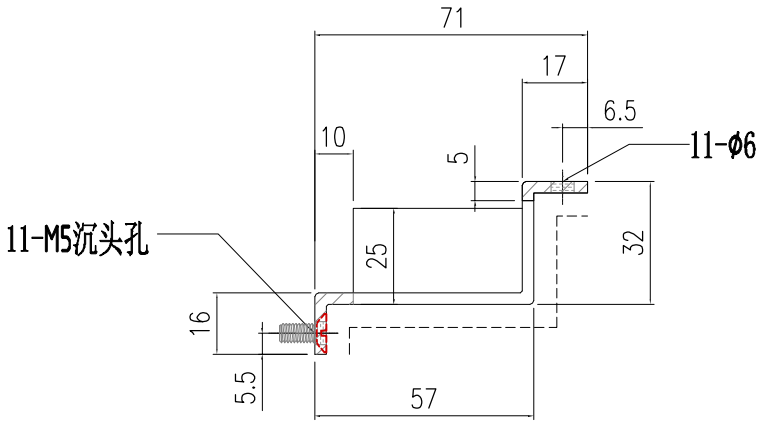


SECTION A-A

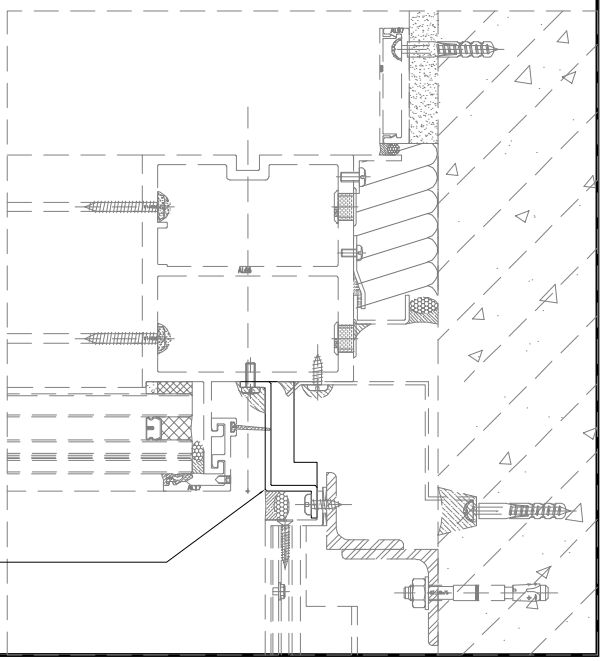


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-738	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	2	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

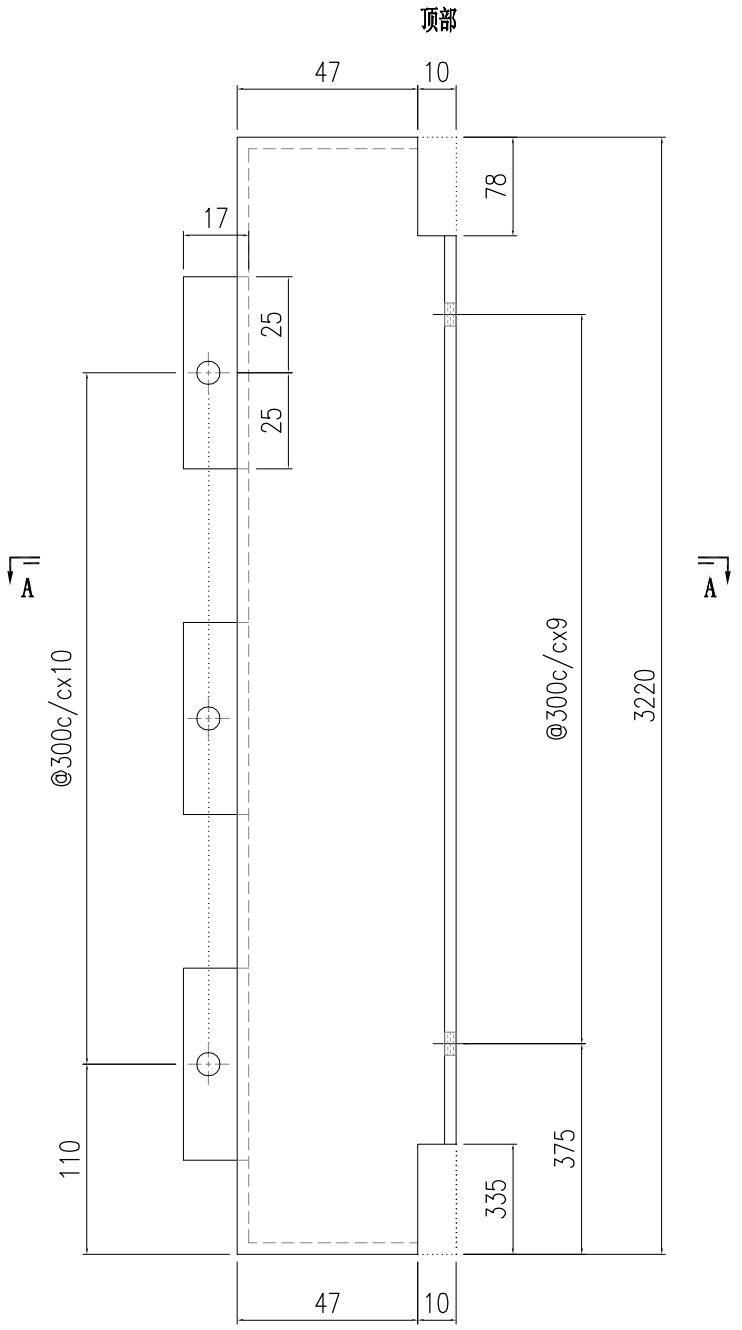

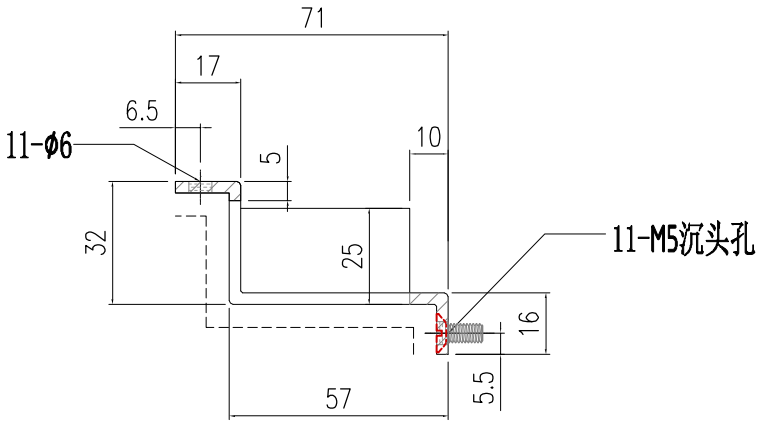


SECTION A-A

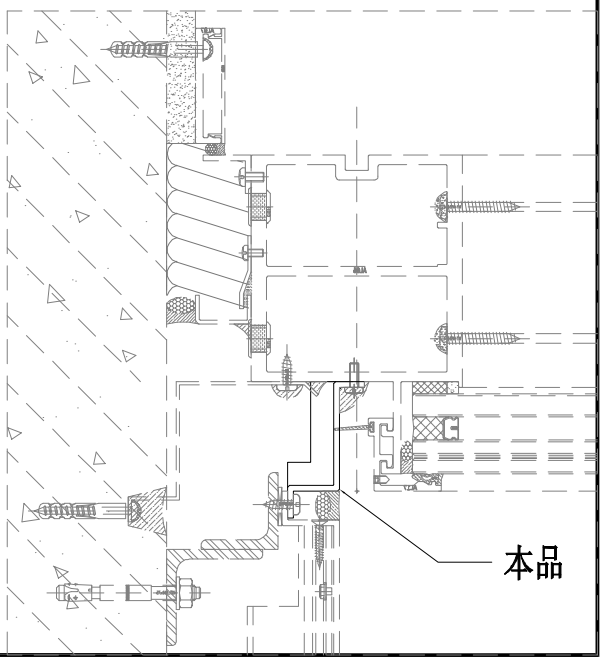


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-739
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	2
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)


顶部

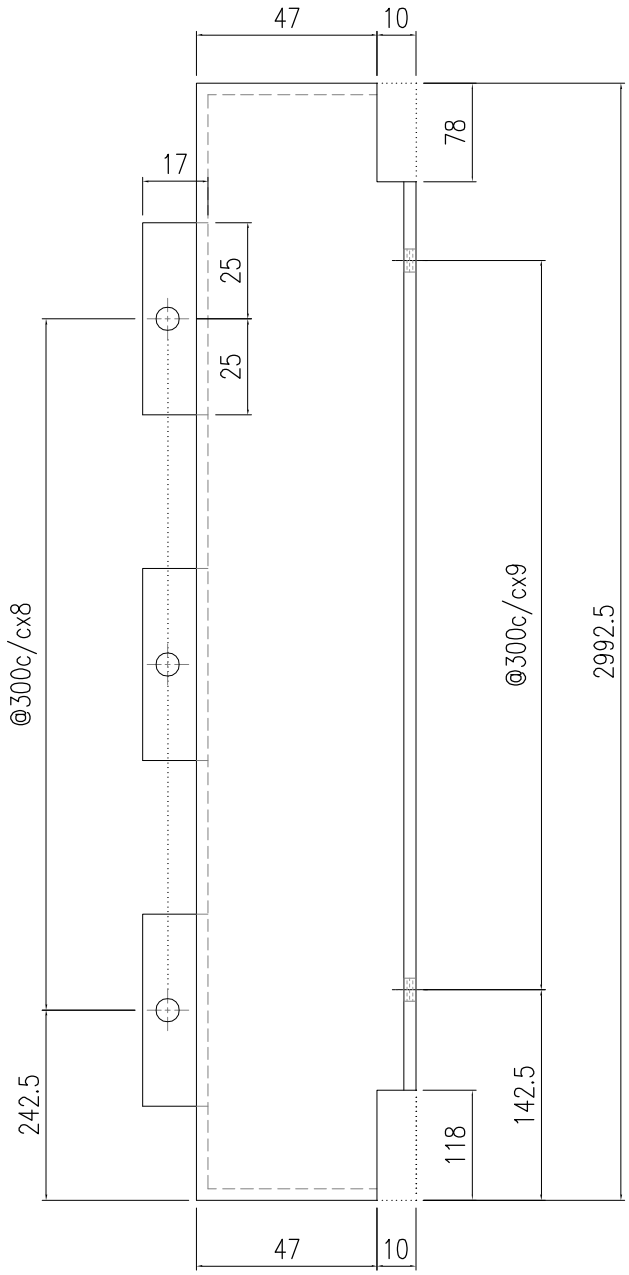

A A

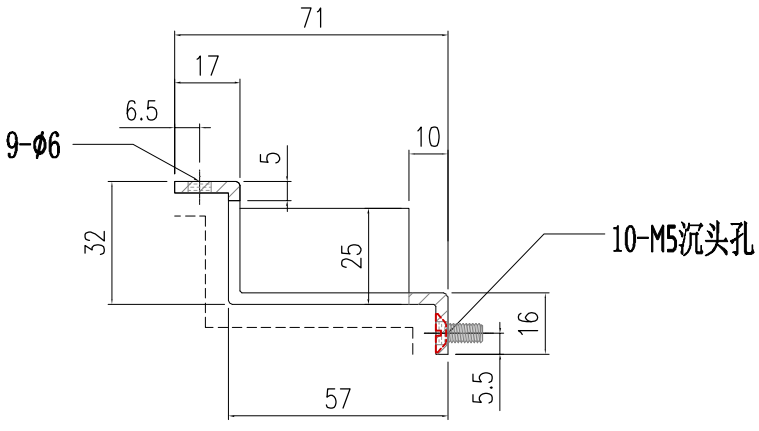



SECTION A-A

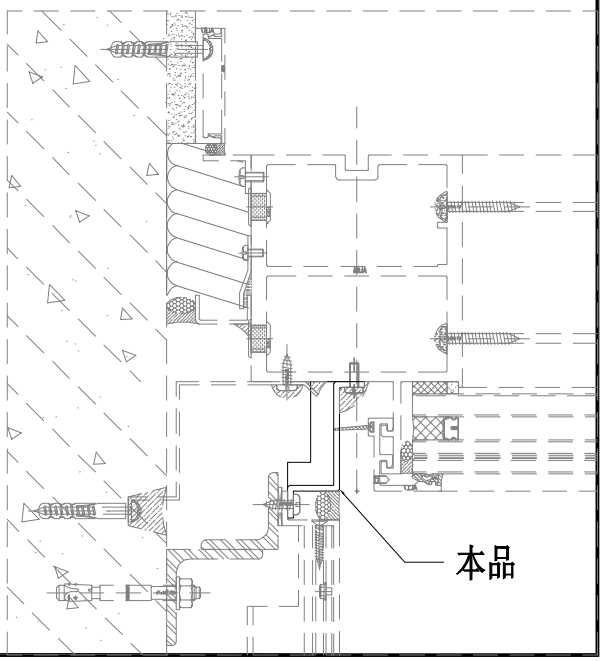


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-740
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

顶部

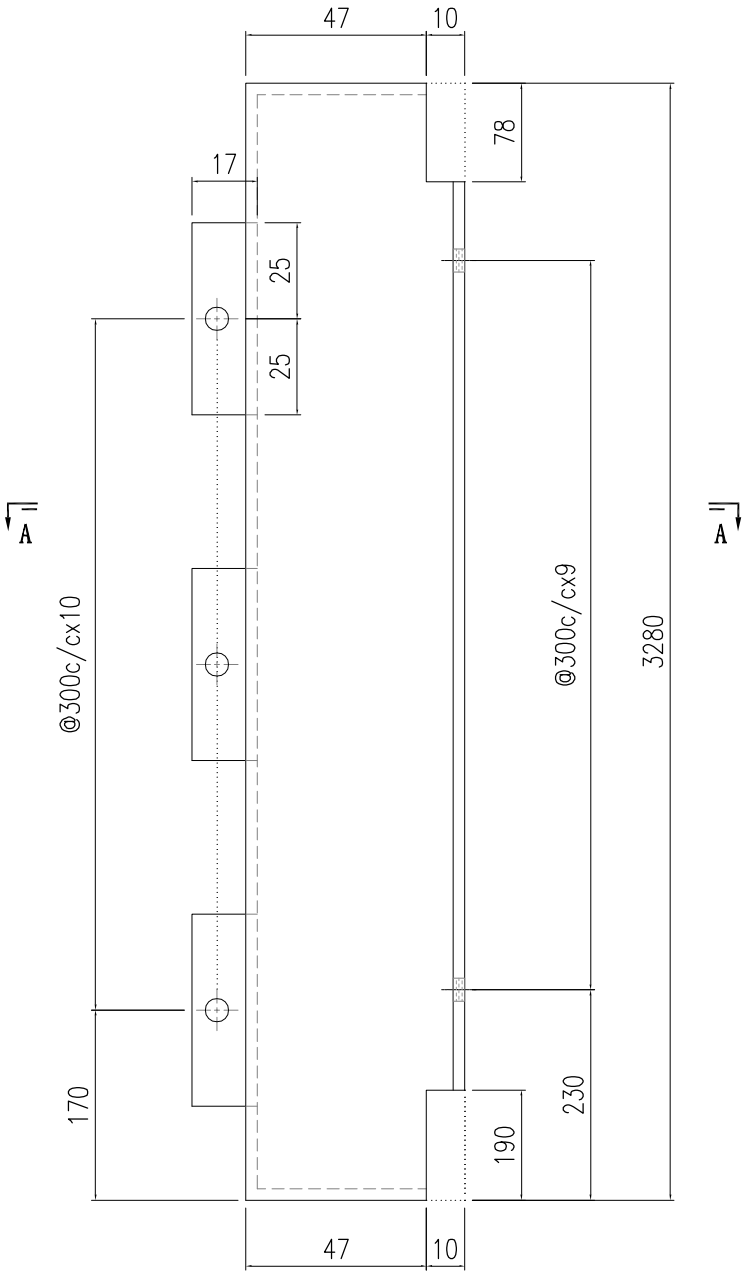

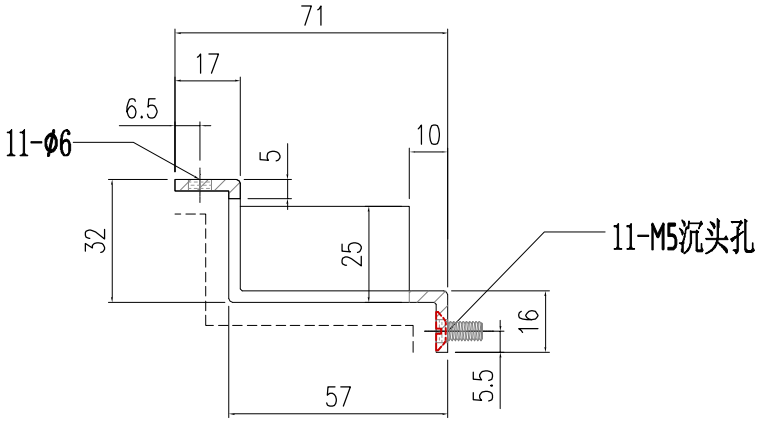



SECTION A-A

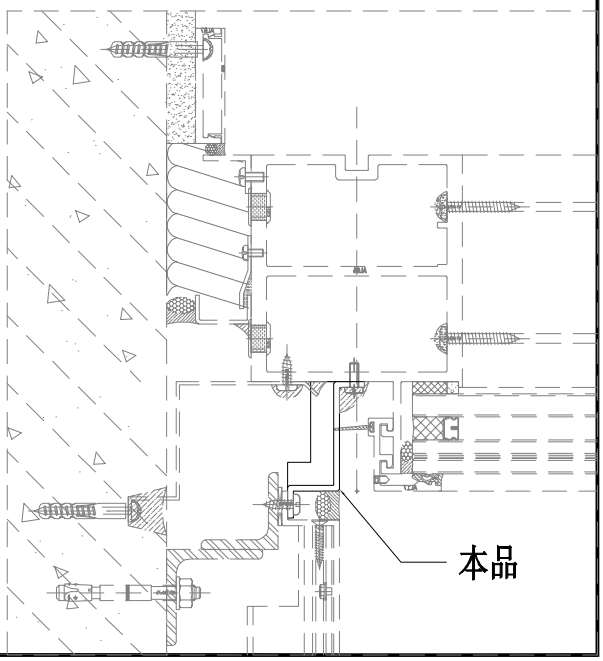


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-741	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

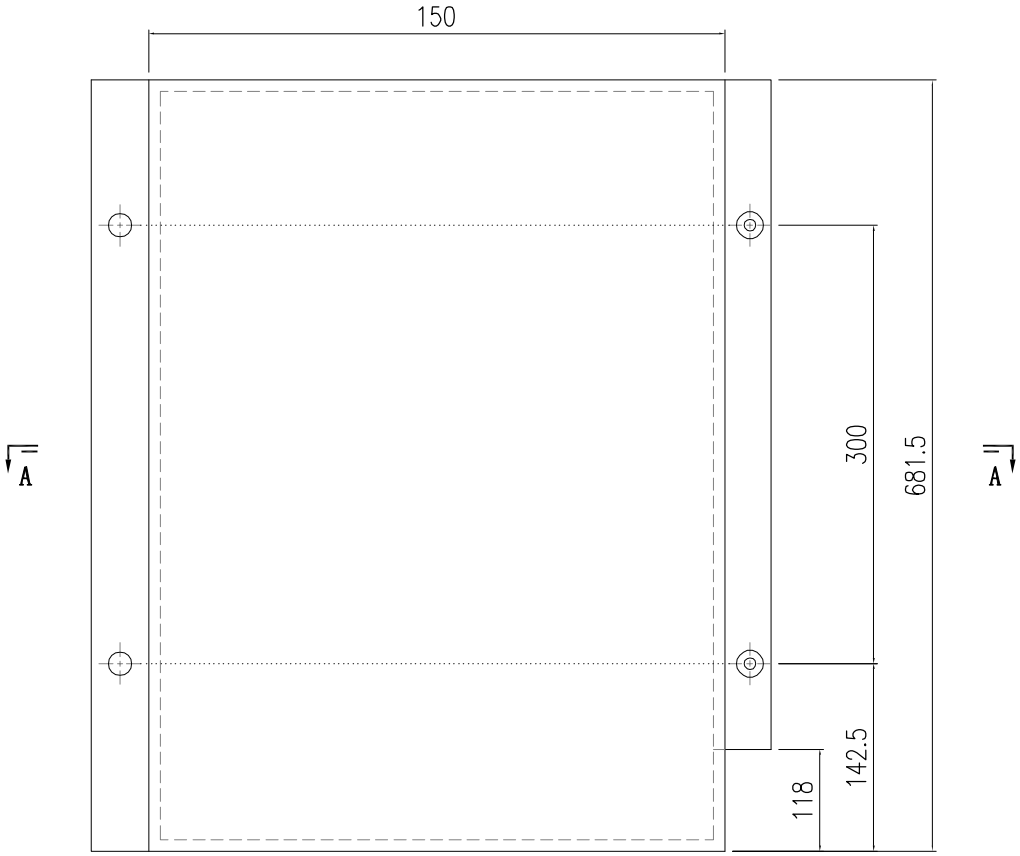

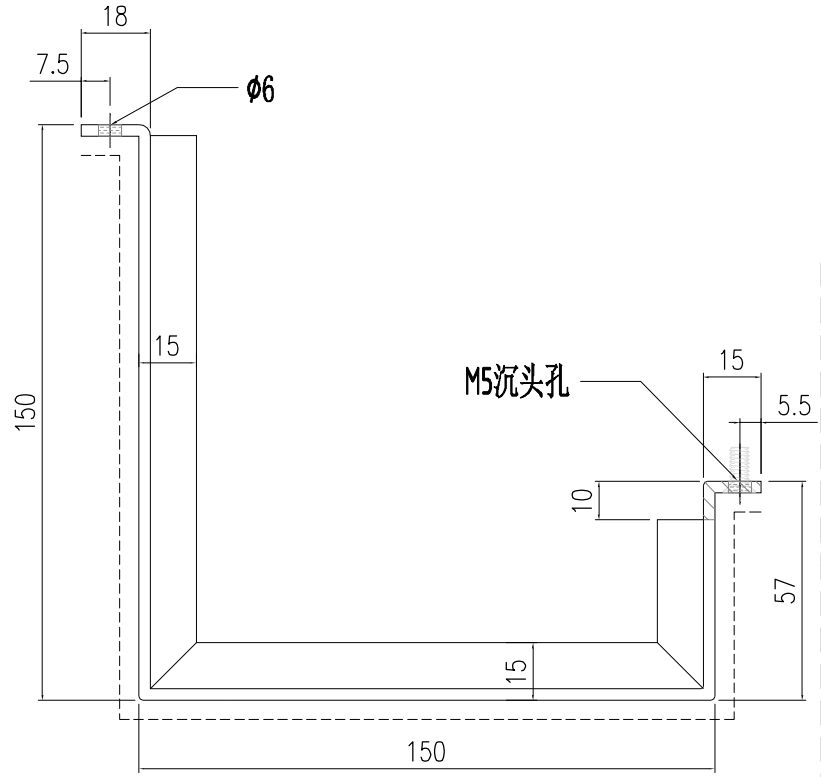



SECTION A-A

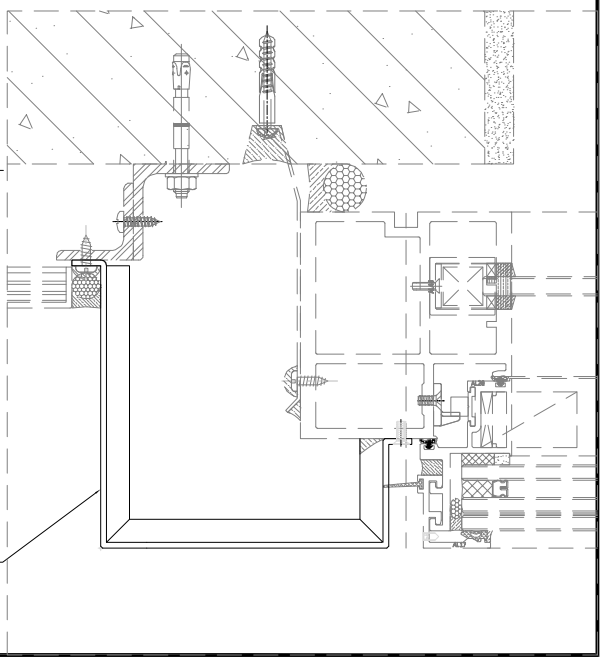

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-742	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)


顶部

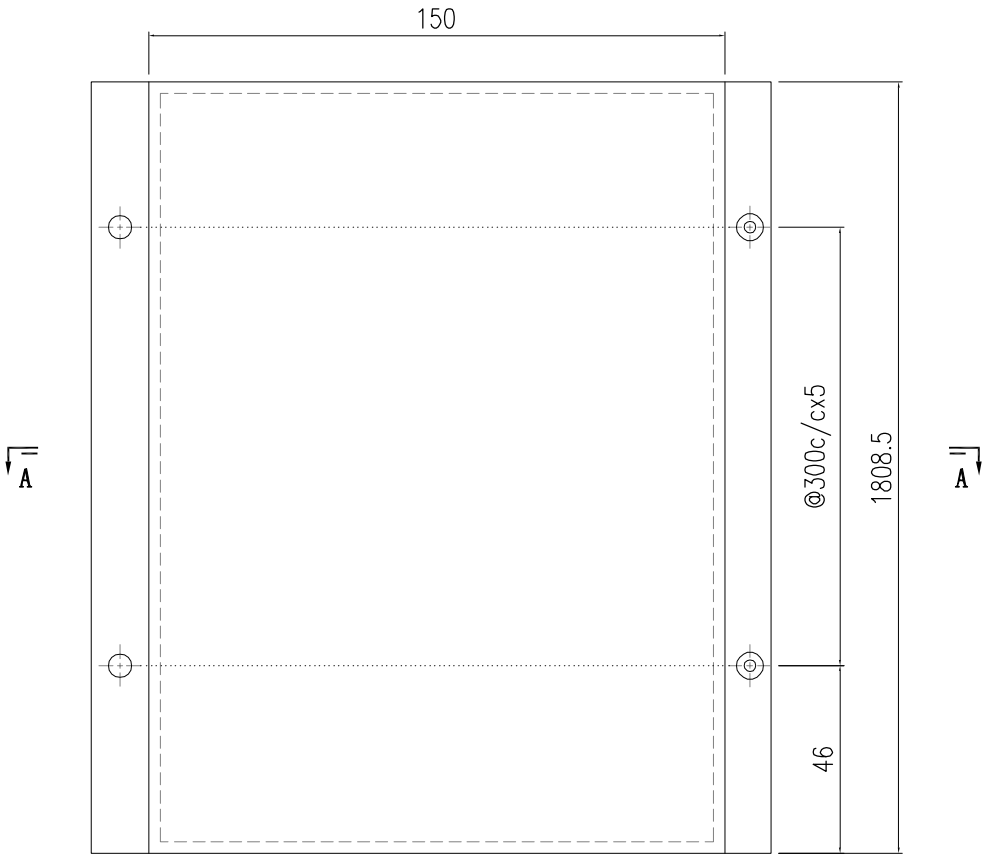


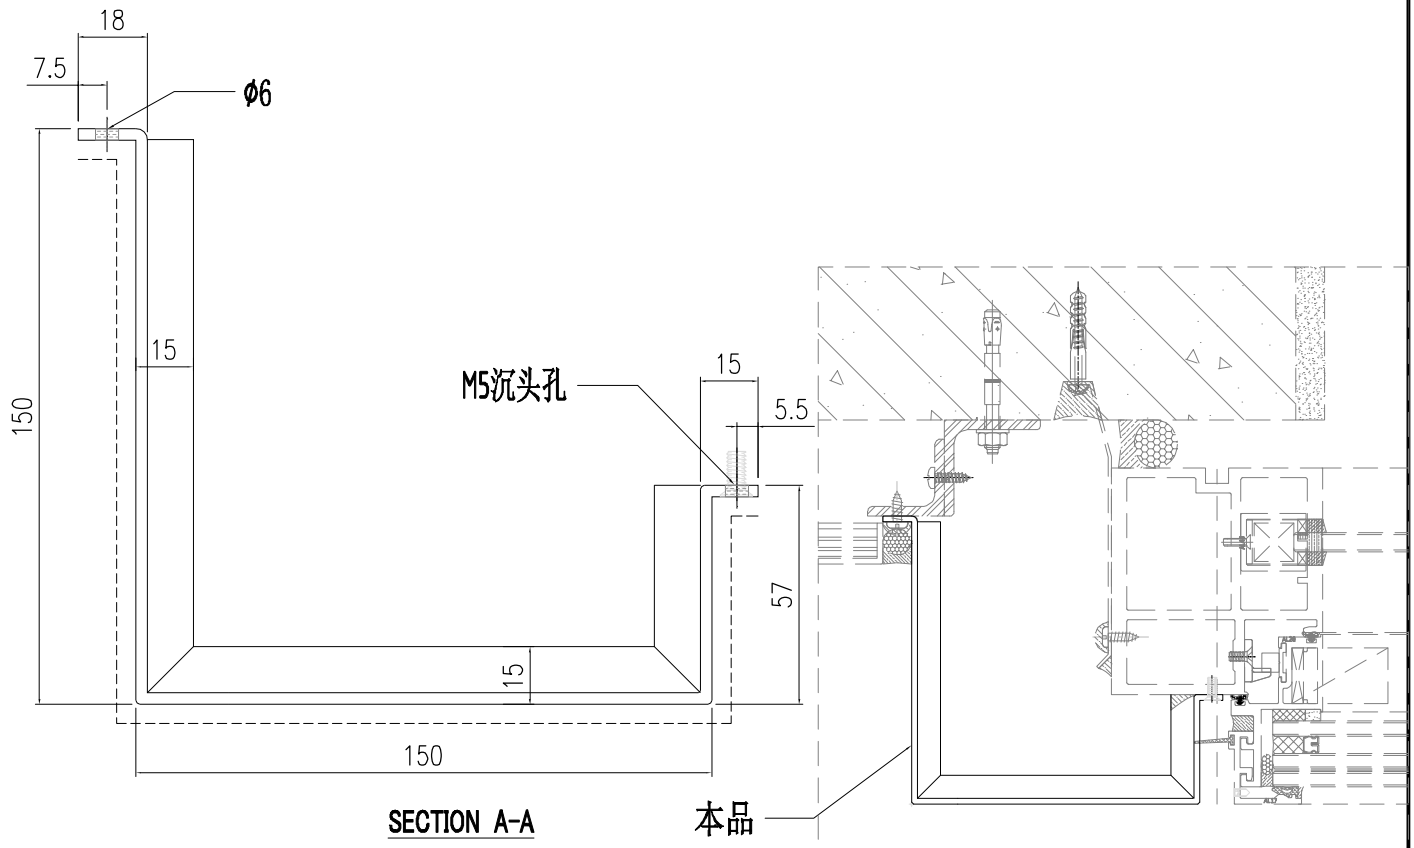

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-743	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)


顶部

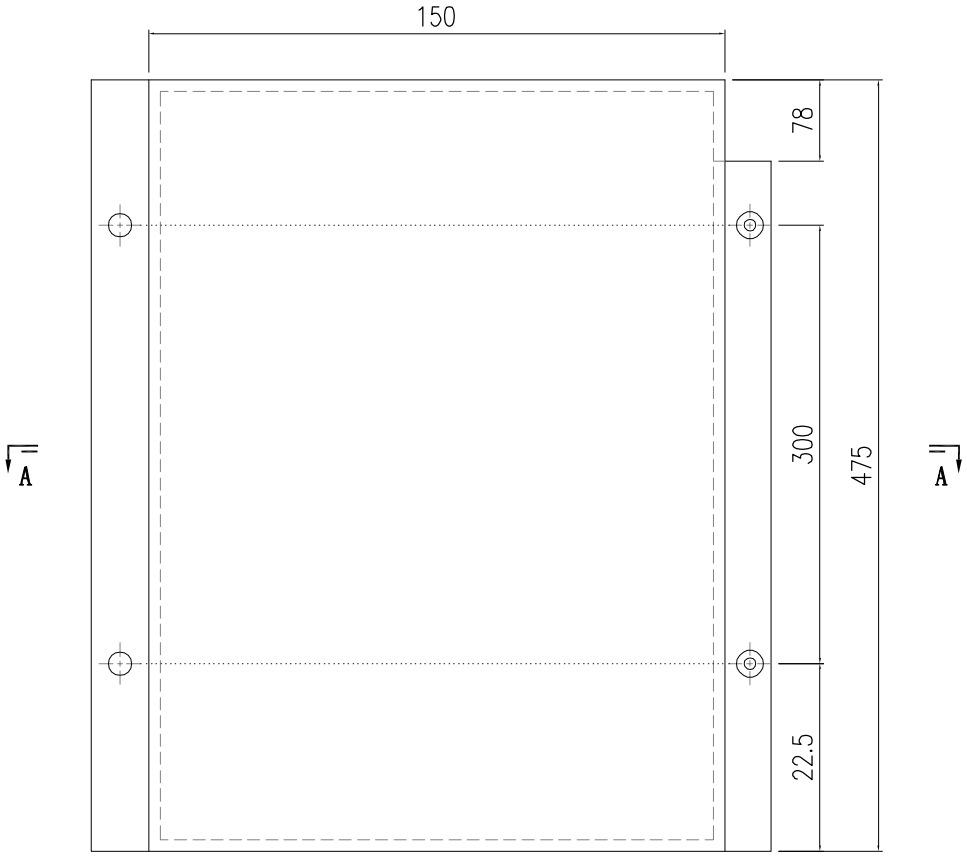


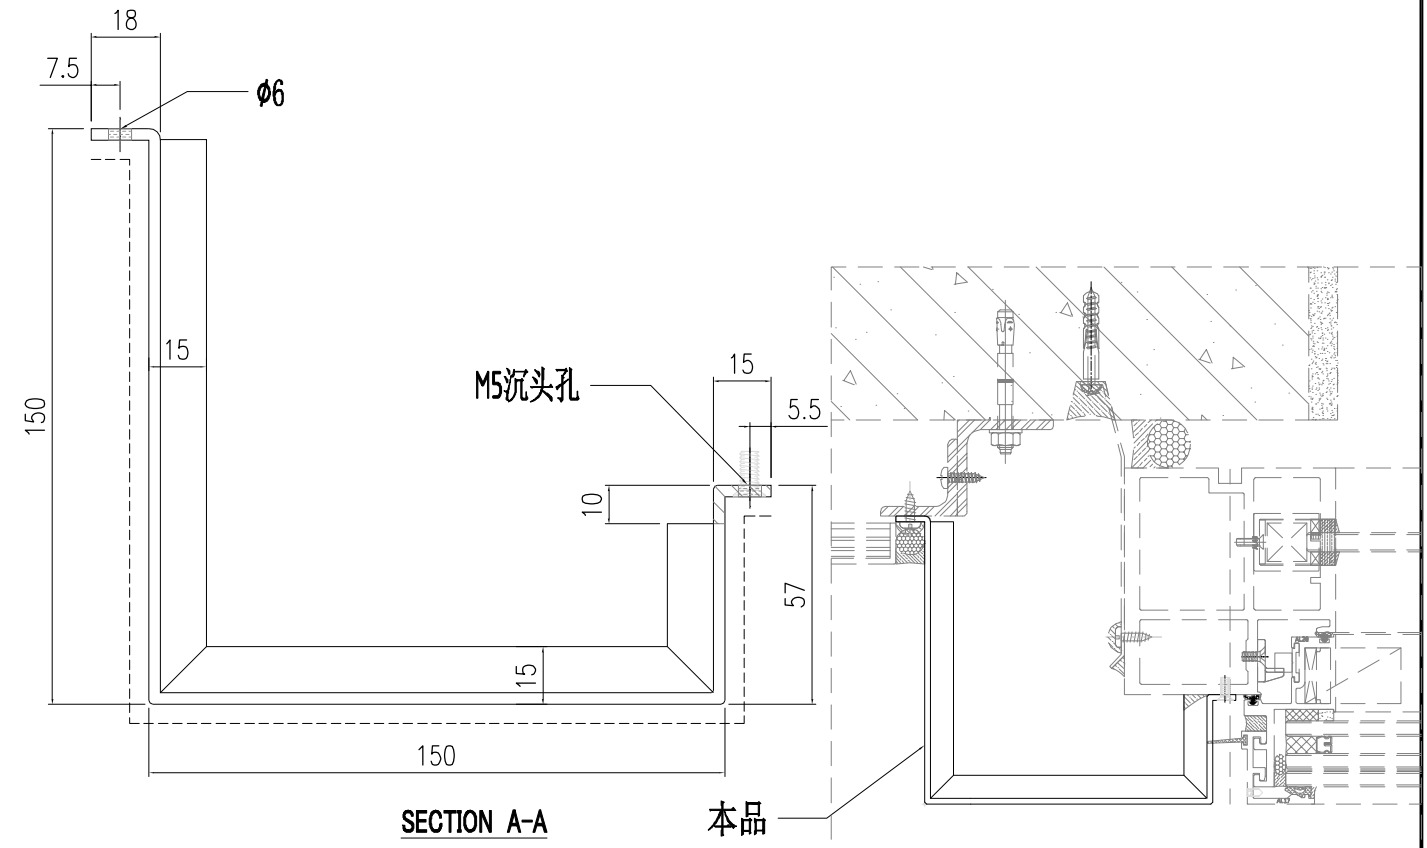


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-729
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

顶部

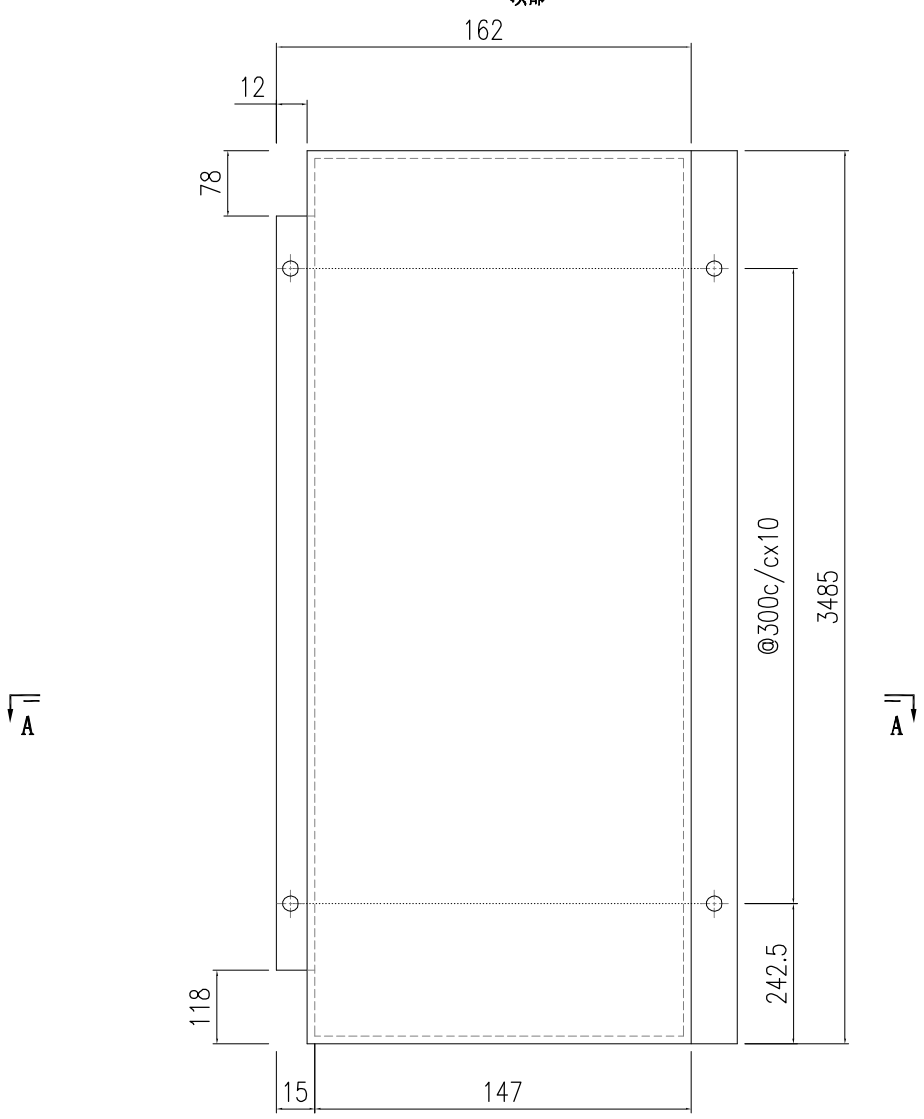

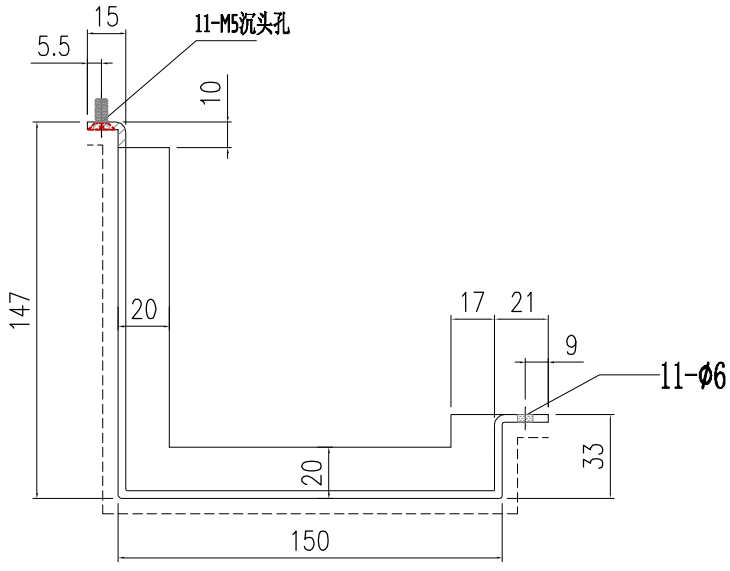



SECTION A-A

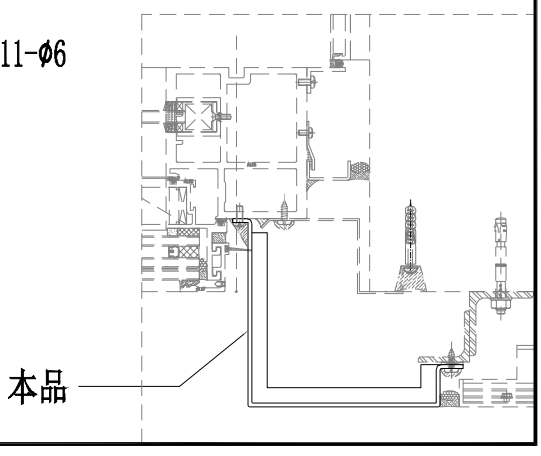


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-730	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

顶部

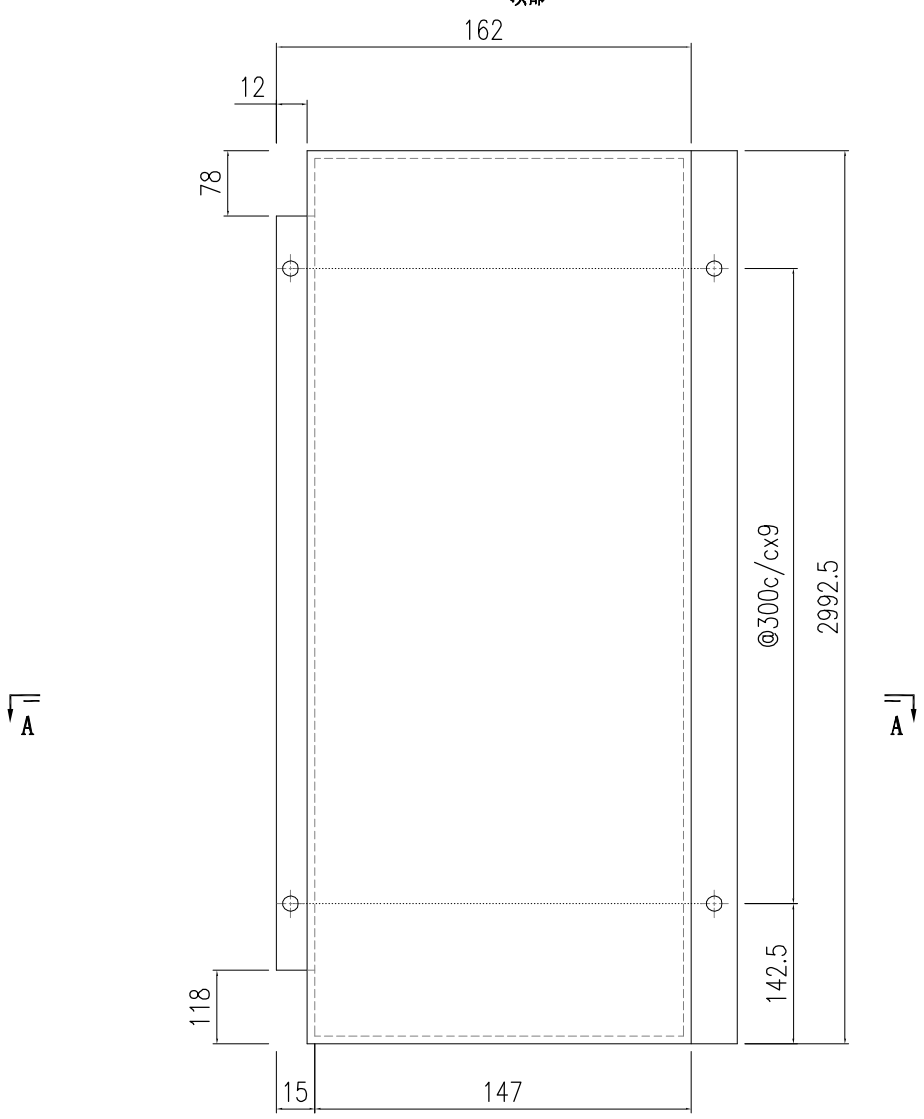

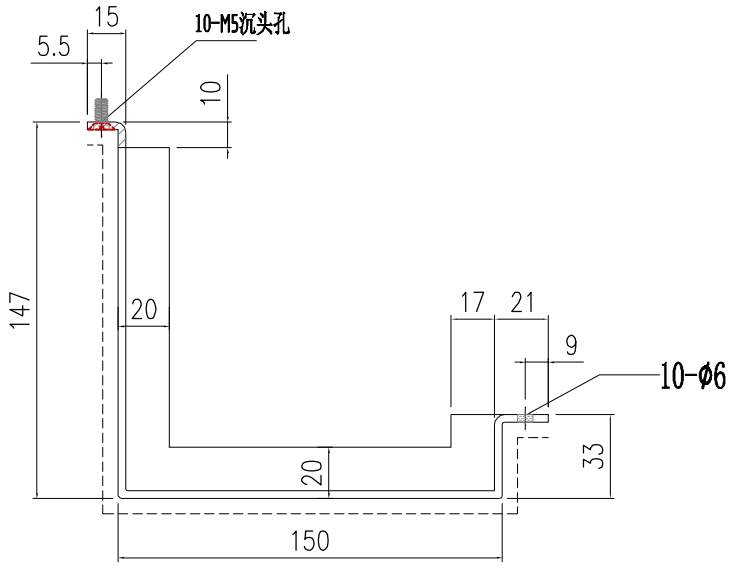



SECTION A-A

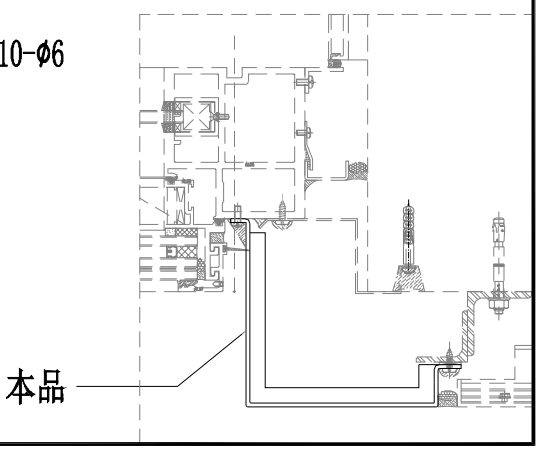


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-731
修改	A	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

顶部

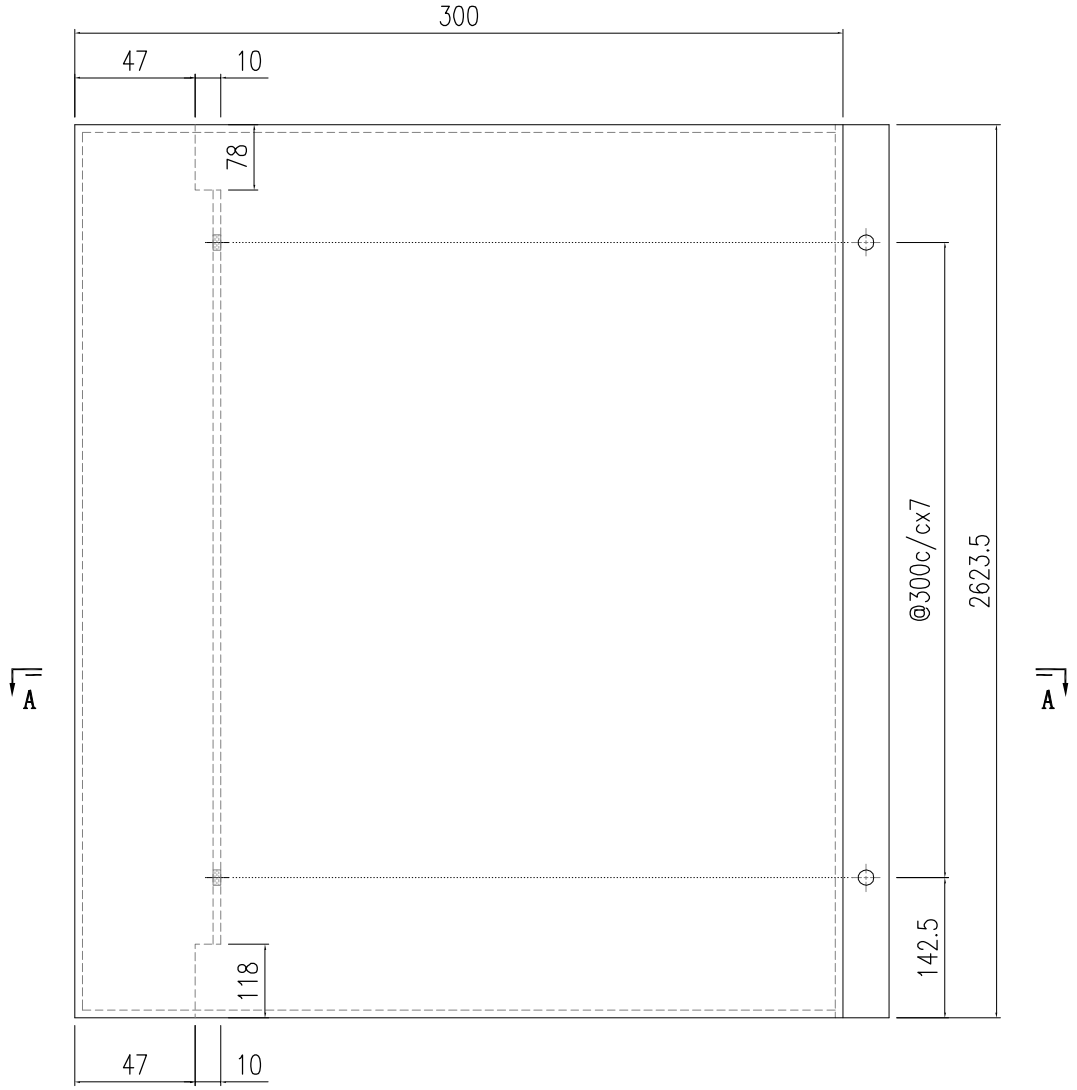

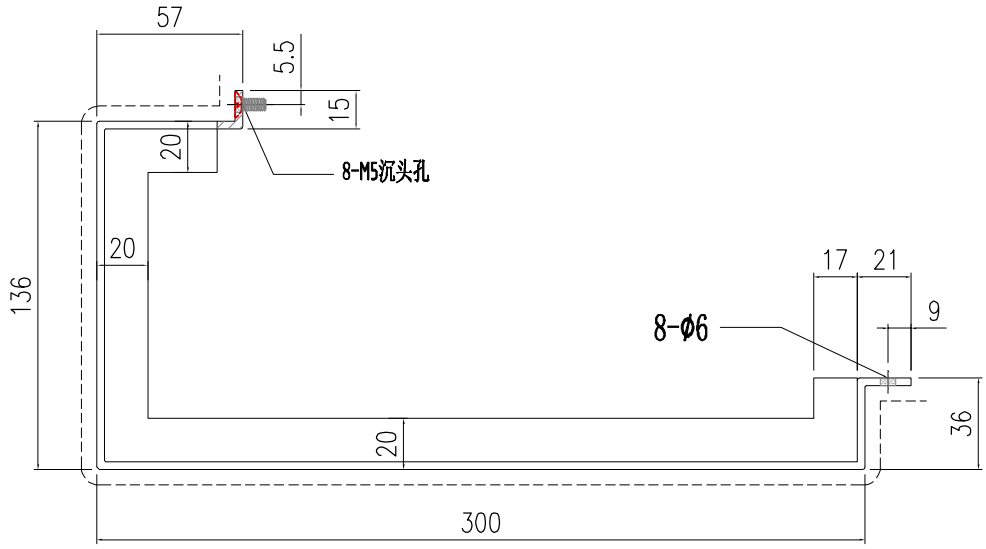



SECTION A-A

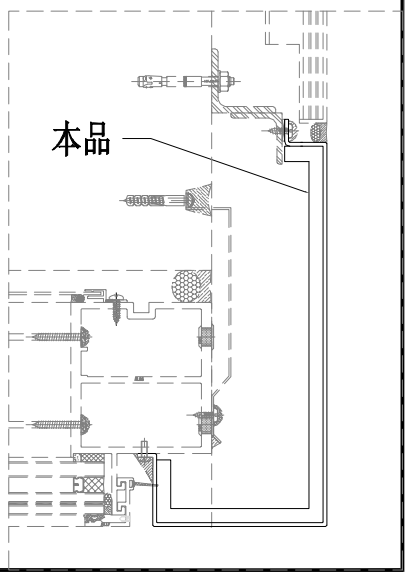


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-744		
修改	A	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1		
日期	9.21	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

顶部

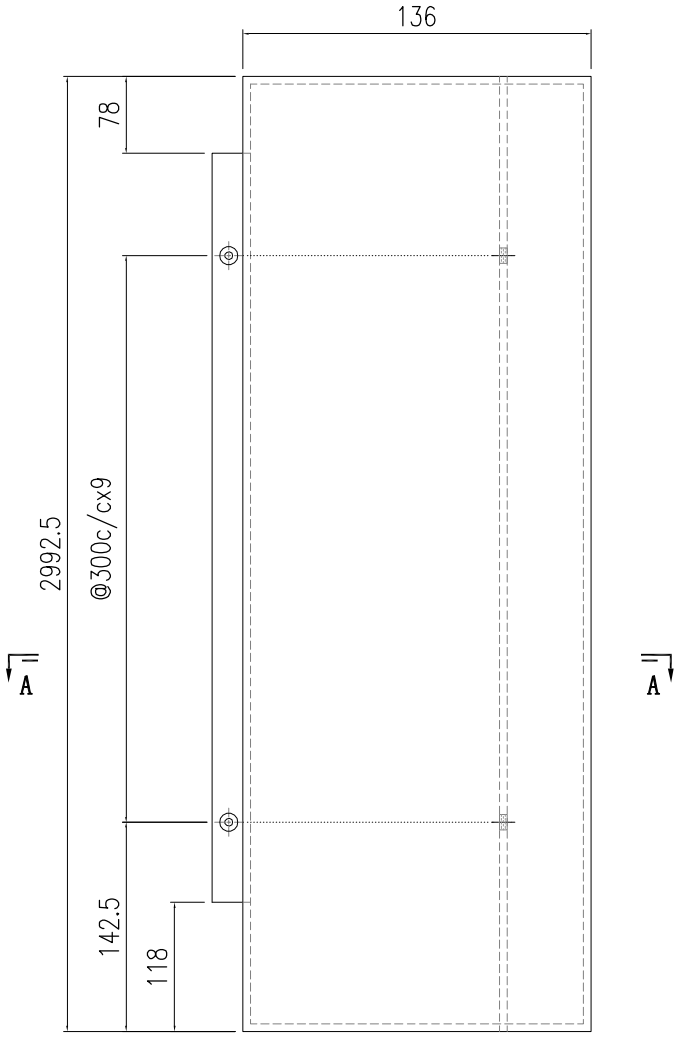


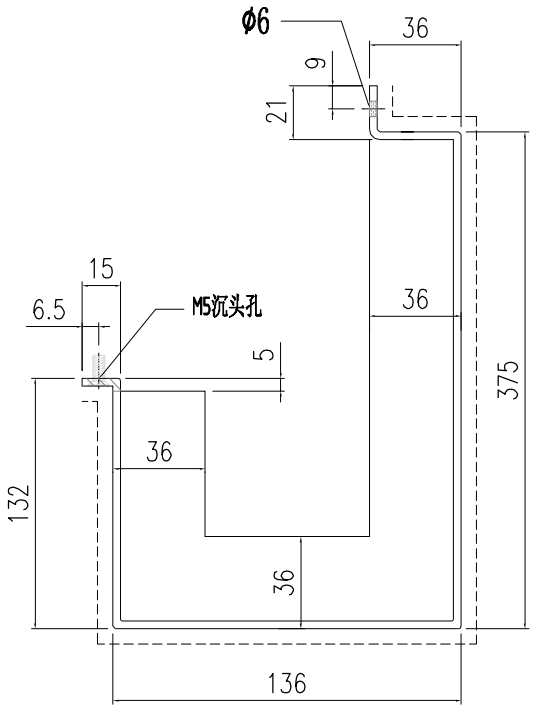


SECTION A-A

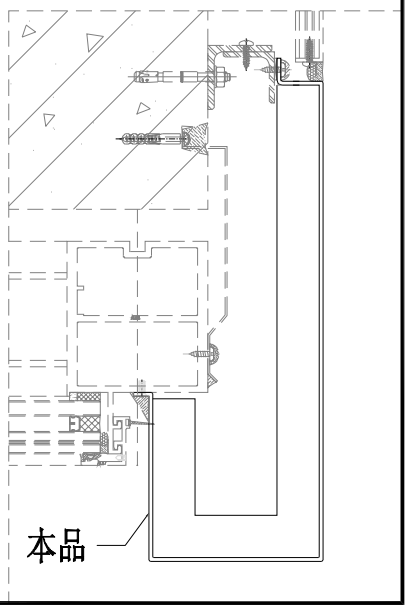


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-801	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 鋁板	批准	林仁安 20221210	單件重量	-	(KG)

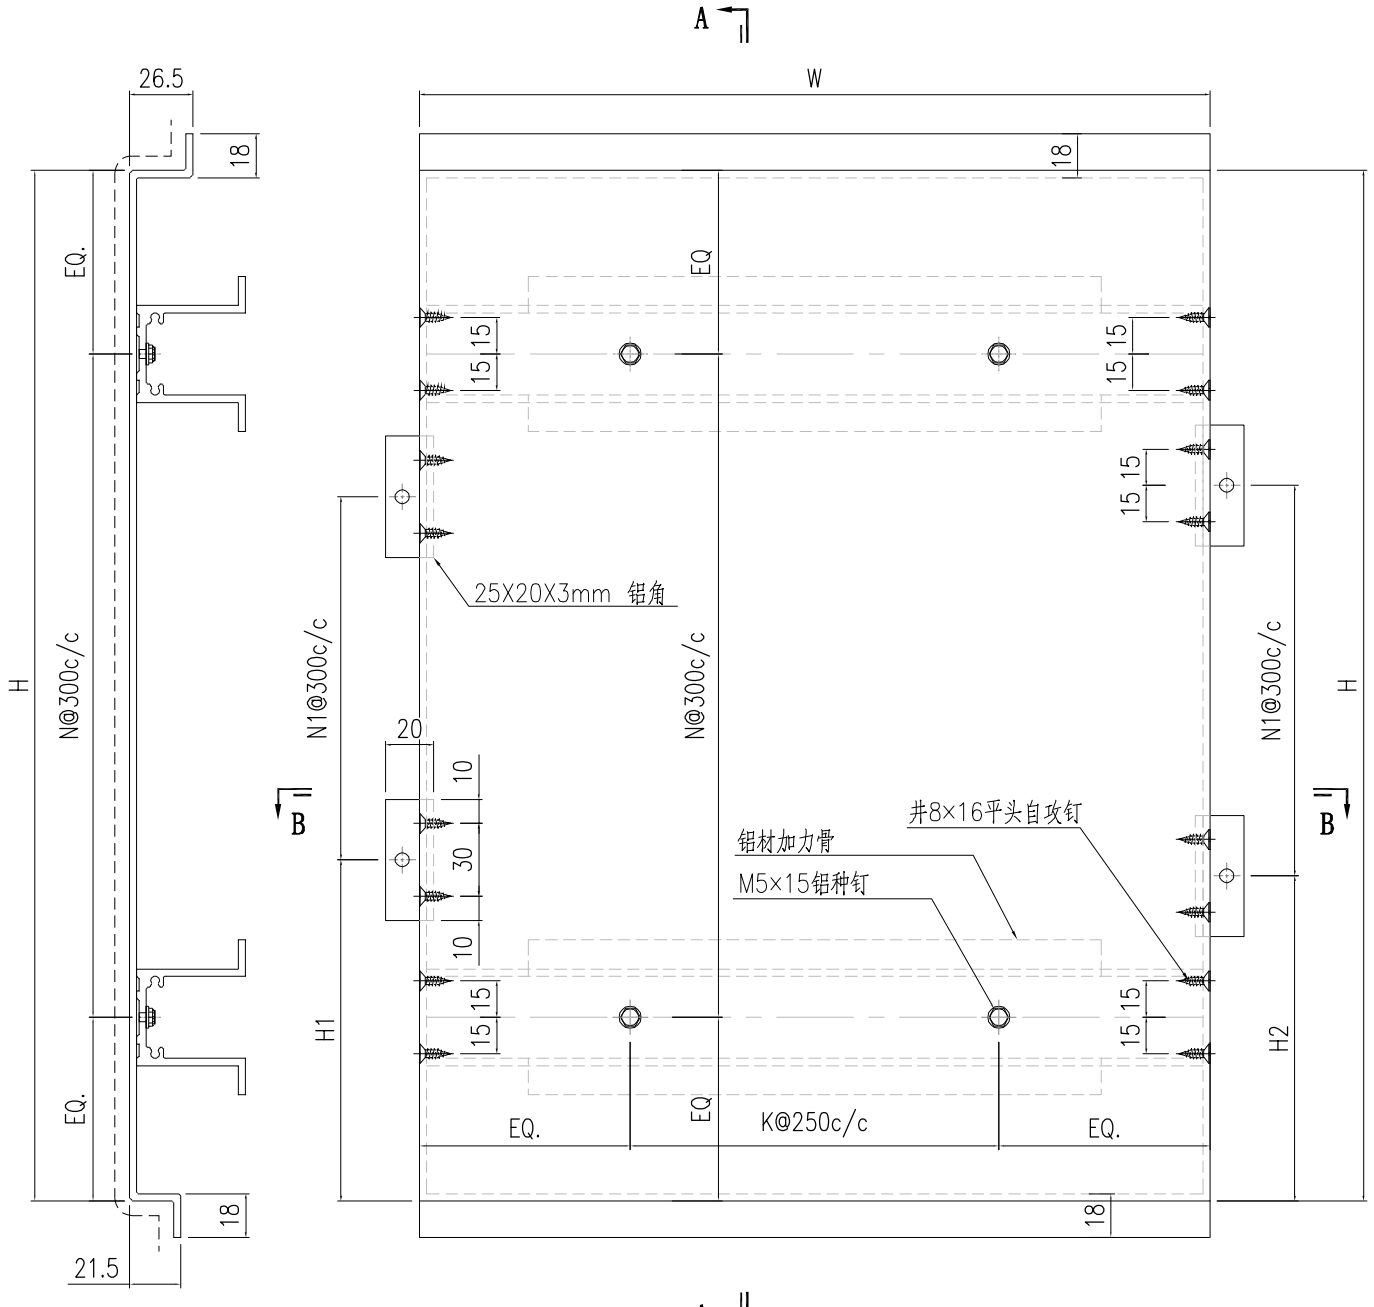

SECTION A-A

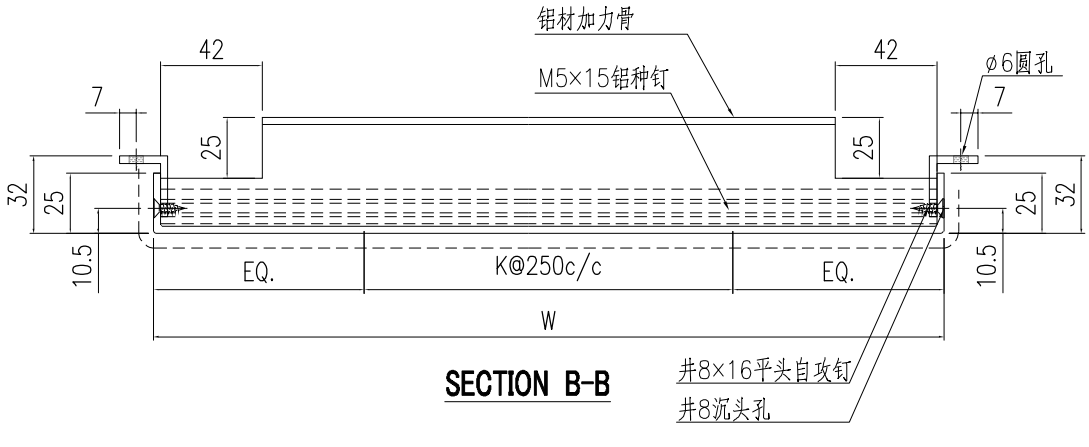

SECTION B-B




铝角码仔孔位示意

铝板长宽数据見AC-801a


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-801a	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	鋁板加工圖	復核	練松文 20221209		數量	-	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

S/N	部件编号	部件数量	W	H	K	N	N1	铝材加力骨	H1	H2
14	AC-801-14	1	827.5	2737.5	3	8	8	X86112-501-10	185	110
13	AC-801-13	1	1242.5	2792.5	4	8	8	X86112-501-9	175	95
12	AC-801-12	1	950	2737.5	3	8	8	X86112-501-6	185	110
11	AC-801-11	1	947.5	2737.5	3	8	8	X86112-501-7	185	110
10	AC-801-10	1	1102.5	2737.5	3	8	8	X86112-501-8	110	185
9	AC-801-9	1	1102.5	2737.5	3	8	8	X86112-501-8	185	110
8	AC-801-8	1	947.5	2737.5	3	8	8	X86112-501-7	110	185
7	AC-801-7	1	950	2737.5	3	8	8	X86112-501-6	110	185
6	AC-801-6	1	975	2792.5	3	8	8	X86112-501-5	95	175
5	AC-801-5	1	602	2508	2	8	7	X86112-501-4	110	175
4	AC-801-4	1	727	965	2	2	2	X86112-501-3	50	250
3	AC-801-3	2	727	2505	2	8	7	X86112-501-3	110	175
2	AC-801-2	1	730	2508	2	8	7	X86112-501-2	110	175
1	AC-801-1	1	760	2508	2	8	7	X86112-501-1	110	175


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-802
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

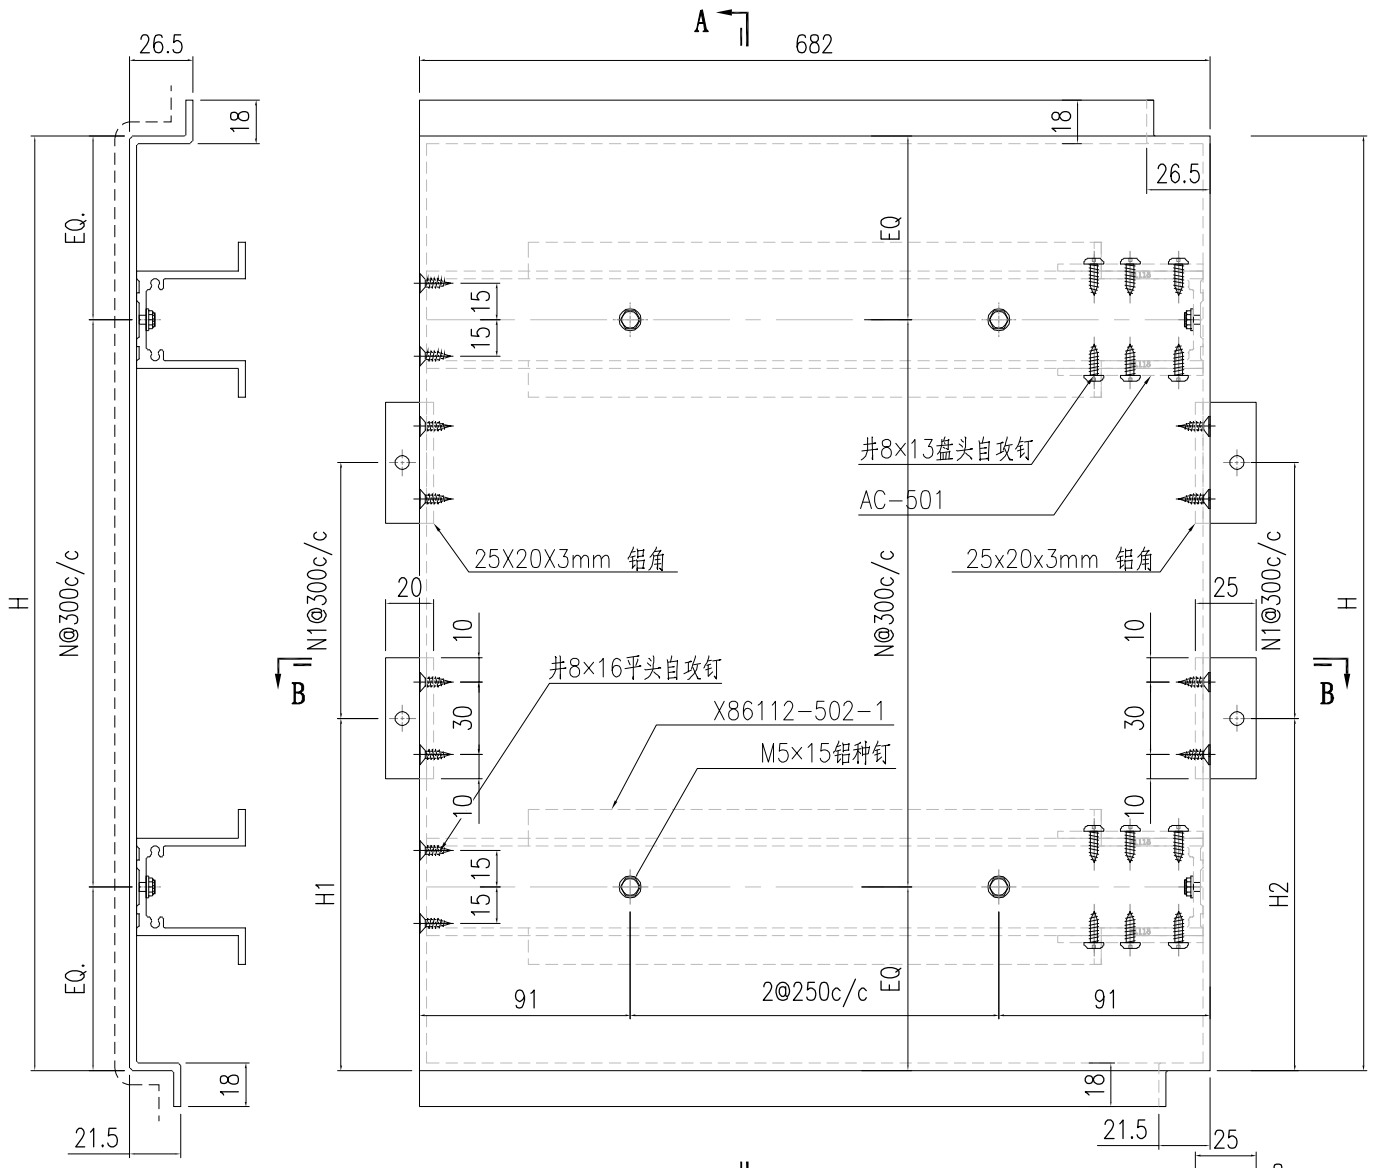

SECTION A-A

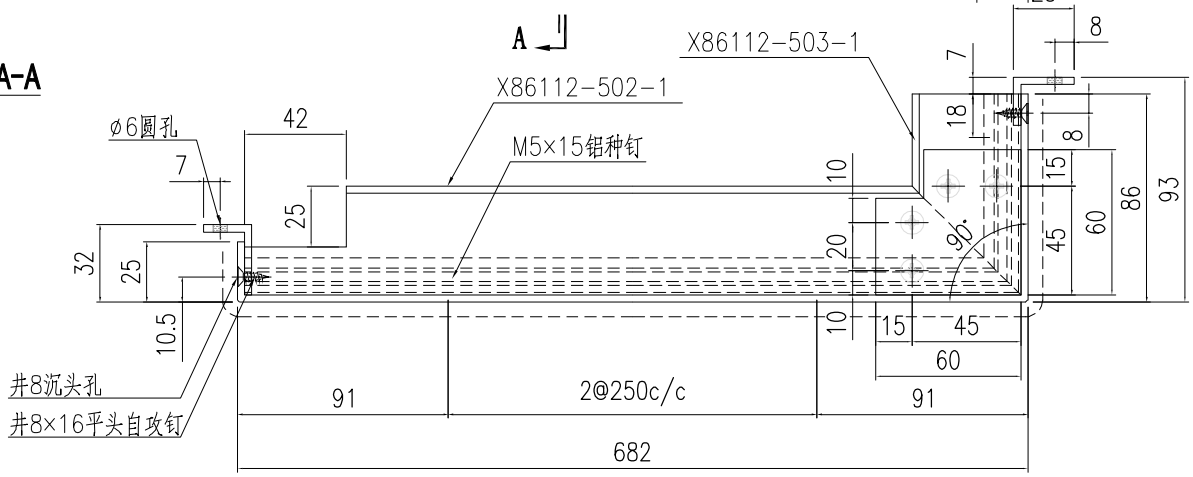


SECTION B-B




铝角码仔孔位示意

2	AC-802-2	1	965	2	2	50	250
1	AC-802-1	2	2505	8	7	110	175
S/N	部件编号	部件数量	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-803
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

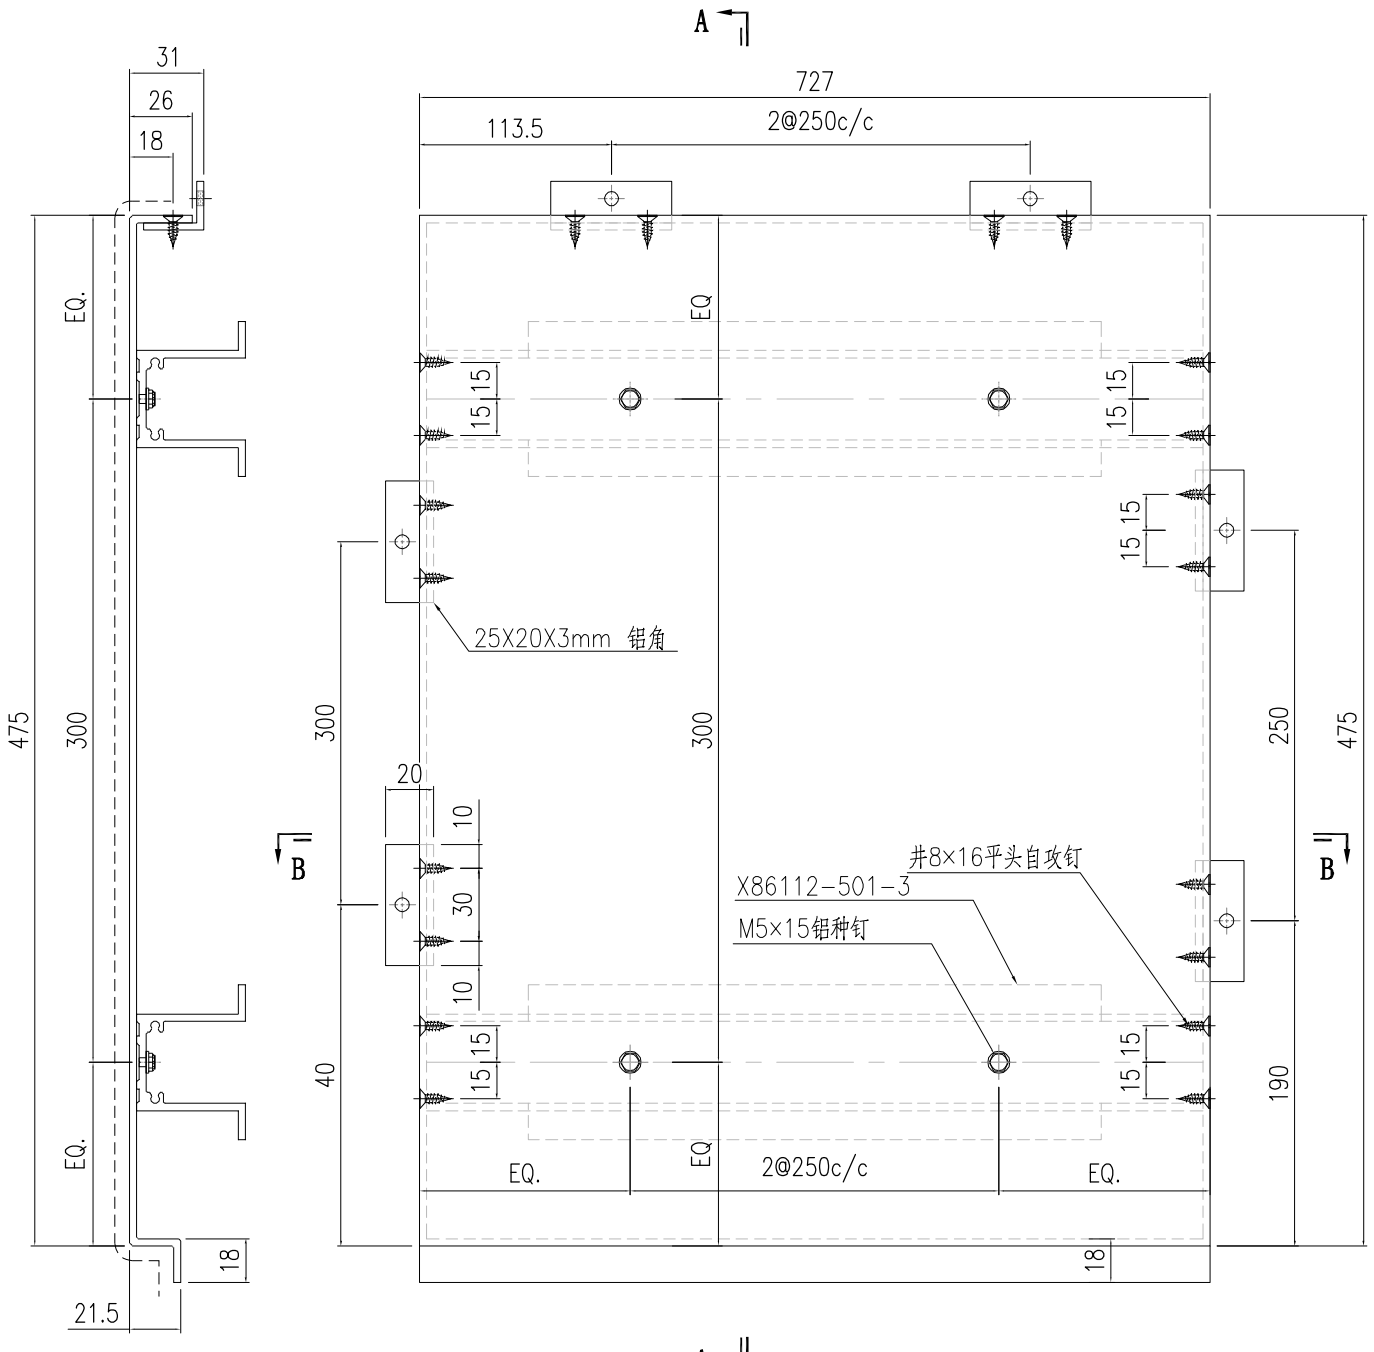

SECTION A-A

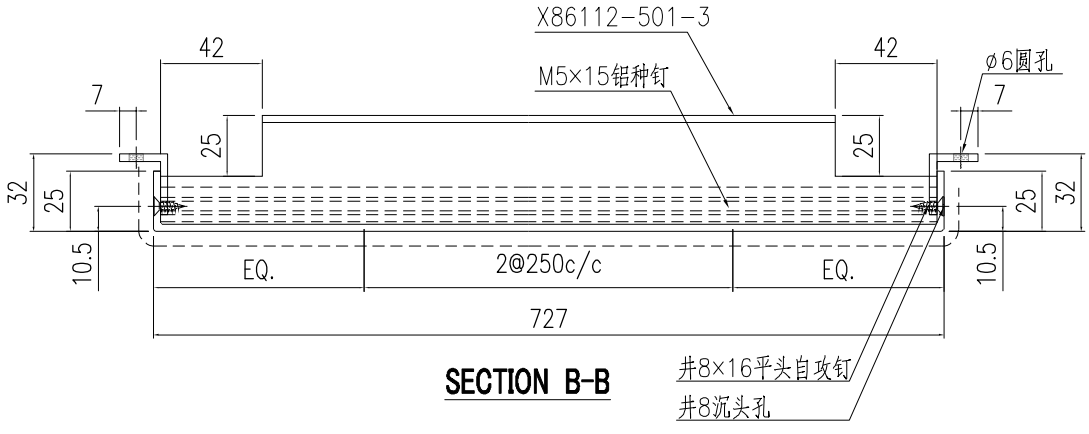



SECTION B-B




铝角码仔孔位示意

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-804
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

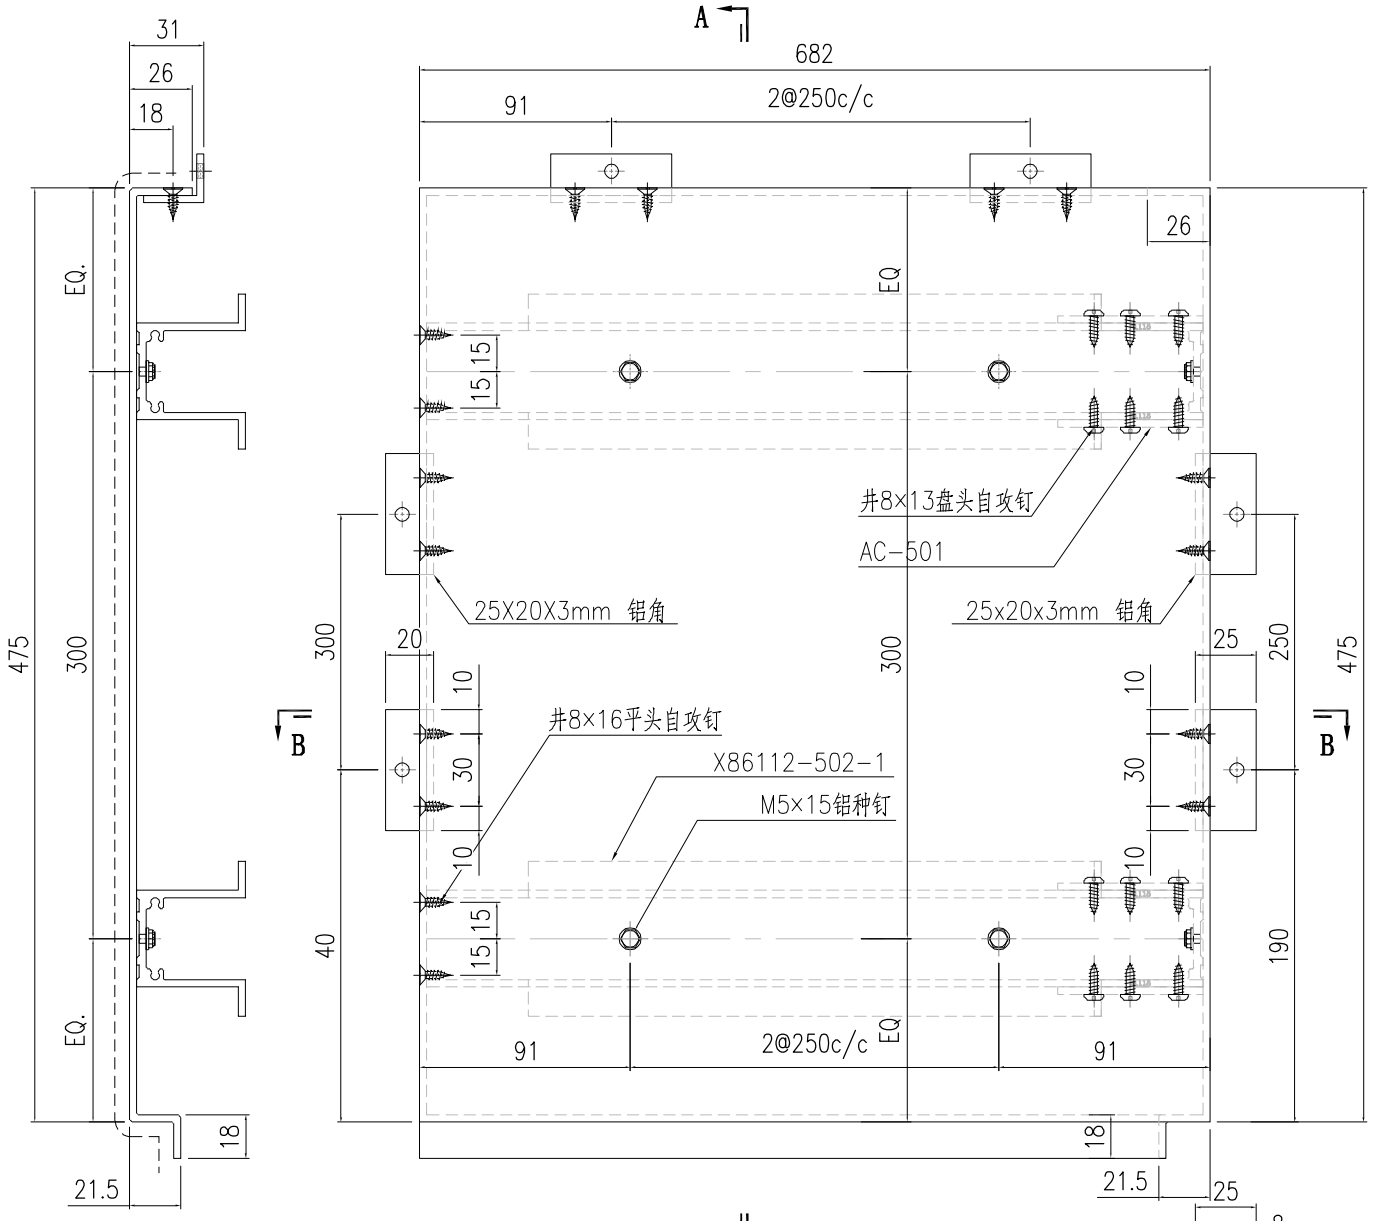

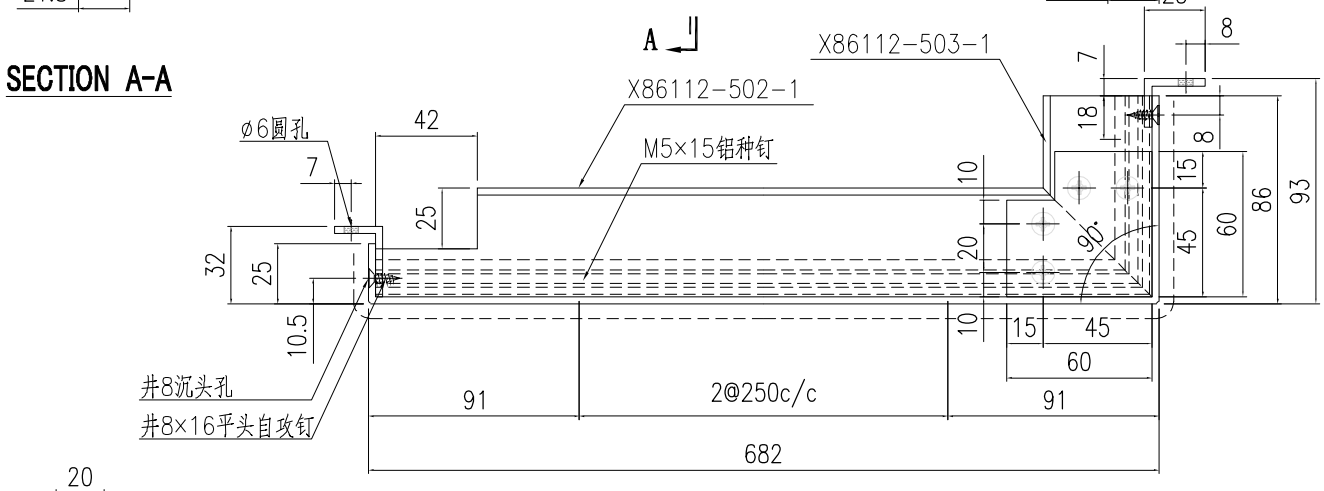


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-805
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

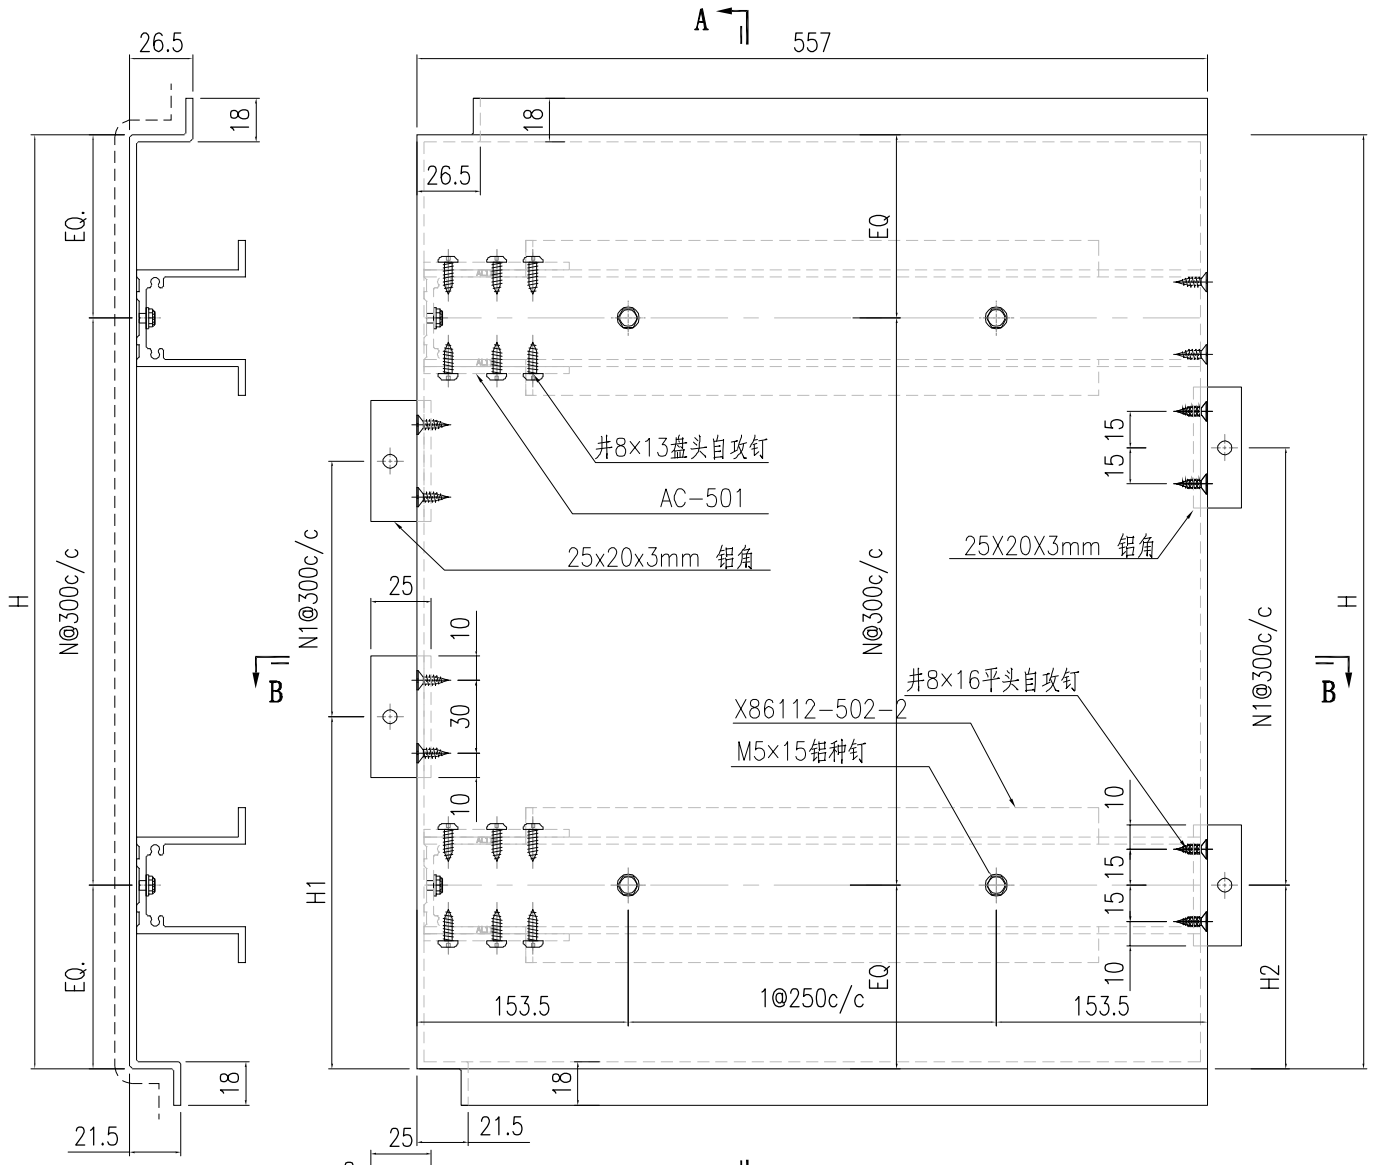

SECTION A-A

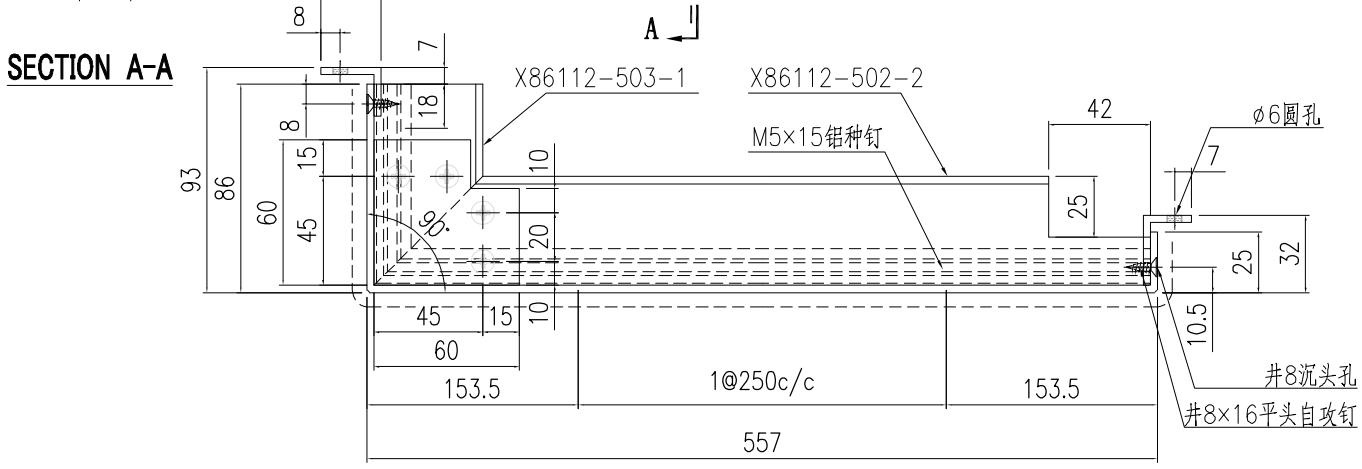


SECTION B-B




铝角码仔孔位示意

1	AC-805-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-806
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

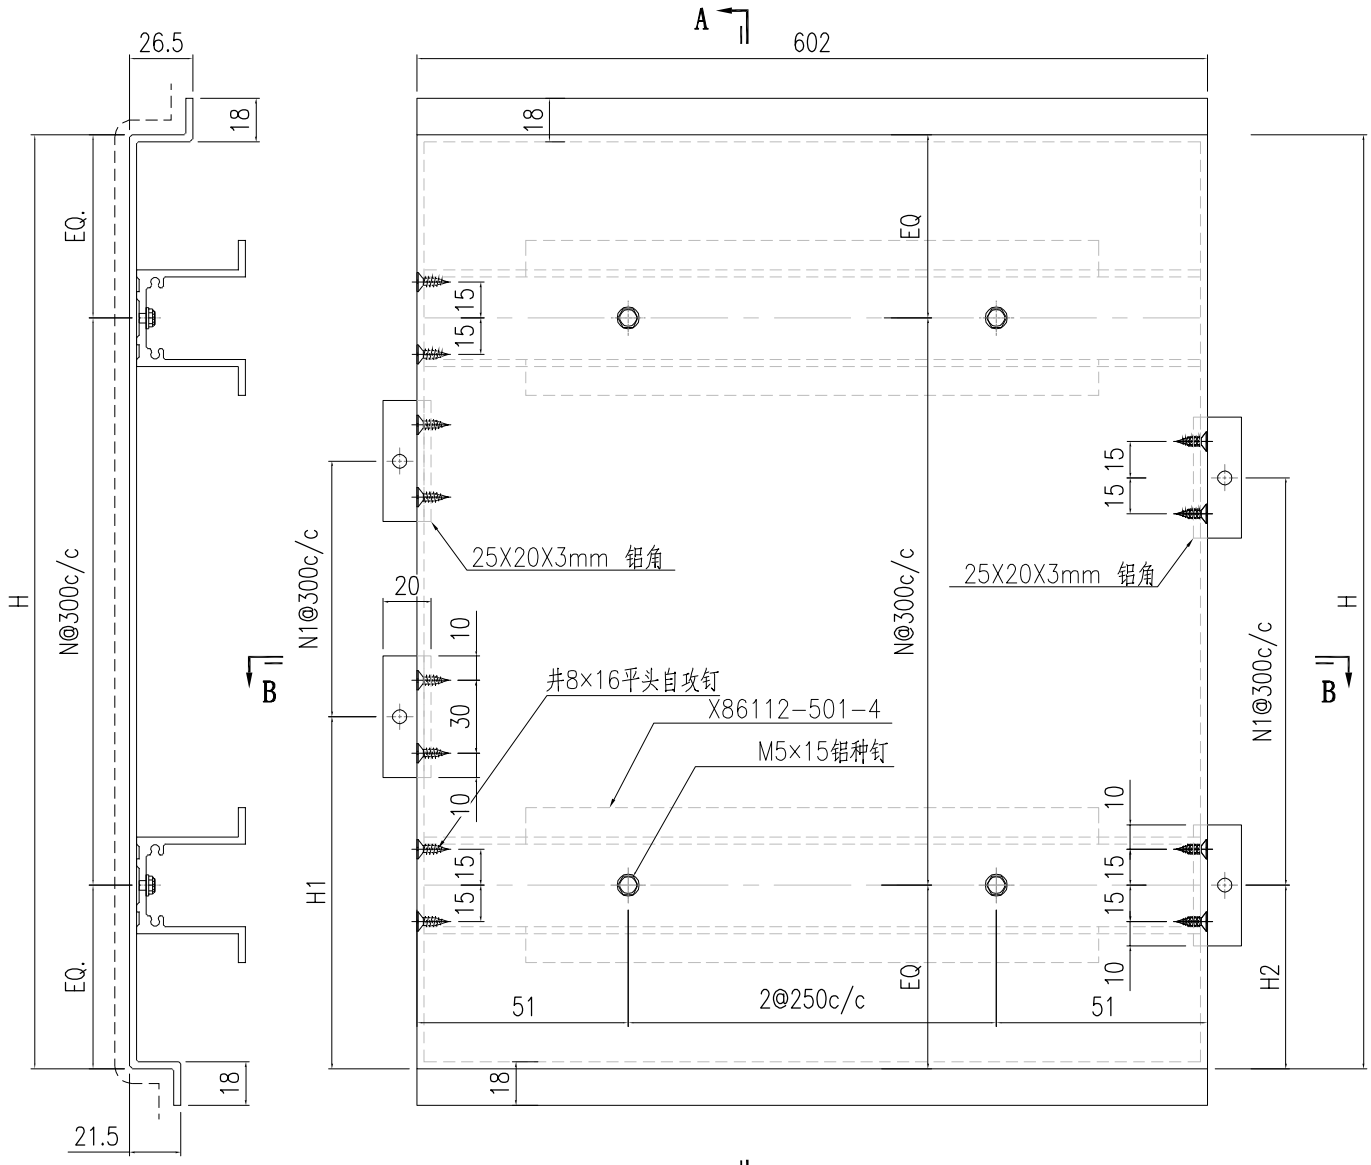

SECTION A-A

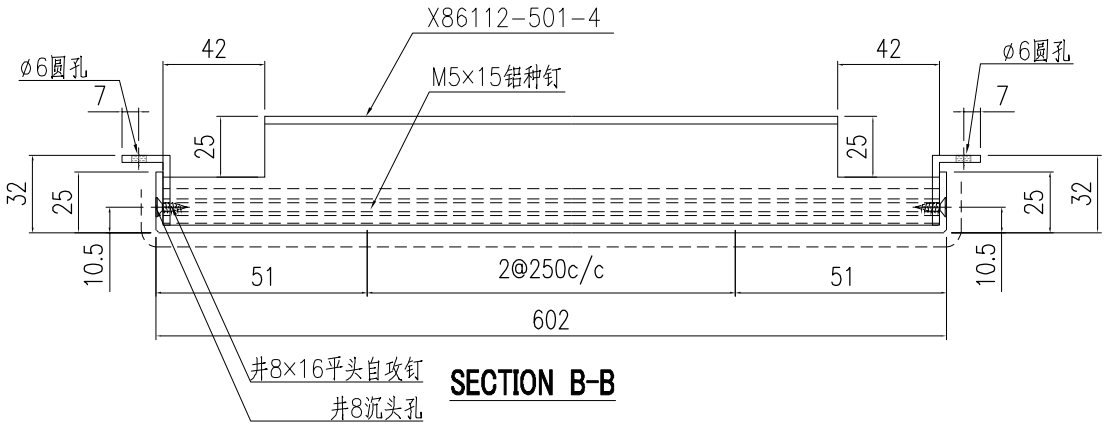


SECTION B-B




铝角码仔孔位示意

1	AC-806-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-807
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

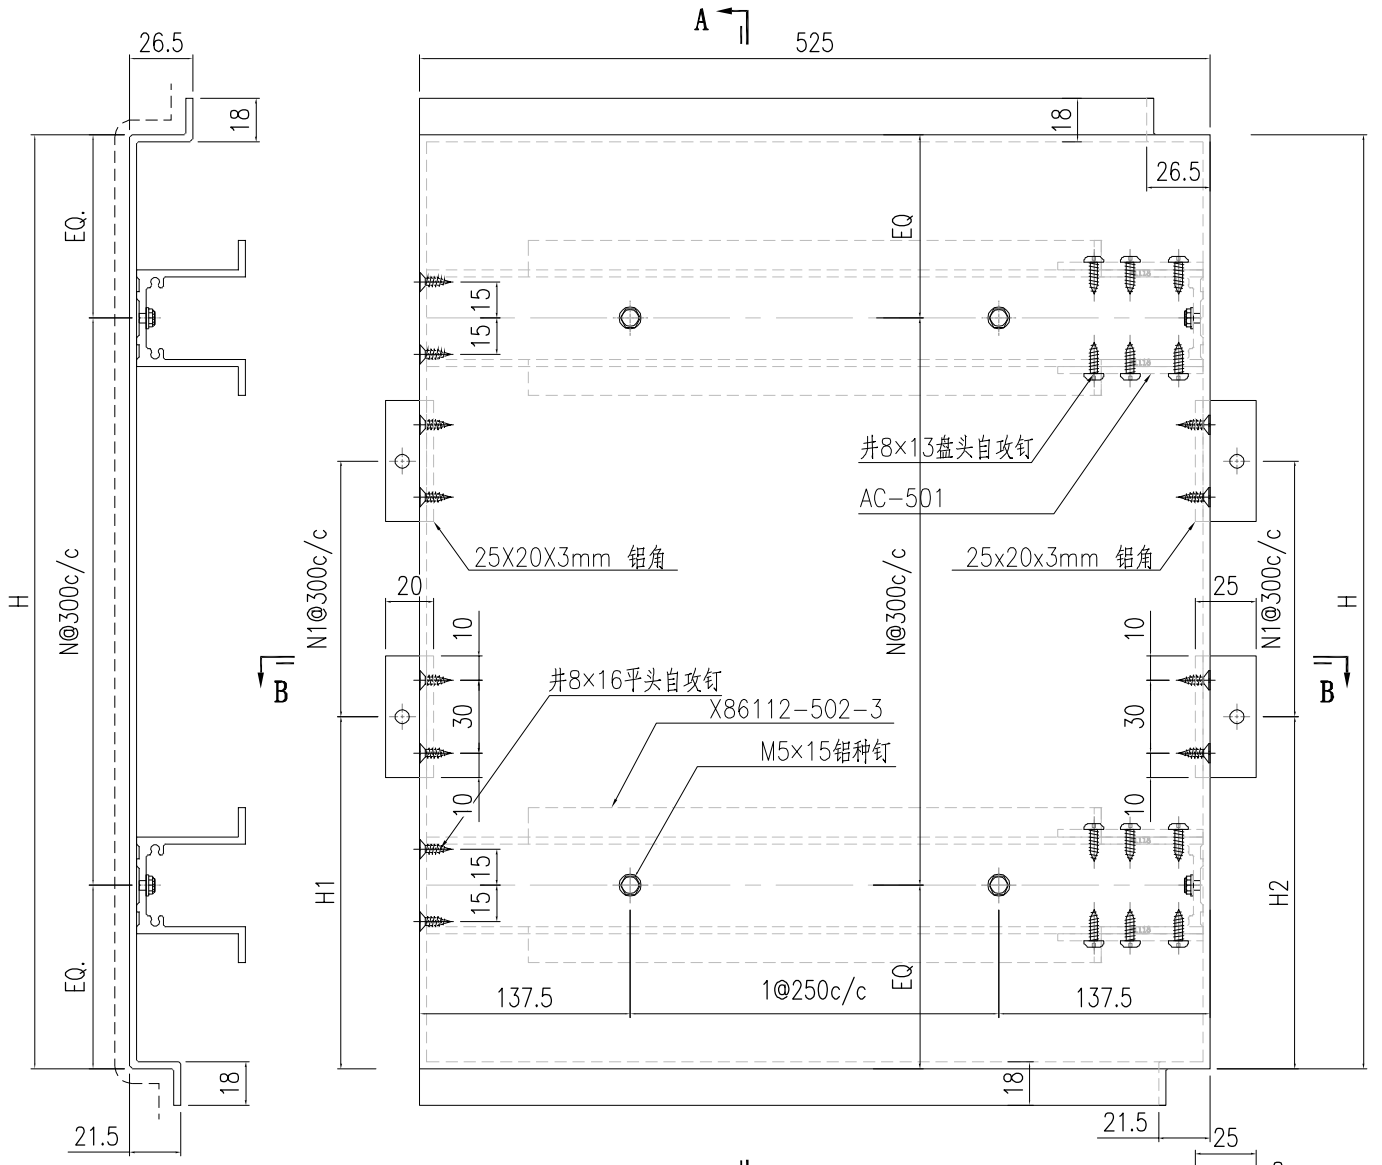

SECTION A-A

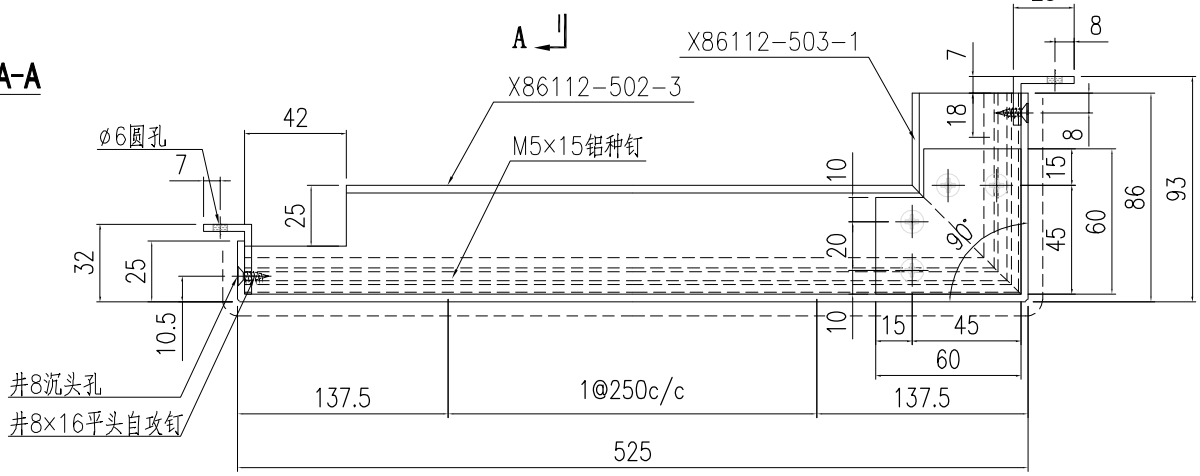


SECTION B-B




铝角码仔孔位示意

1	AC-807-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-808
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

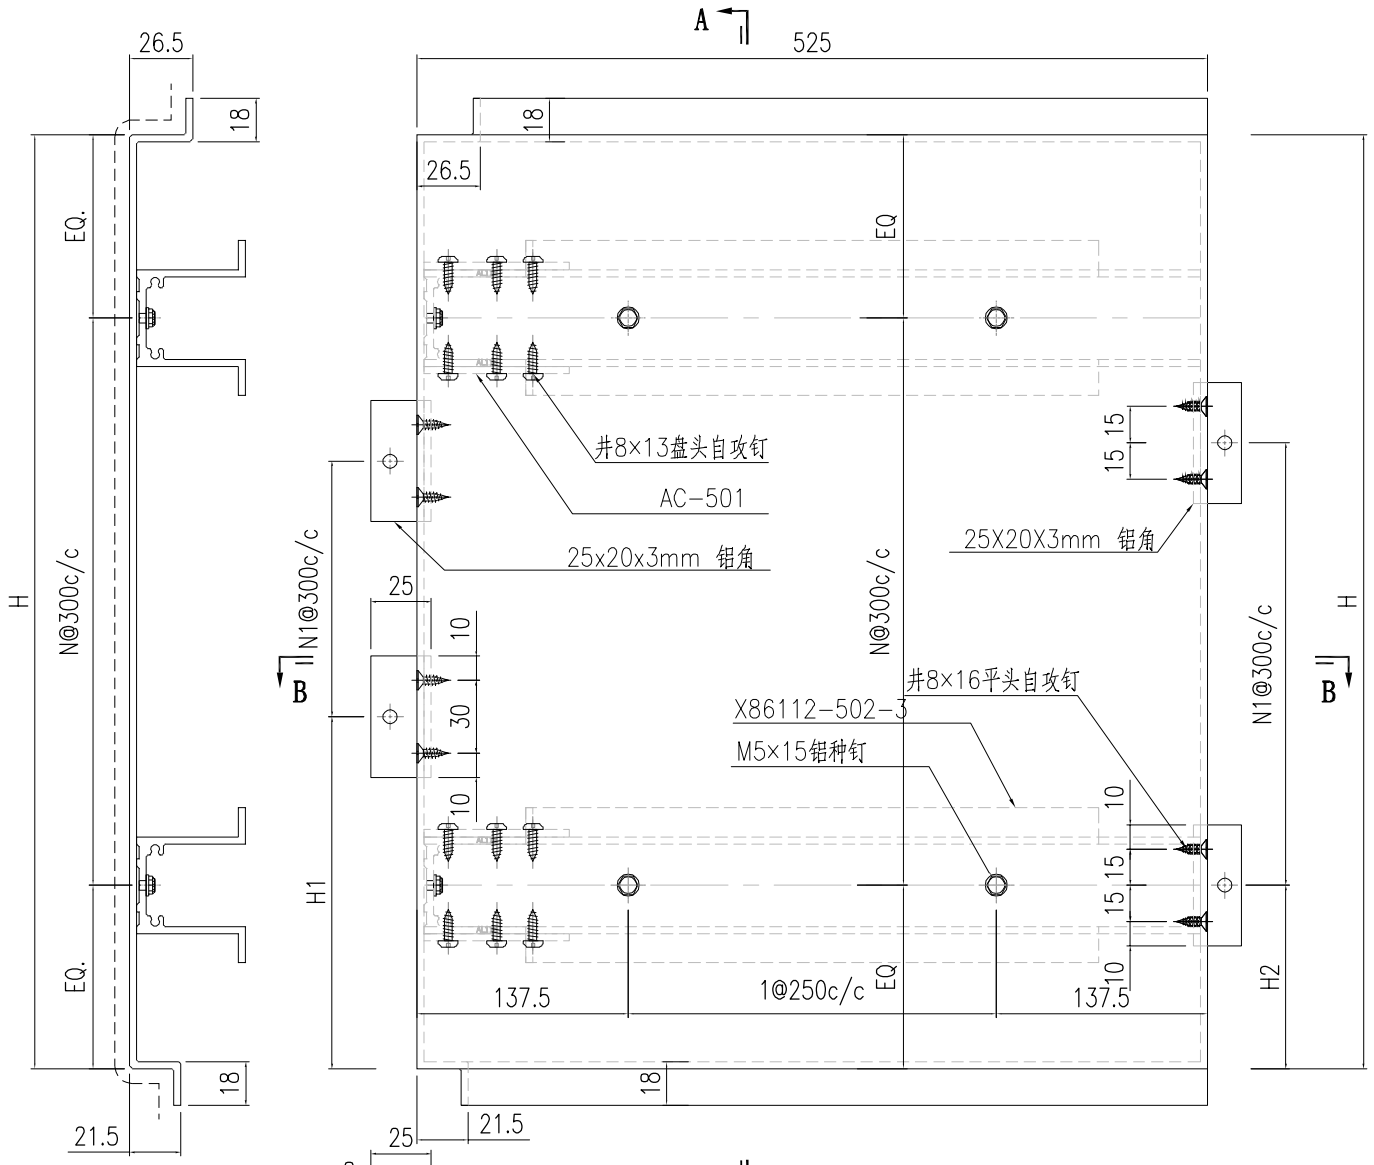

SECTION A-A

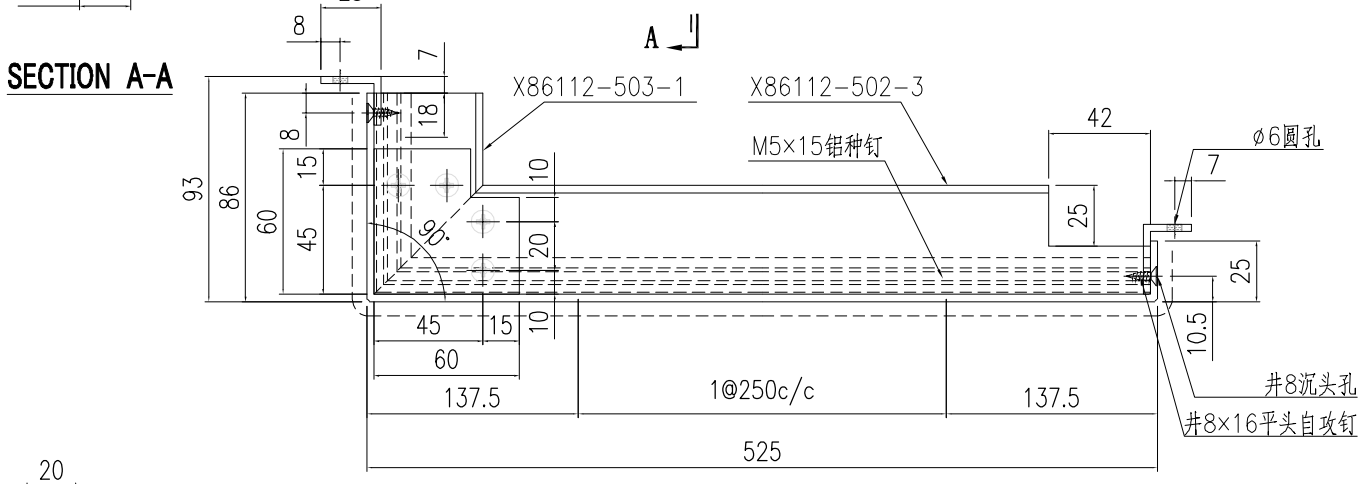


SECTION B-B




铝角码仔孔位示意

1	AC-808-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-809
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

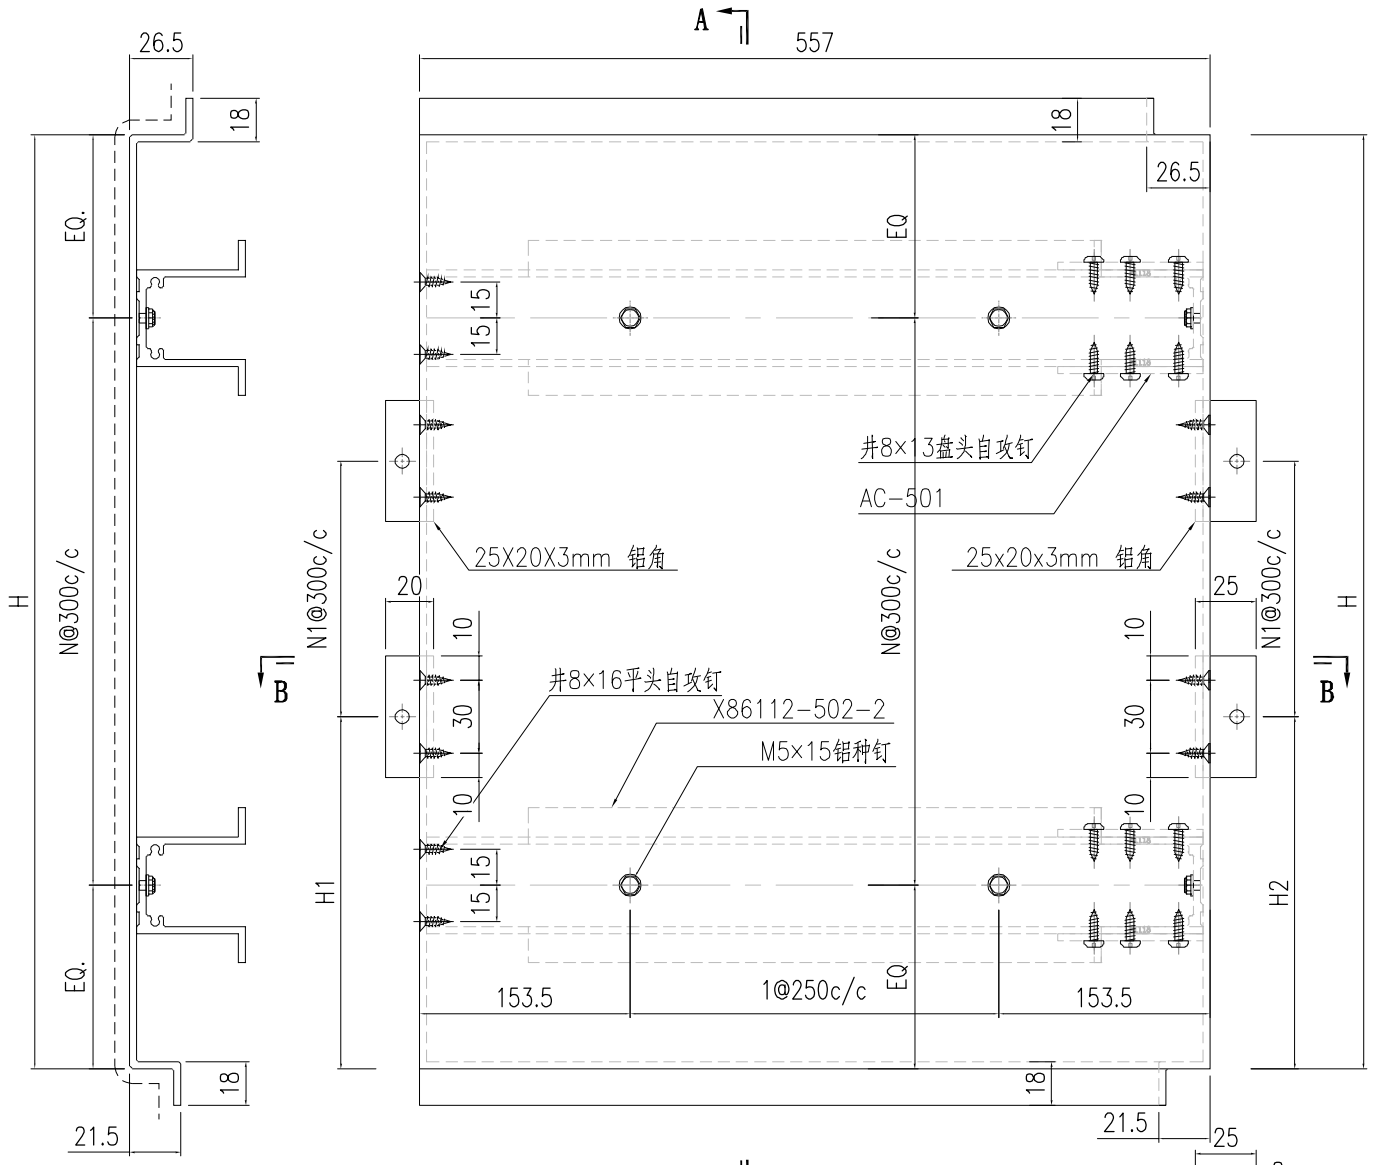

SECTION A-A

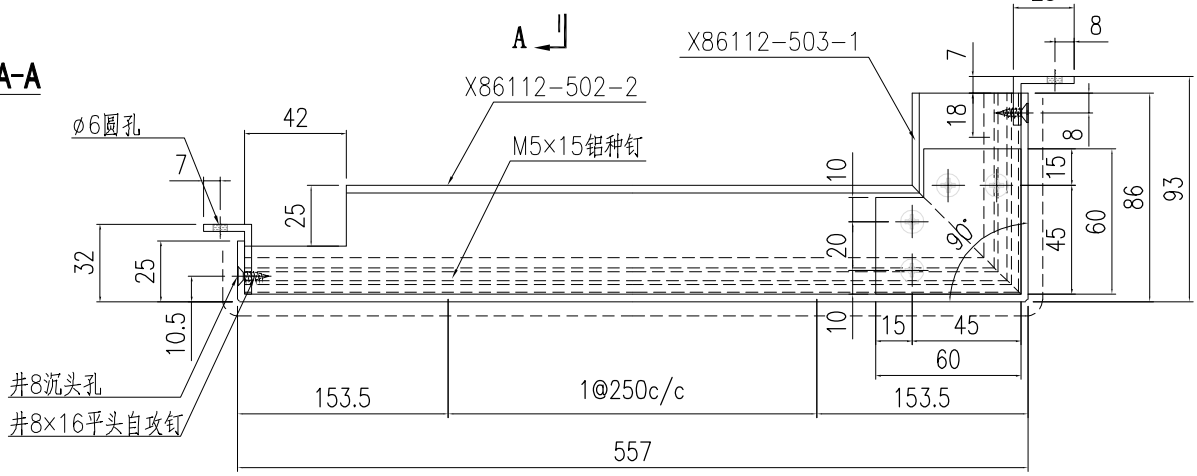


SECTION B-B




铝角码仔孔位示意

1	AC-809-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-810		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

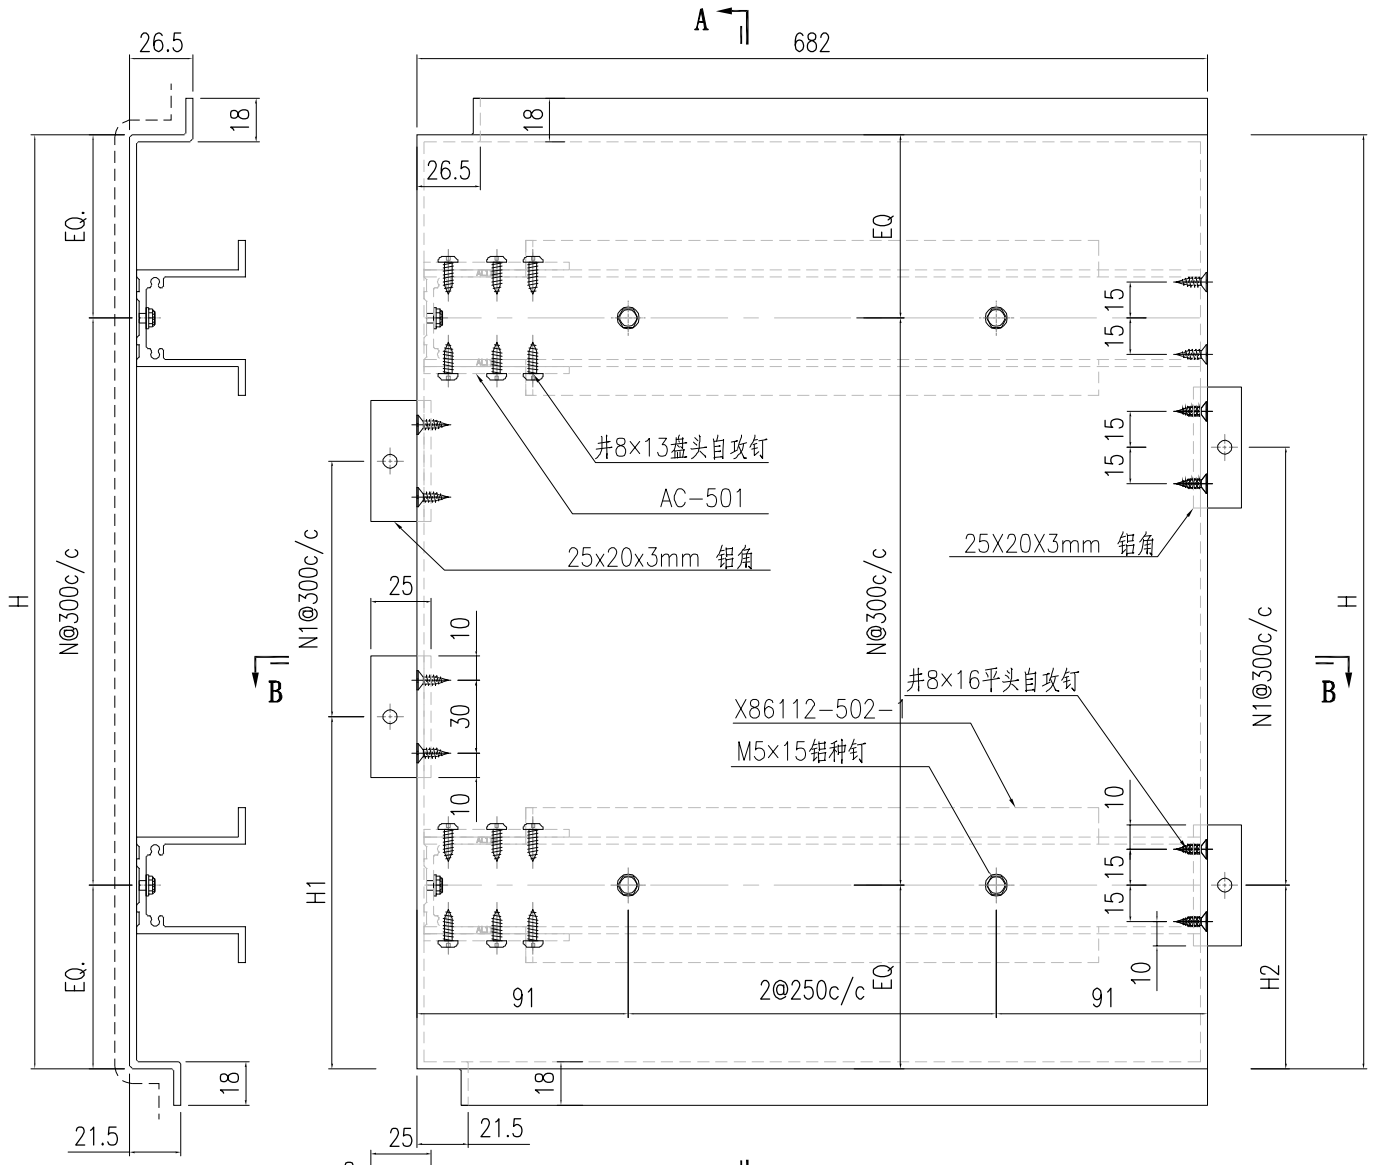

SECTION A-A

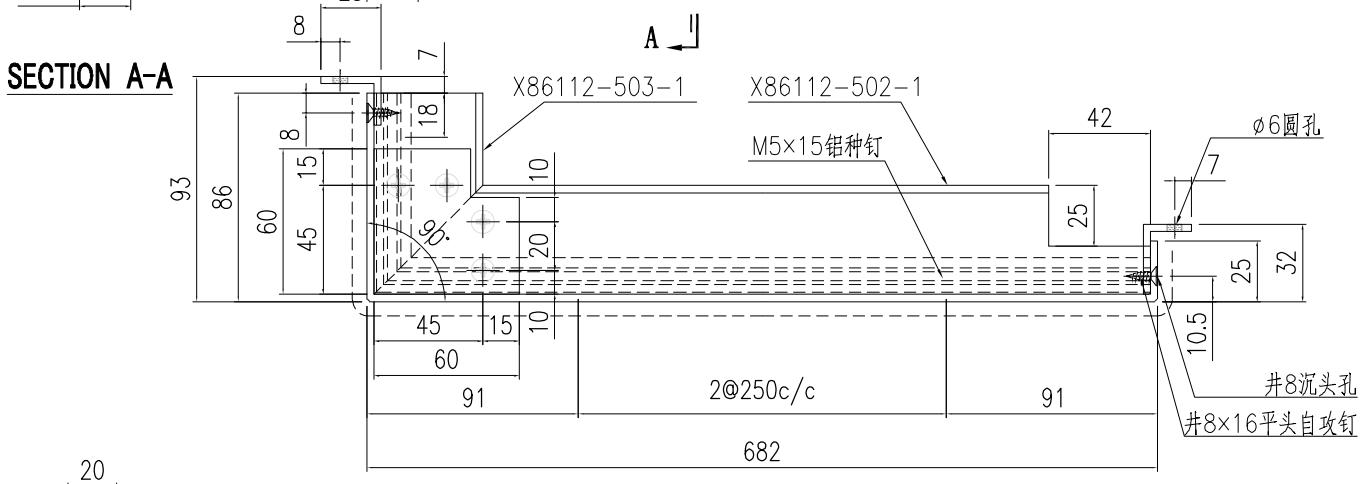


SECTION B-B




铝角码仔孔位示意

2	AC-810-2	1	965	2	2	50	250
1	AC-810-1	2	2505	8	7	110	175
S/N	部件编号	部件数量	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-811
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

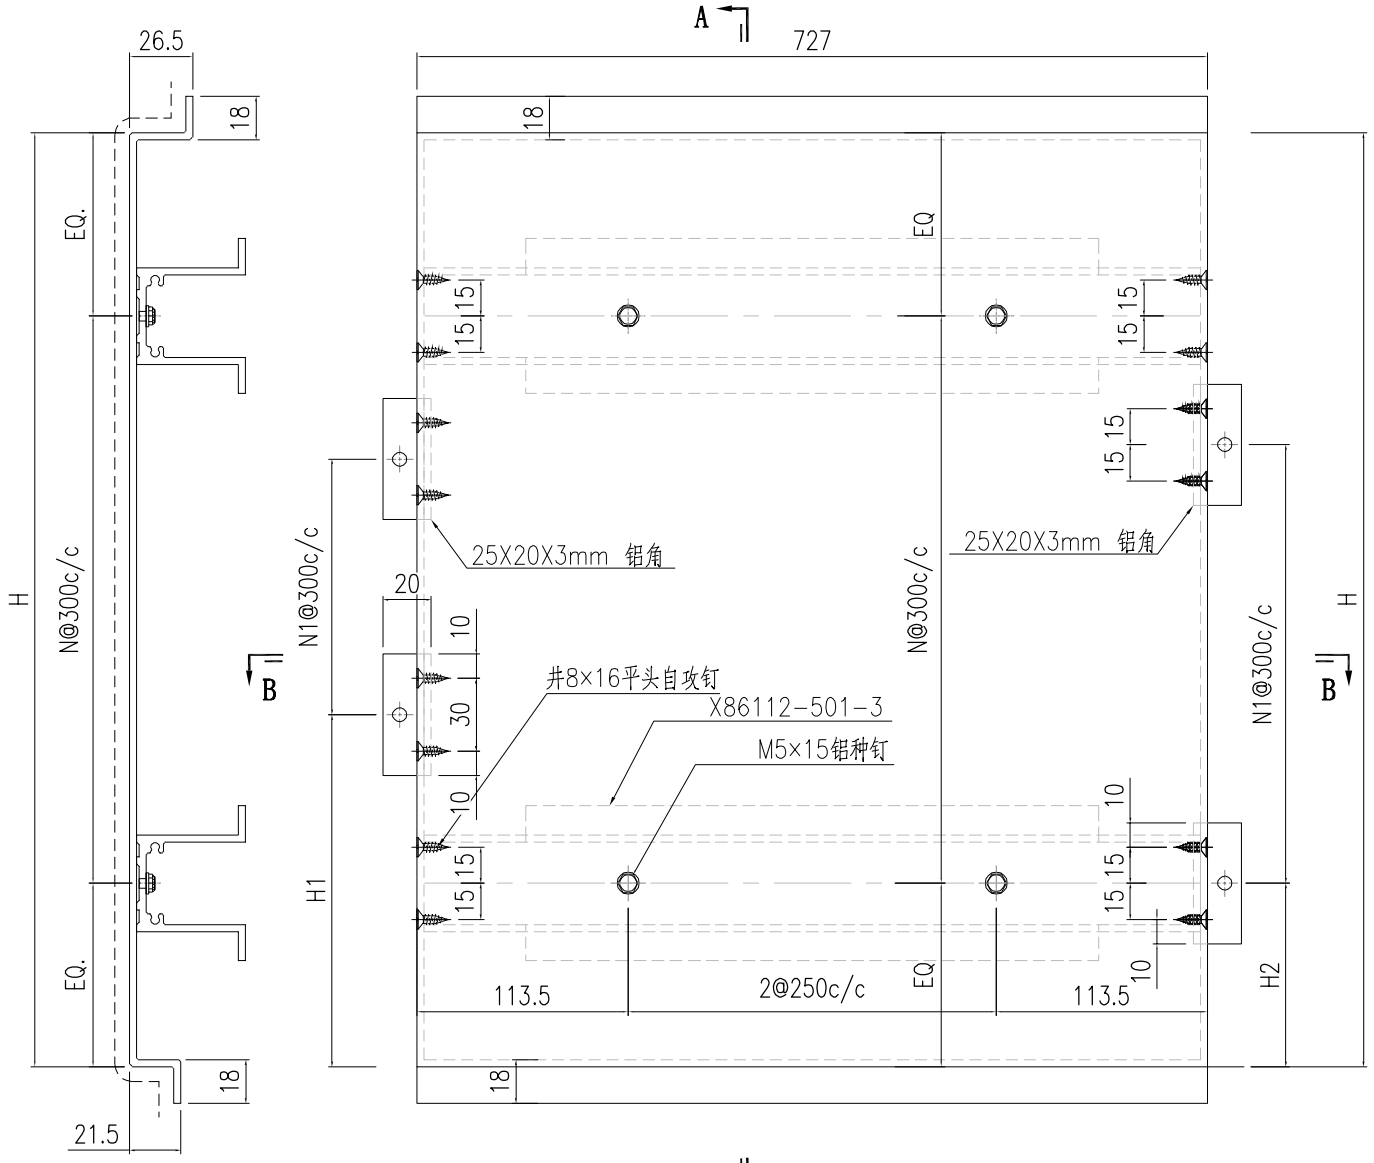

SECTION A-A

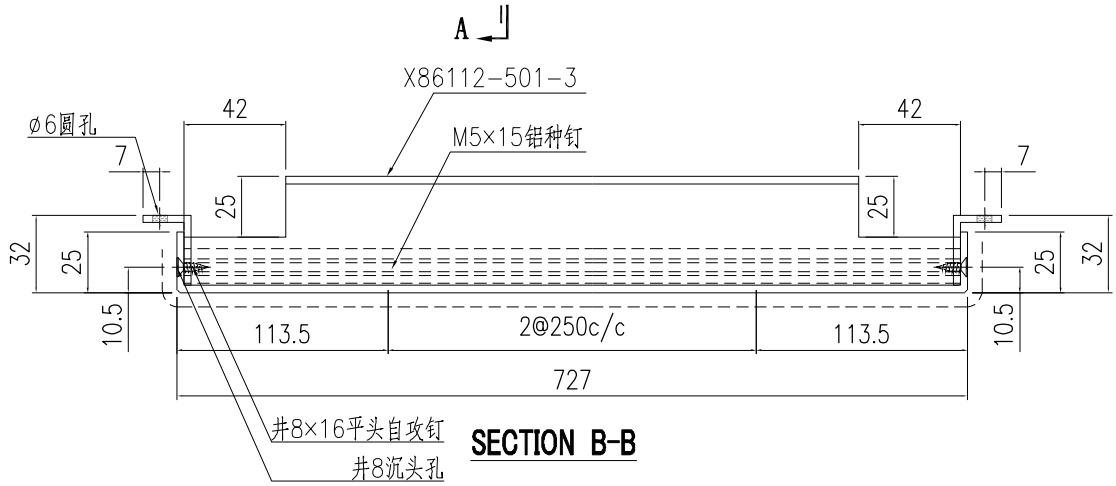


SECTION B-B




铝角码仔孔位示意


S/N	部件编号	部件数量	H	N	N1	H1	H2
2	AC-811-2	1	965	2	2	50	250
1	AC-811-1	2	2505	8	7	110	175

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-812
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

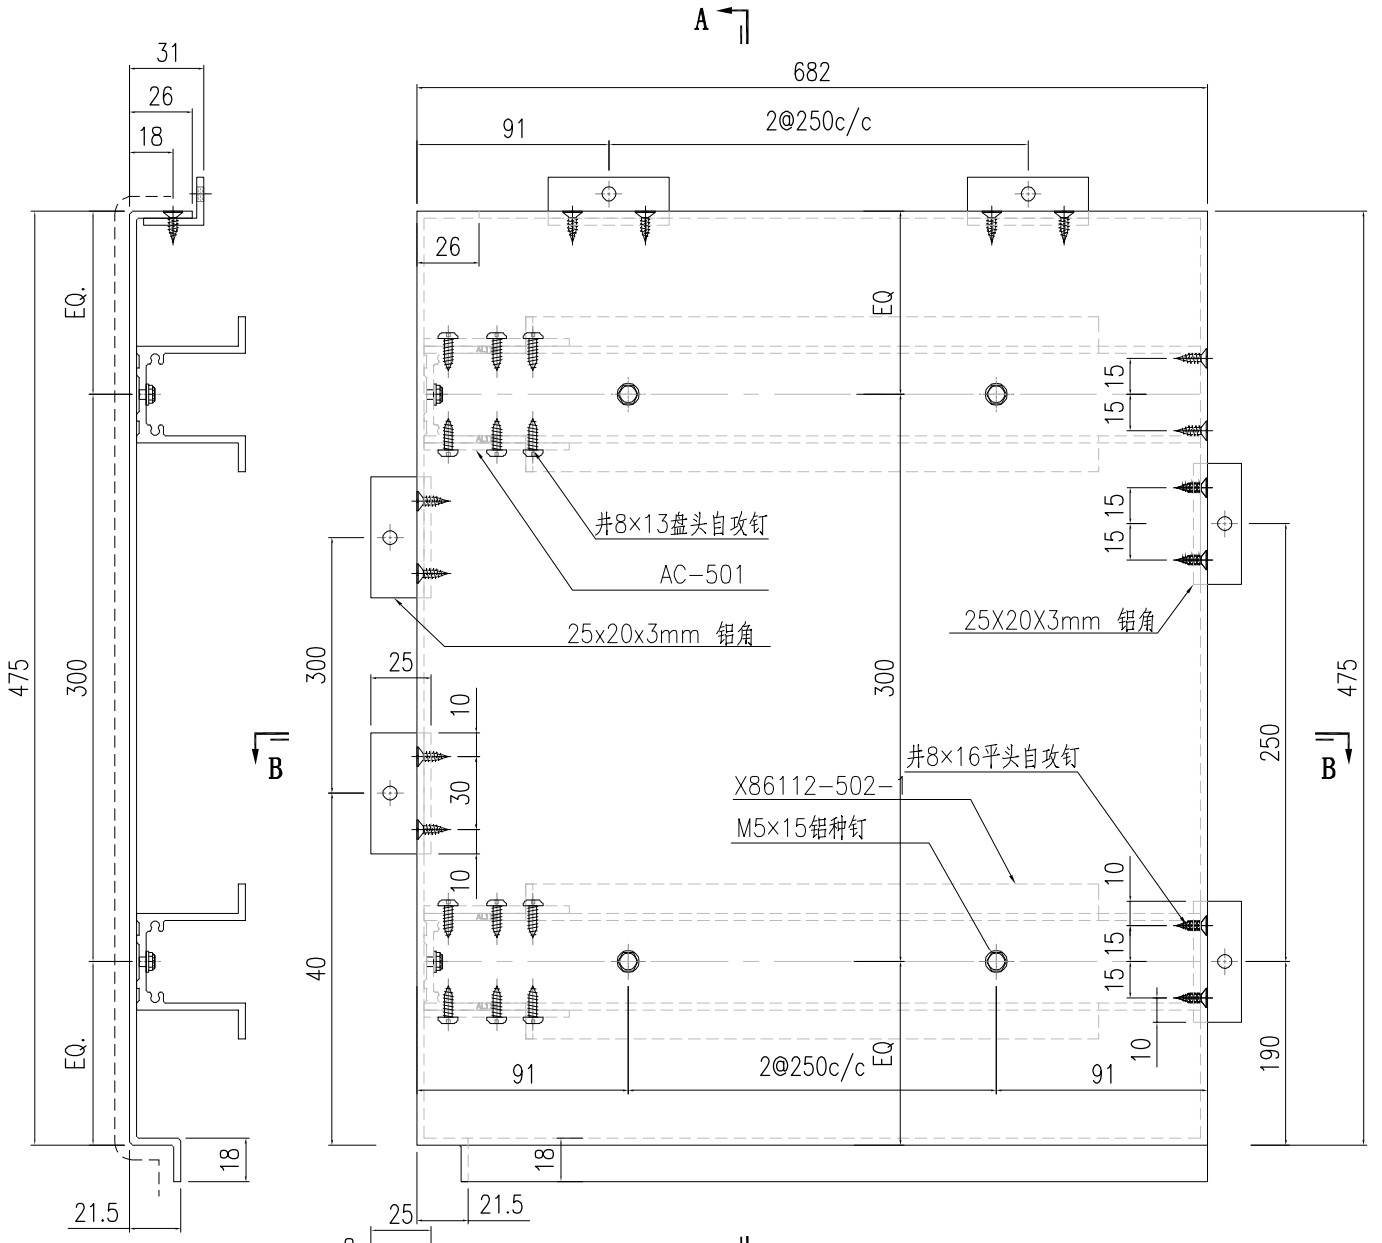

SECTION A-A

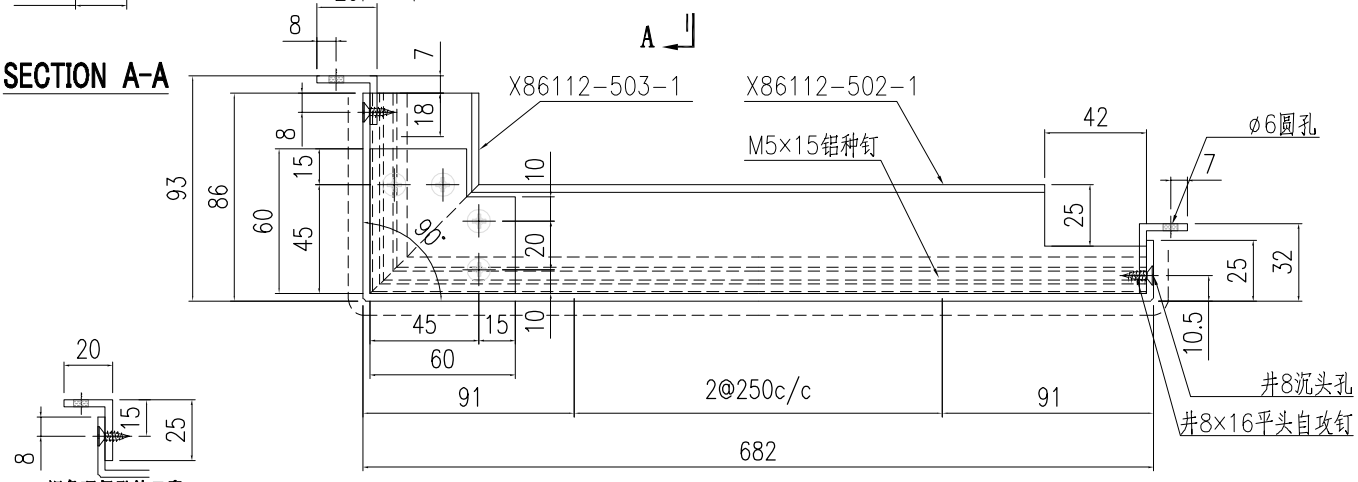





铝角码仔孔位示意

SECTION B-B


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-813	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

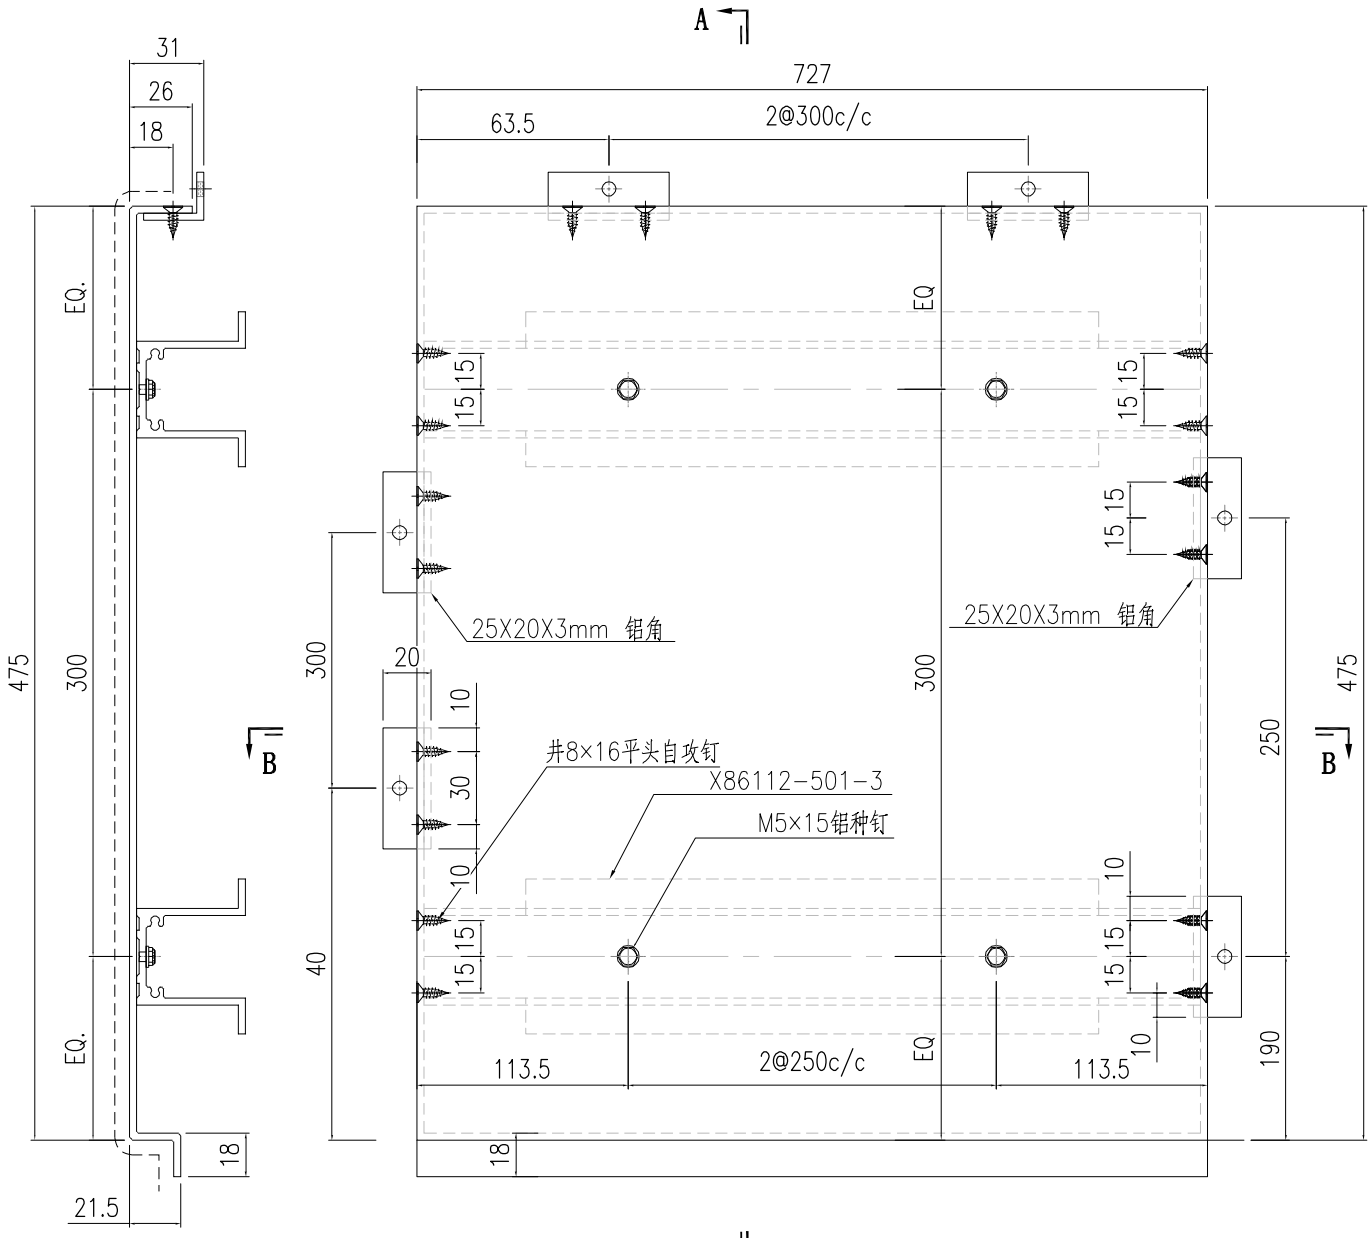

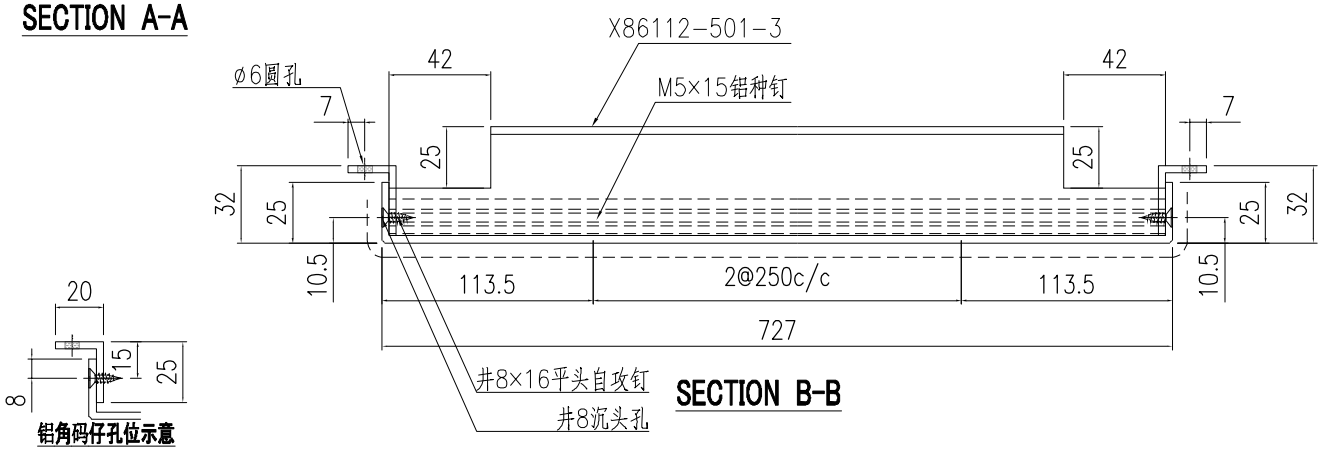


铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
修改	-	-	-	採用	工廠	-	地盤	✓	工程號	J857	類別		物料號	-		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-814
									图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
									材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

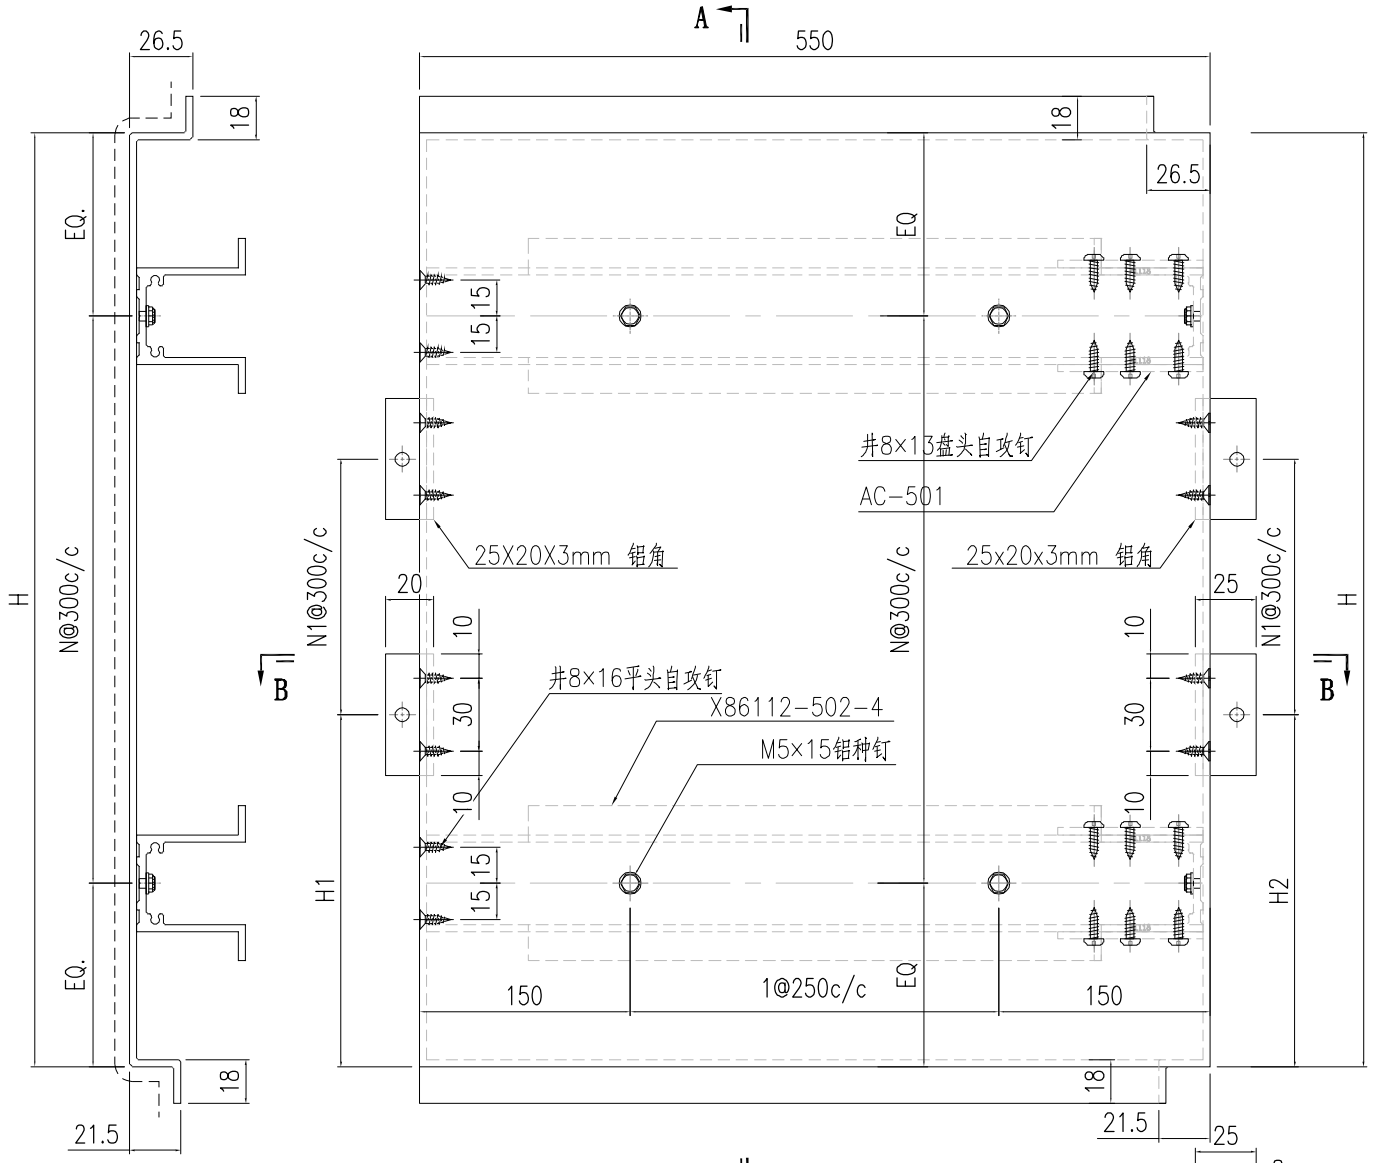

SECTION A-A

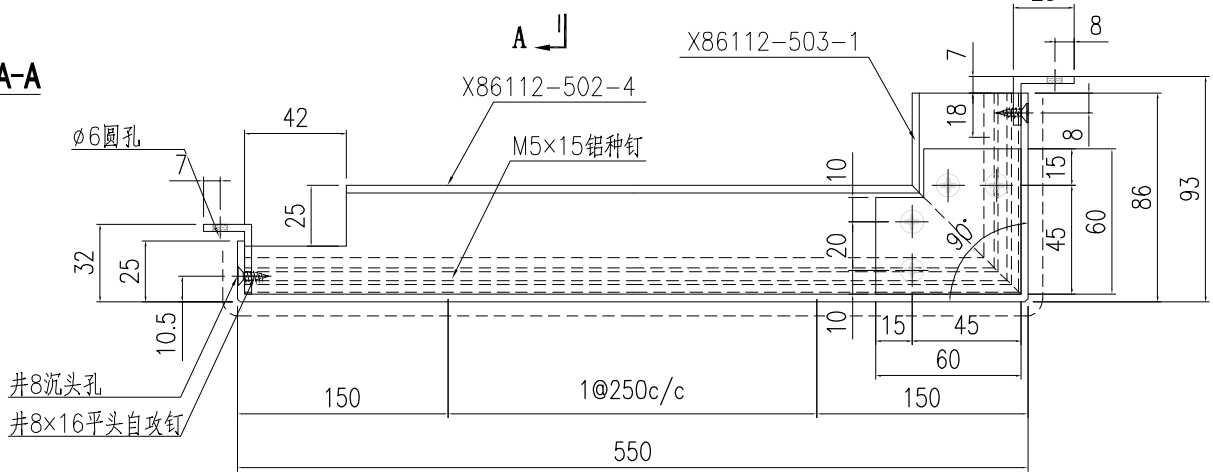


SECTION B-B




铝角码仔孔位示意

1	AC-814-1	2508	8	7	110	175
S/N	部件编号	H	N	N1	H1	H2


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
修改	-	-	-	採用	工廠	-	地盤	✓	工程號	J857	類別		物料號	-
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-815
									图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
									材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

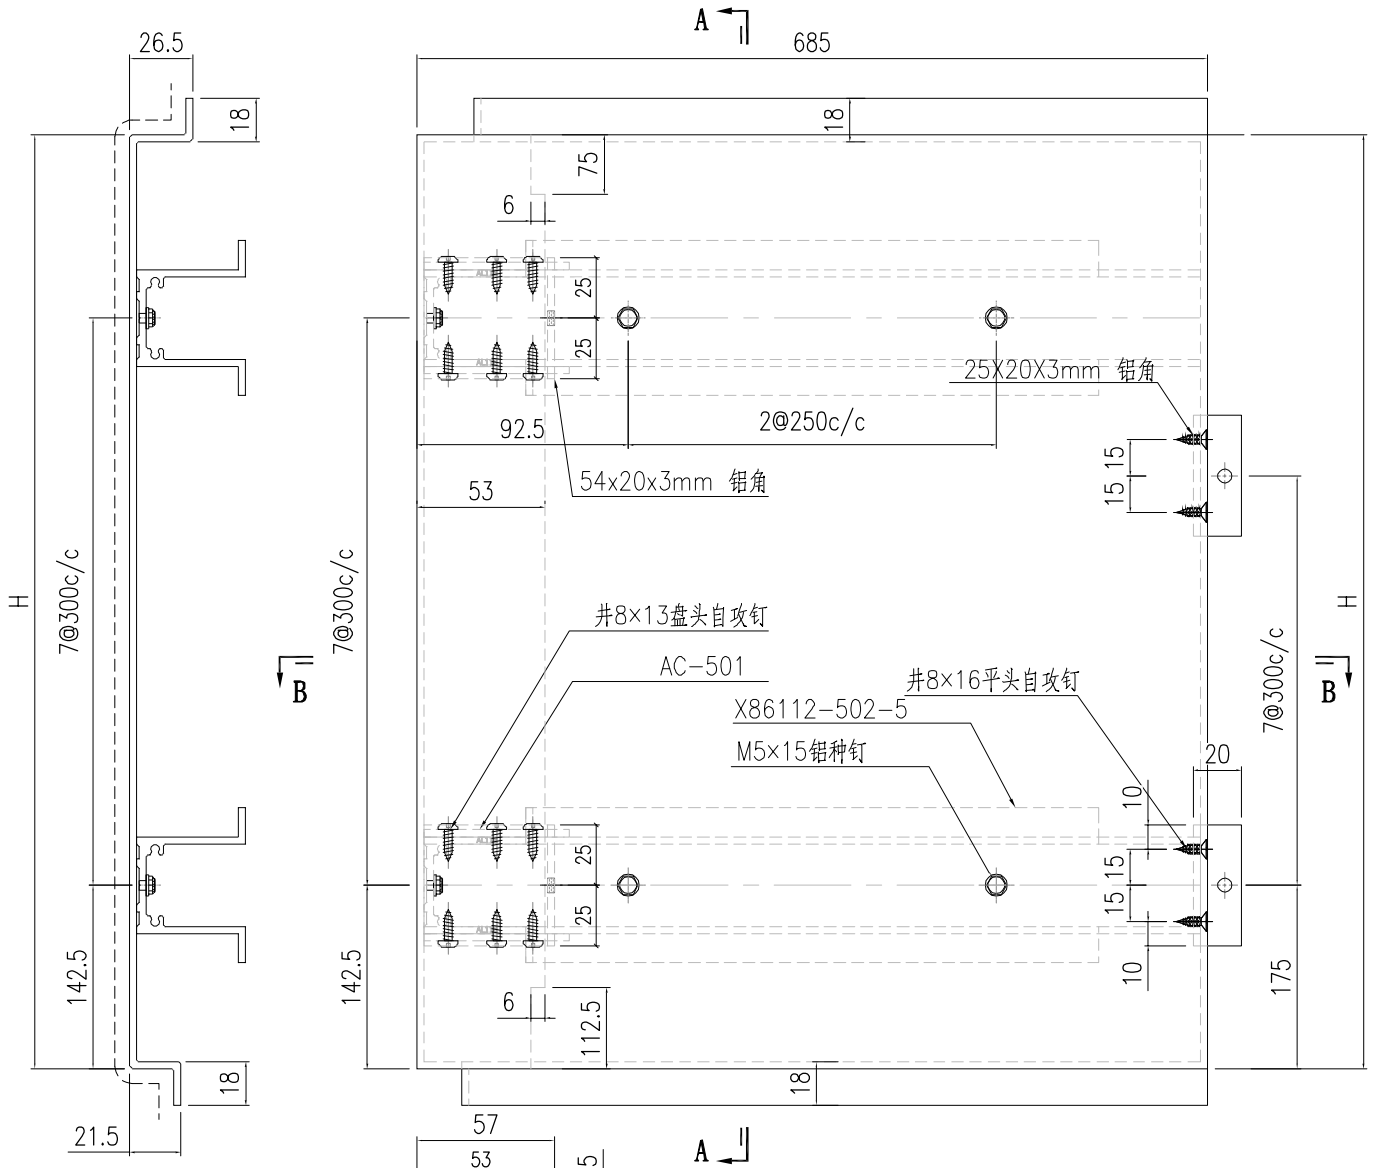

SECTION A-A

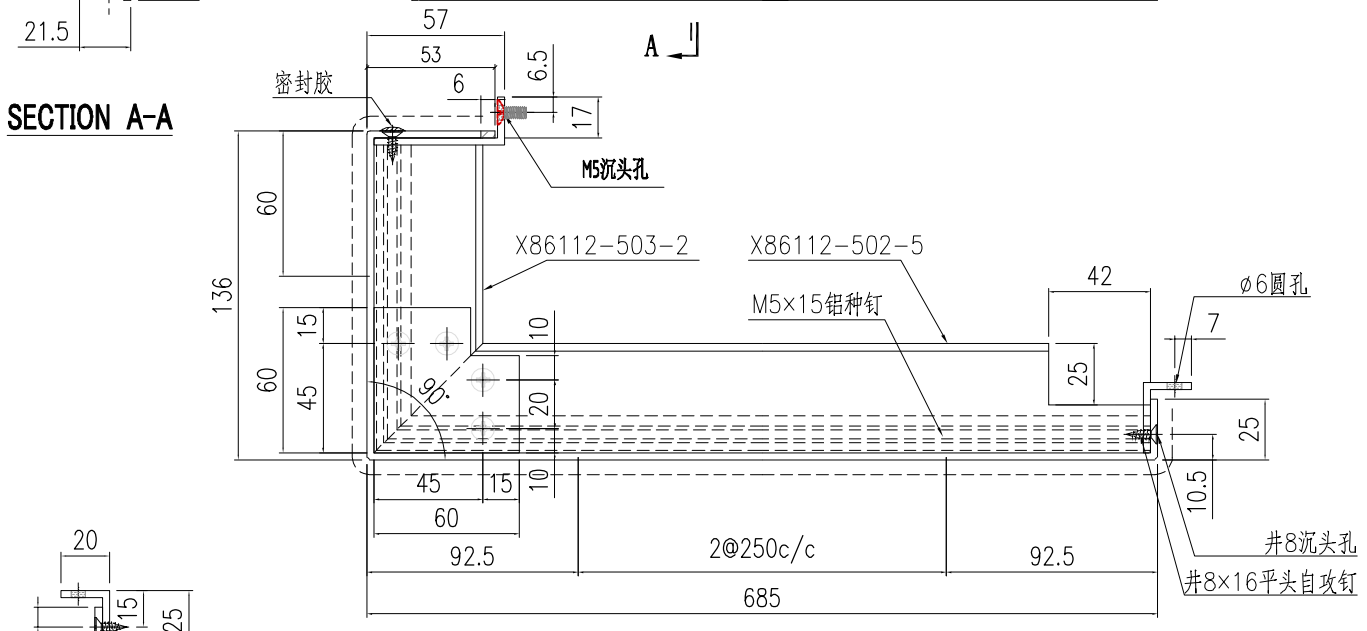


SECTION B-B




铝角码仔孔位示意

1	AC-815-1	2508
S/N	部件编号	H


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
修改	-	-	-	採用	工廠	-	地盤	✓	工程號	J857	類別		物料號	-
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-816
									图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
									材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

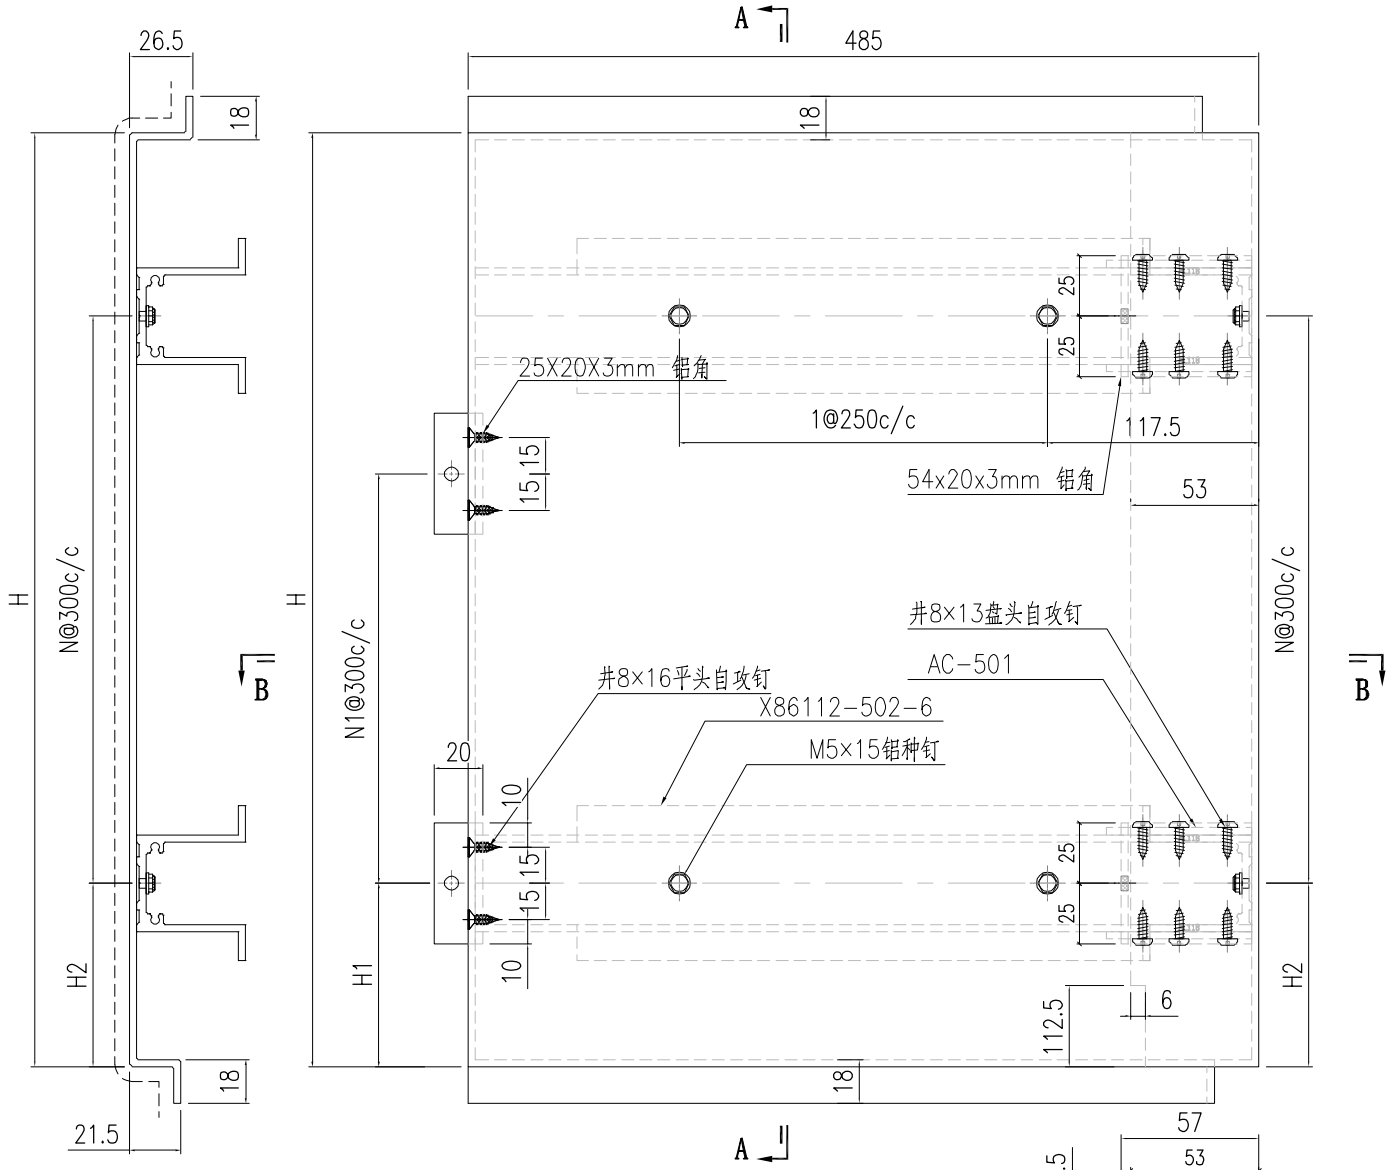

SECTION A-A

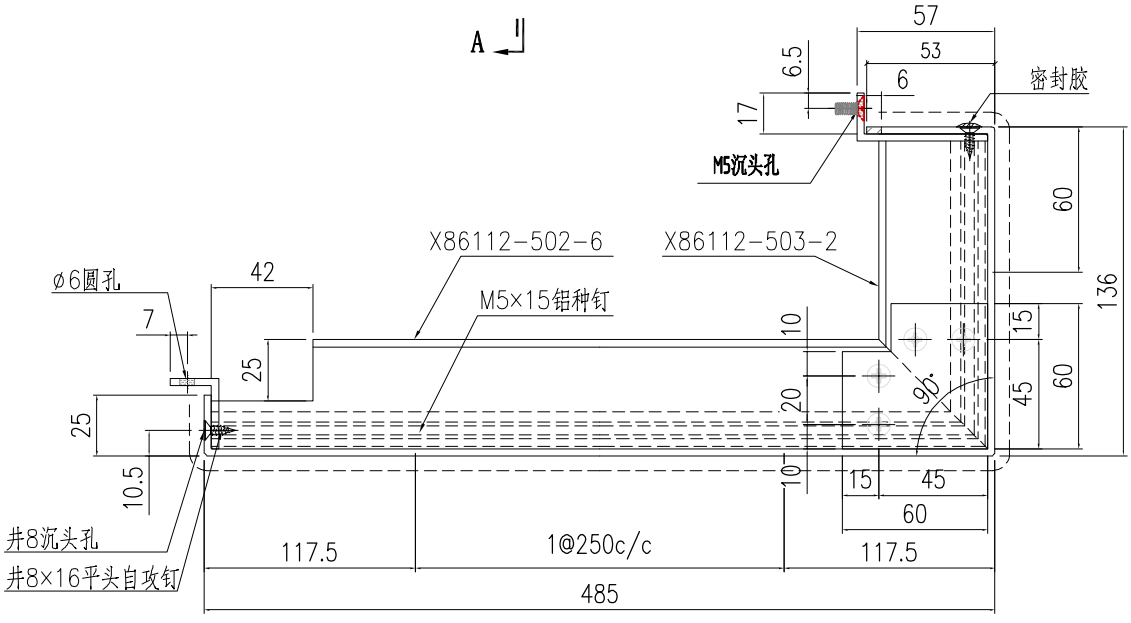


SECTION B-B



铝角码仔孔位示意


S/N	部件编号	部件数量	H	N	N1	H1	H2
3	AC-816-3	1	2505	7	7	110	142.5
2	AC-816-2	1	965	2	2	50	122.5
1	AC-816-1	1	2505	7	7	110	242.5

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-817
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

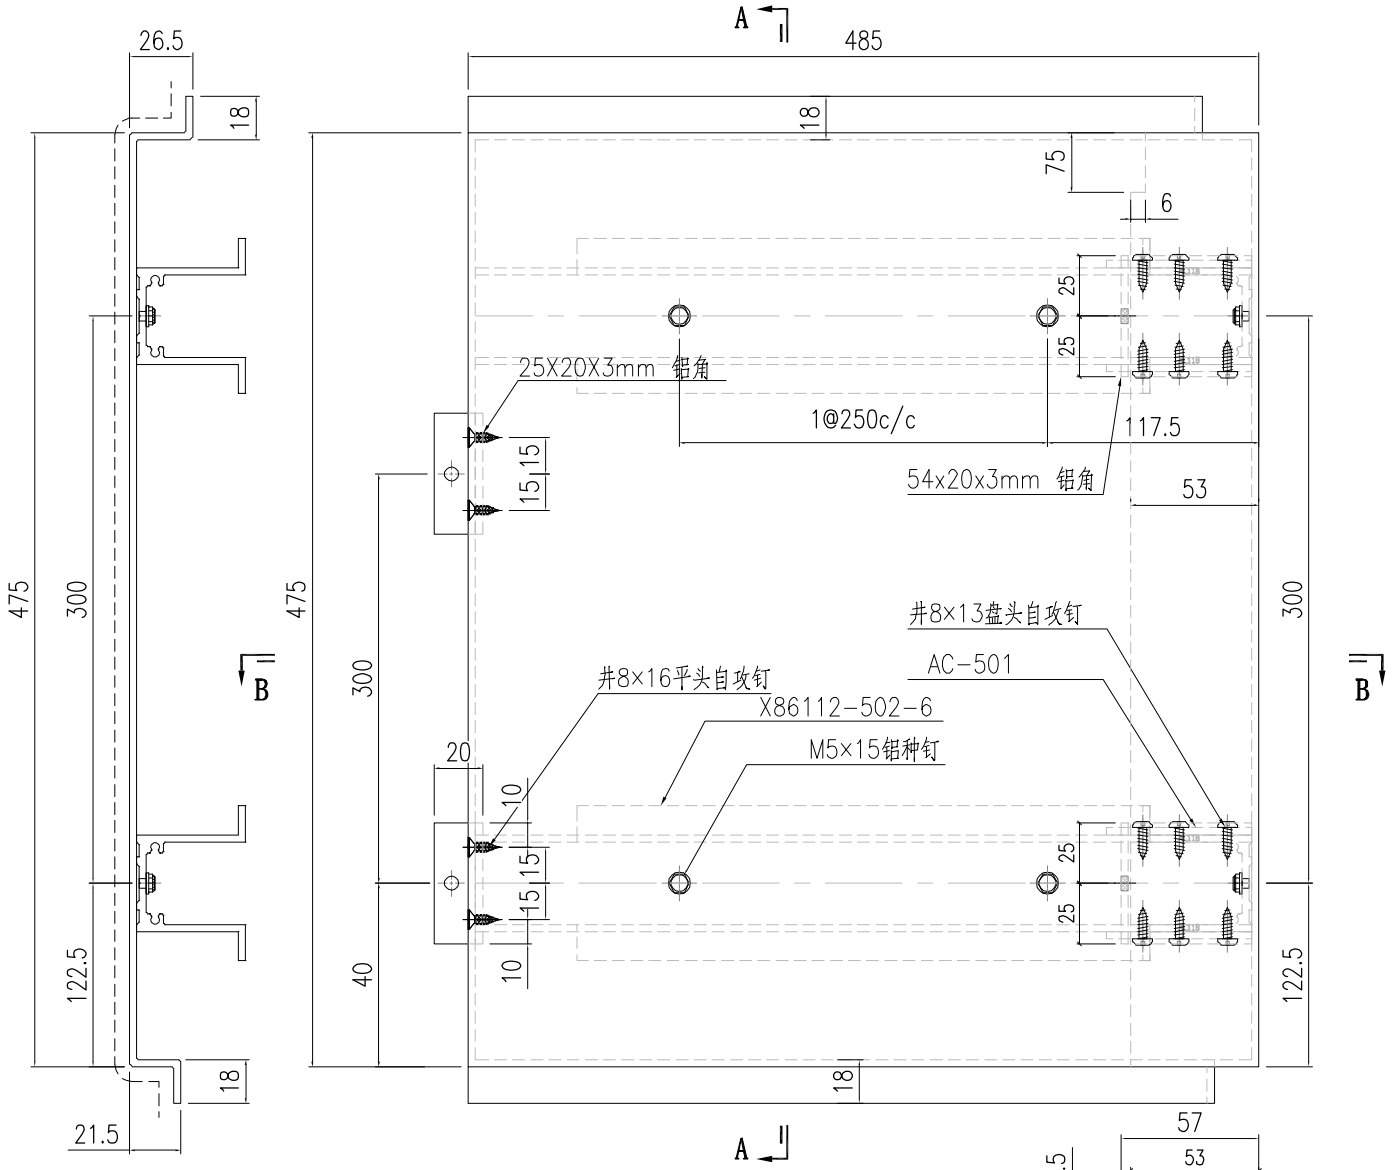


SECTION A-A


SECTION B-B




铝角码仔孔位示意

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-818
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 鋁板	批准	林仁安 20221210	單件重量	- (KG)

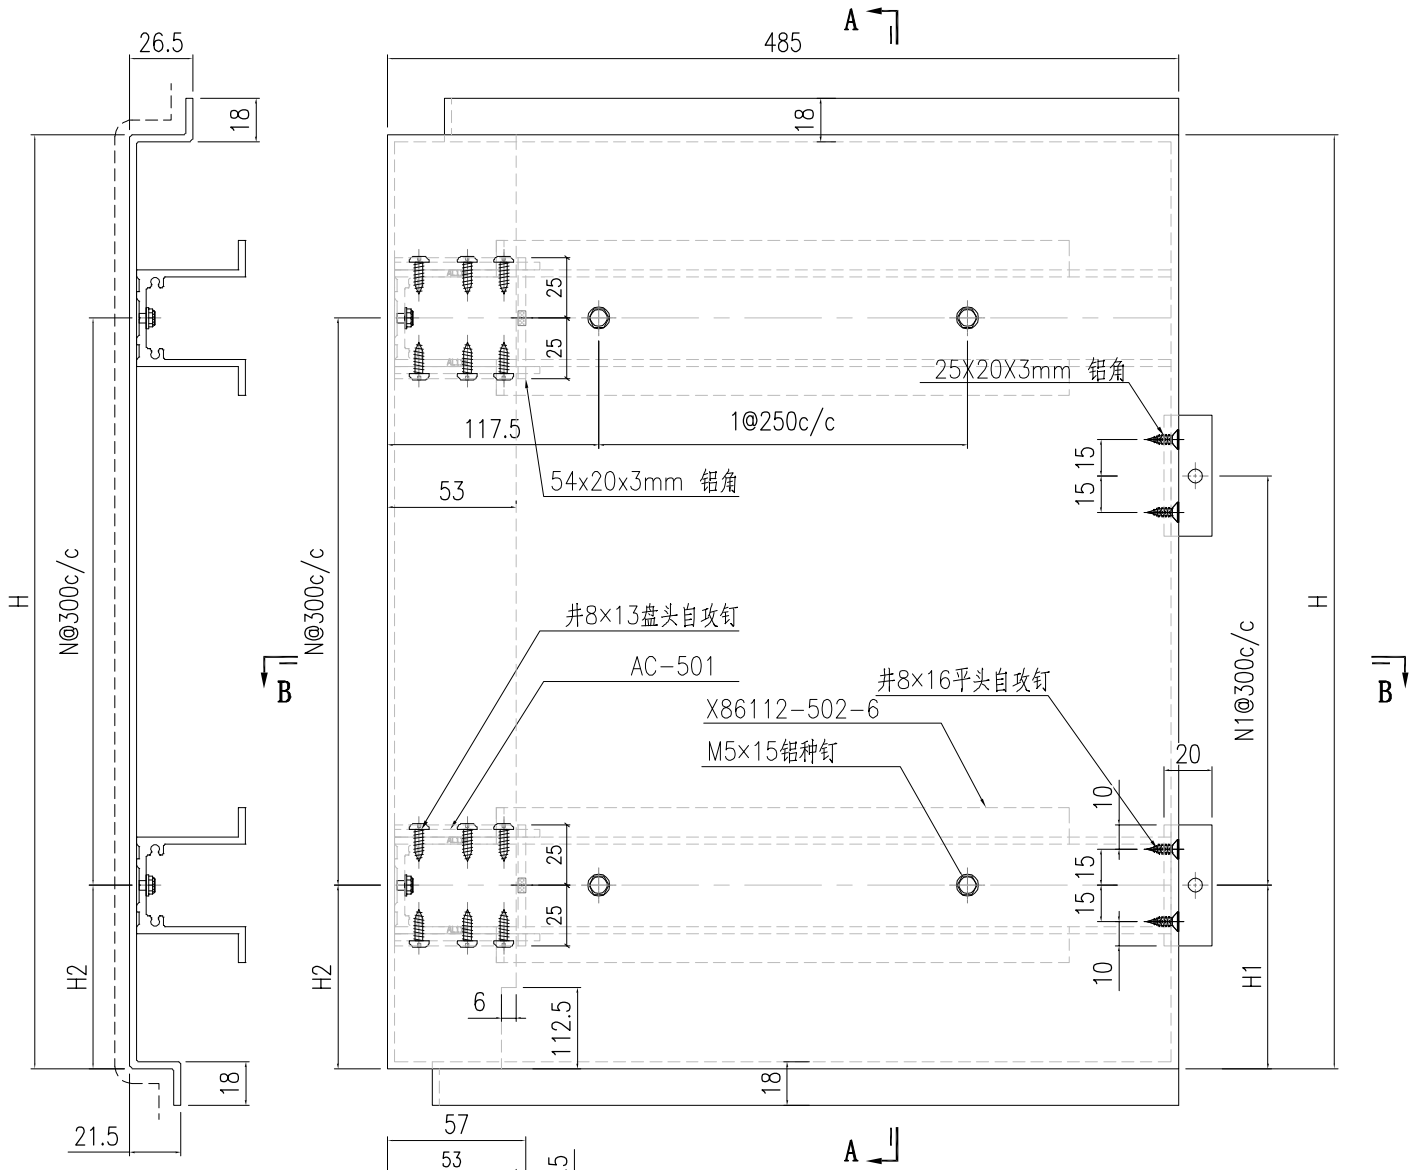

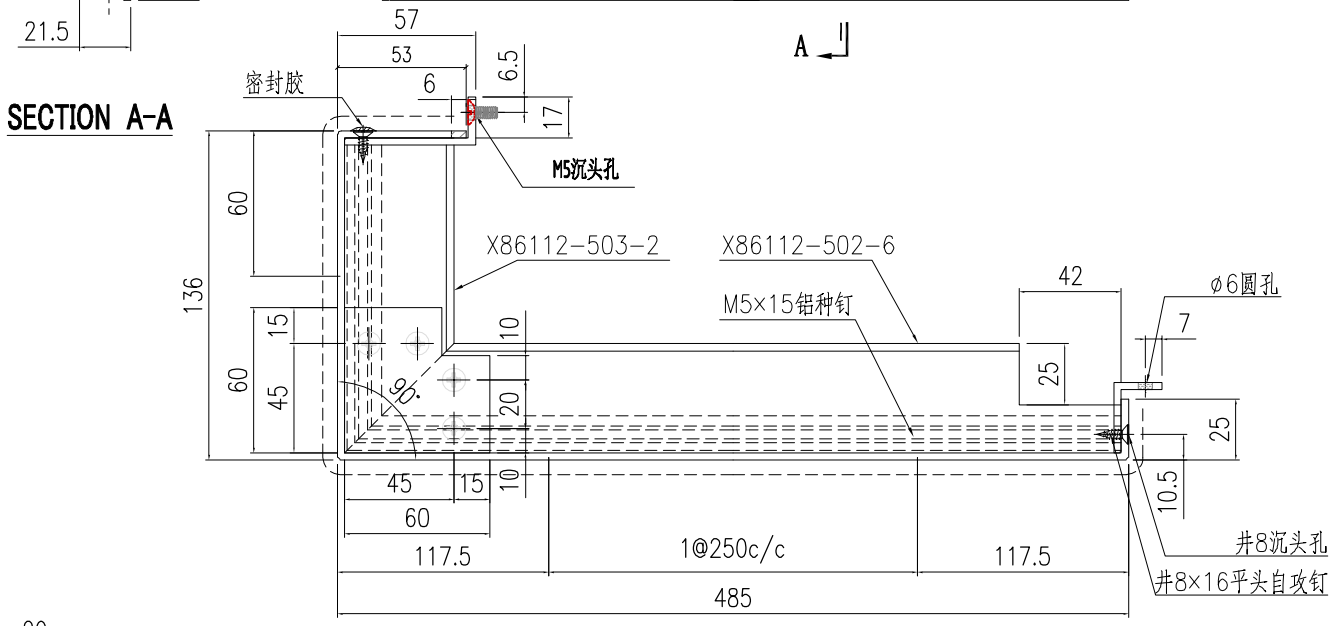






SECTION B-B

S/N	部件编号	部件数量	H	N	N1	H1	H2
3	AC-818-3	1	2505	7	7	110	142.5
2	AC-818-2	1	965	2	2	50	122.5
1	AC-818-1	1	2505	7	7	110	242.5

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-819
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

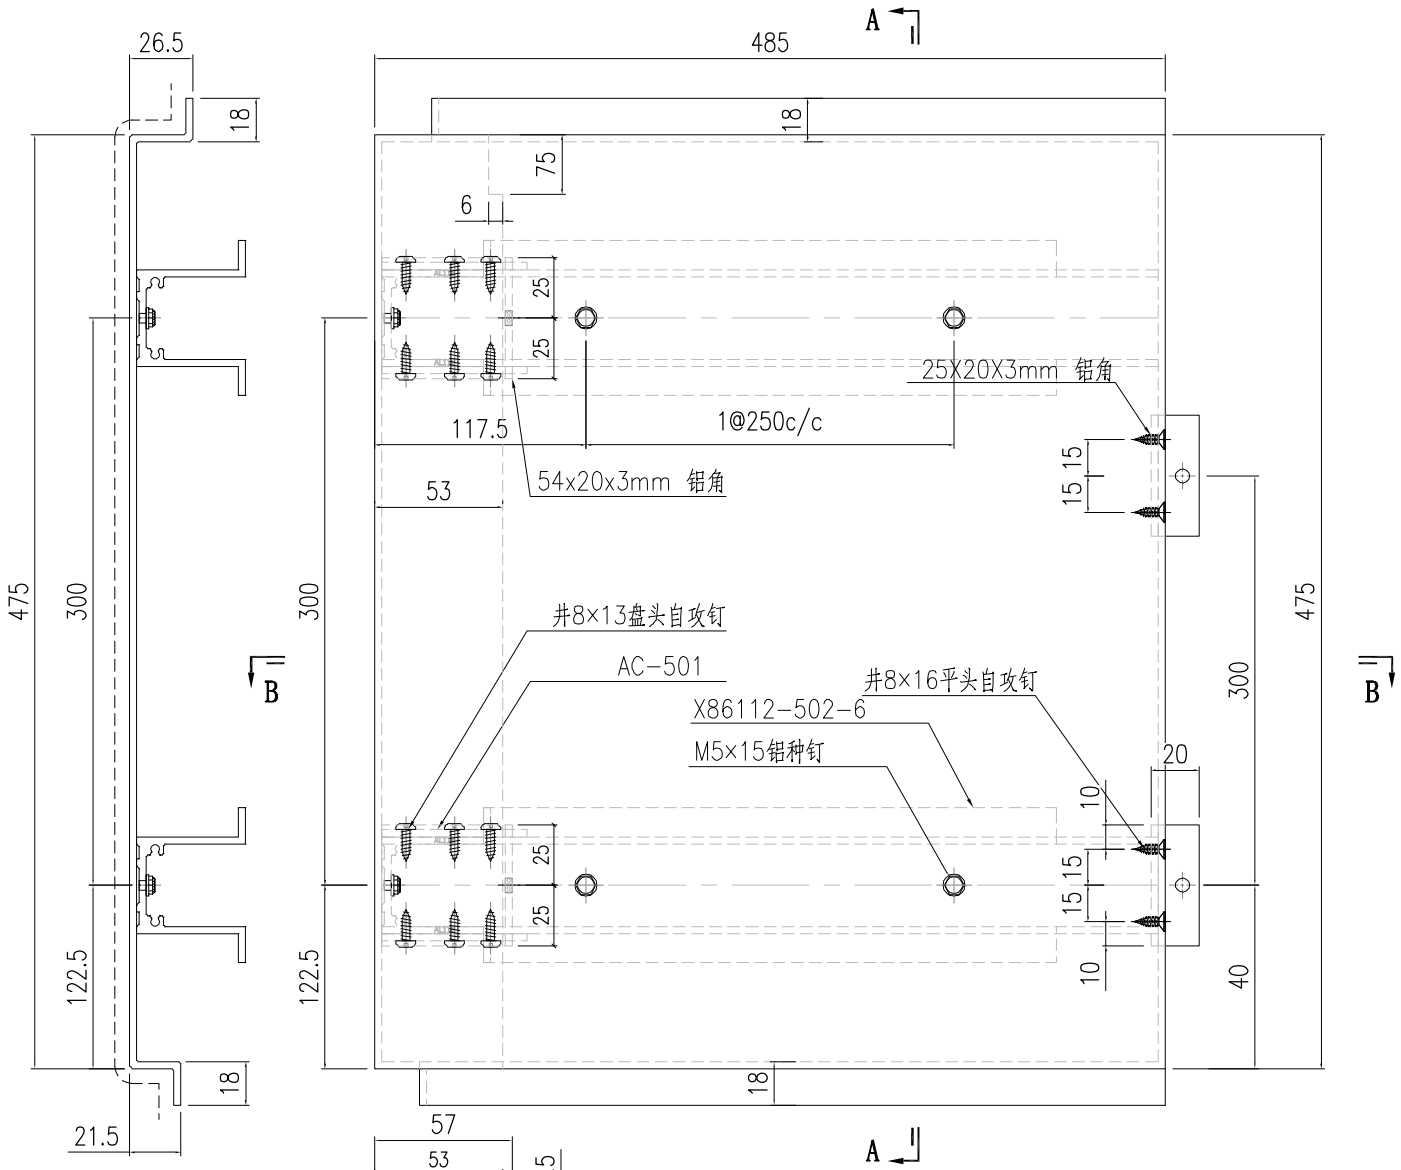


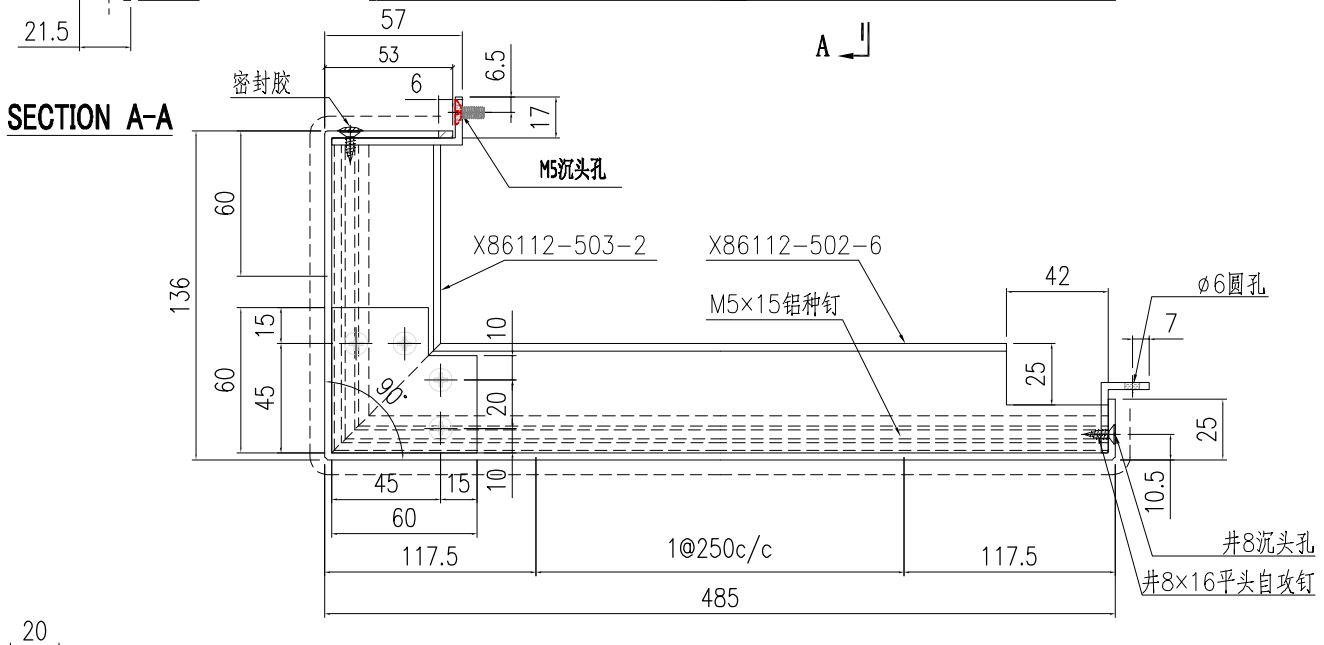




SECTION B-B


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-820		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

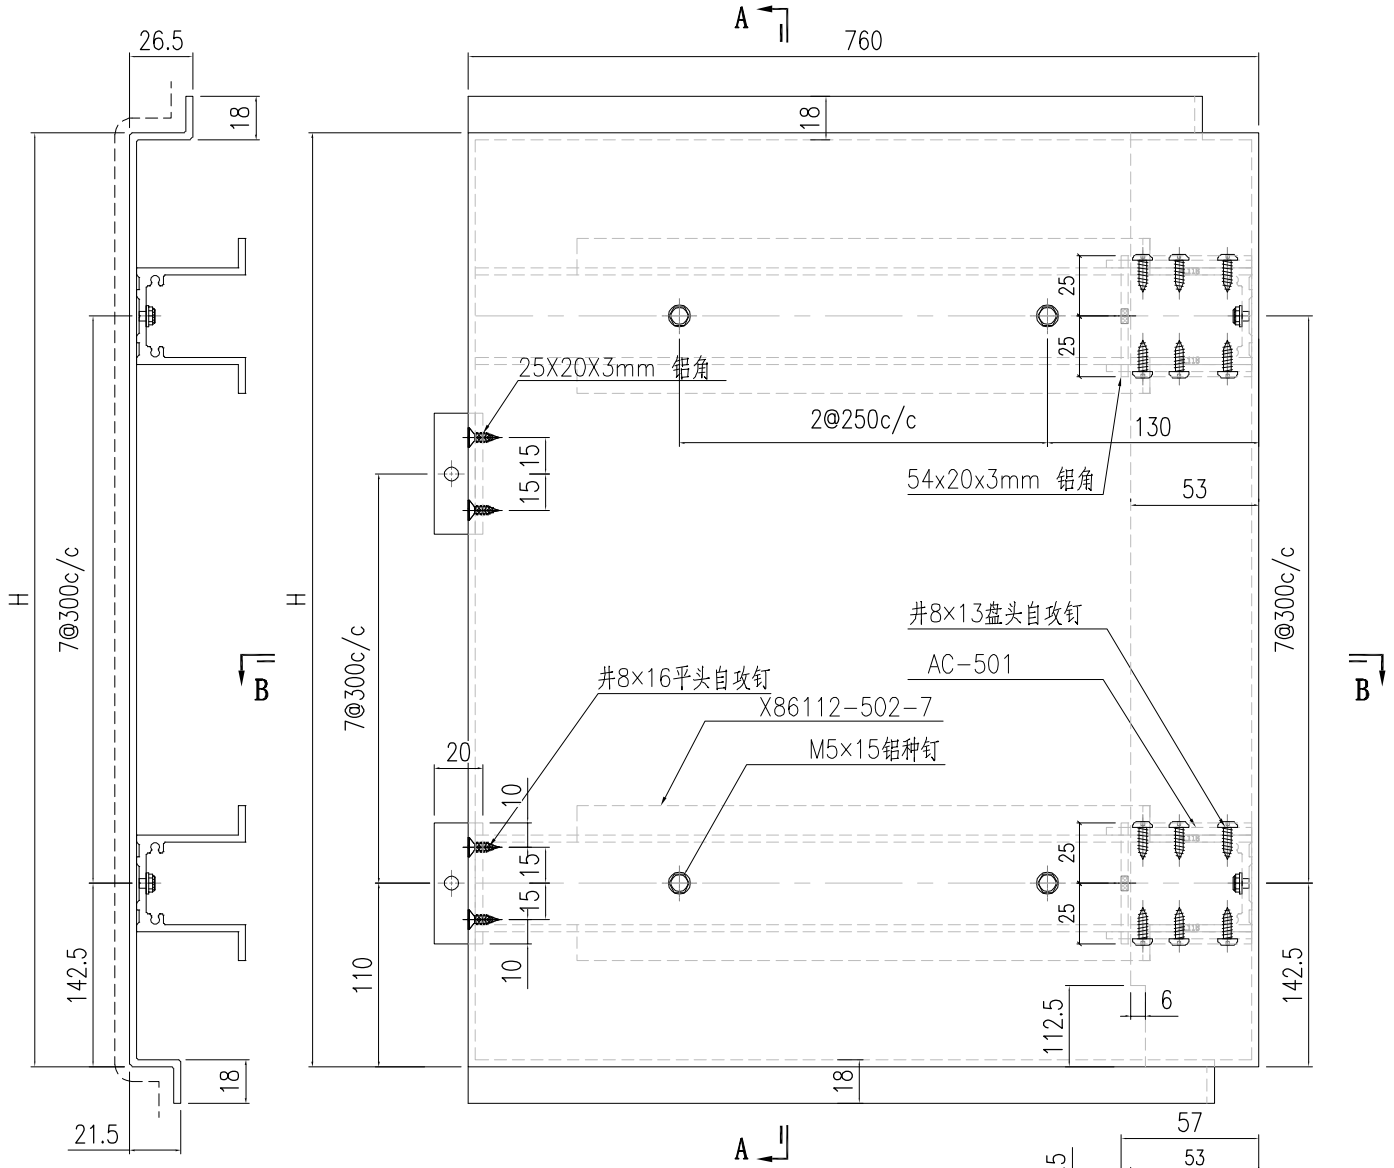

SECTION A-A

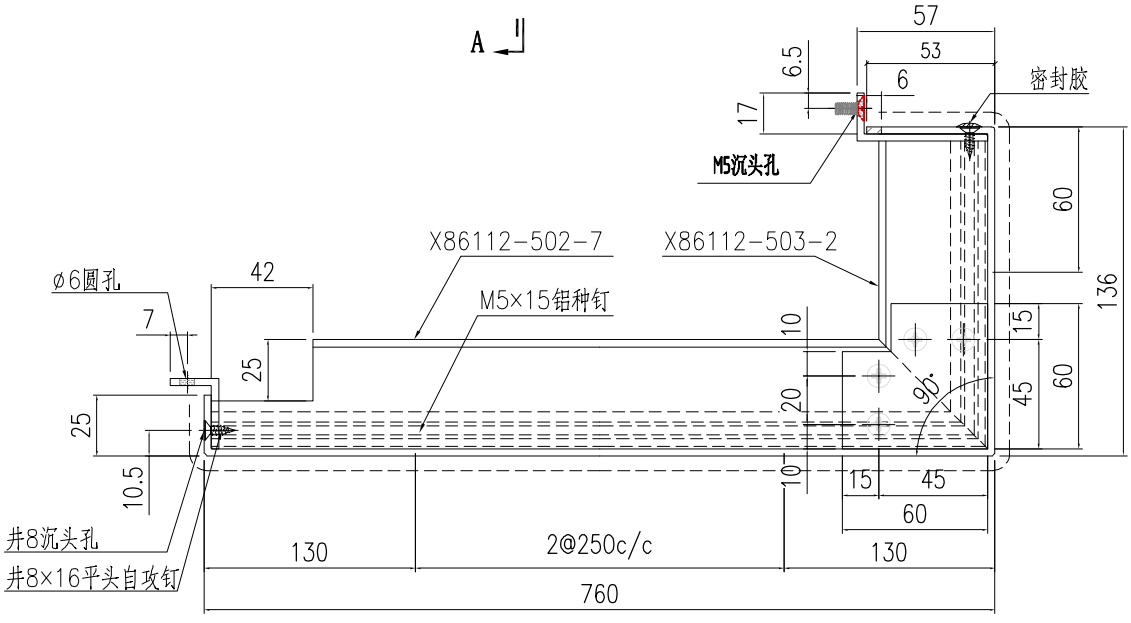


SECTION B-B




铝角码仔孔位示意


1	AC-820-1	2508
S/N	部件编号	H

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-821	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

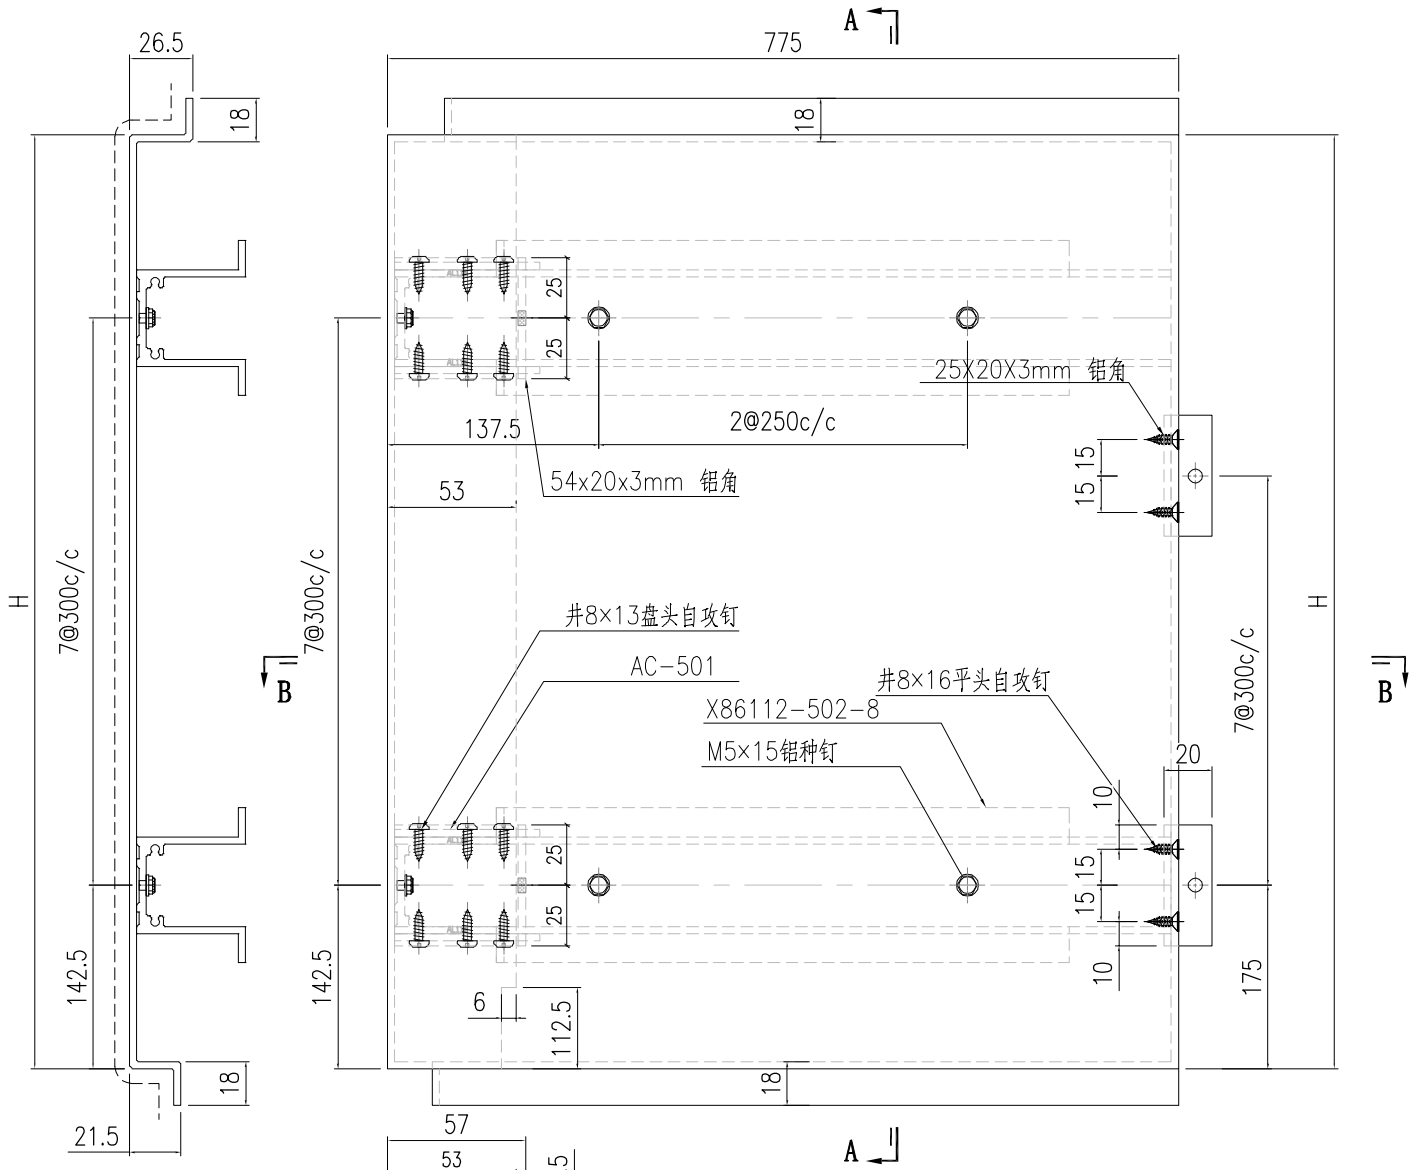

SECTION A-A

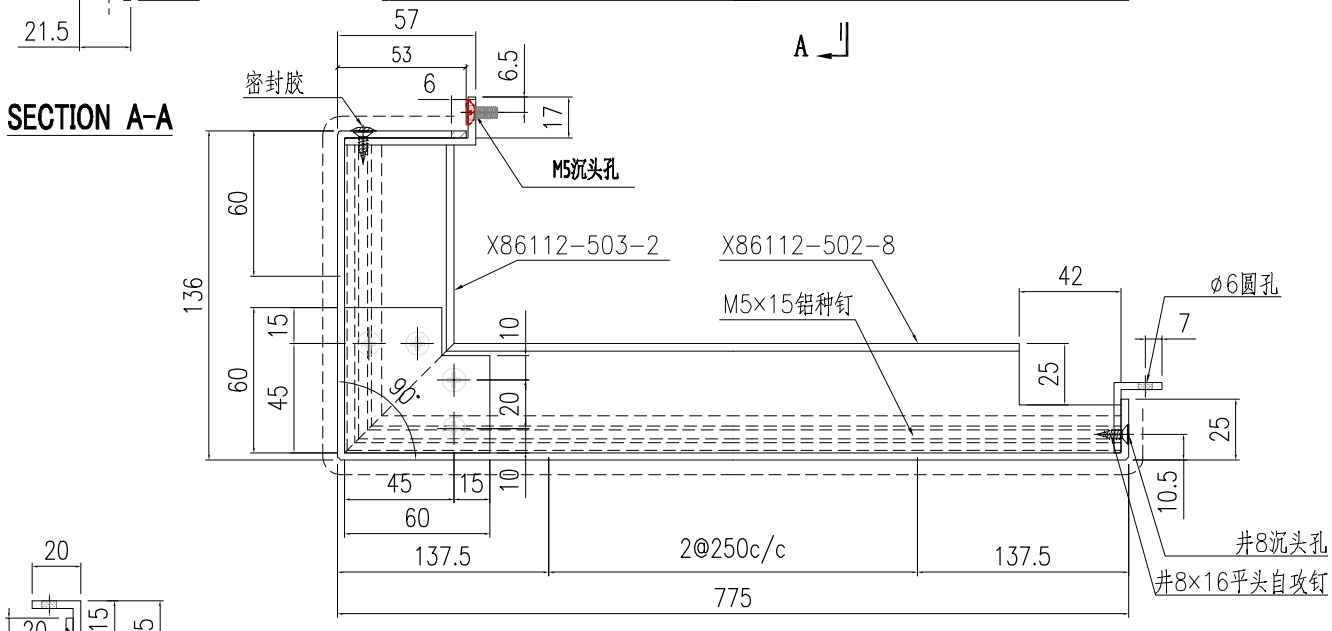




铝角码仔孔位示意


SECTION B-B

1	AC-821-1	2508
S/N	部件编号	H


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
工程號	J857	類別		物料號	-									
地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-822									
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 鋁板	批准	林仁安 20221210	單件重量	- (KG)

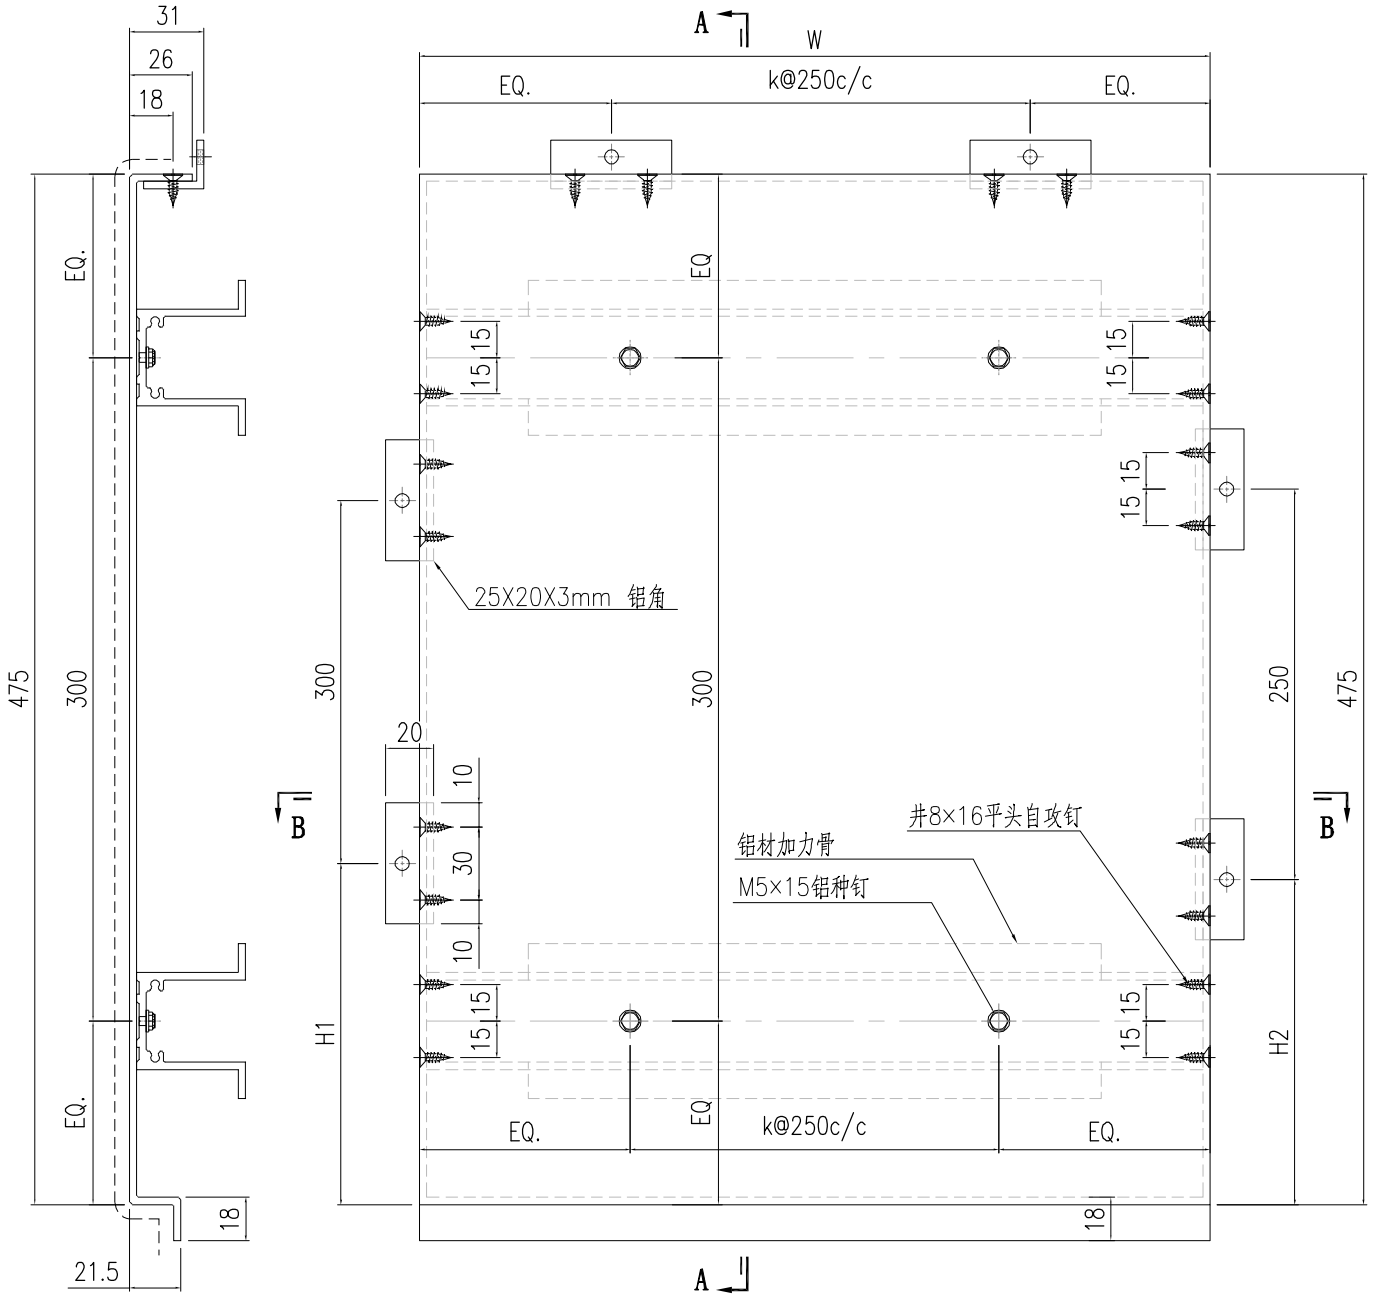

SECTION A-A

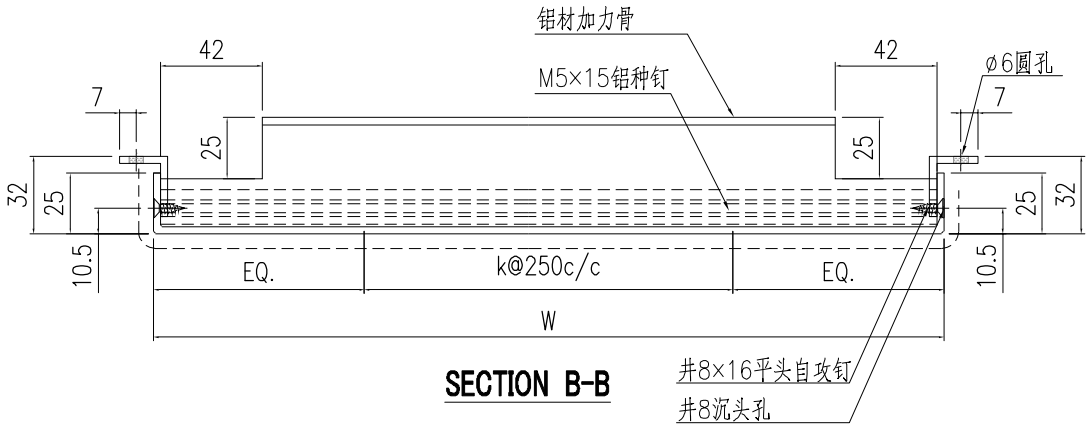

SECTION B-B




铝角码仔孔位示意

铝板长宽数据見AC-822a


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-822a	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209		數量	-	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

S/N	部件编号	部件数量	W	H1	H2	K	铝材加力骨
8	AC-822-8	1	1242.5	65	132.5	4	X86112-501-11
7	AC-822-7	1	950	132.5	65	3	X86112-501-6
6	AC-822-6	1	947.5	132.5	65	3	X86112-501-7
5	AC-822-5	1	1102.5	65	132.5	3	X86112-501-8
4	AC-822-4	1	1102.5	132.5	65	3	X86112-501-8
3	AC-822-3	1	947.5	65	132.5	3	X86112-501-7
2	AC-822-2	1	950	65	132.5	3	X86112-501-6
1	AC-822-1	1	975	132.5	65	3	X86112-501-5


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-823
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

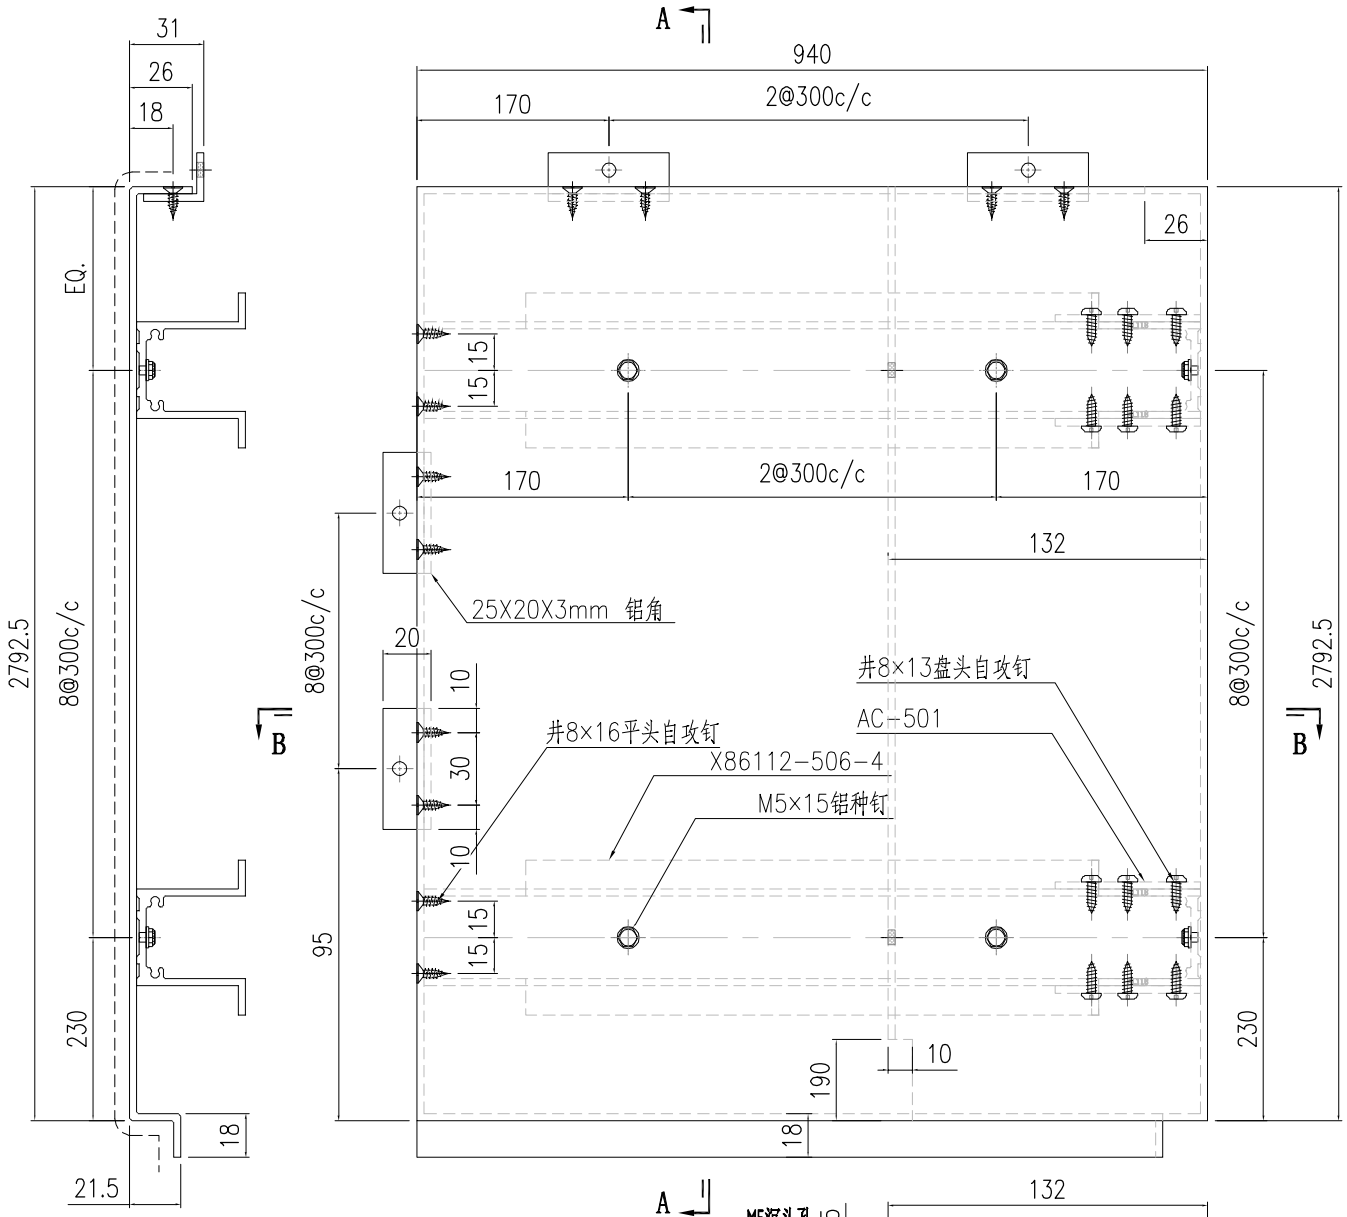

SECTION A-A

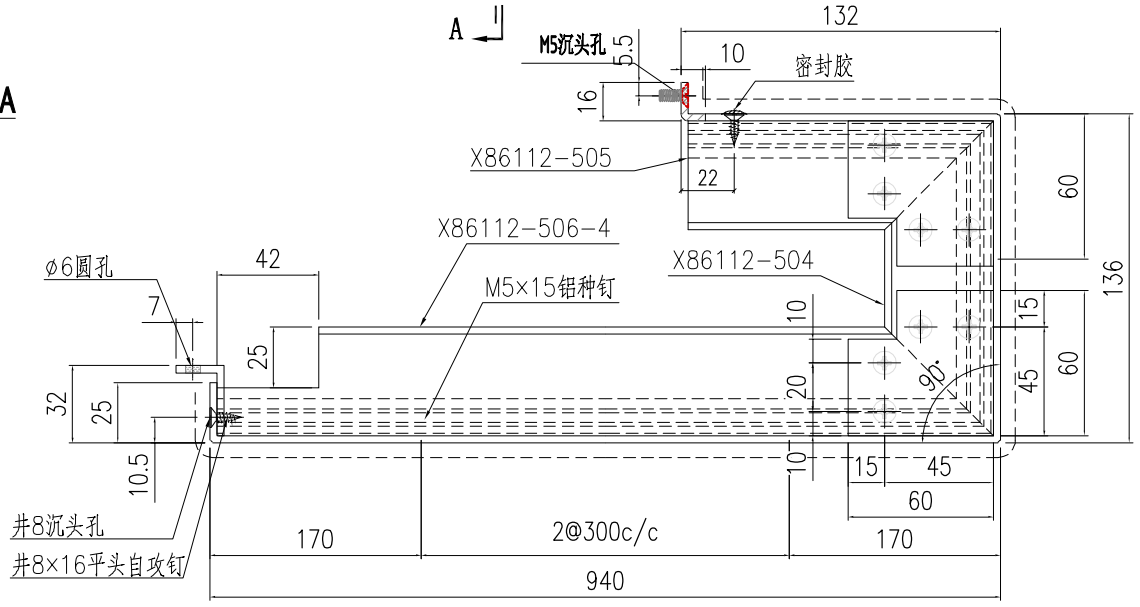


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-824
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

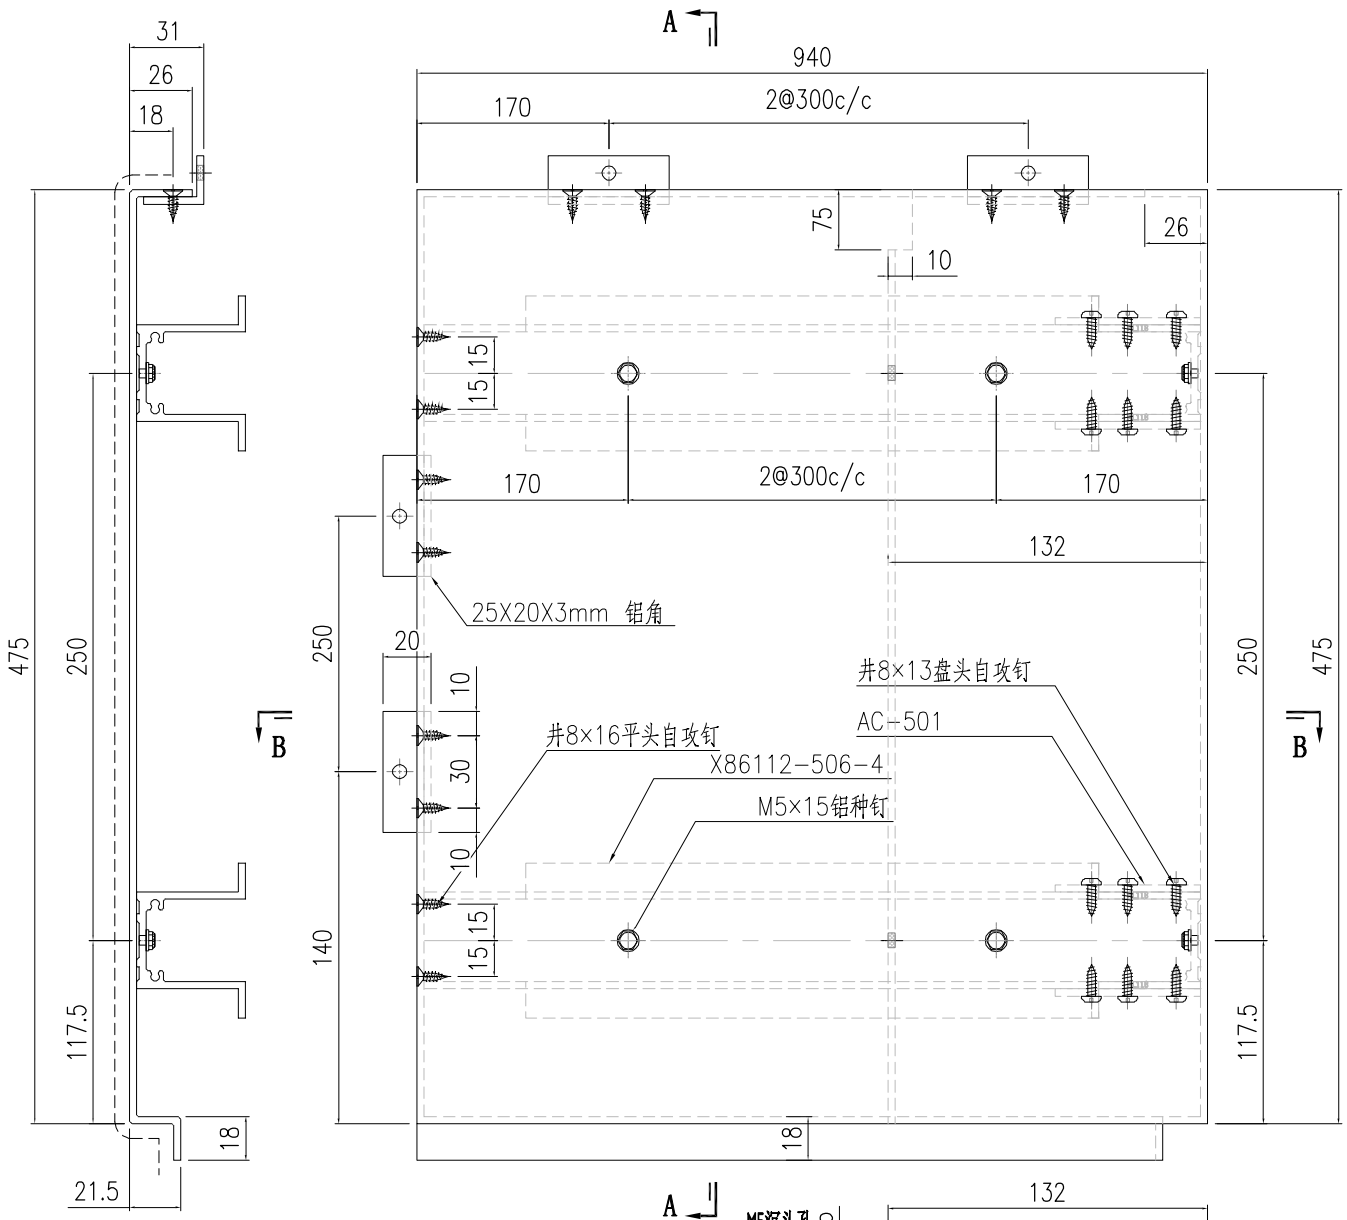

SECTION A-A

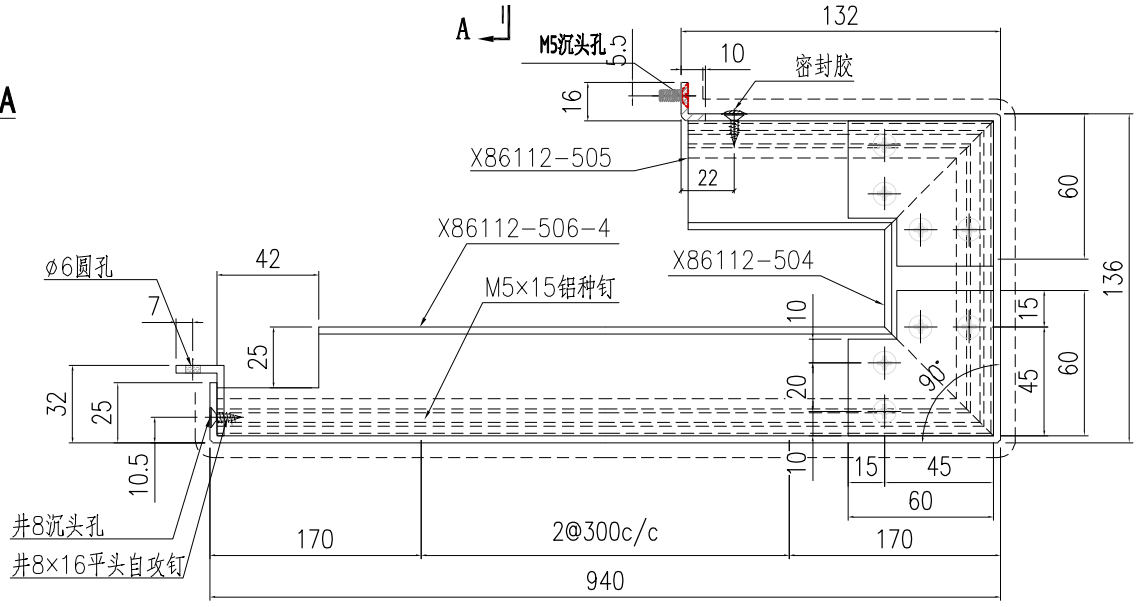


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-825
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

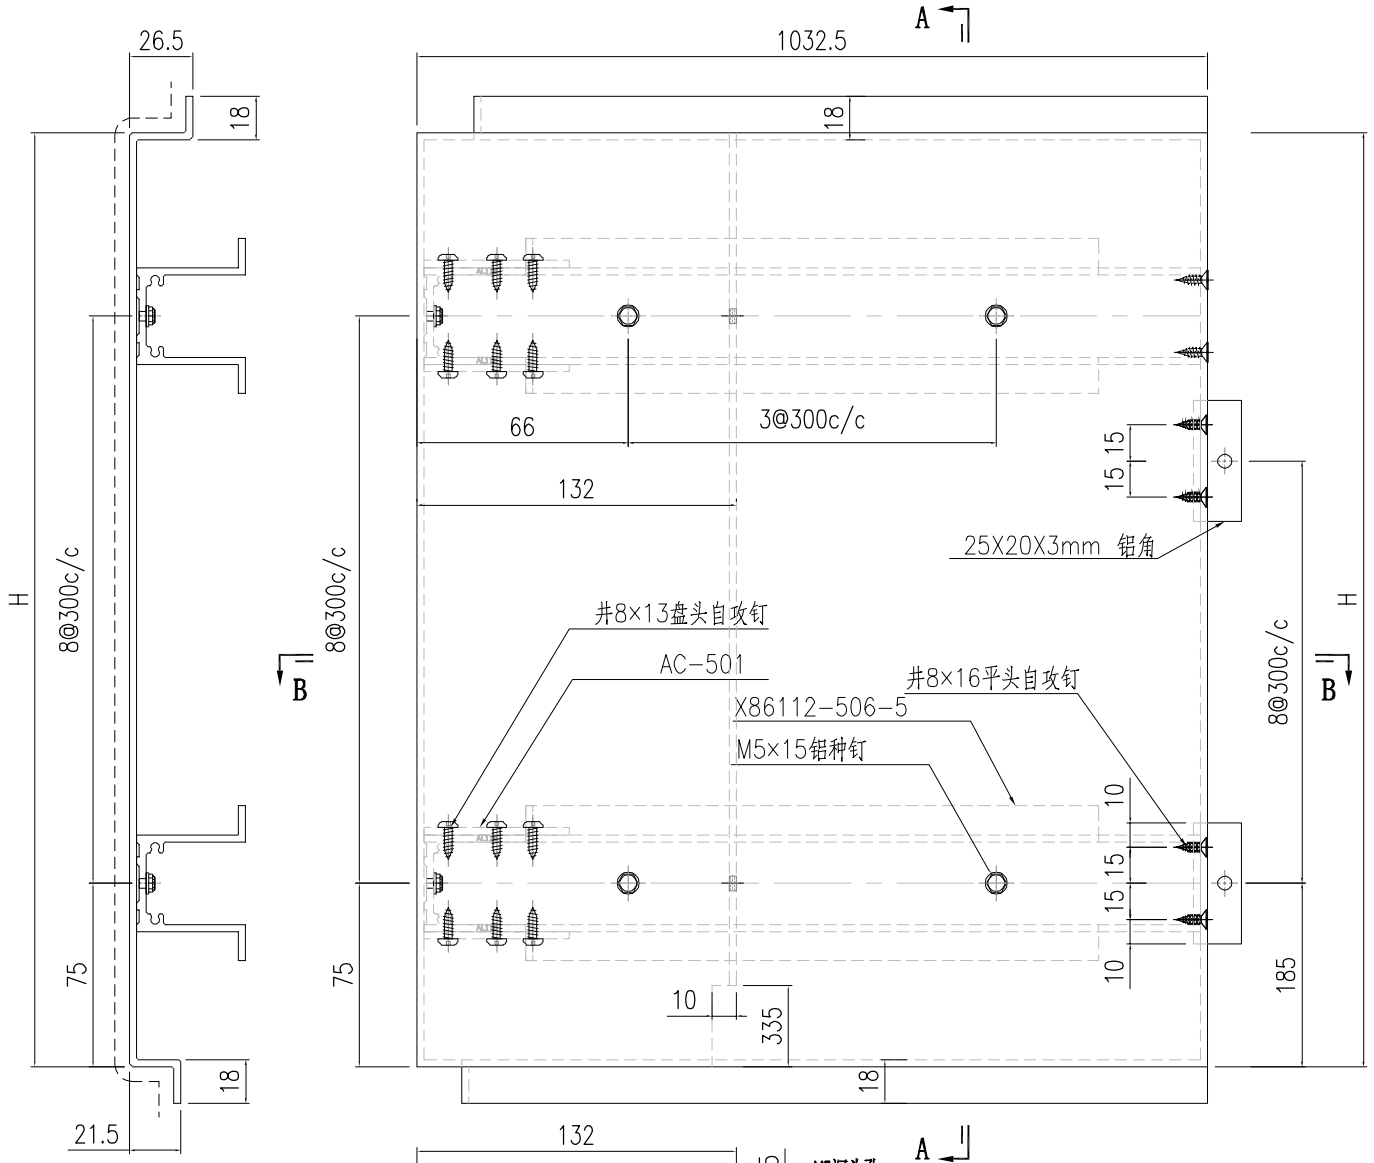

SECTION A-A

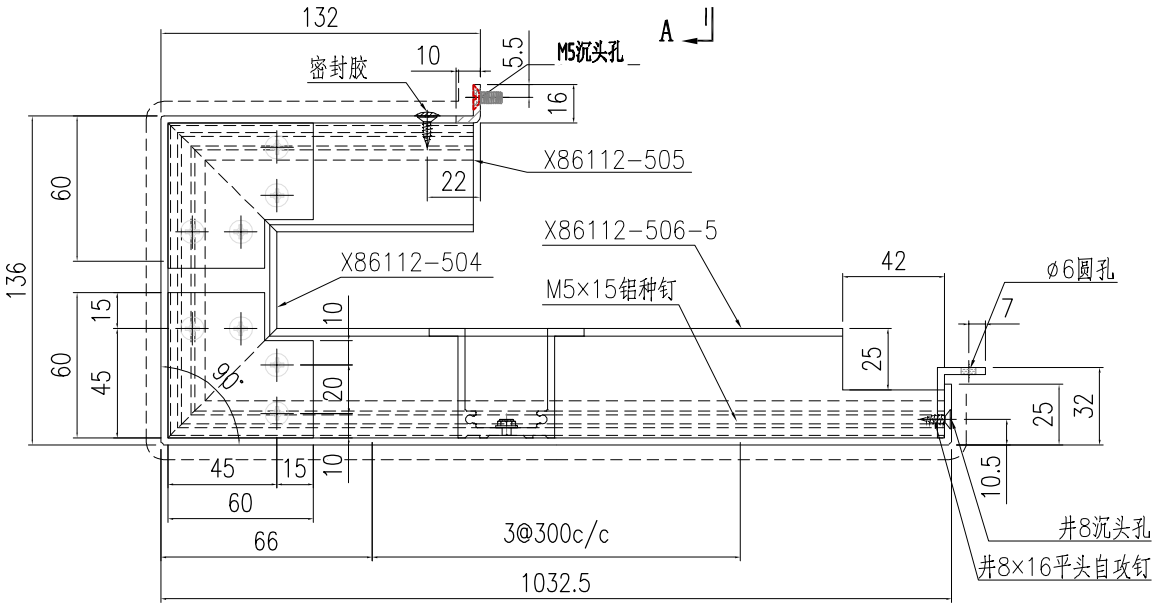


SECTION B-B




铝角码仔孔位示意

1	AC-825-1	2737.5
S/N	部件编号	H


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-826
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

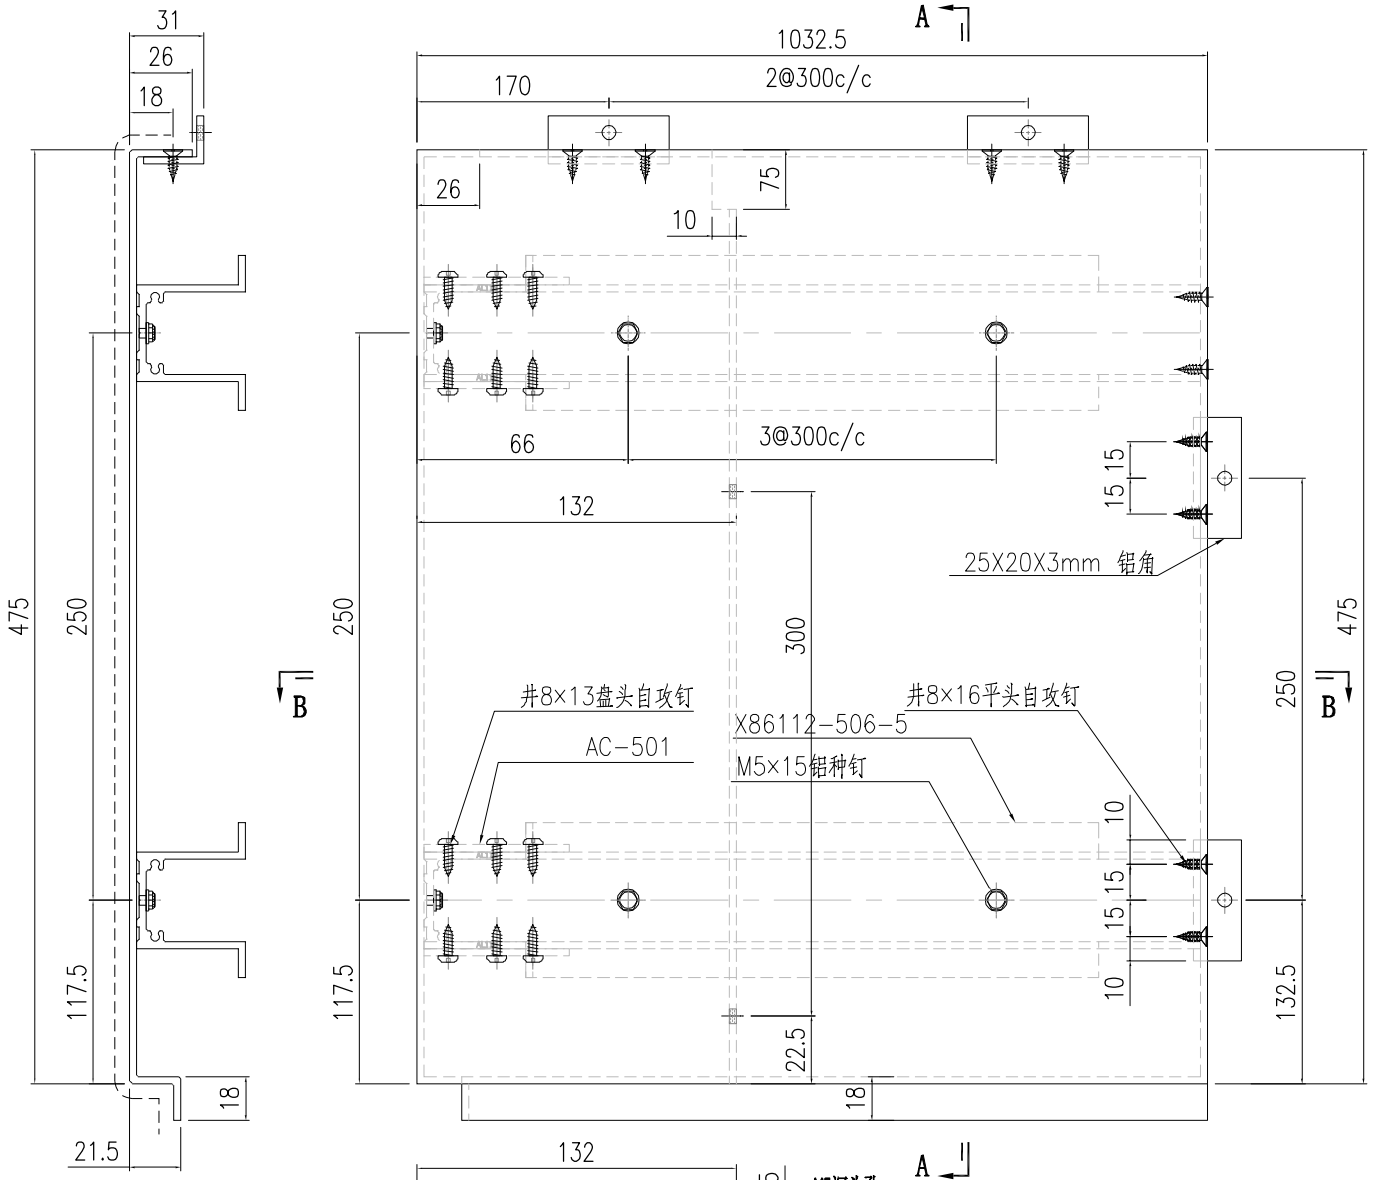

SECTION A-A

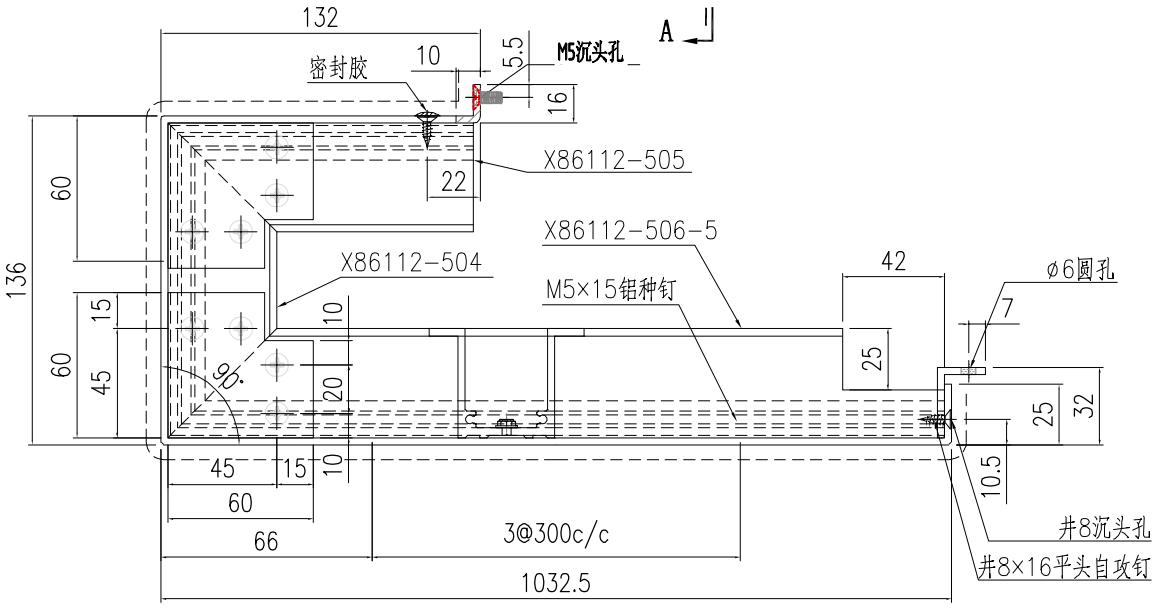


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
工程號	J857	類別		物料號	-									
地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-827									
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

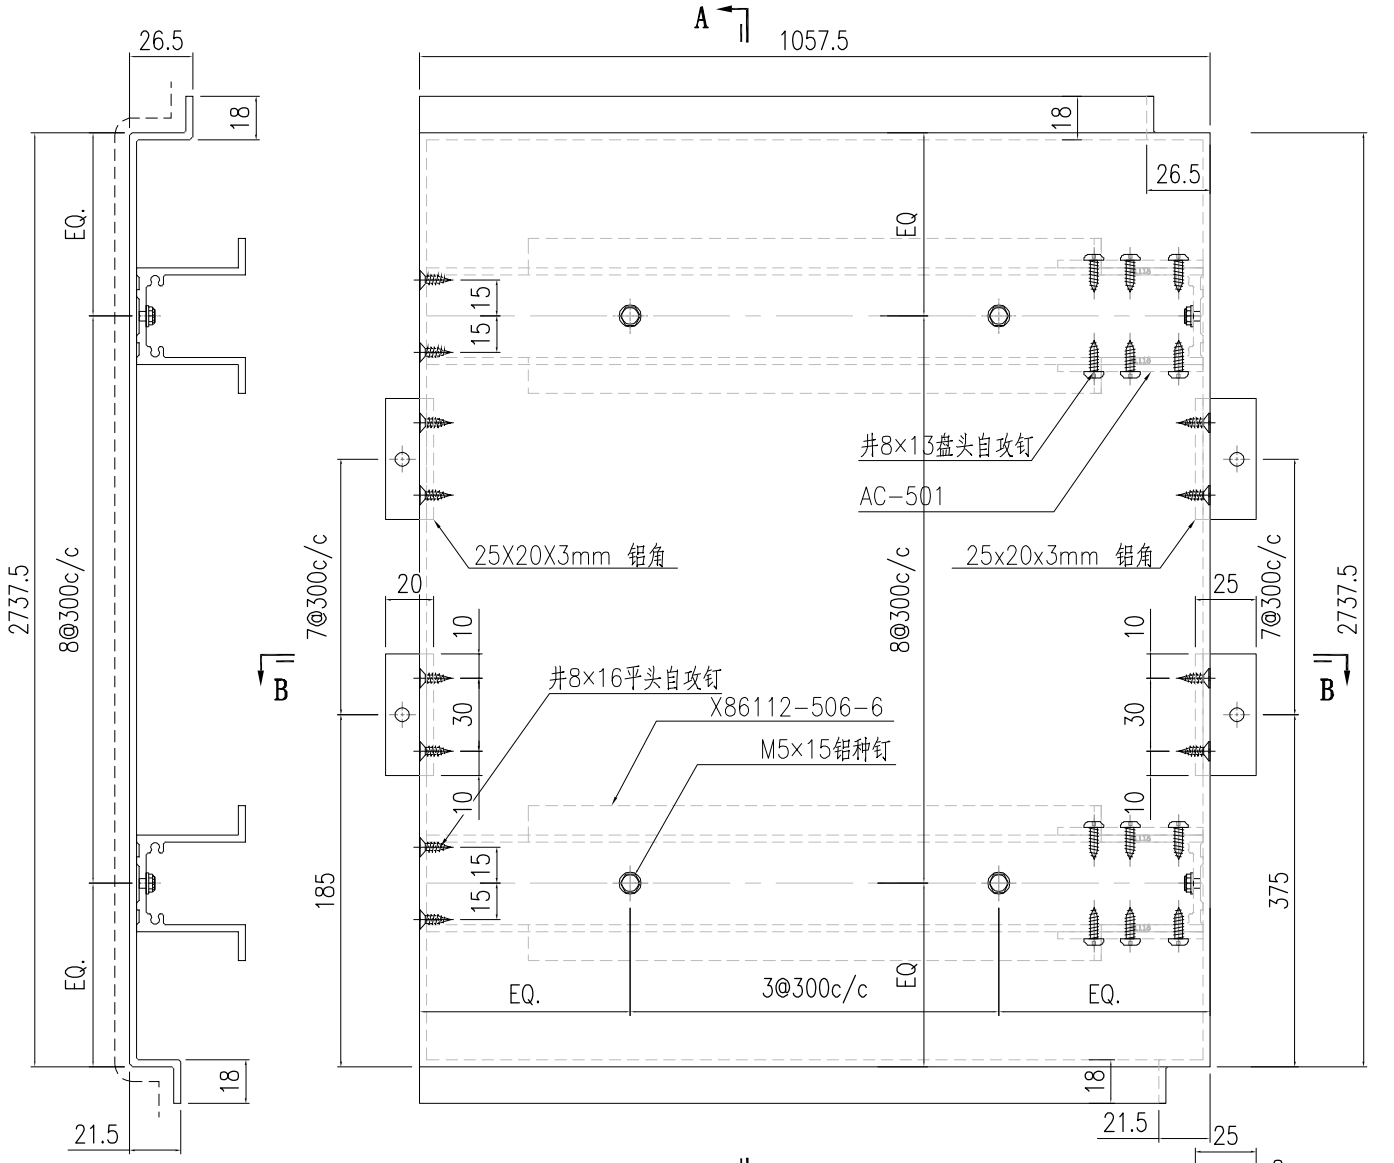

SECTION A-A

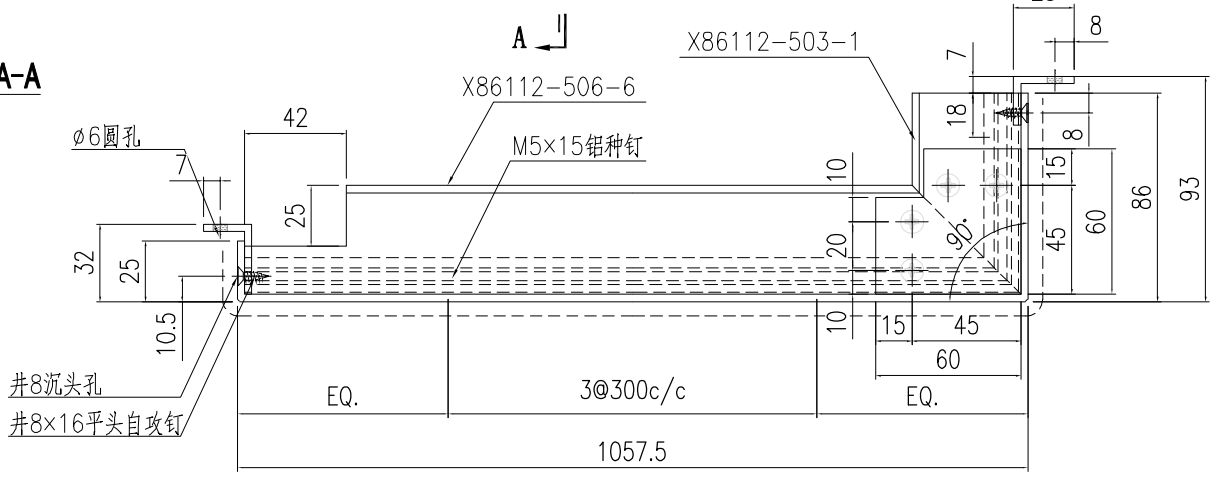


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
工程號	J857	類別		物料號	-									
地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-828									
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

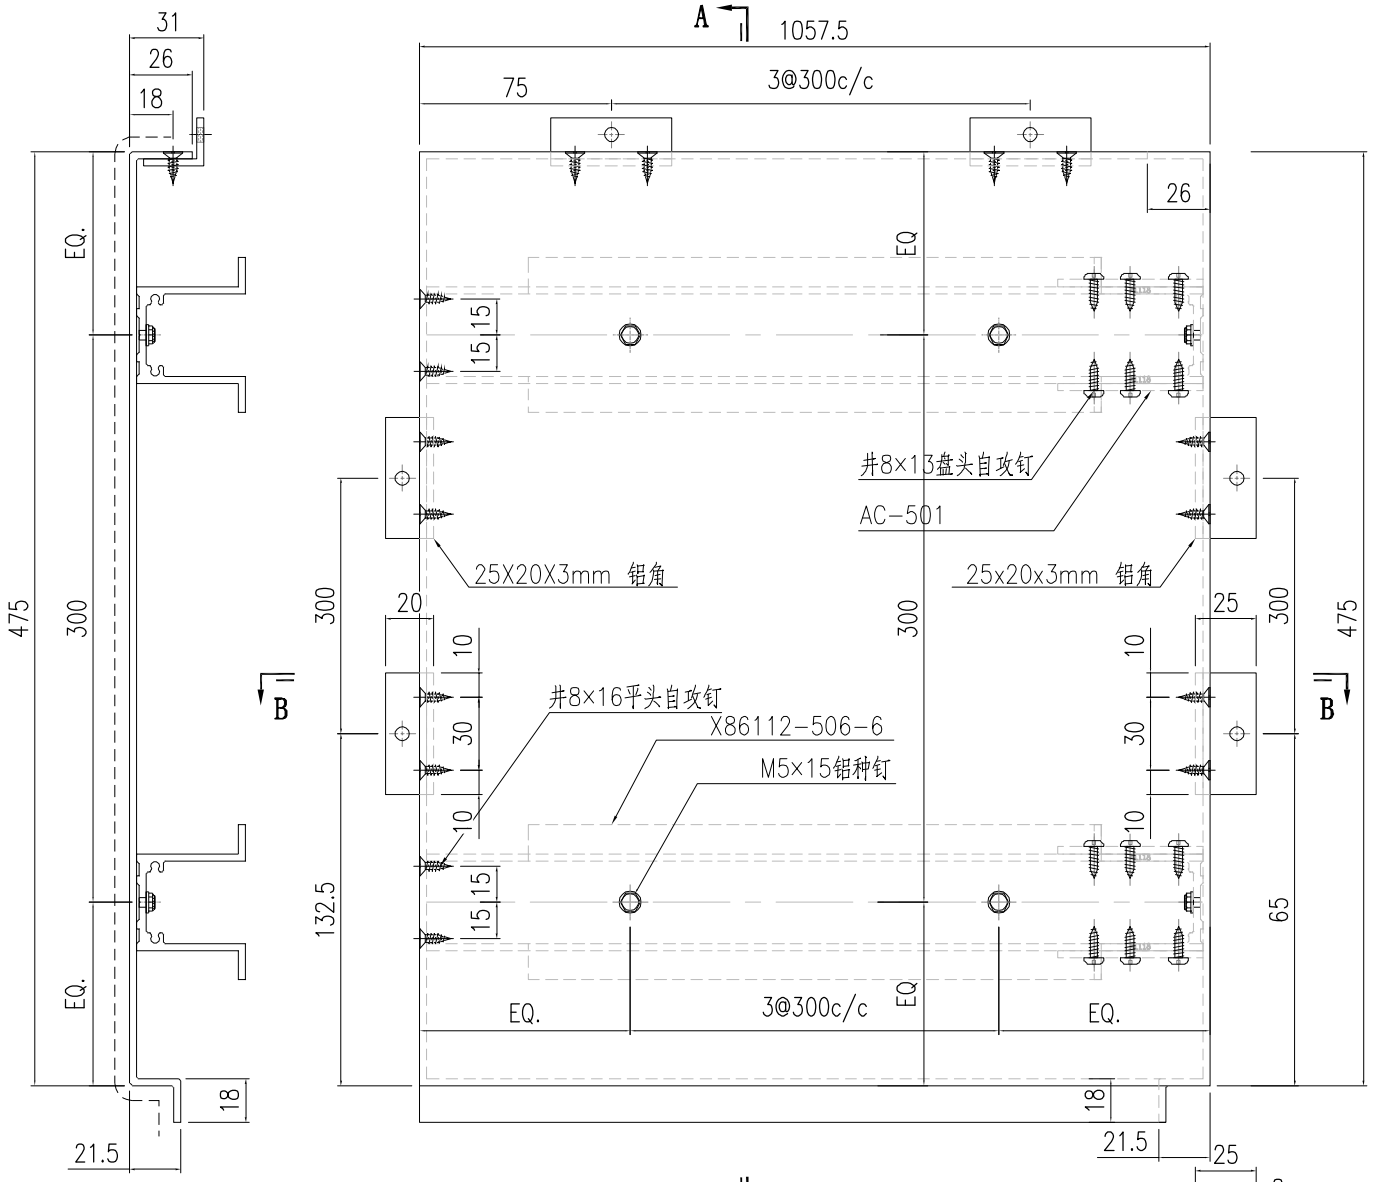

SECTION A-A

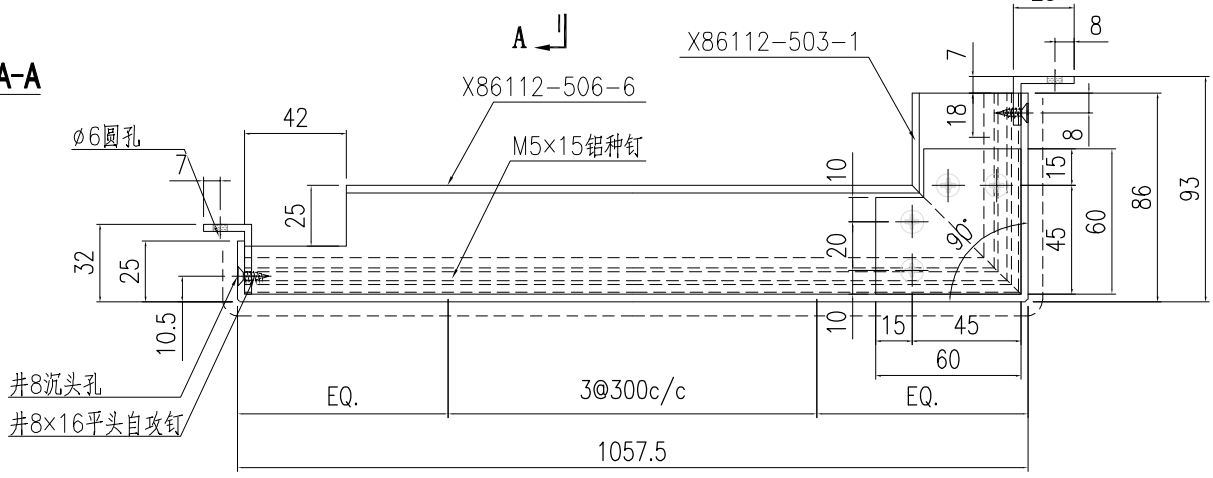


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-829
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

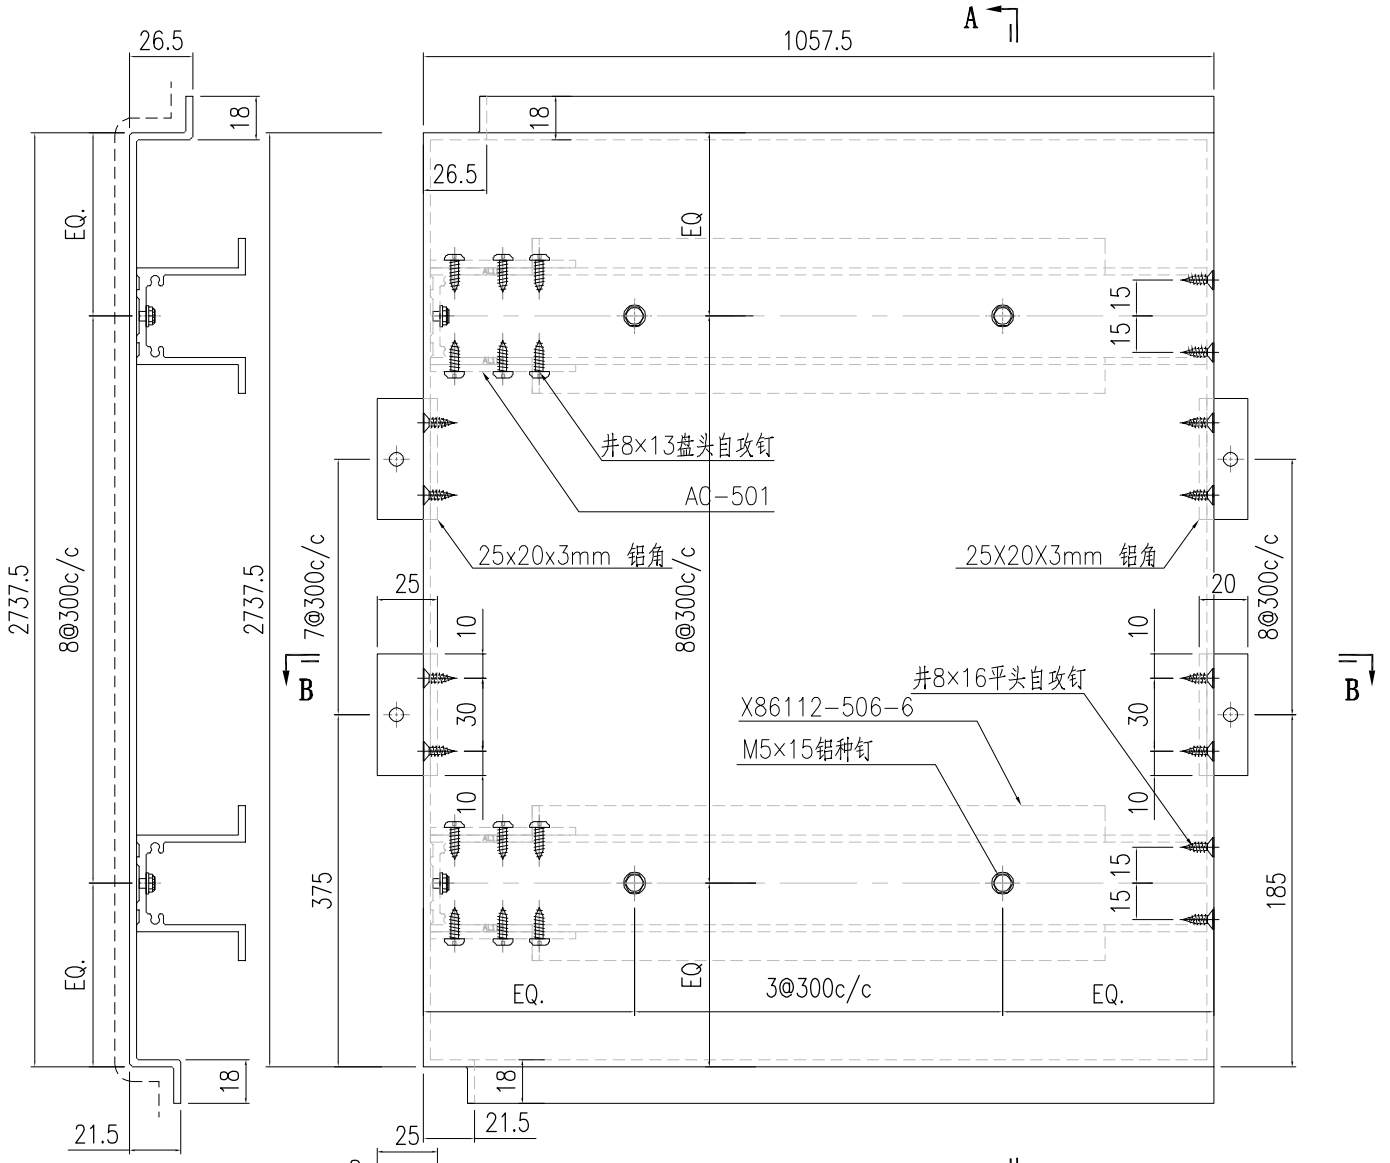

SECTION A-A

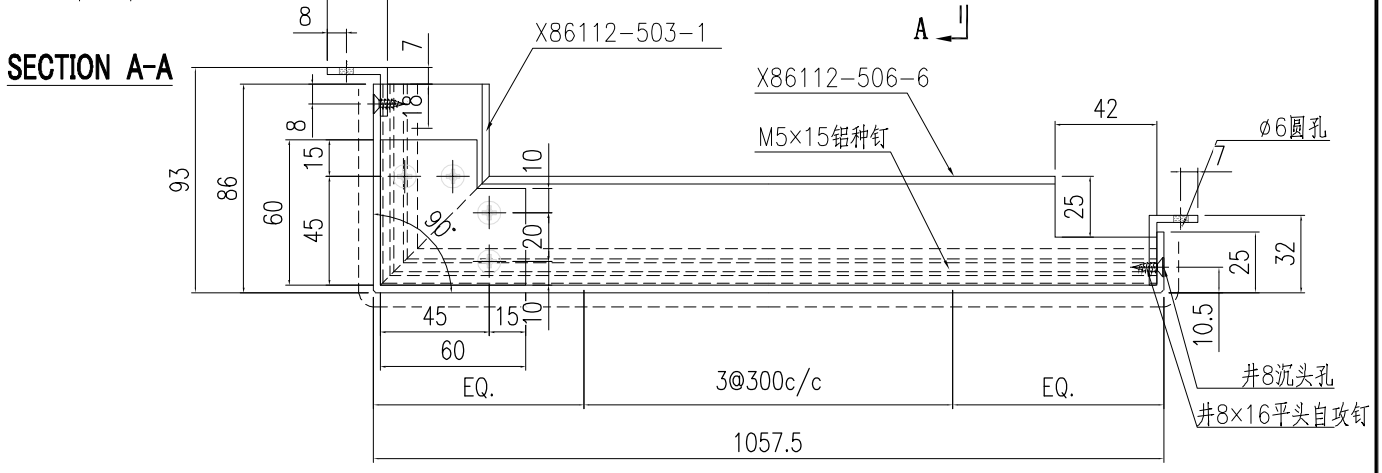


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-830		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

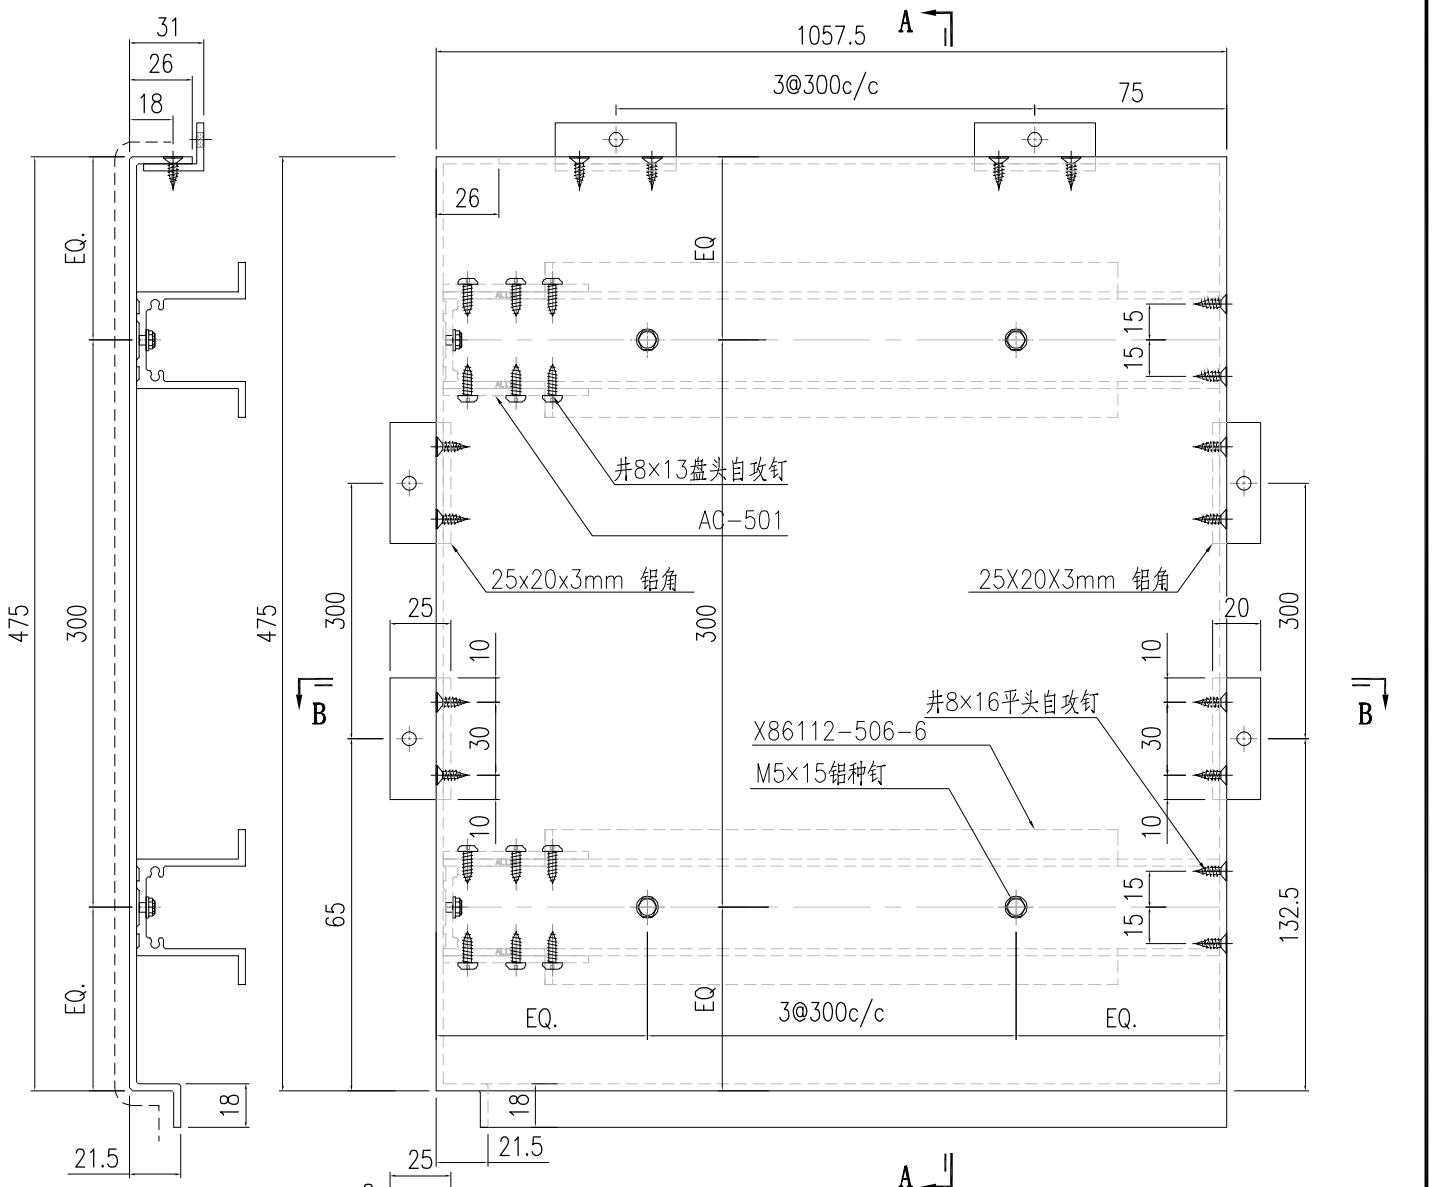

SECTION A-A

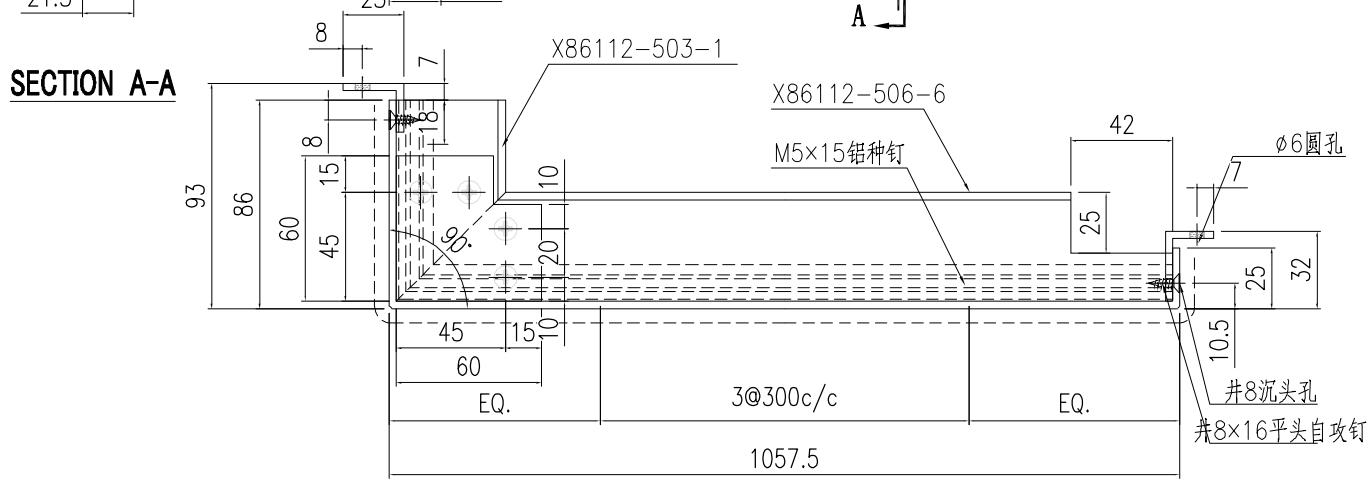


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-831		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

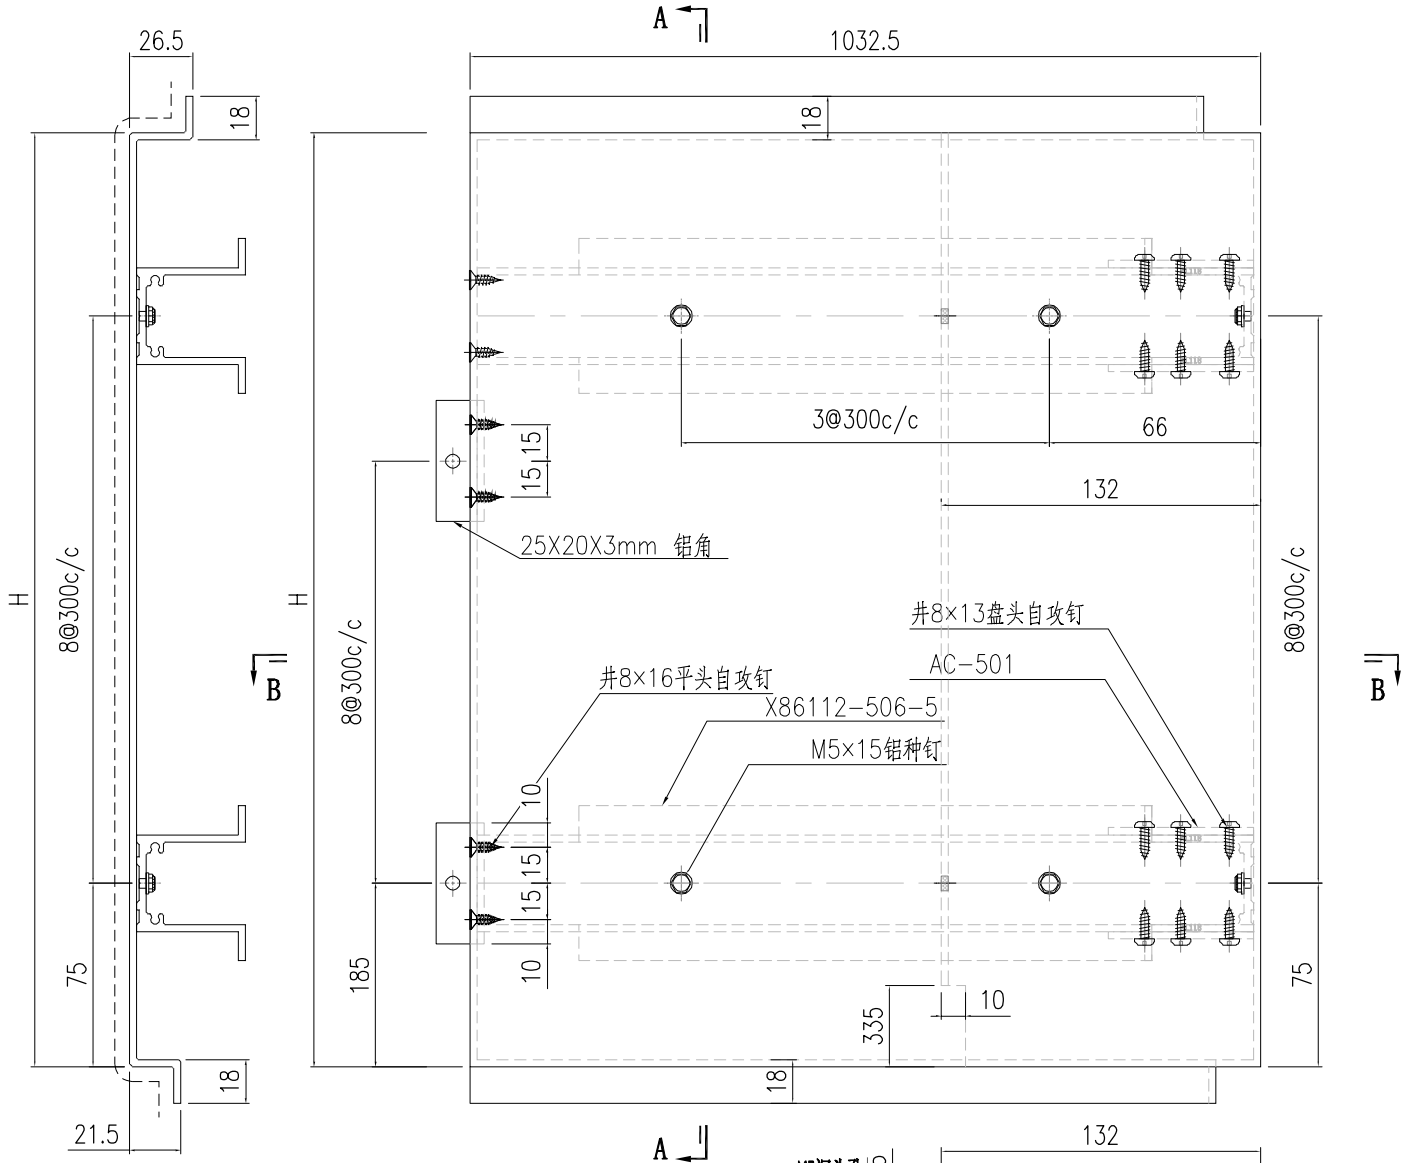

SECTION A-A

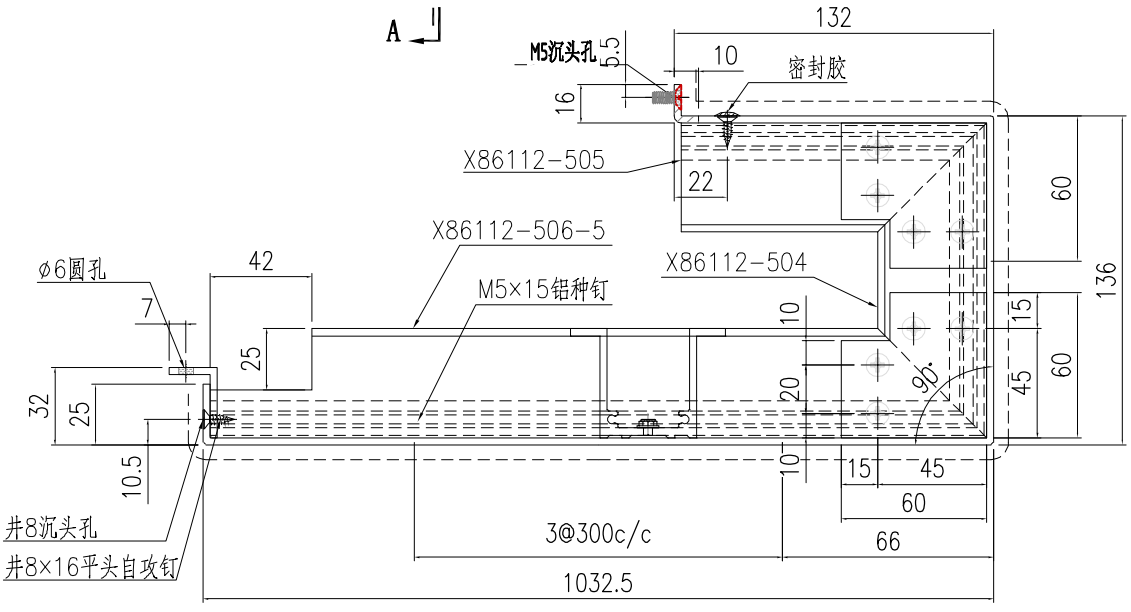


SECTION B-B




铝角码仔孔位示意

1	AC-825-1	2737.5
S/N	部件编号	H


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
工程號	J857	類別		物料號	-									
地盤	啟德6552	制圖	陳梓豪 20221206	圖號	AC-832									
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

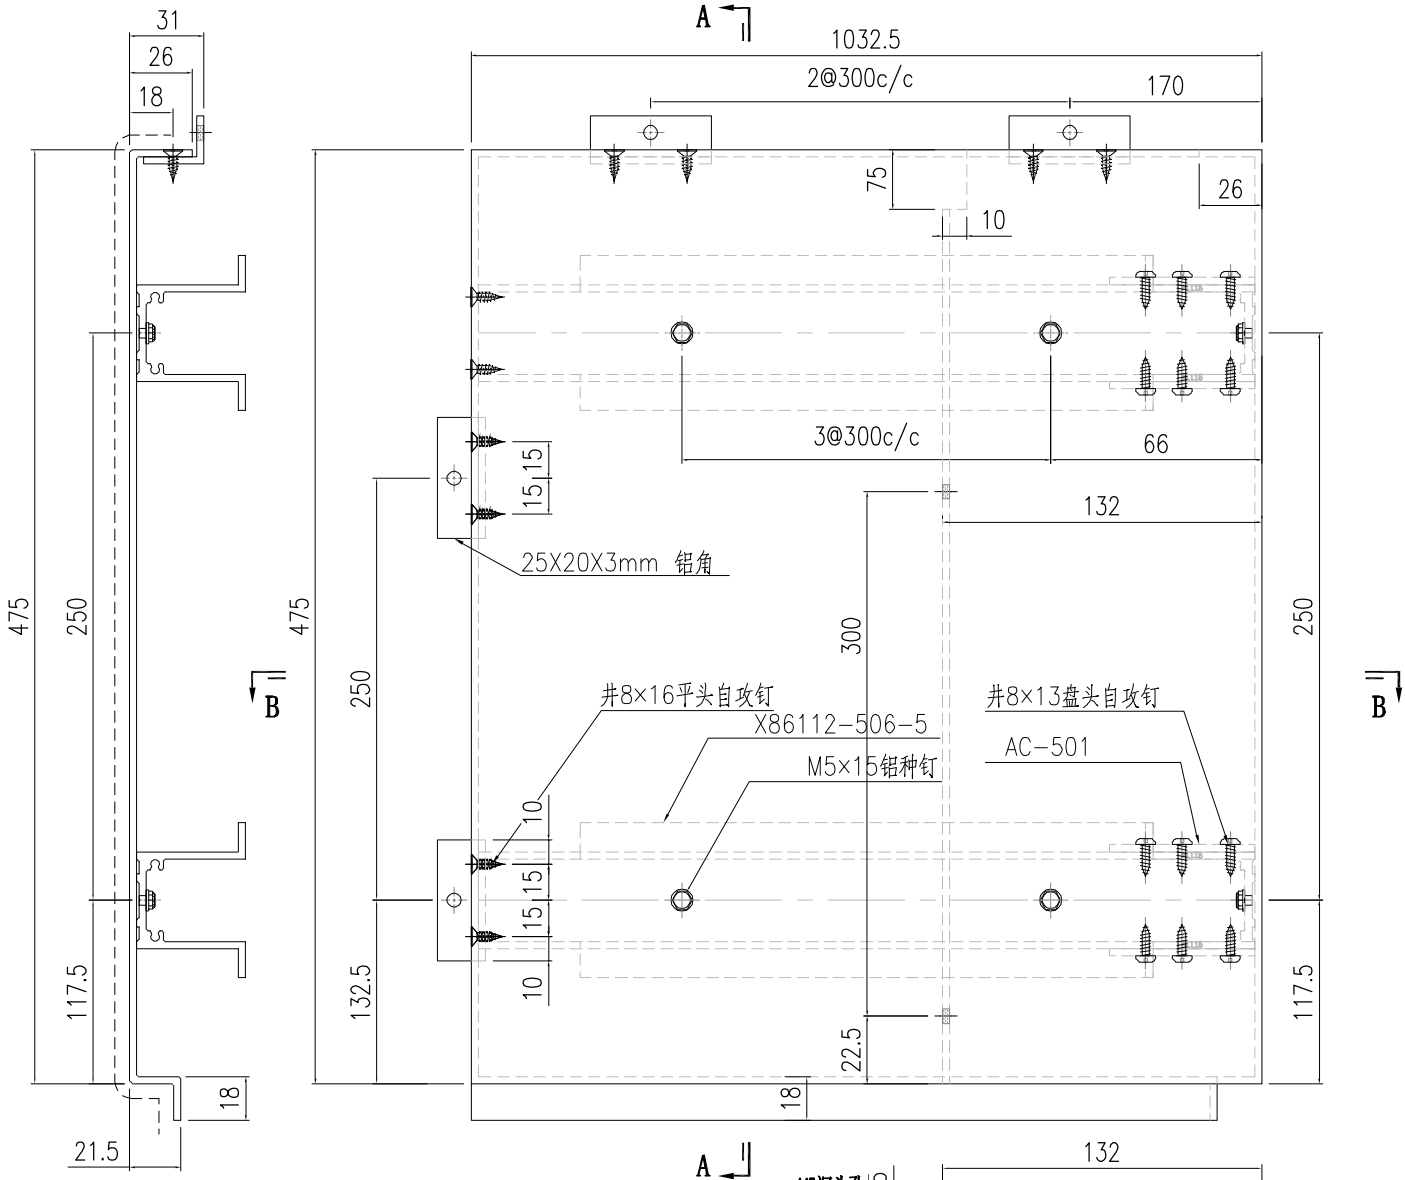

SECTION A-A

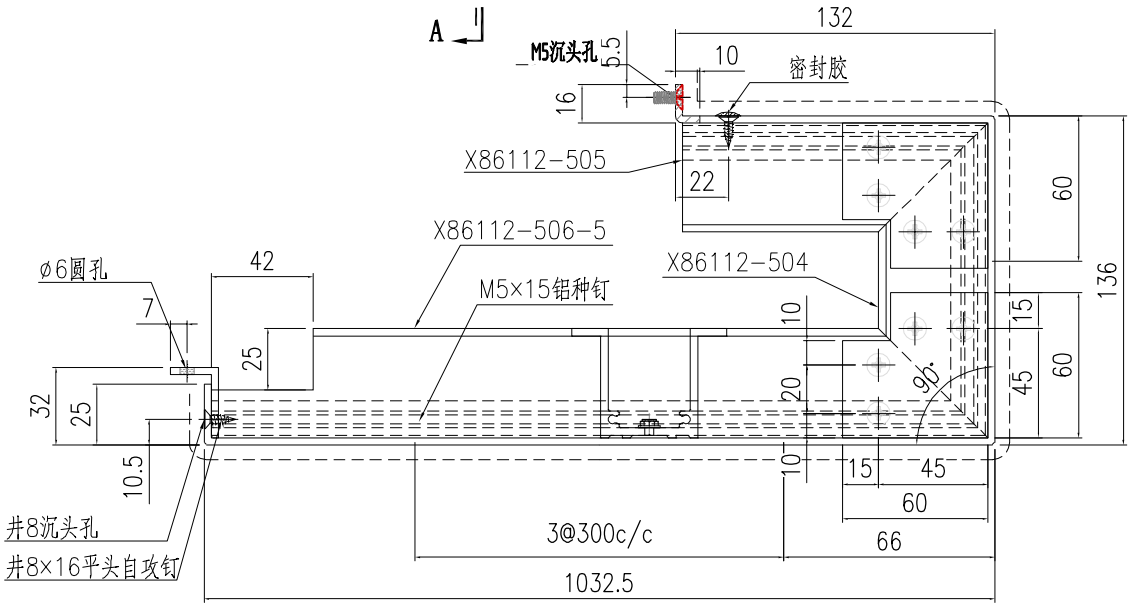


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-833
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

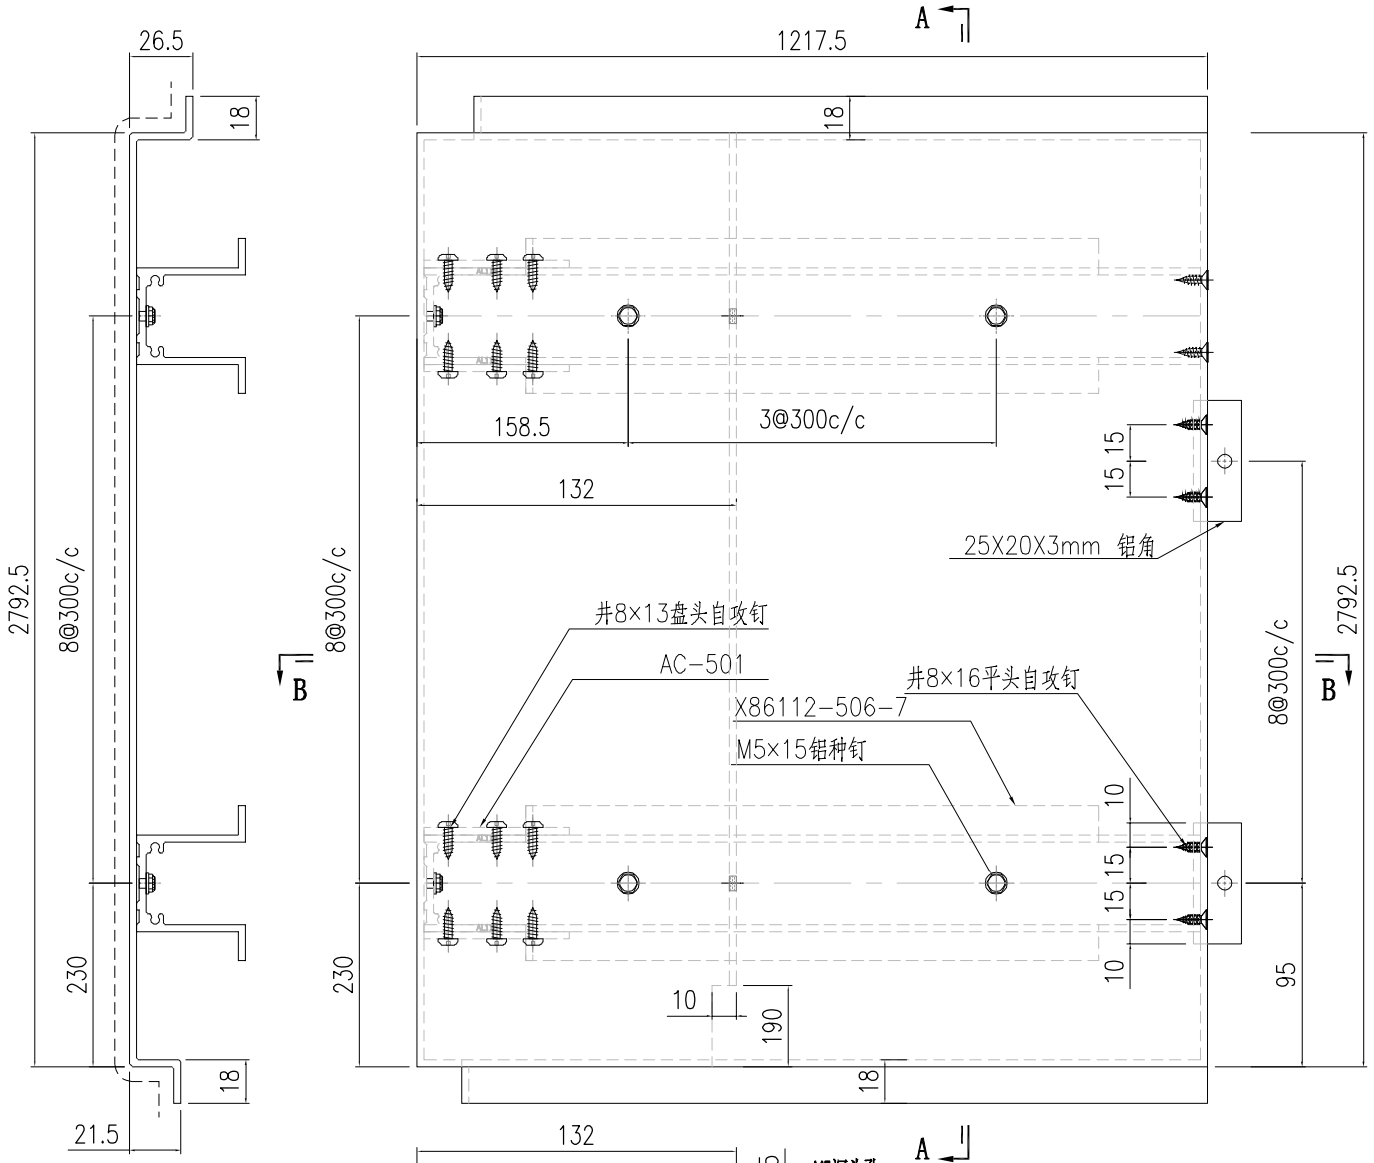

SECTION A-A

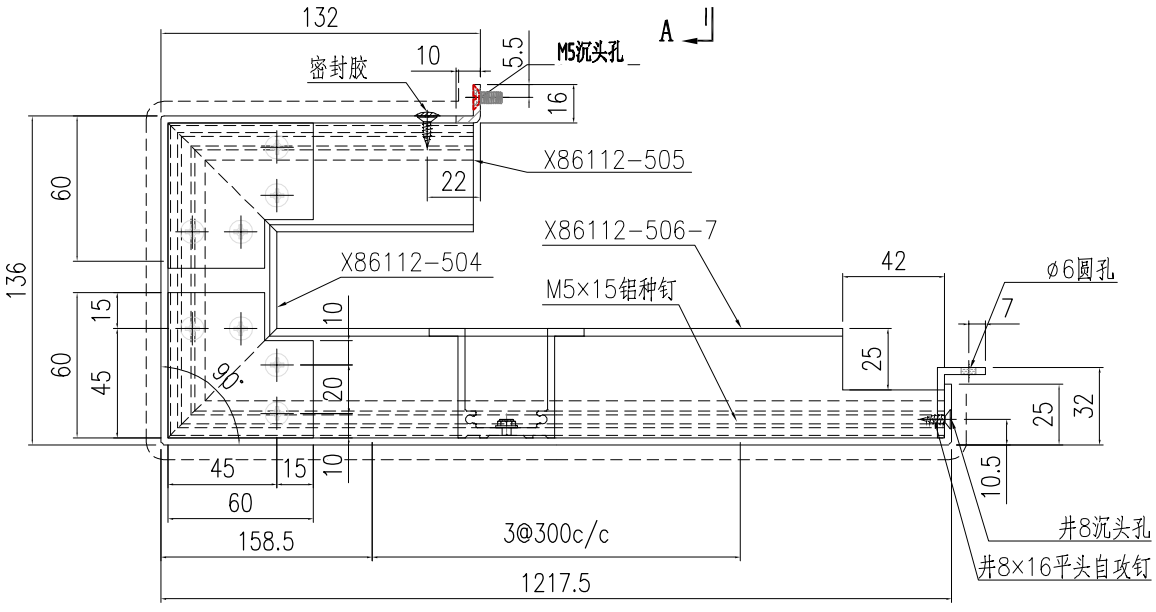


SECTION B-B




铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-834
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

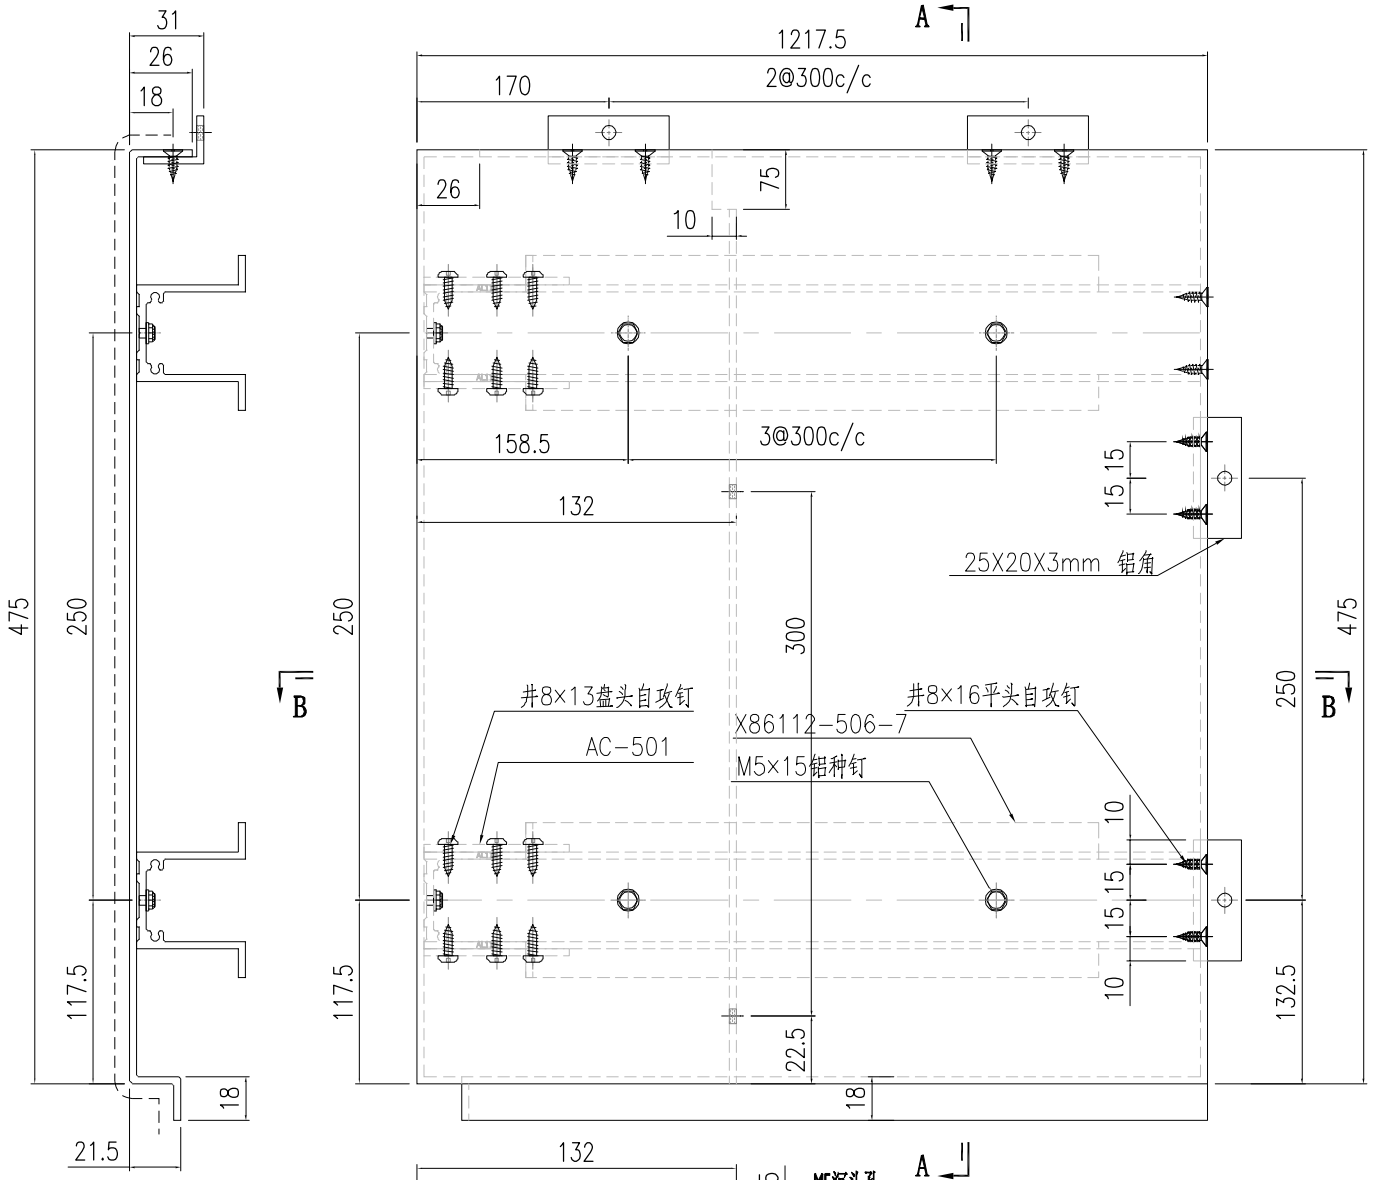

SECTION A-A

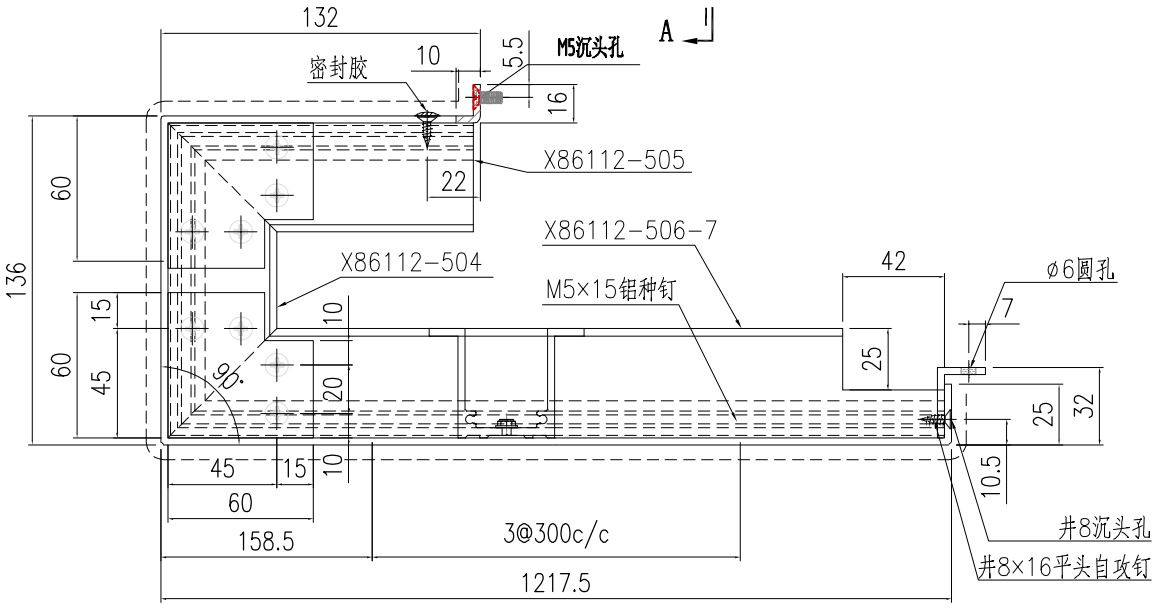



SECTION B-B



铝角码仔孔位示意


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-835		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

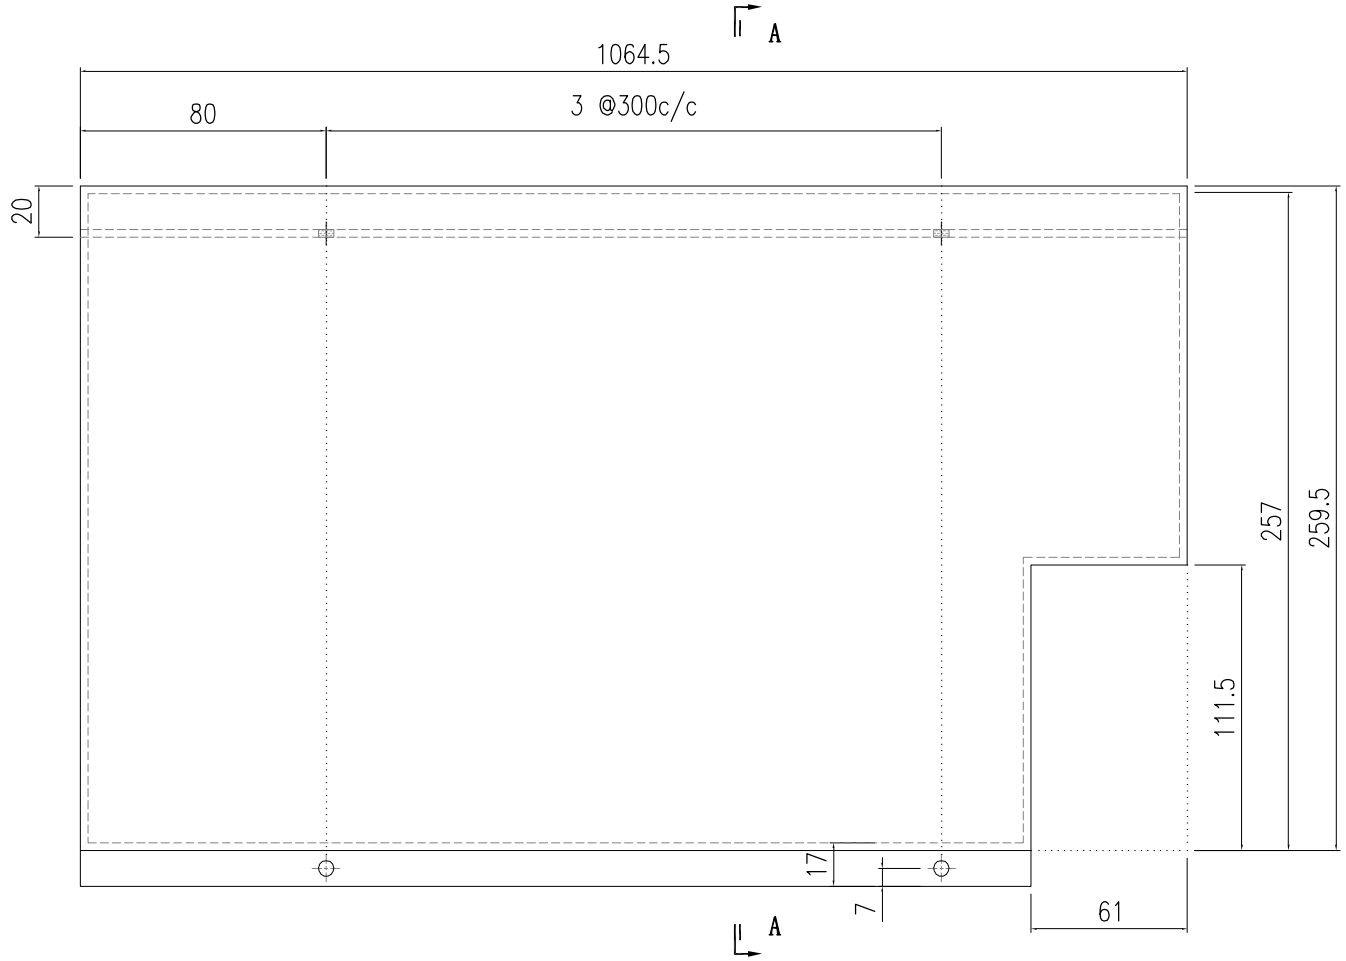


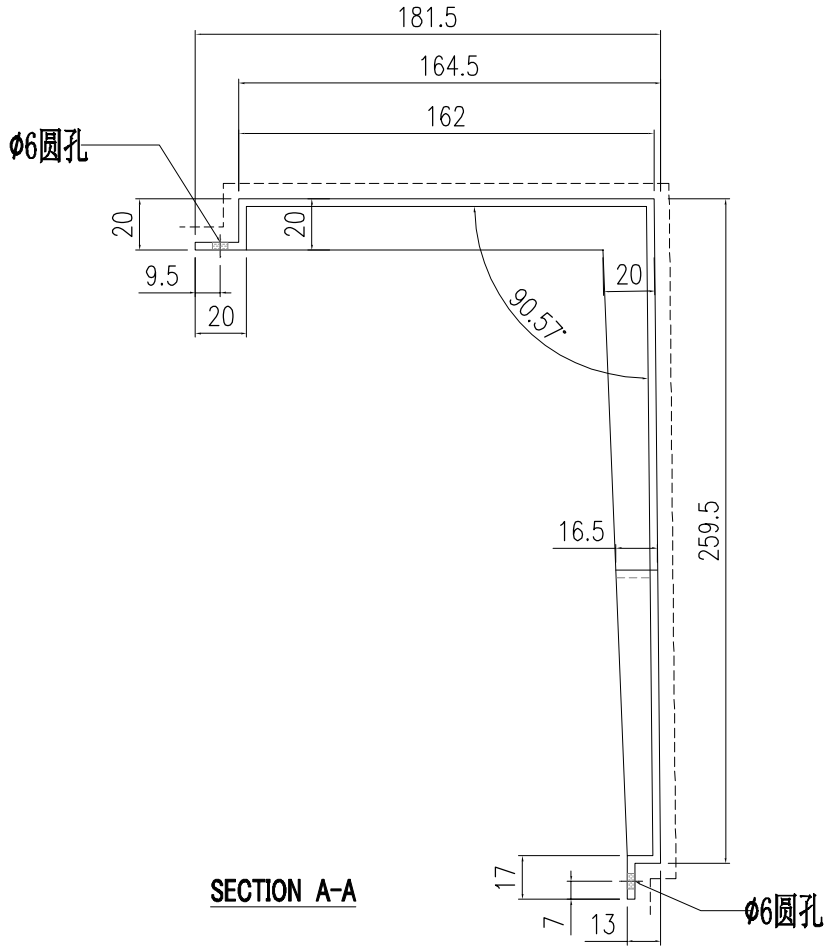

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-836	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

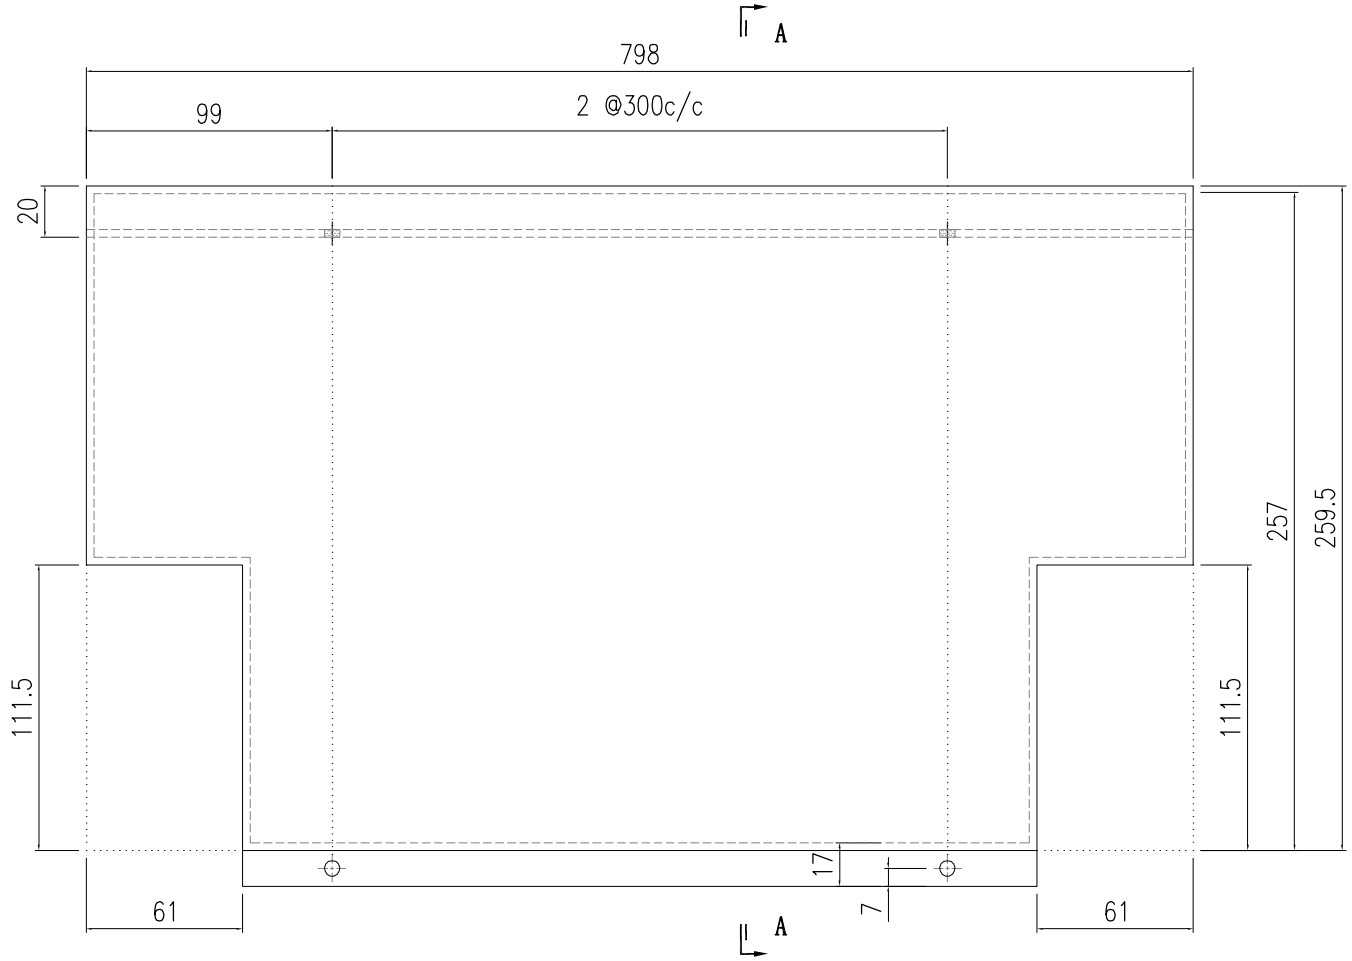


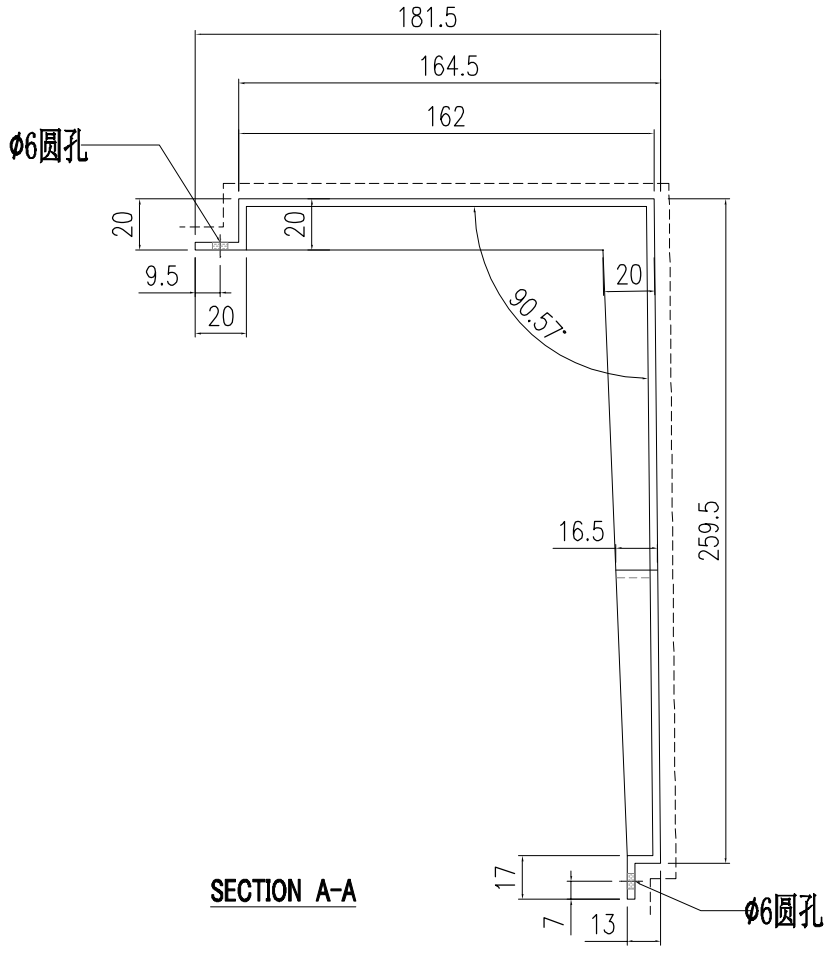

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-837		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

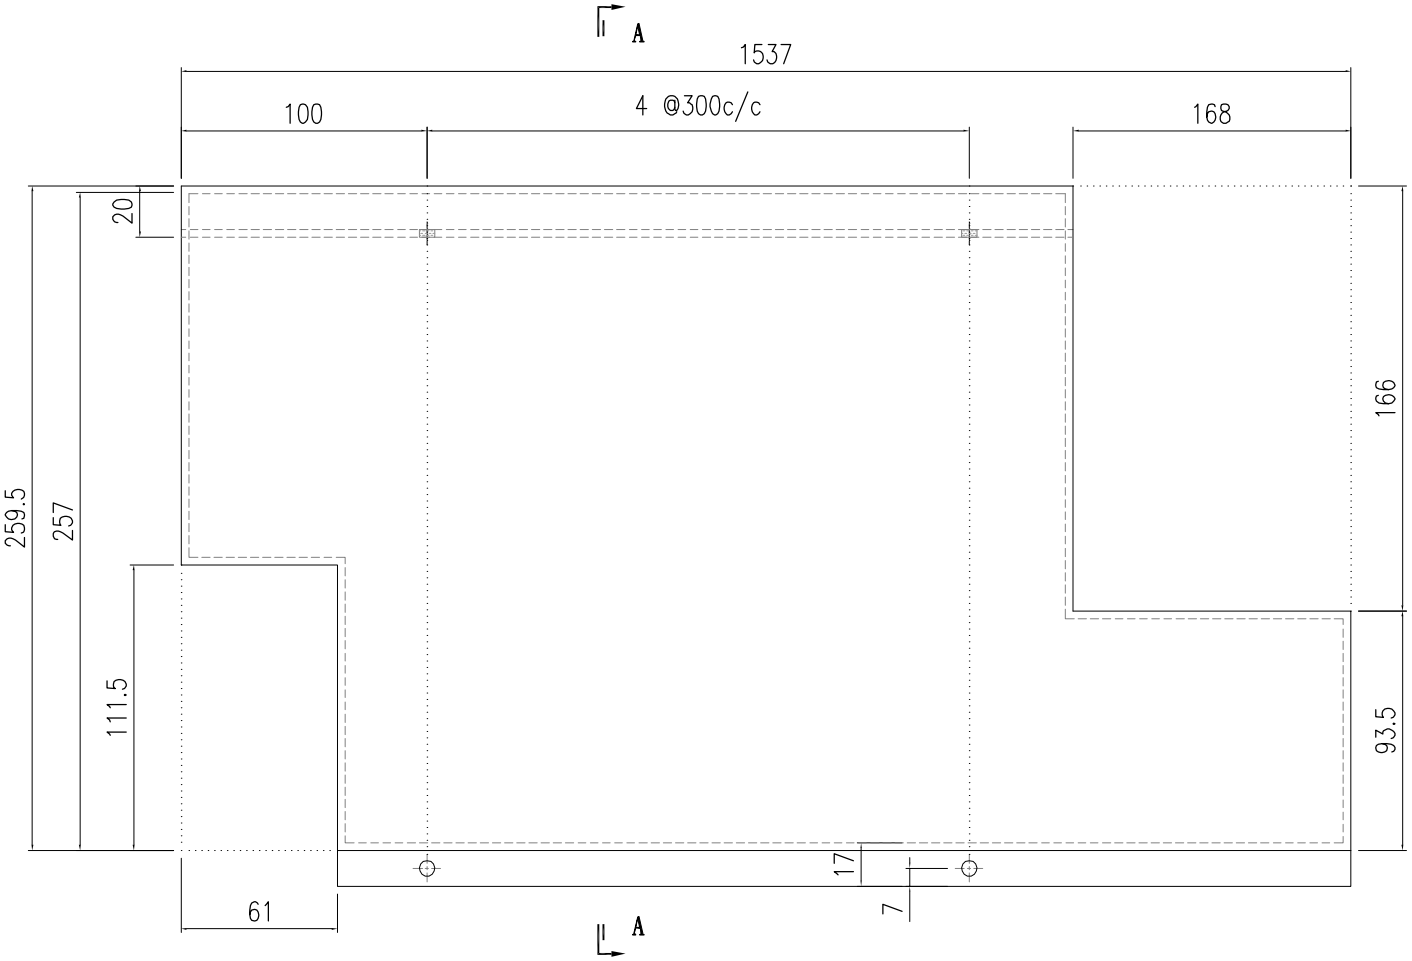


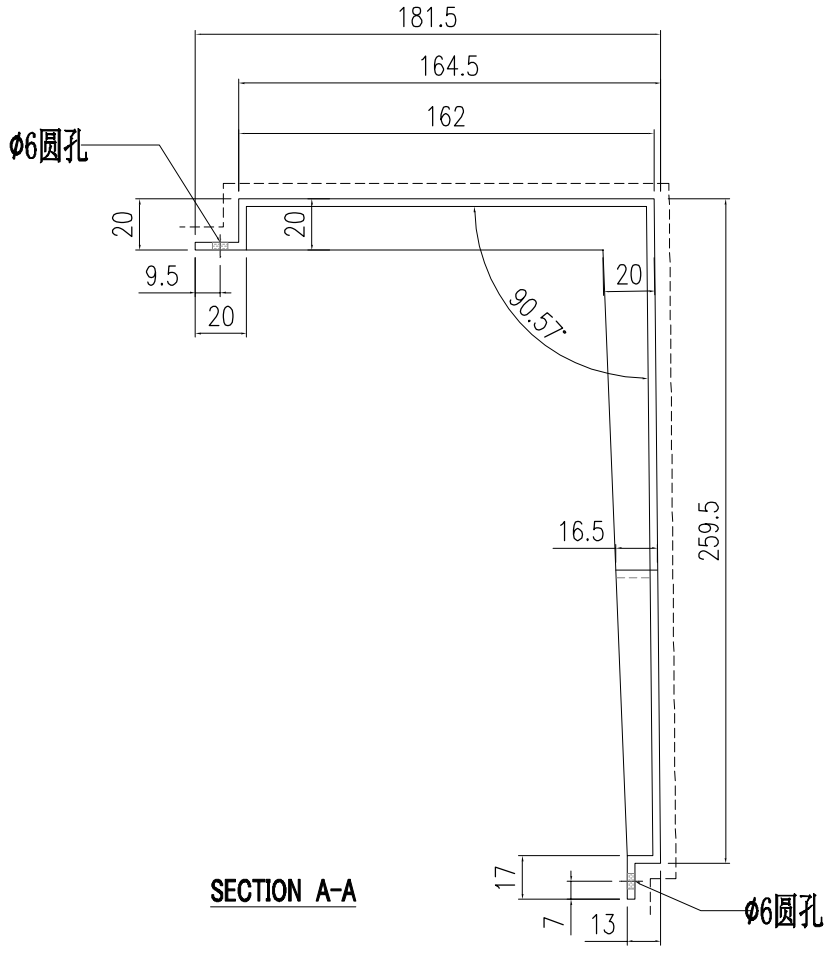

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-839		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	防水铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料颜色	鉻化				材料	1.5mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

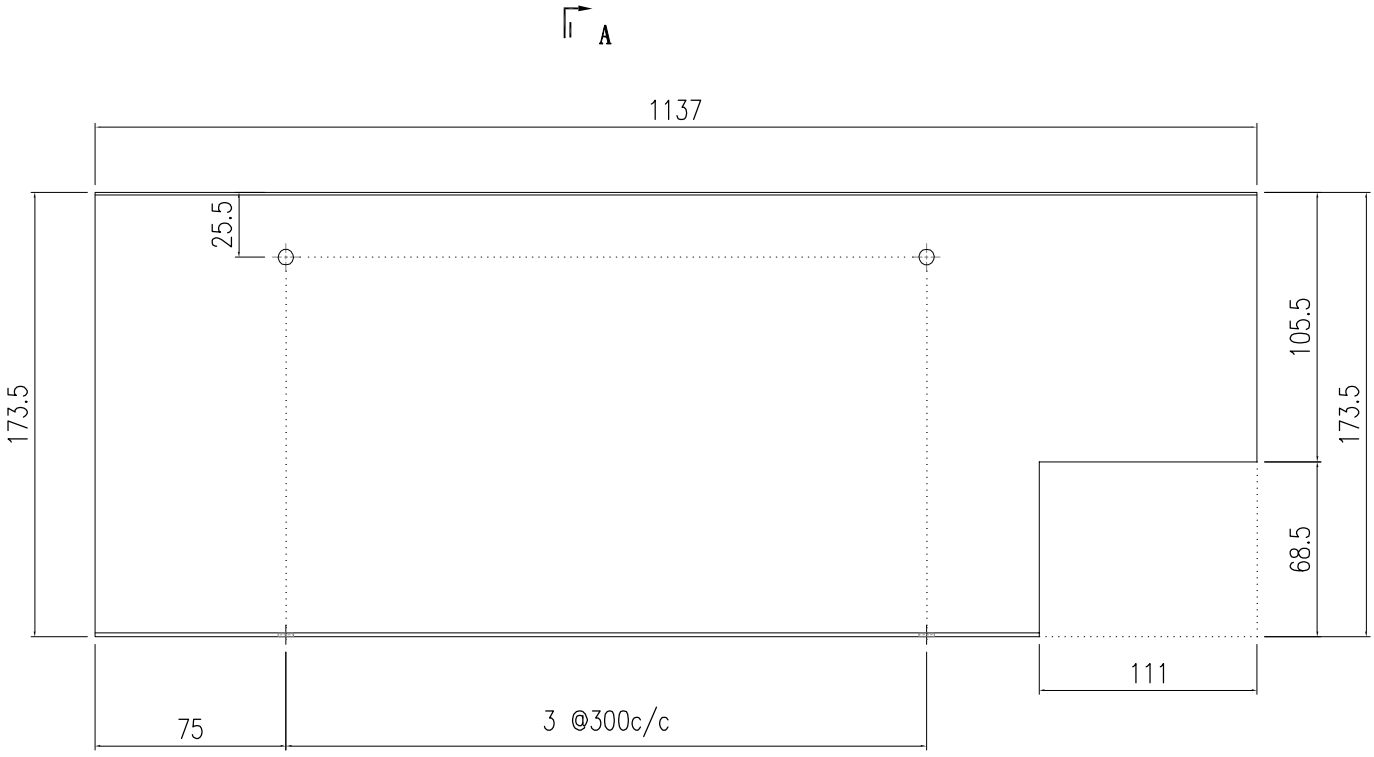


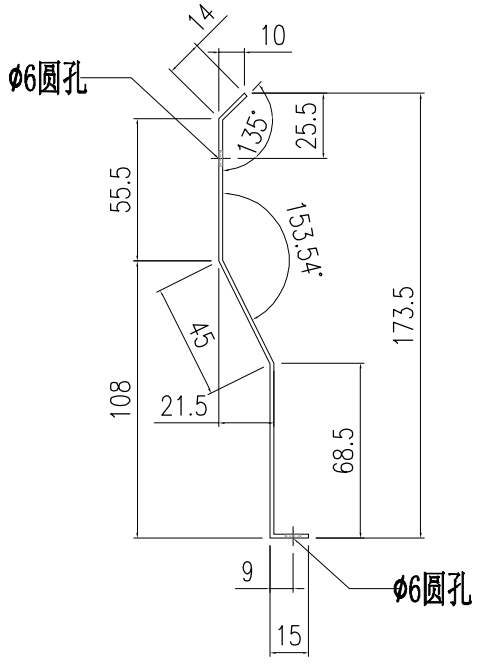

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-840		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	防水铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料颜色	鉻化			材料	1.5mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

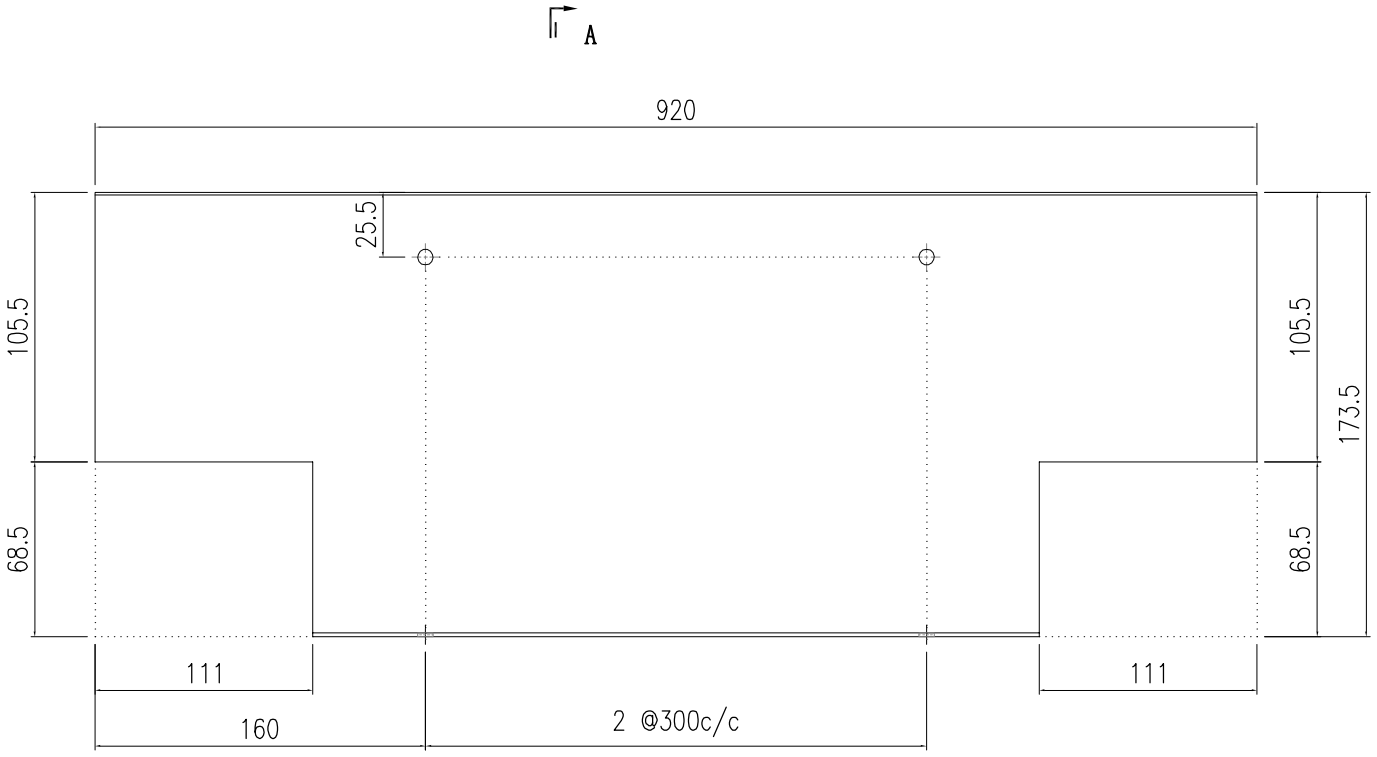


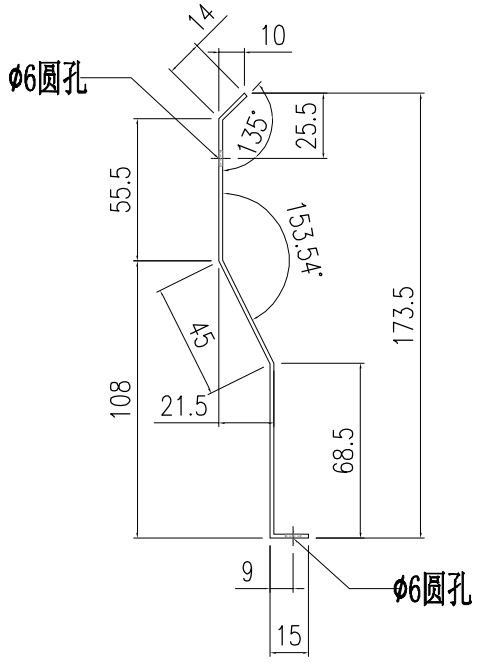

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-841		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	防水铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	鉻化				材料	1.5mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

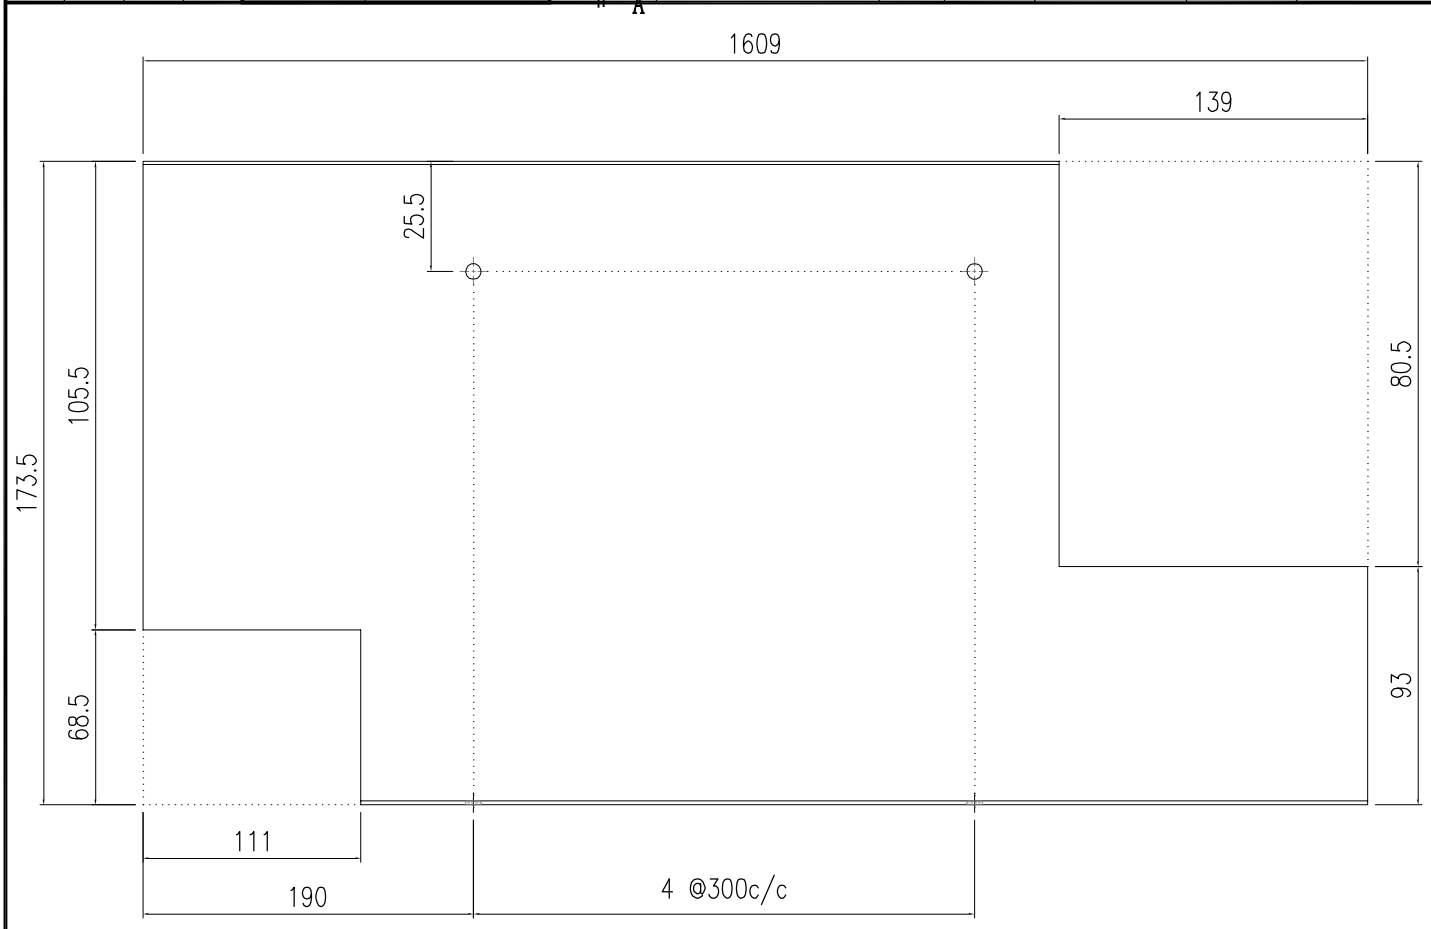


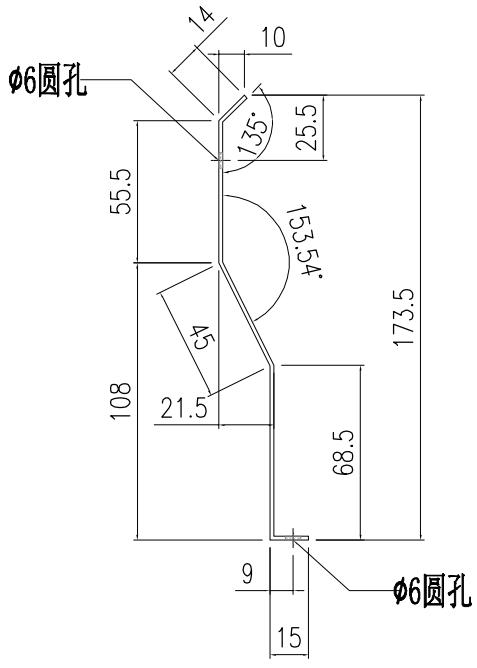

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-842		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	防水铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	鉻化			材料	1.5mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

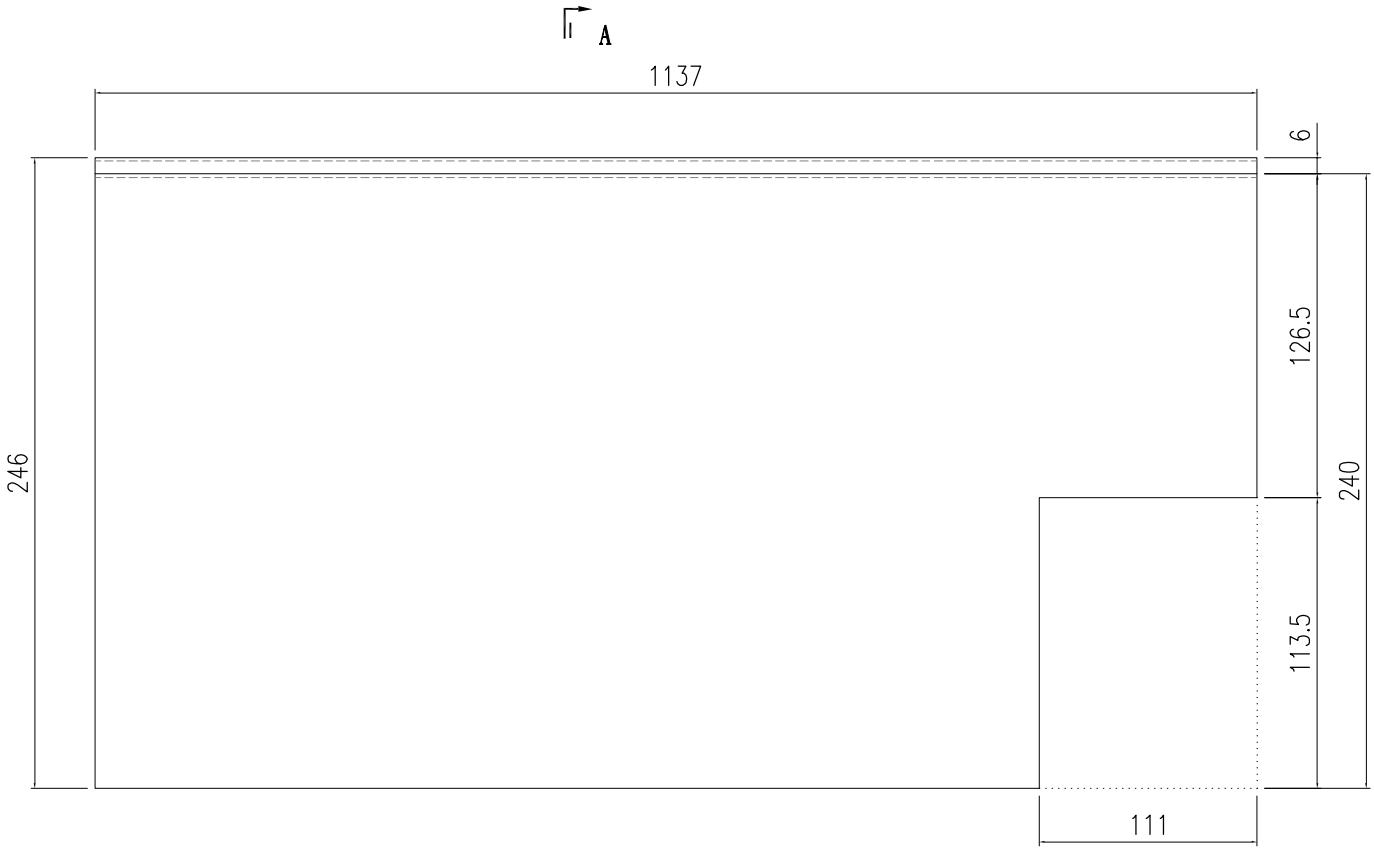


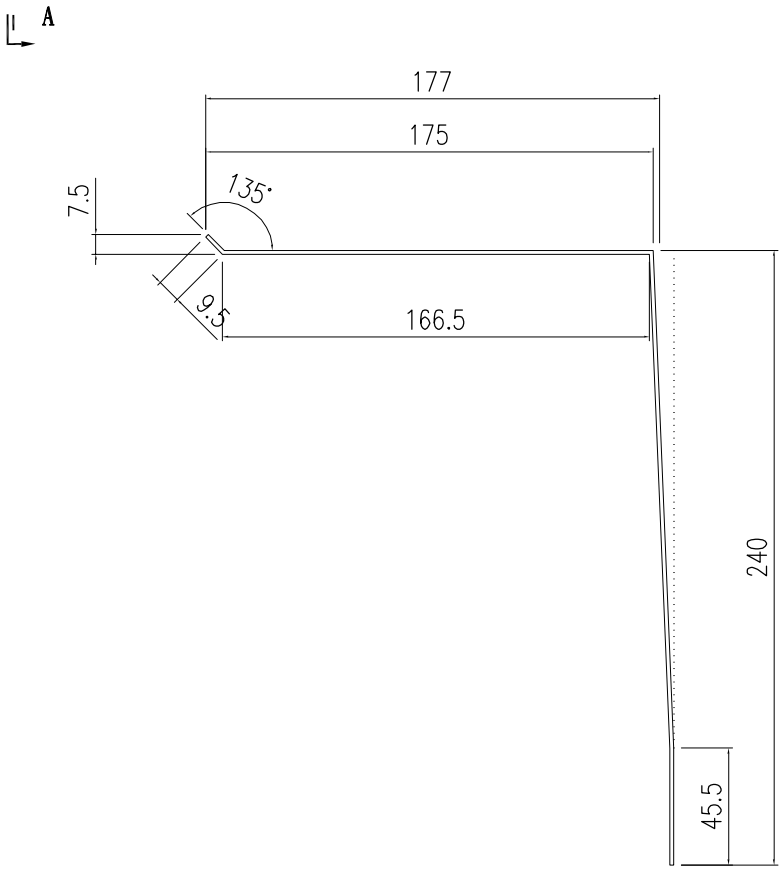

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-843		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	防水铝板	復核	練松文	20221209	數量	1		
日期	-	-	-	材料顏色	鉻化				材料	1.5mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

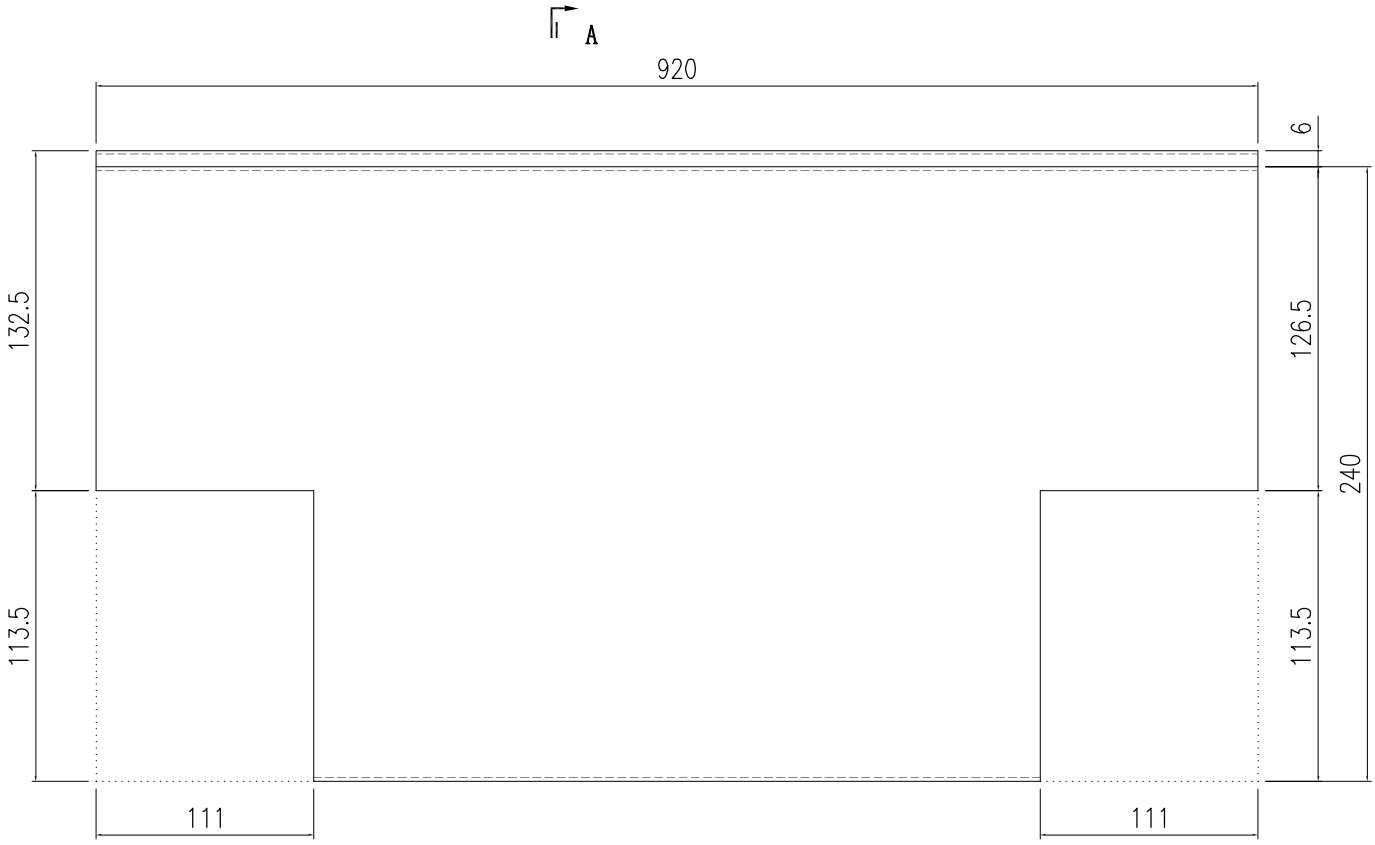


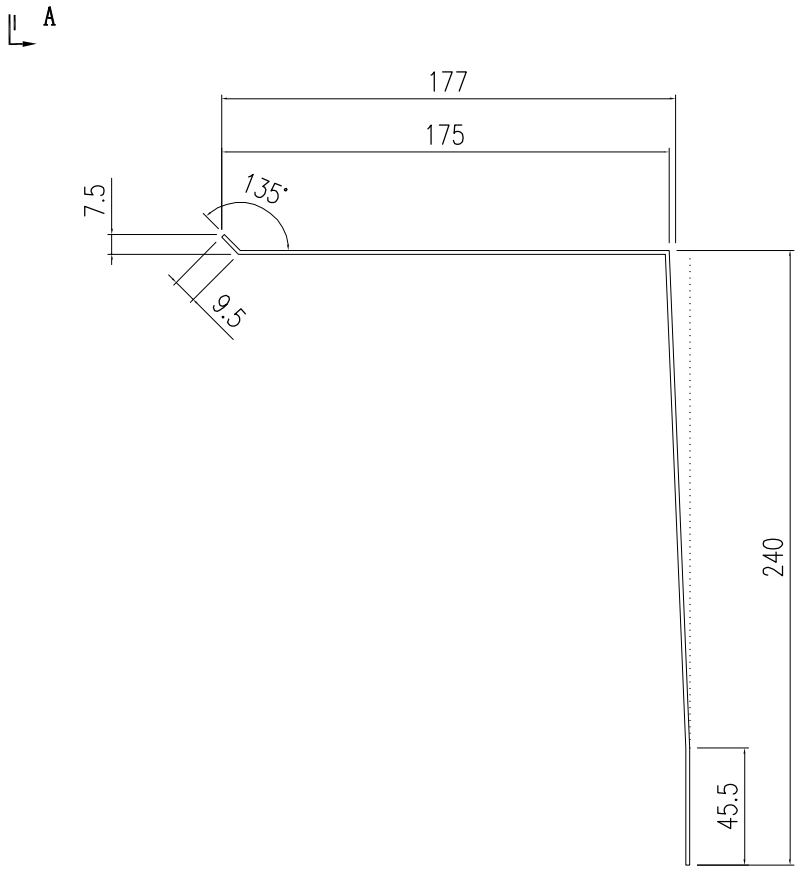

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-844		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	防水铝板	復核	練松文	20221209	數量	1		
日期	-	-	-	材料顏色	鉻化				材料	1.5mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

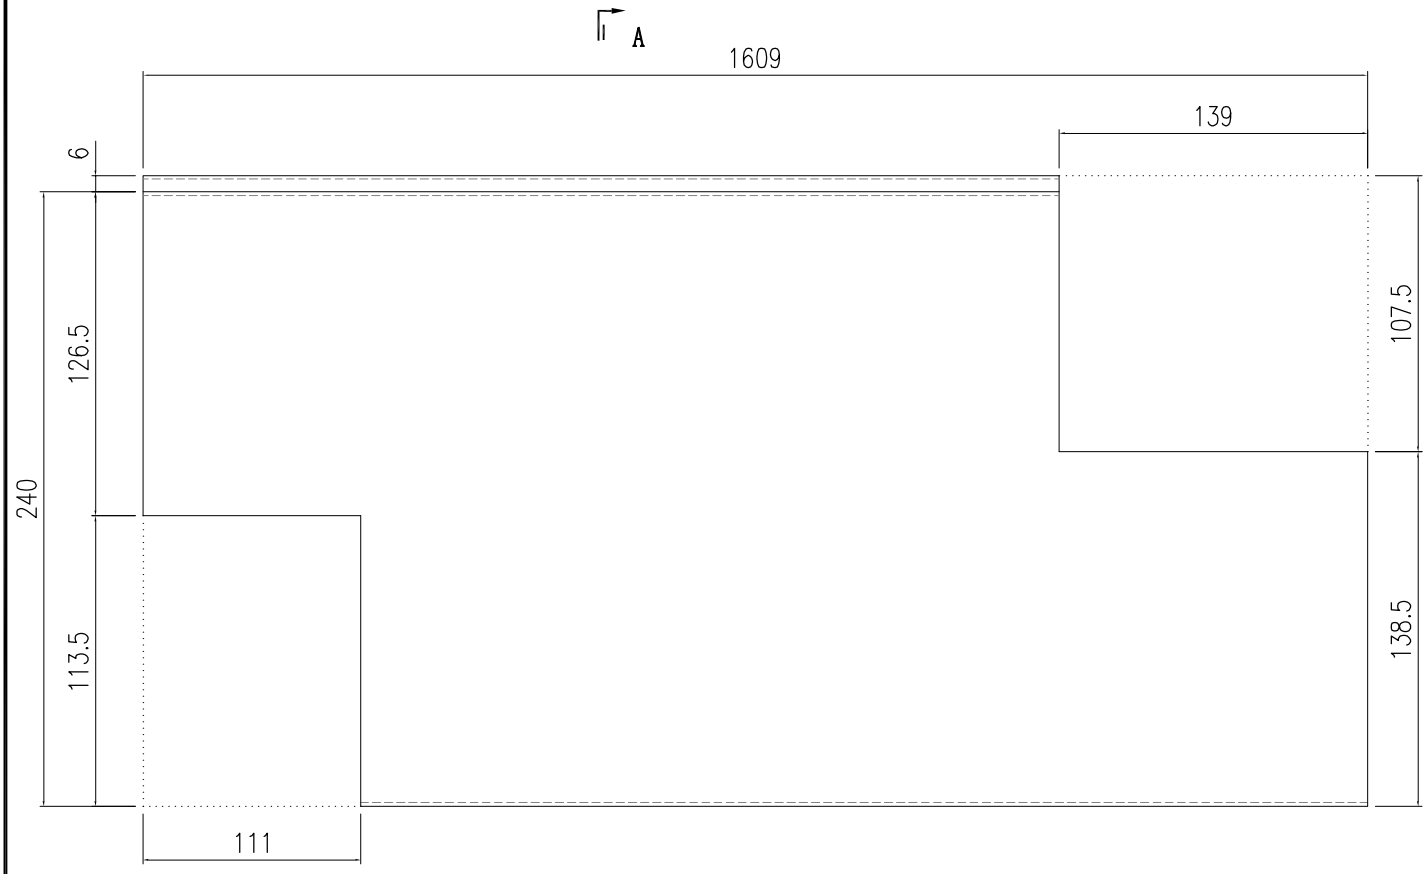


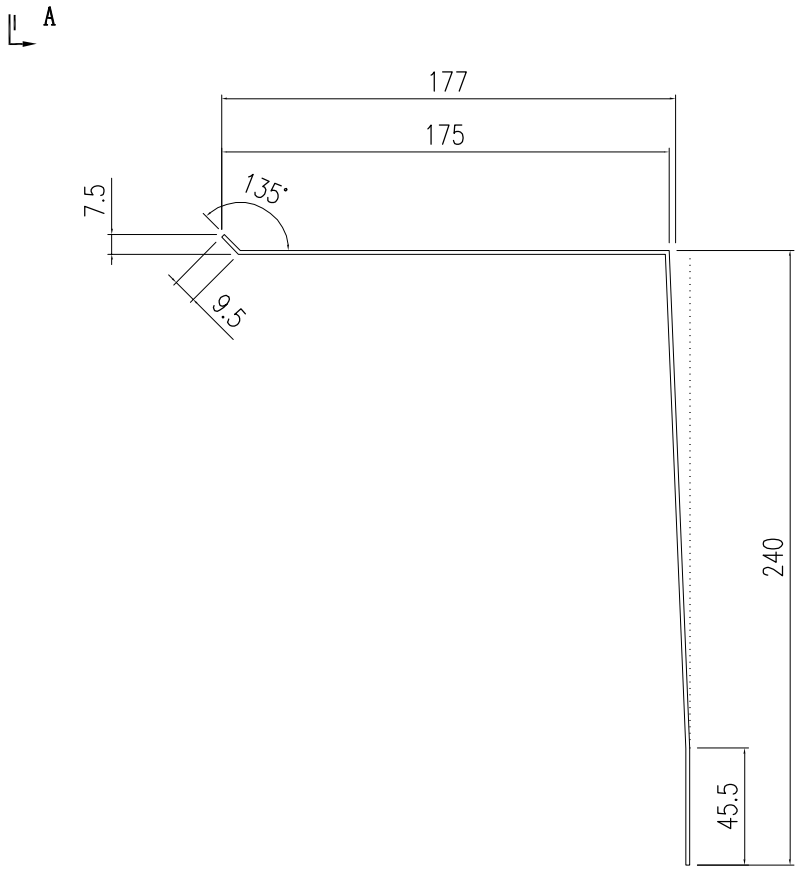

SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-845		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

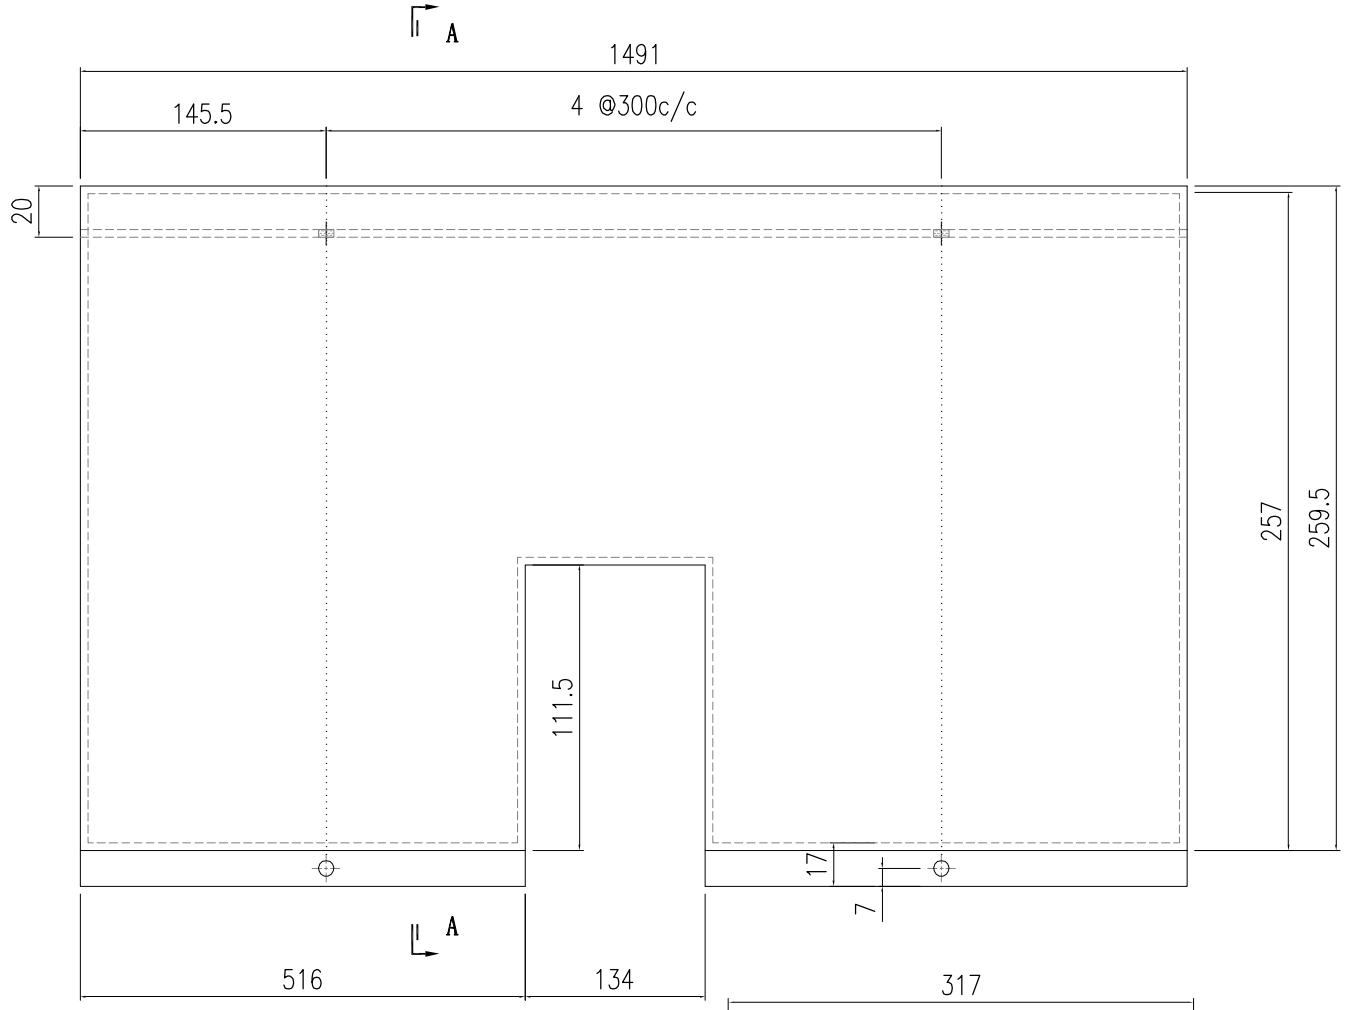


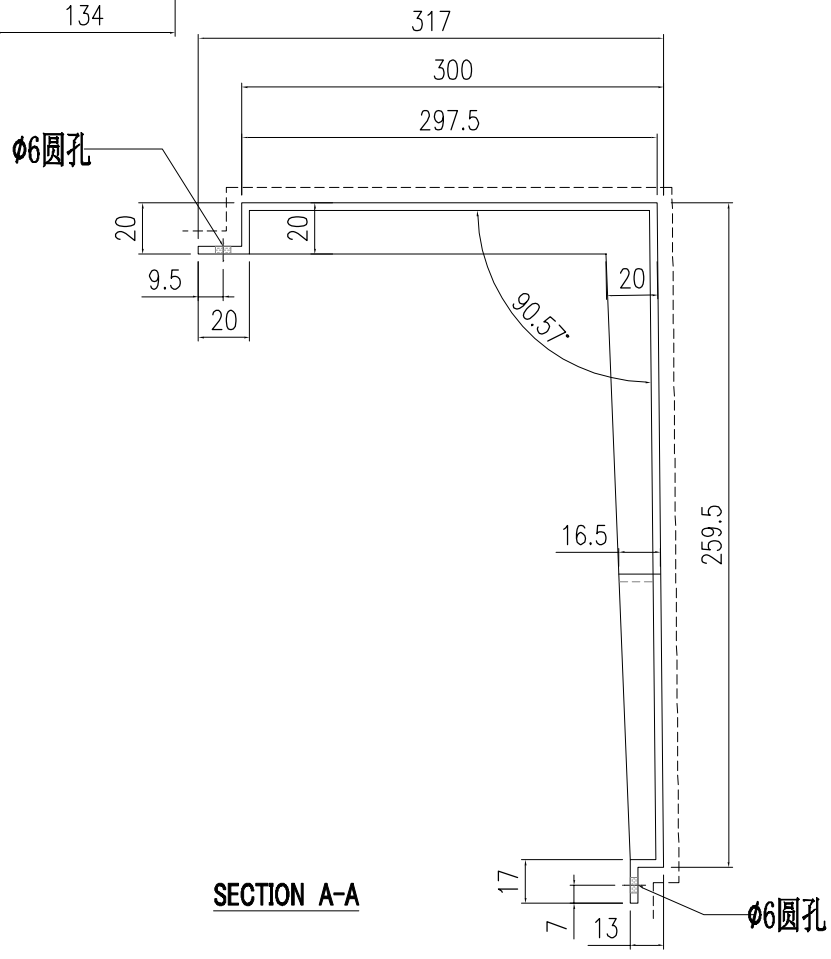


SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
工程號	J857	類別		物料號	-												
地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-846											
图纸名称	防水铝板	復核	練松文	20221209	數量	1											
材料	1.5mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)										


修改	-	-	-	採用	工廠	-	地盤	✓
日期	-	-	-	材料顏色	鉻化			

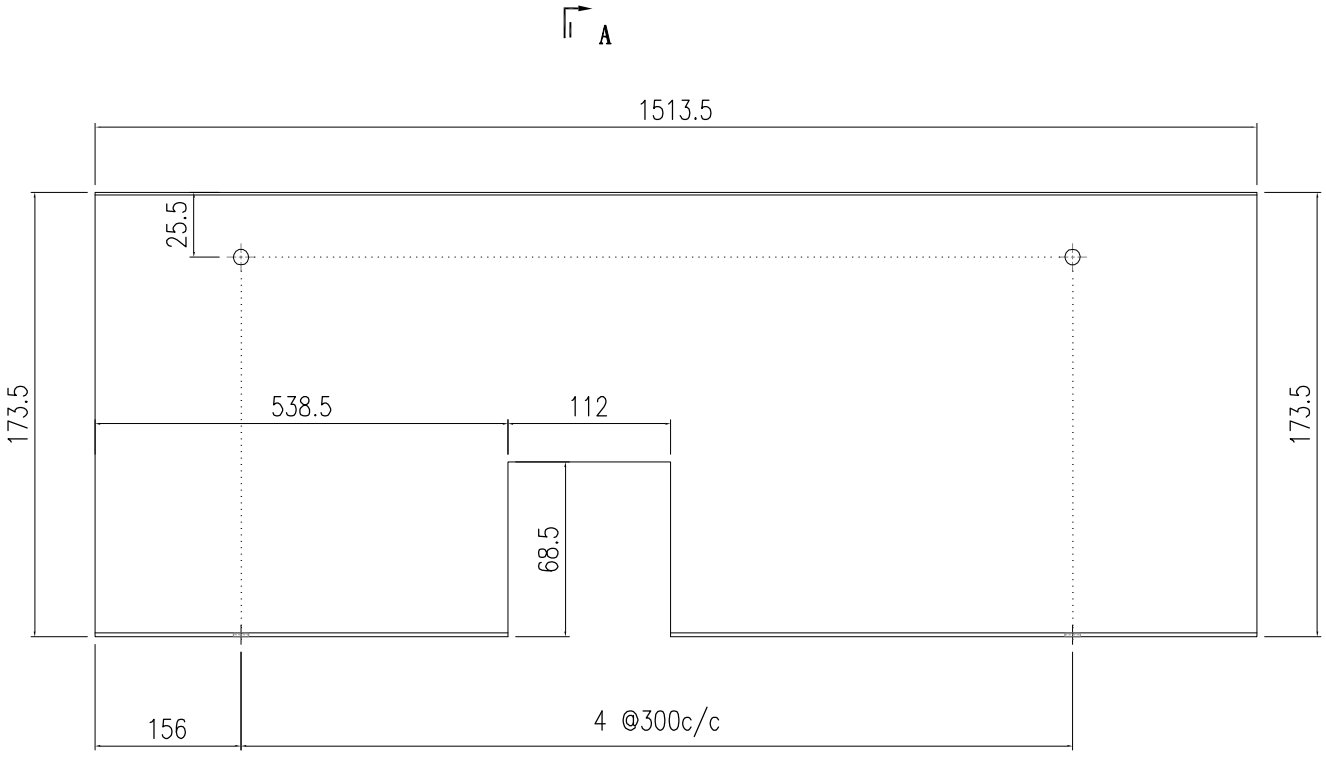


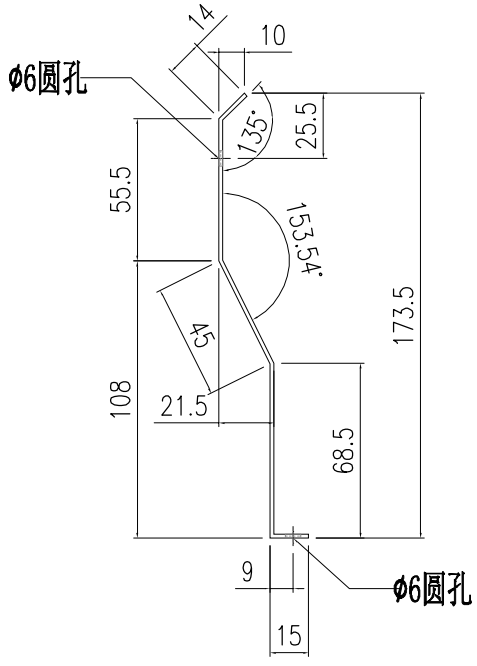

SECTION A-A


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-847		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	防水铝板	復核	練松文	20221209	數量	1		
日期	-	-	-	材料顏色	鉻化				材料	1.5mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

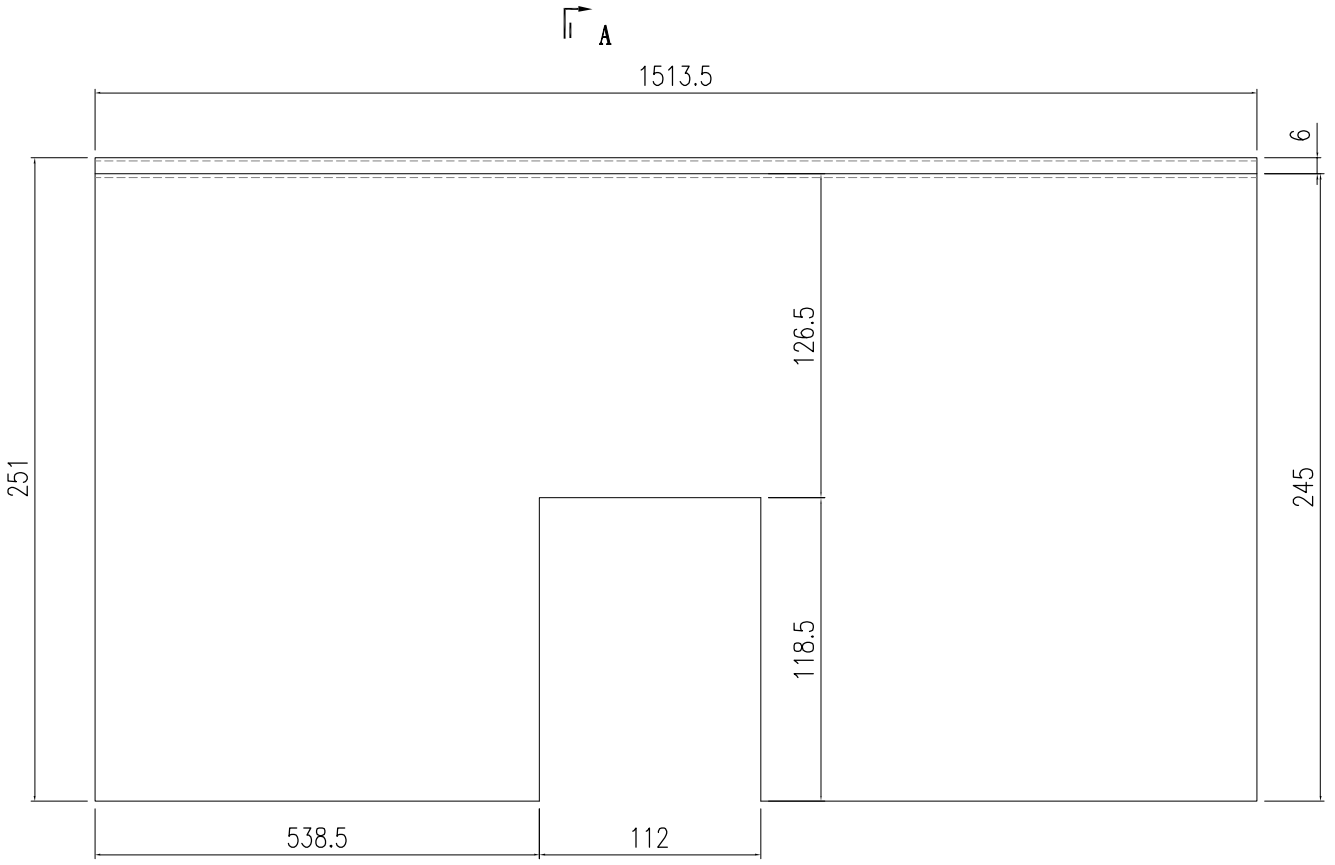


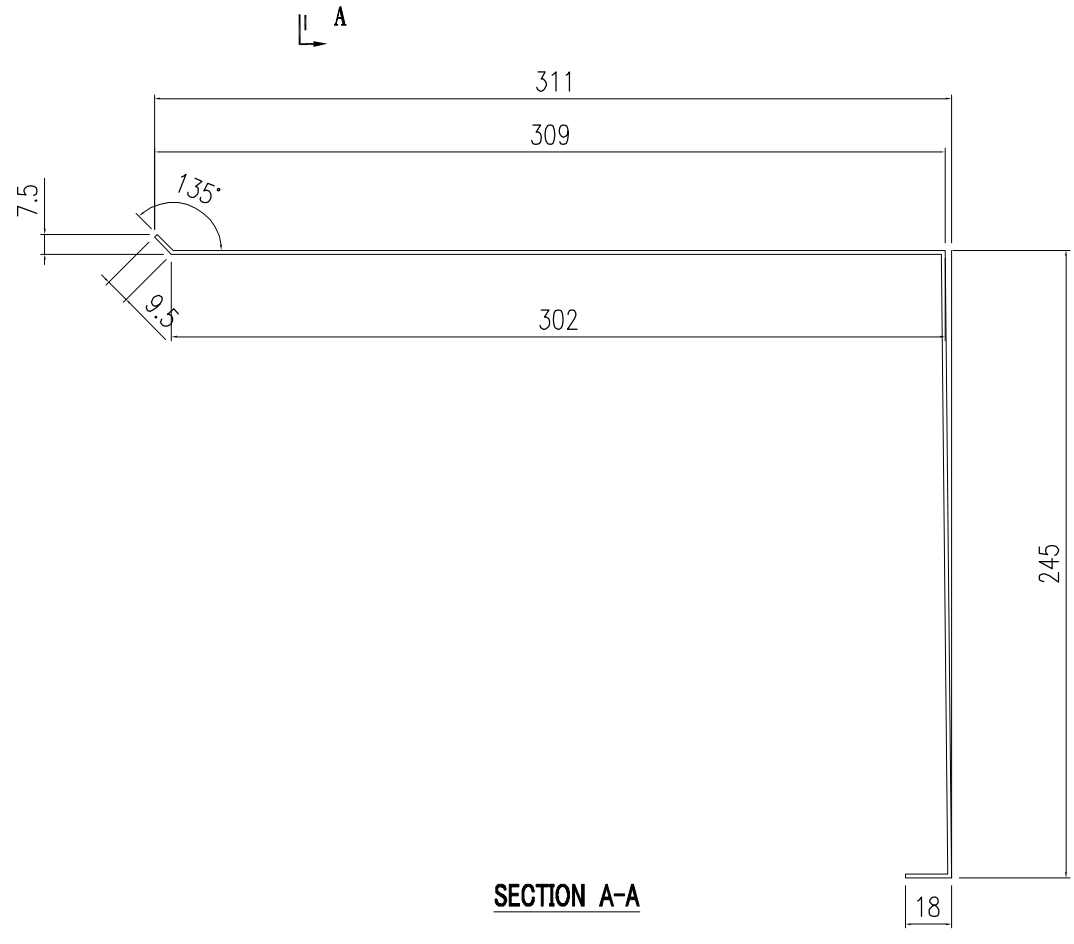


SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-851	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文	20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

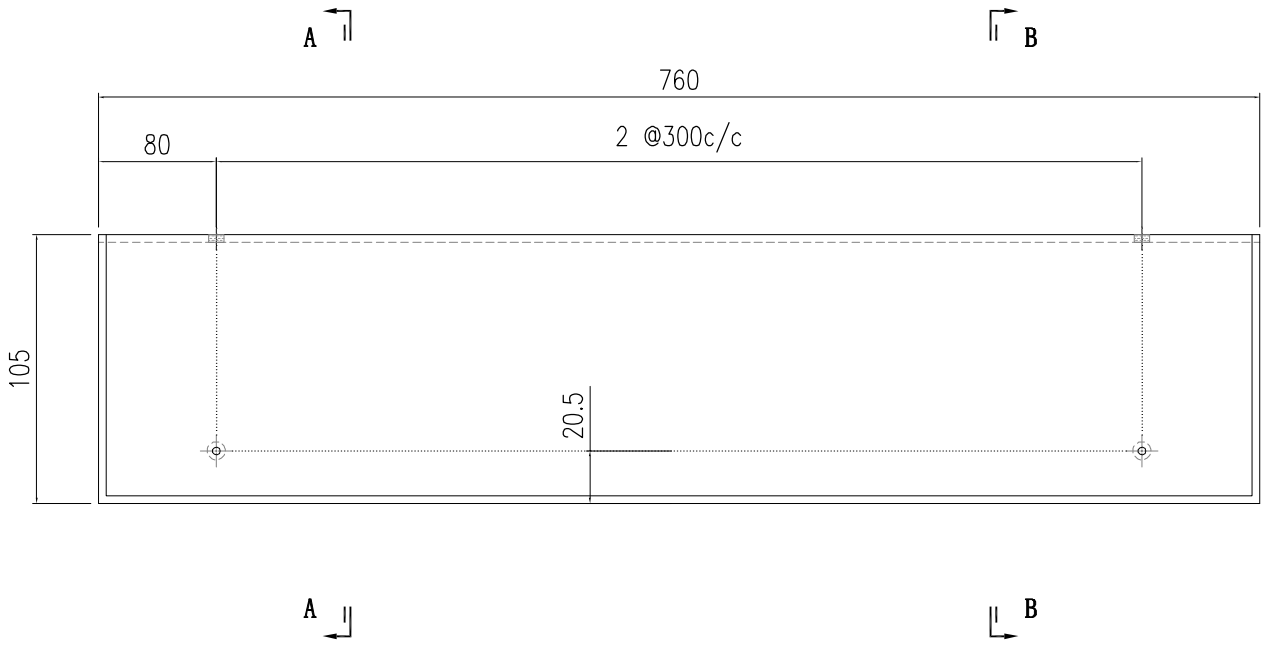

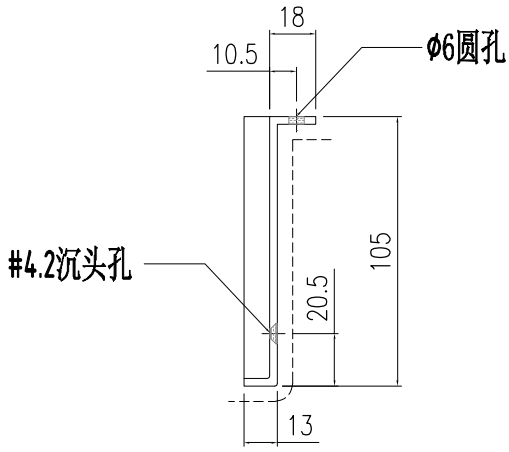



SECTION A-A

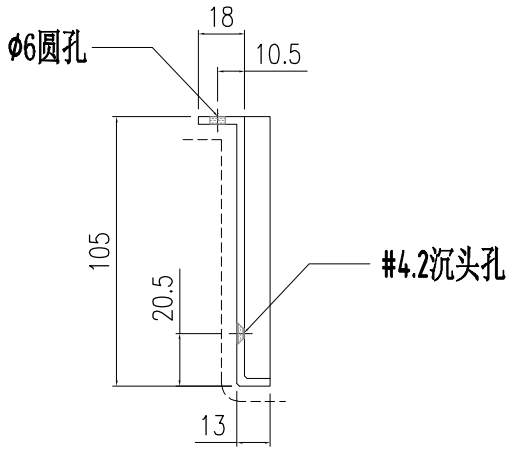


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-852	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

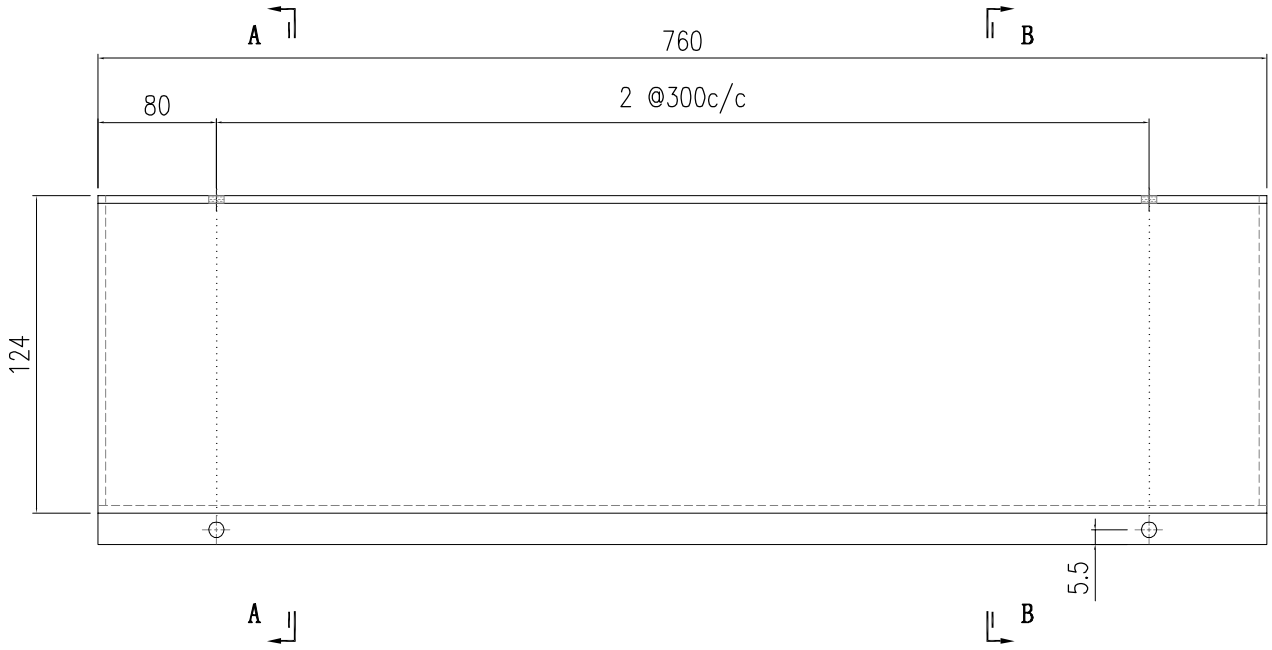

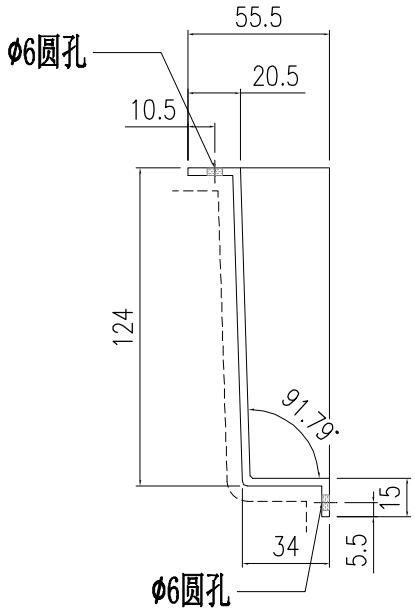



SECTION A-A

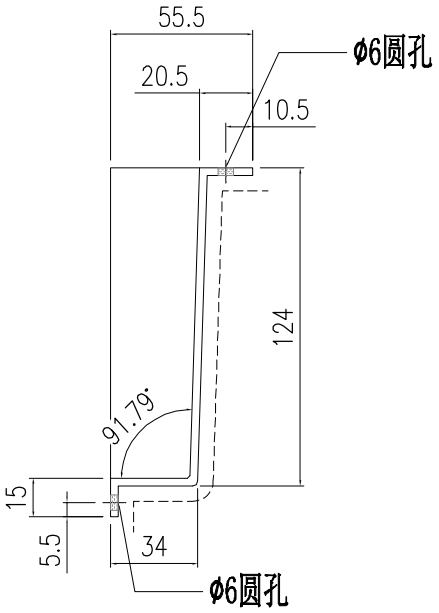


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-853	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文	20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

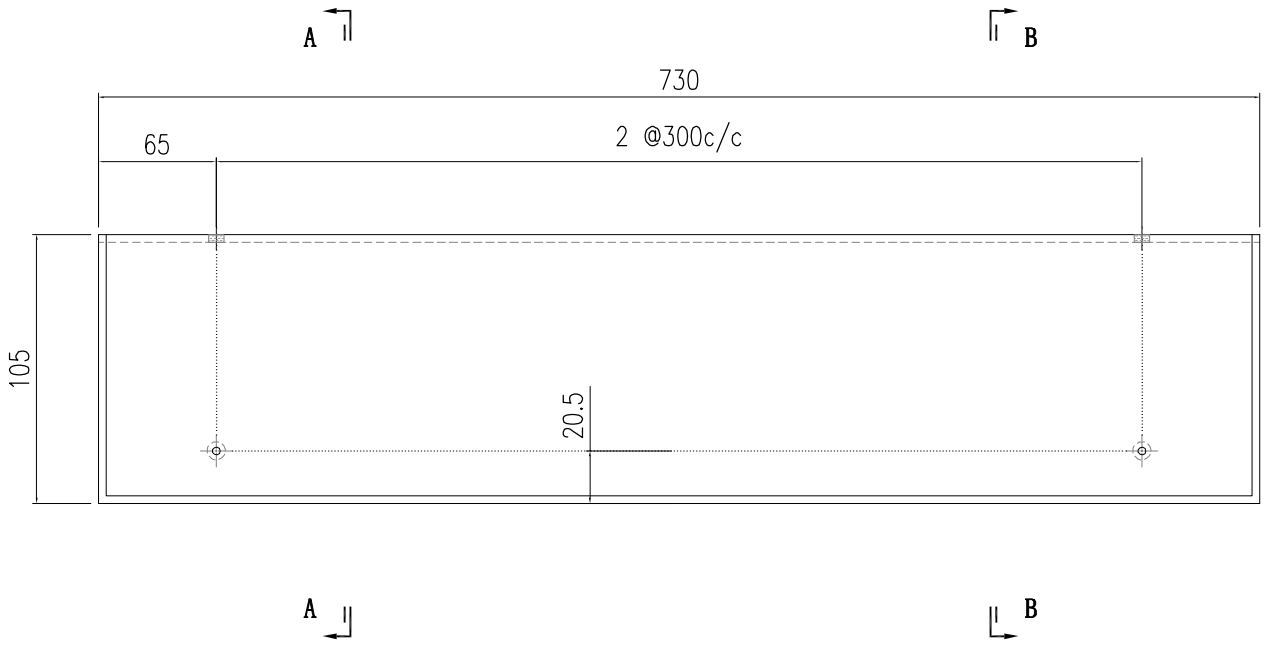

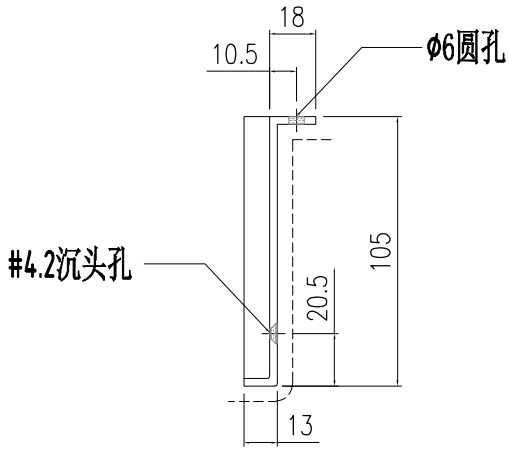



SECTION A-A

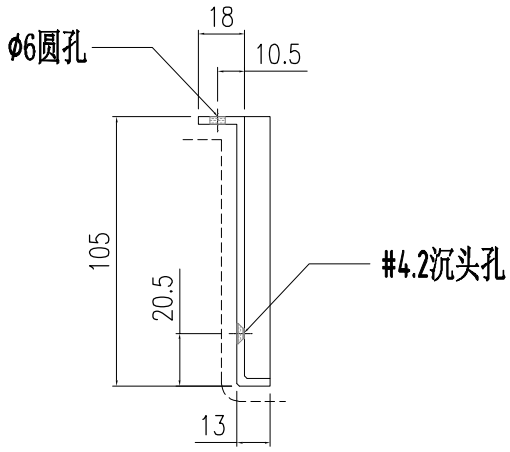


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-854
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

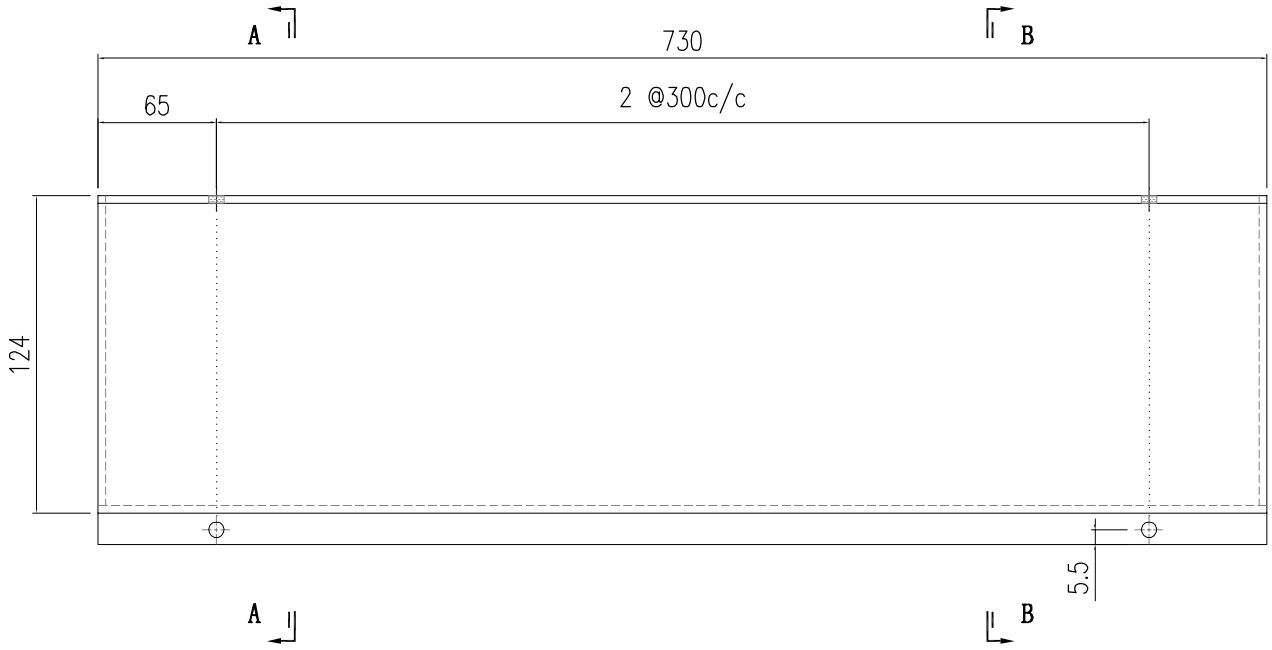

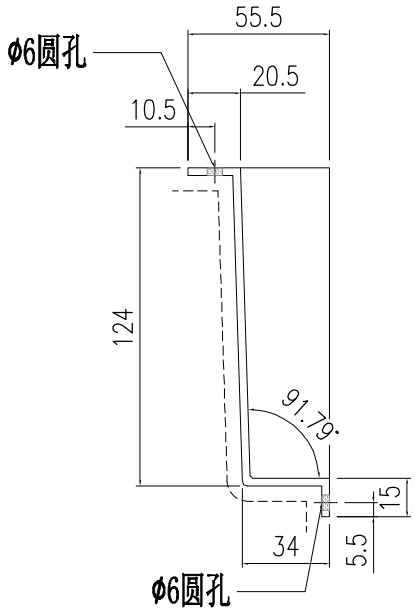



SECTION A-A

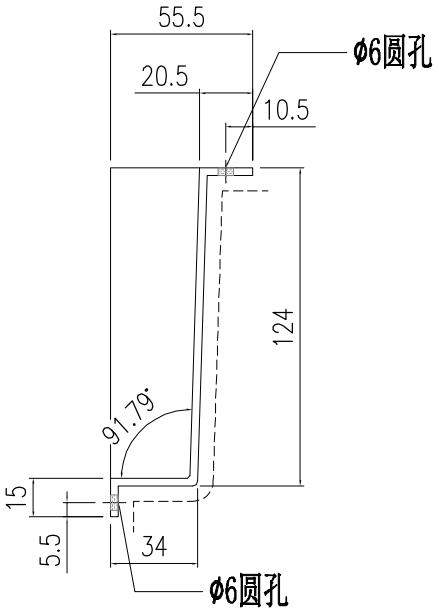


SECTION B-B


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-855	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	鉻化				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

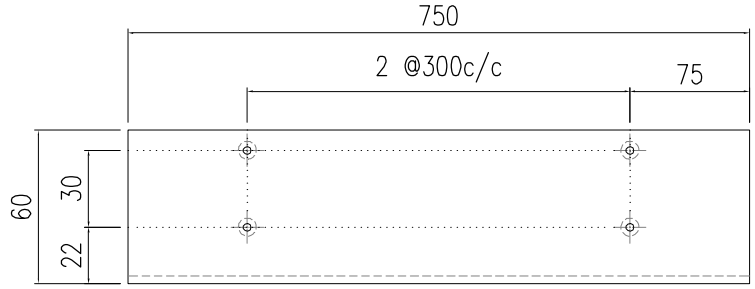





美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-856
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	鉻化				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

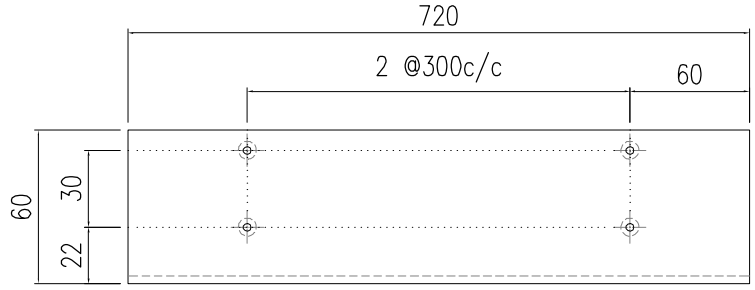




美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-857		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文	20221209	數量	2		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

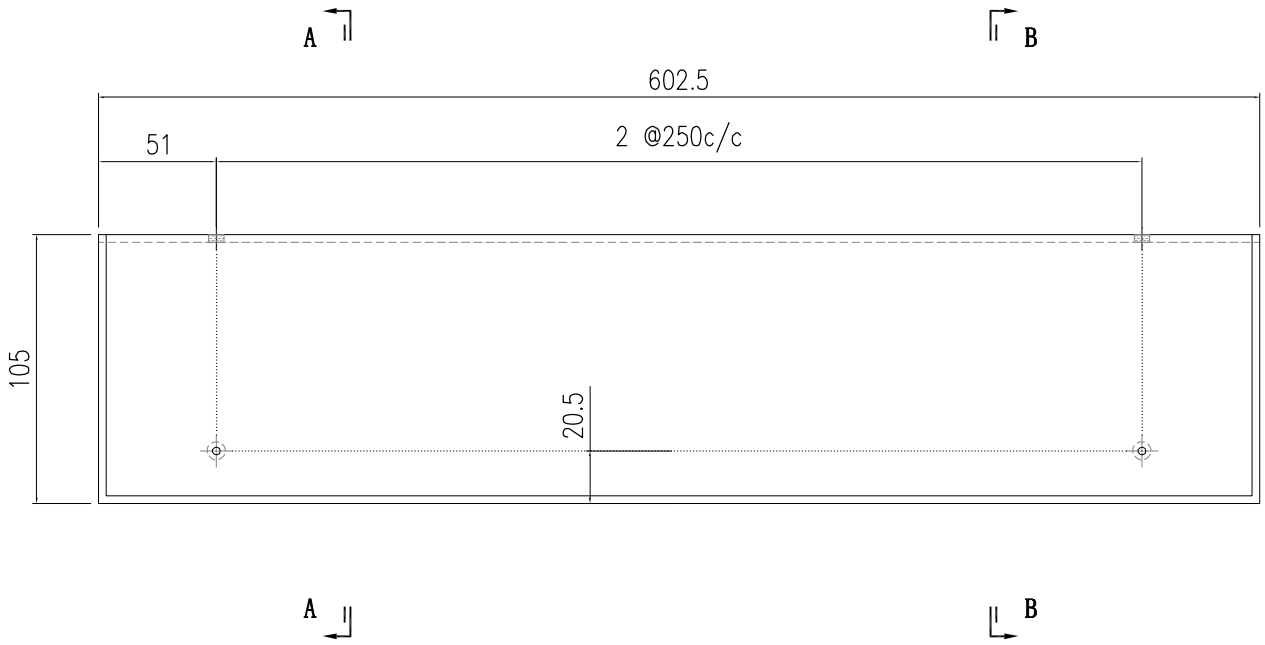

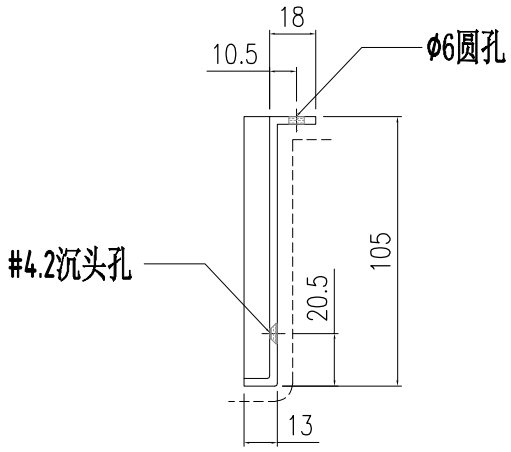



SECTION A-A

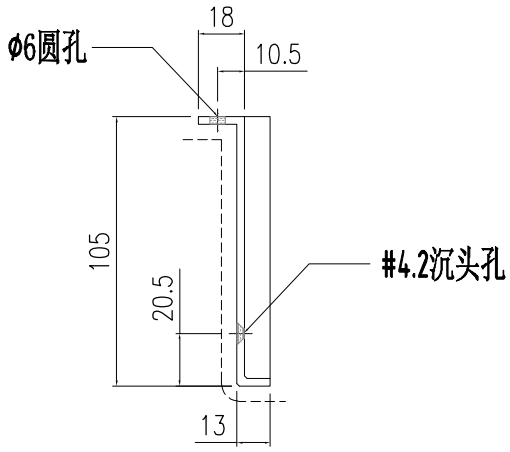


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-858
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	2
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

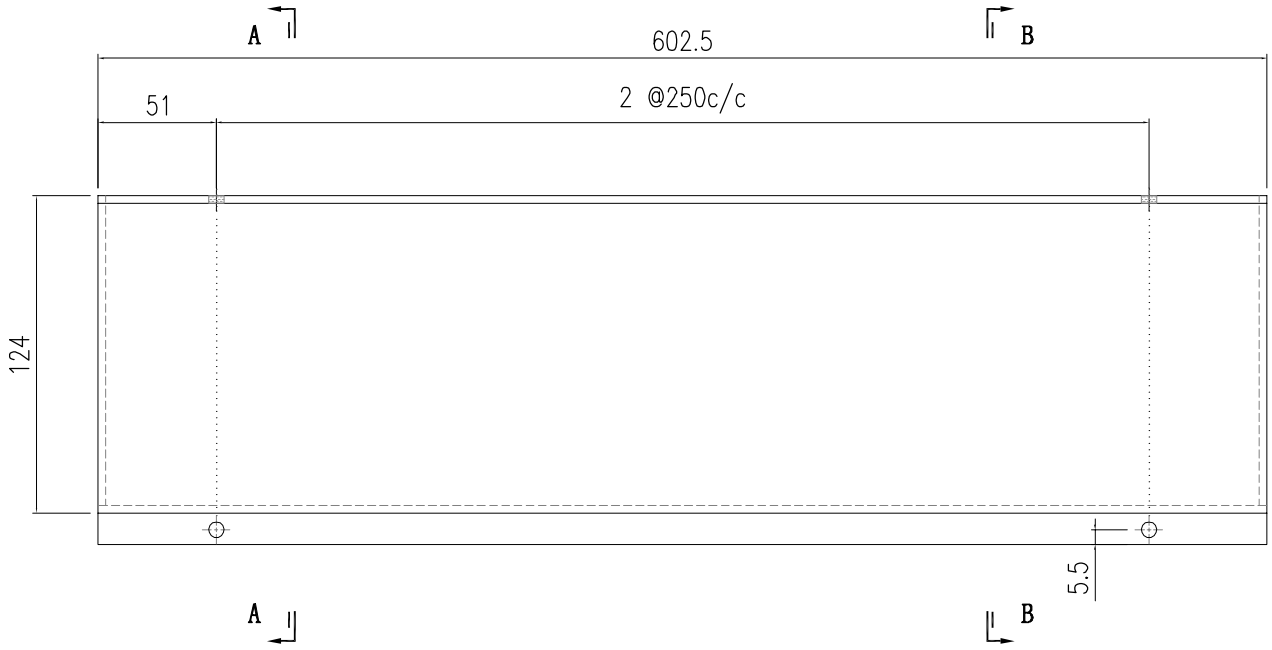

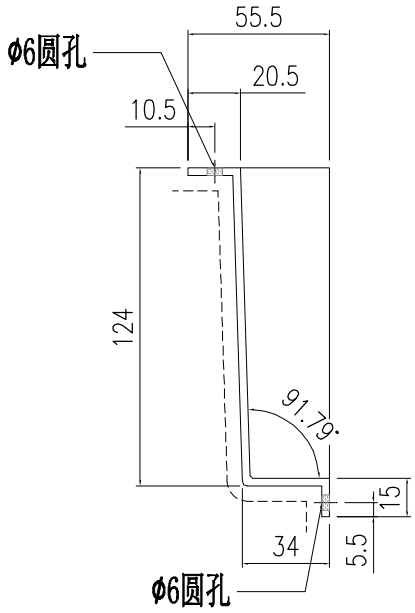



SECTION A-A

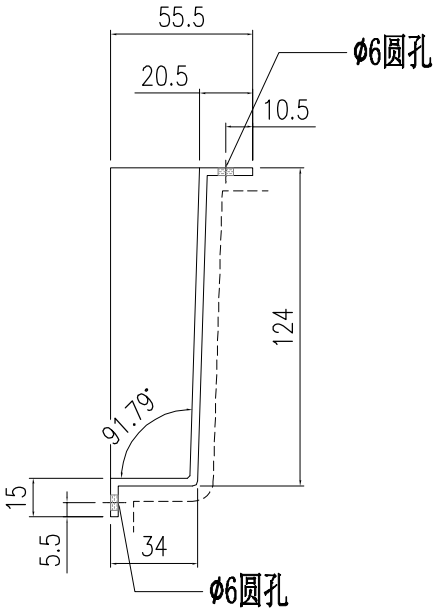


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-859		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	-		
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

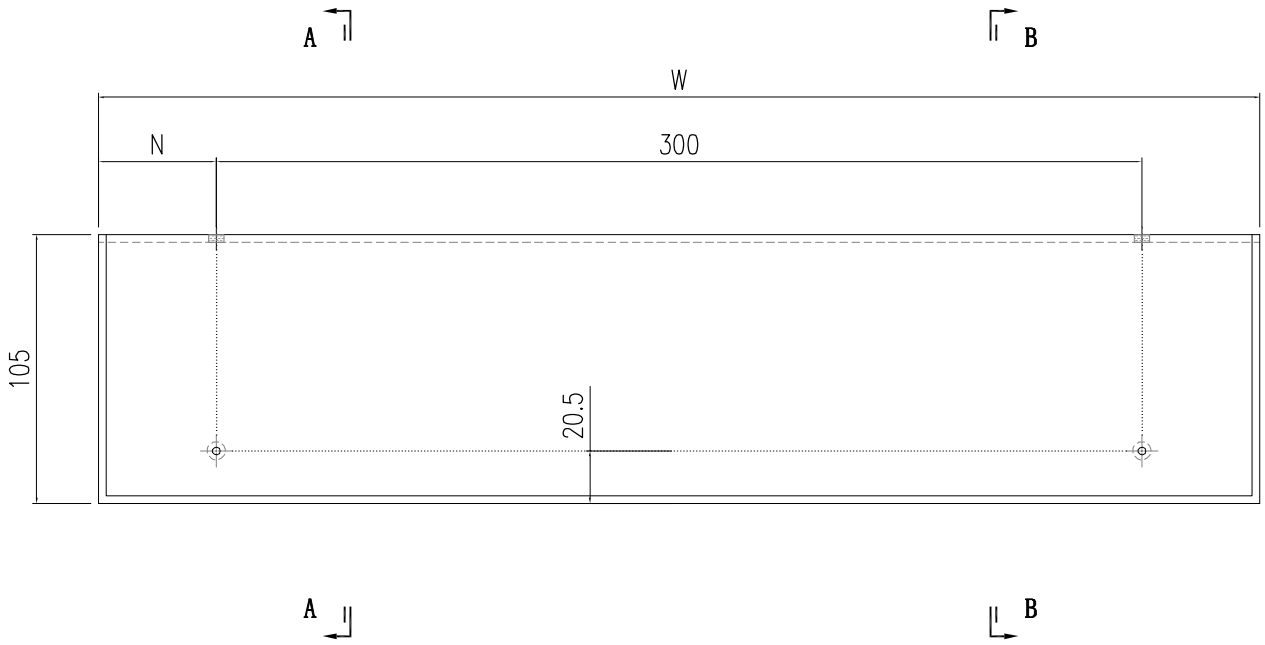

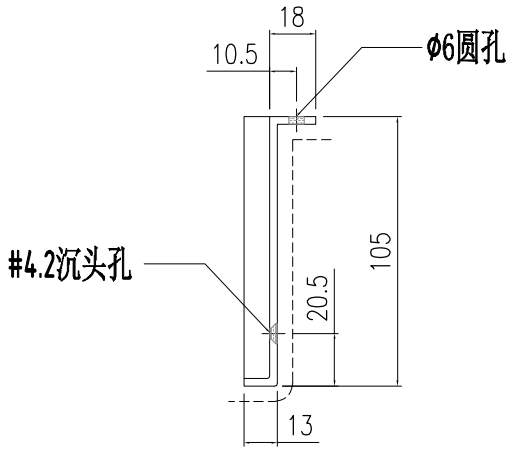


SECTION A-A

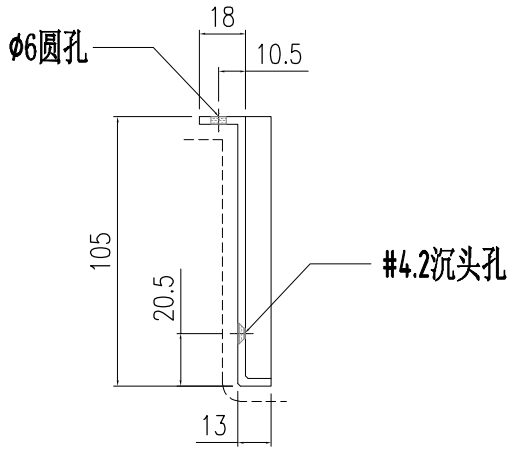


SECTION B-B


S/N	部件编号	部件数量	W	N
3	AC-859-3	1	550	125
2	AC-859-2	2	525	112.5
1	AC-859-1	2	557.5	129

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-860	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	-	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

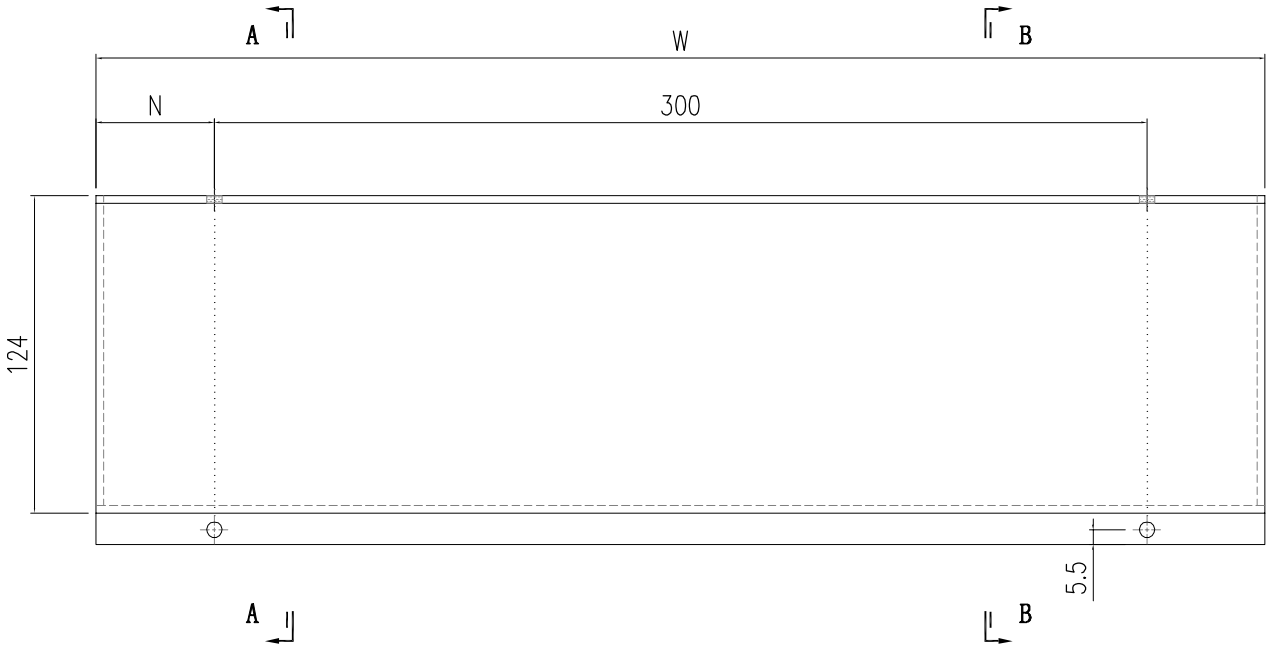

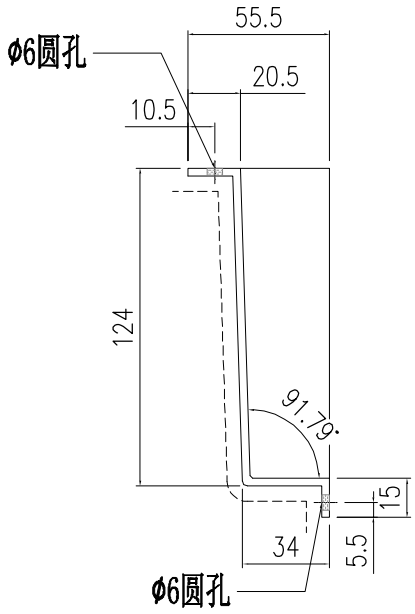


SECTION A-A

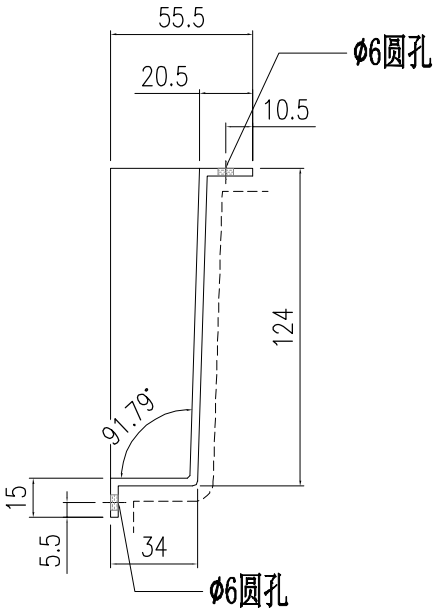


SECTION B-B


S/N	部件编号	部件数量	W	N
3	AC-860-3	1	550	125
2	AC-860-2	2	525	112.5
1	AC-860-1	2	557.5	129


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-861	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文	20221209	數量	2	
日期	-	-	-	材料顏色	鉻化			材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

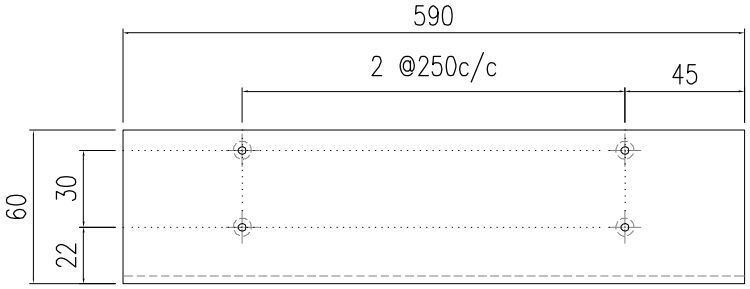




美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-862	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文	20221209	數量	-	
日期	-	-	-	材料颜色	鉻化				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

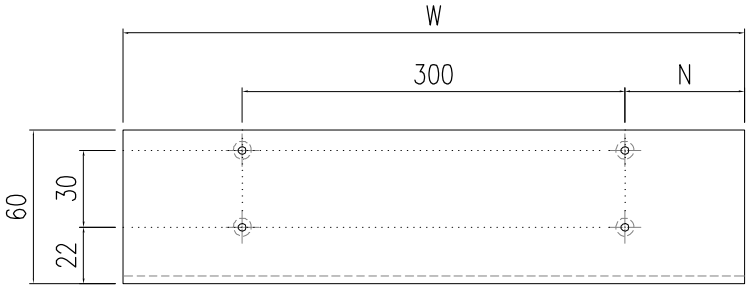





S/N	部件编号	部件数量	W	N
3	AC-862-3	1	540	120
2	AC-862-2	2	515	107.5
1	AC-862-1	2	550	125

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-863	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209		數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

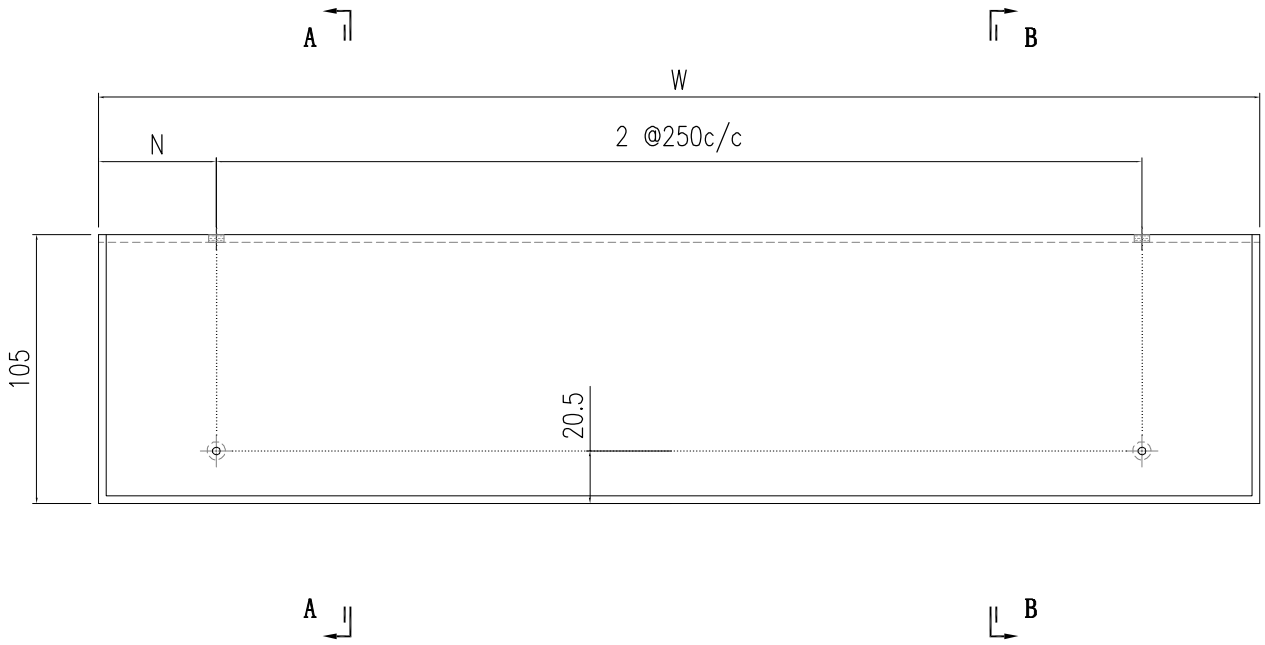

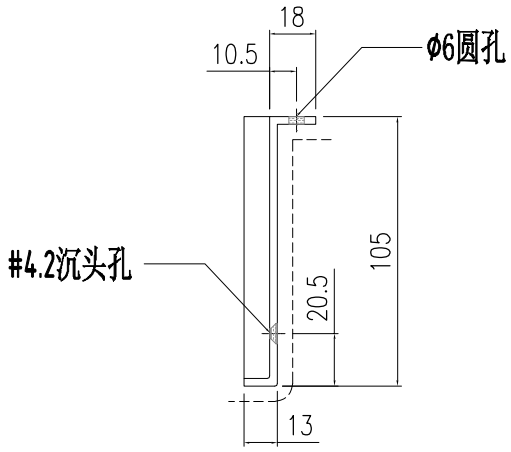


SECTION A-A

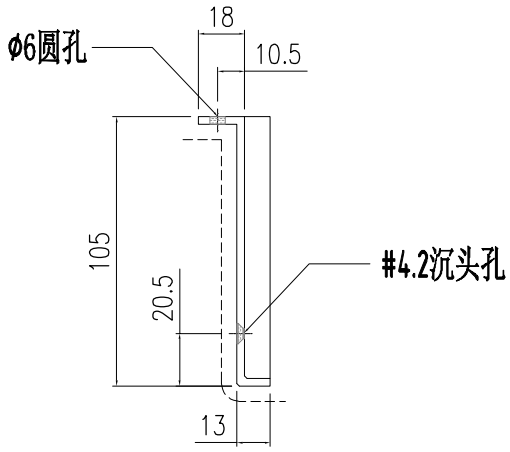


SECTION B-B


1	AC-863-1	685	92.5
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-864		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

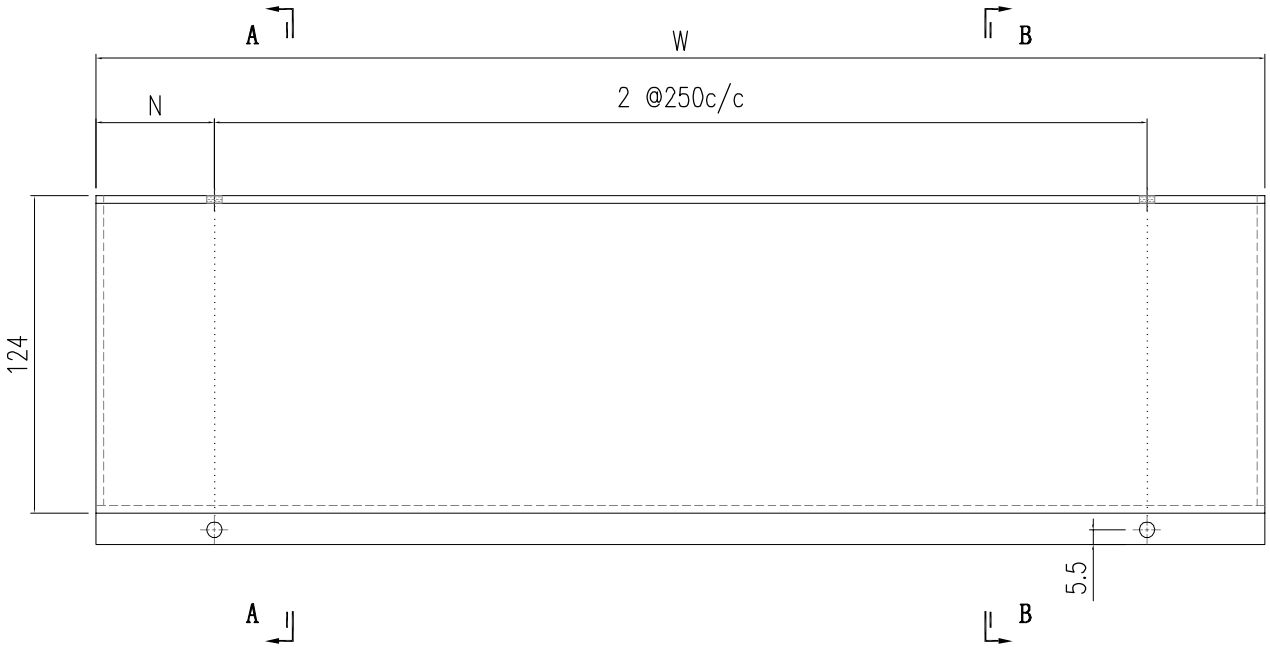

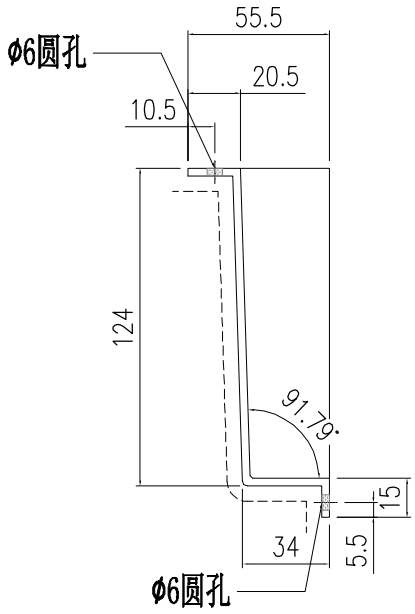


SECTION A-A

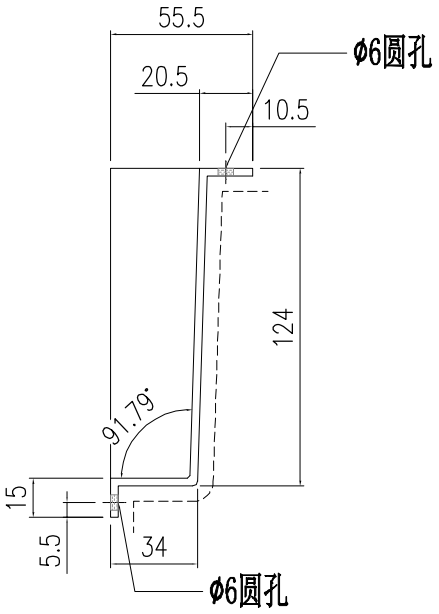


SECTION B-B

1	AC-864-1	685	92.5
S/N	部件编号	W	N


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-865	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	鉻化			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

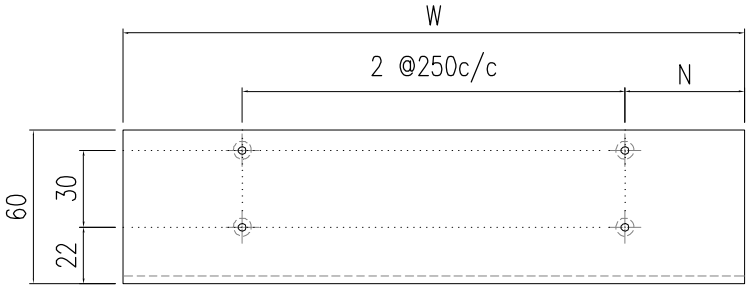





1	AC-865-1	675	87.5
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-866	
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209		數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

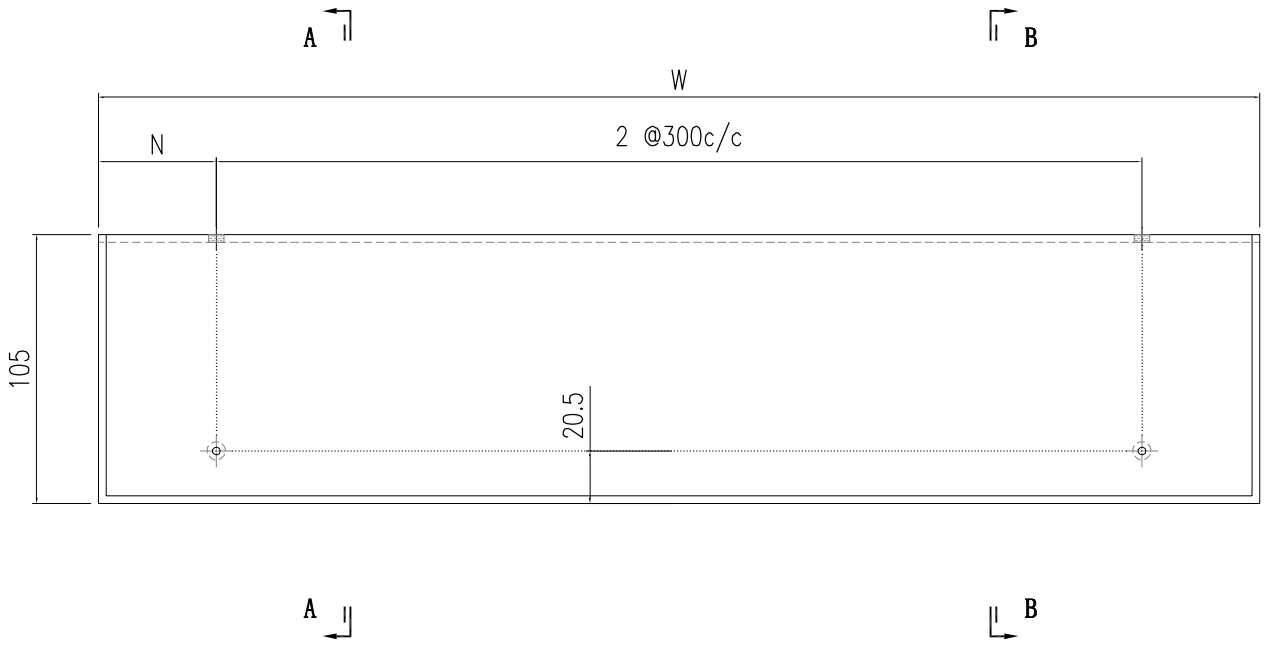

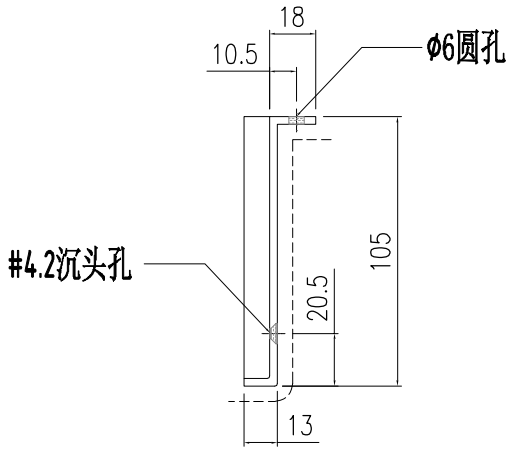


SECTION A-A

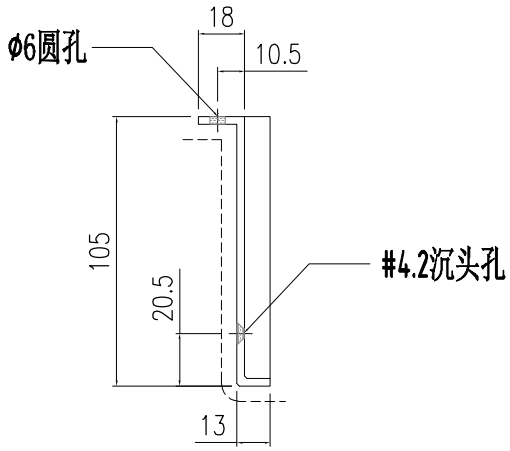


SECTION B-B


1	AC-866-1	760	80
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-867		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

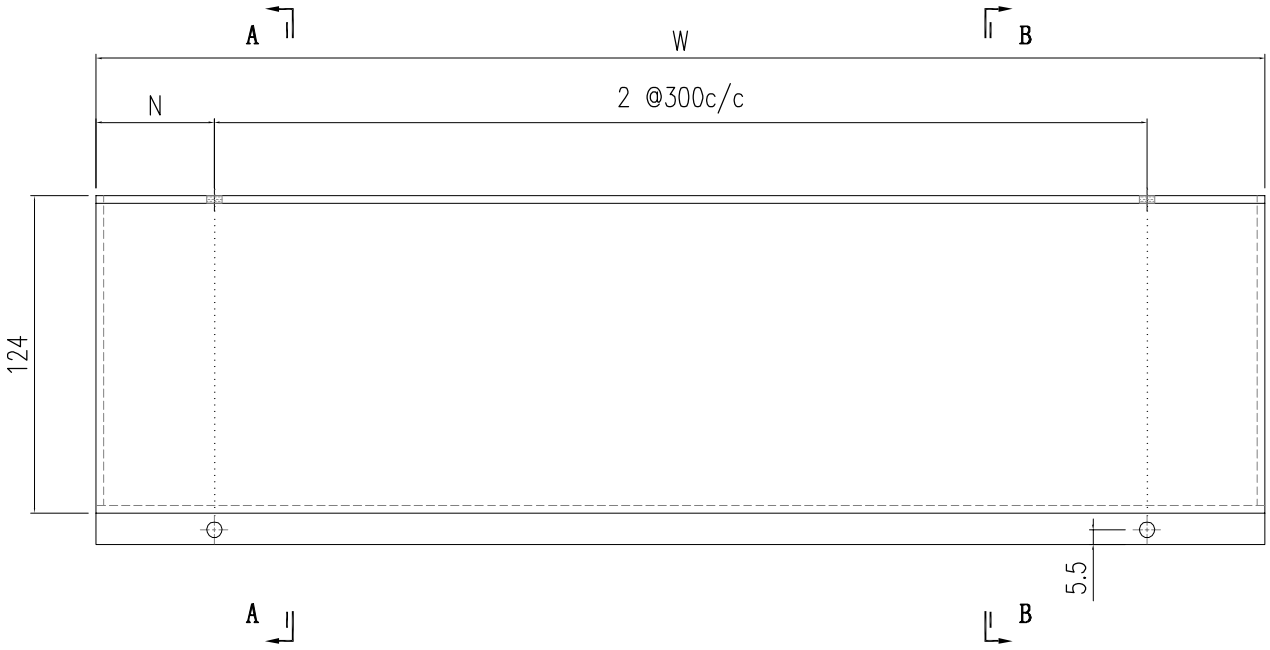

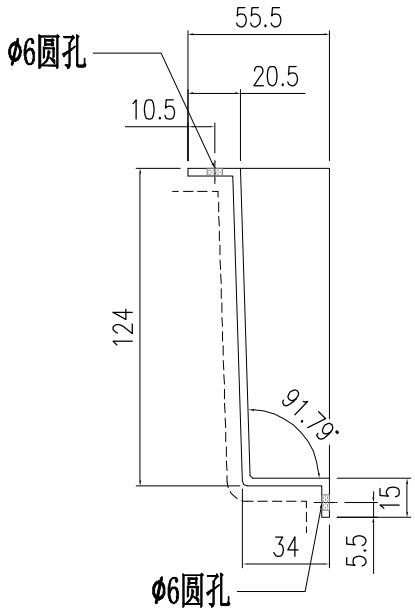


SECTION A-A

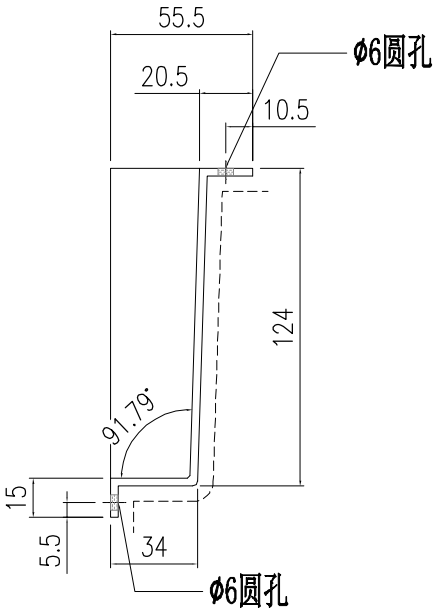


SECTION B-B

1	AC-867-1	760	80
S/N	部件编号	W	N


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-868	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	鉻化			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

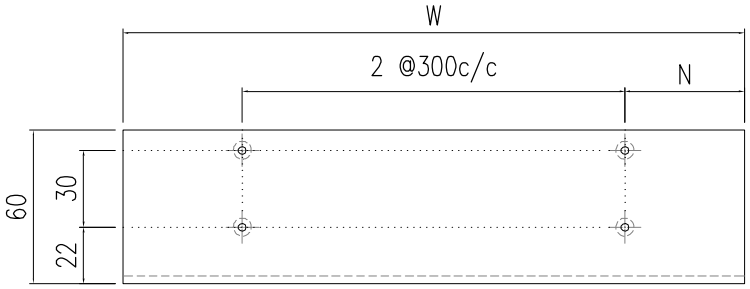





1	AC-868-1	750	75
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-869		
修改	-	-	-	採用	工廠	-	地盤 ✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

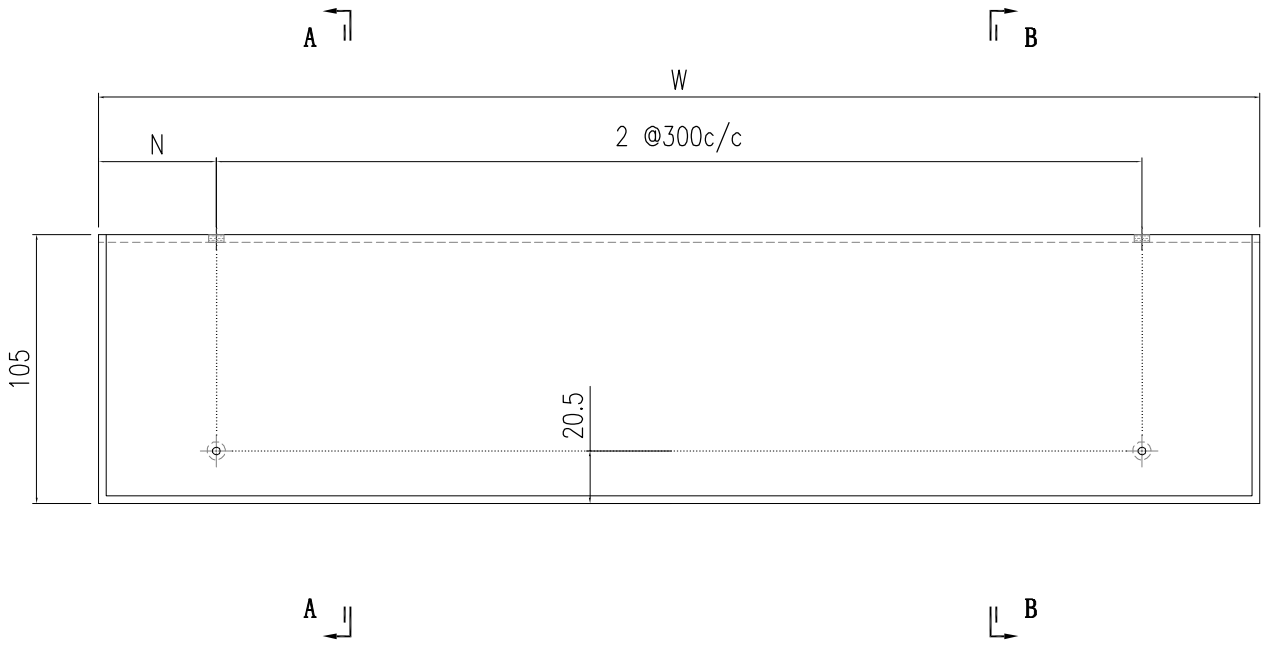

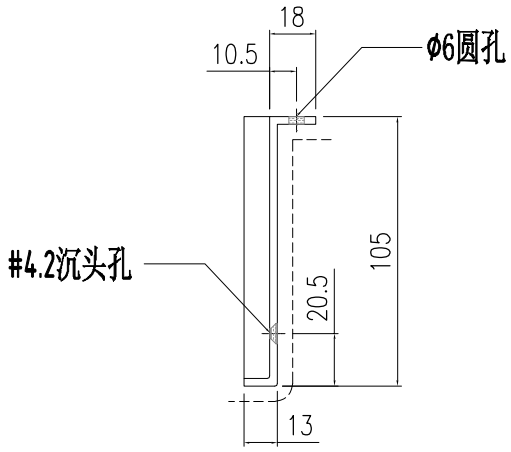


SECTION A-A

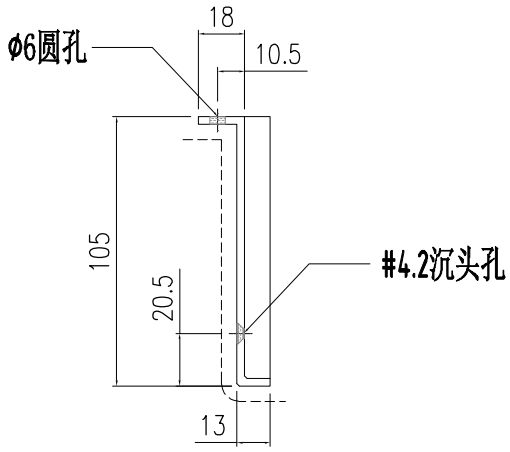


SECTION B-B


1	AC-869-1	775	87.5
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-870		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

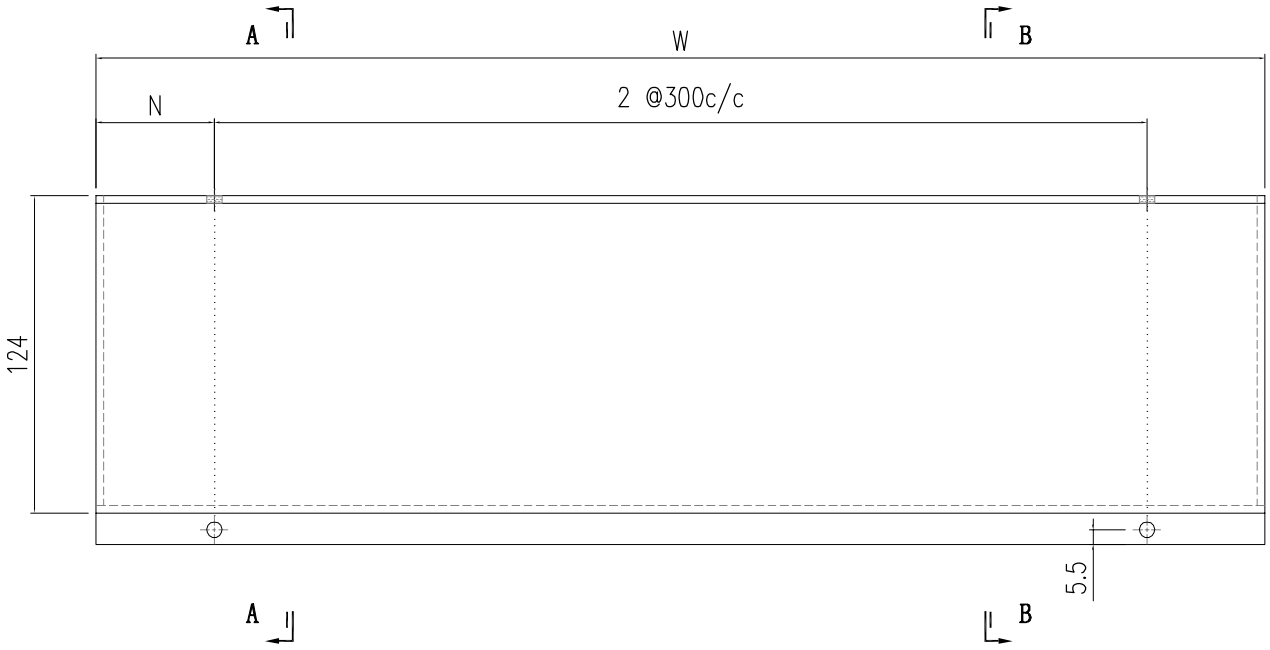

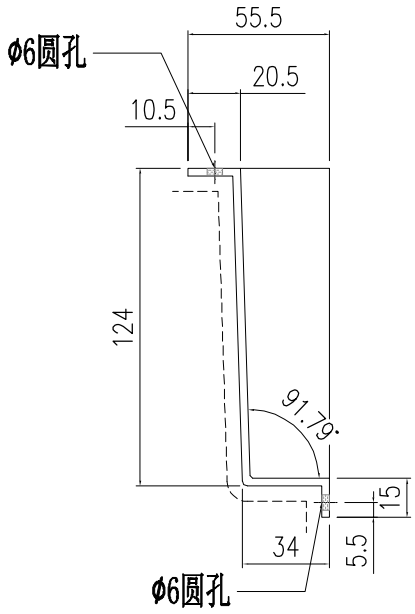


SECTION A-A

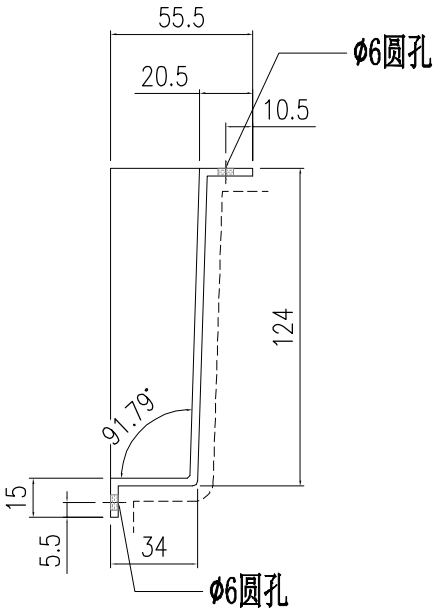


SECTION B-B

1	AC-870-1	775	87.5
S/N	部件编号	W	N


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-871		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	收边铝板	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	鉻化				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

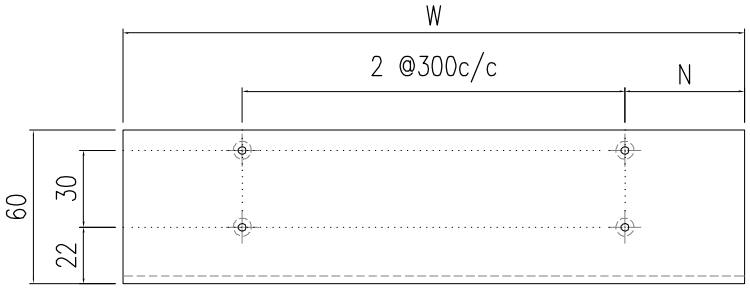





1	AC-871-1	765	82.5
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-901		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	3		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

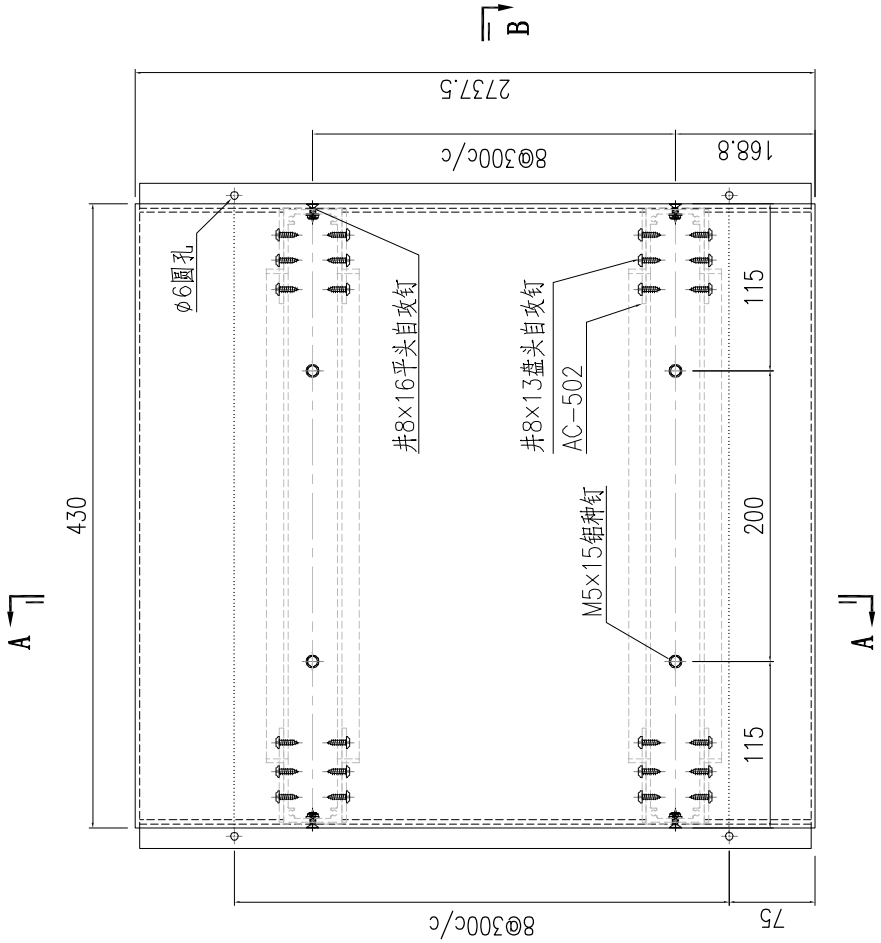

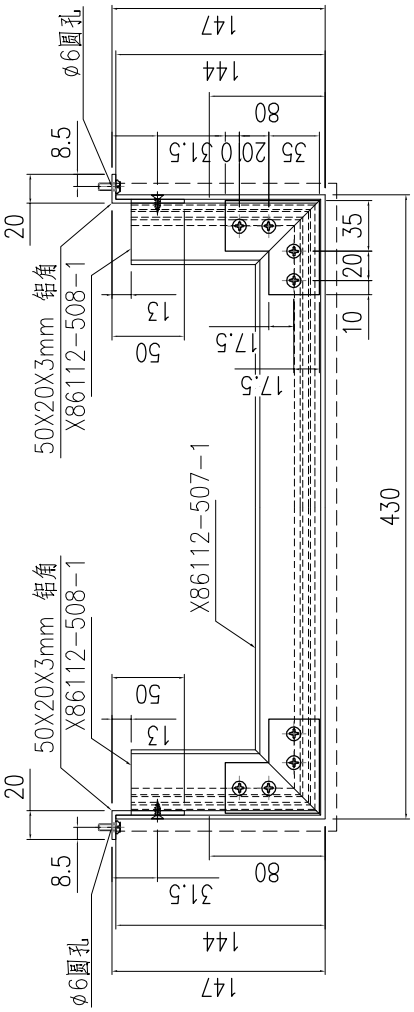



SECTION B-B




SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盤	啟德6552	制圖	陈梓豪 20221206		圖號	AC-902		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209		數量	3		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210		單件重量	-		(KG)

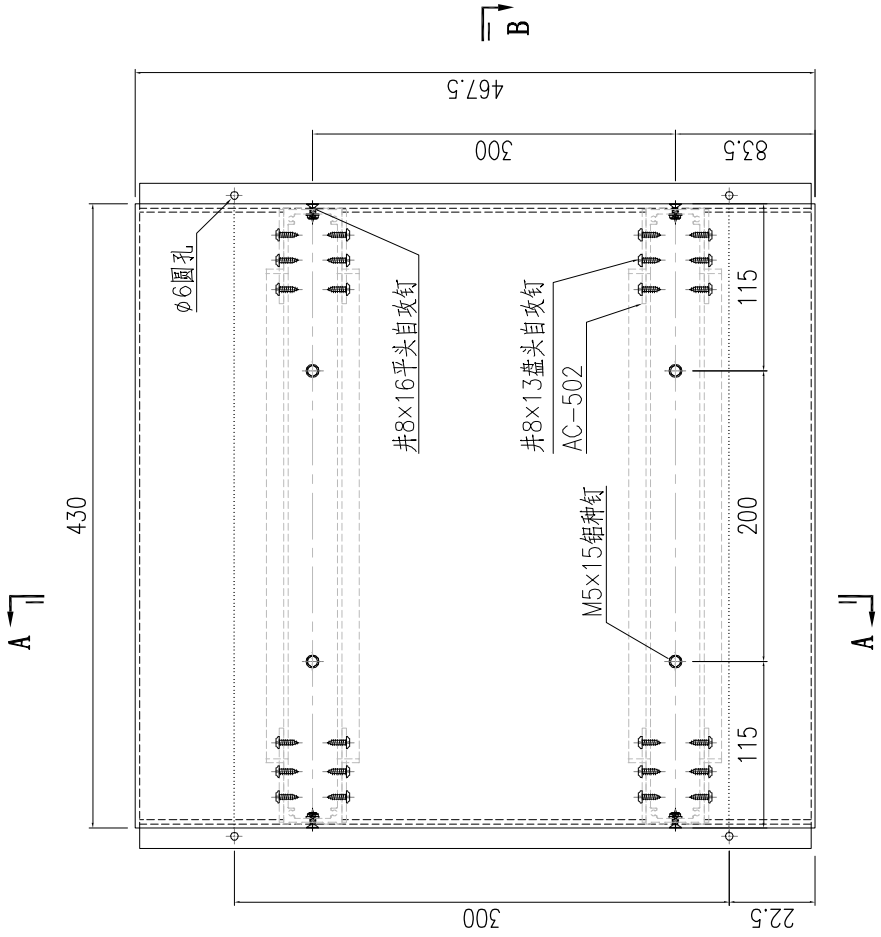

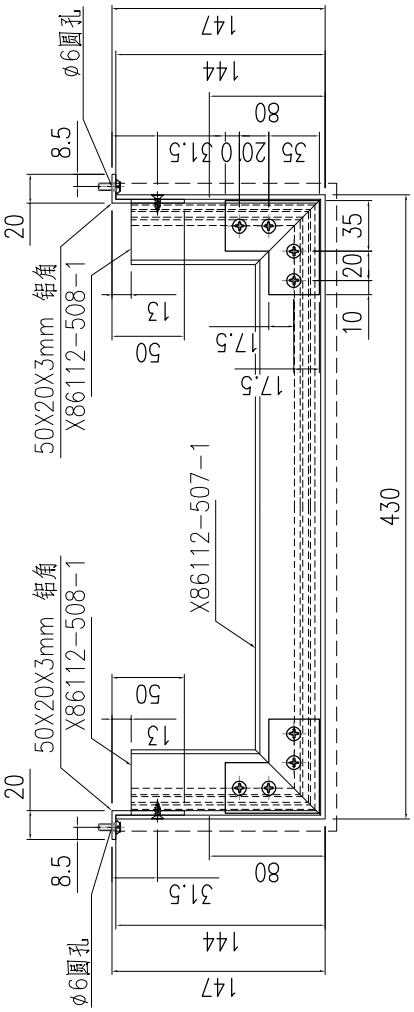



SECTION B-B

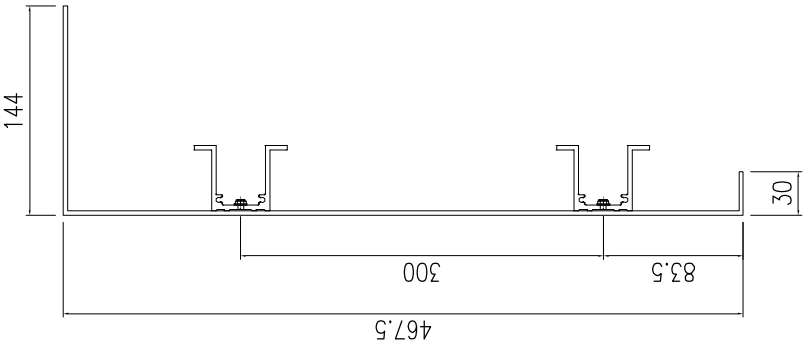


SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-903		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

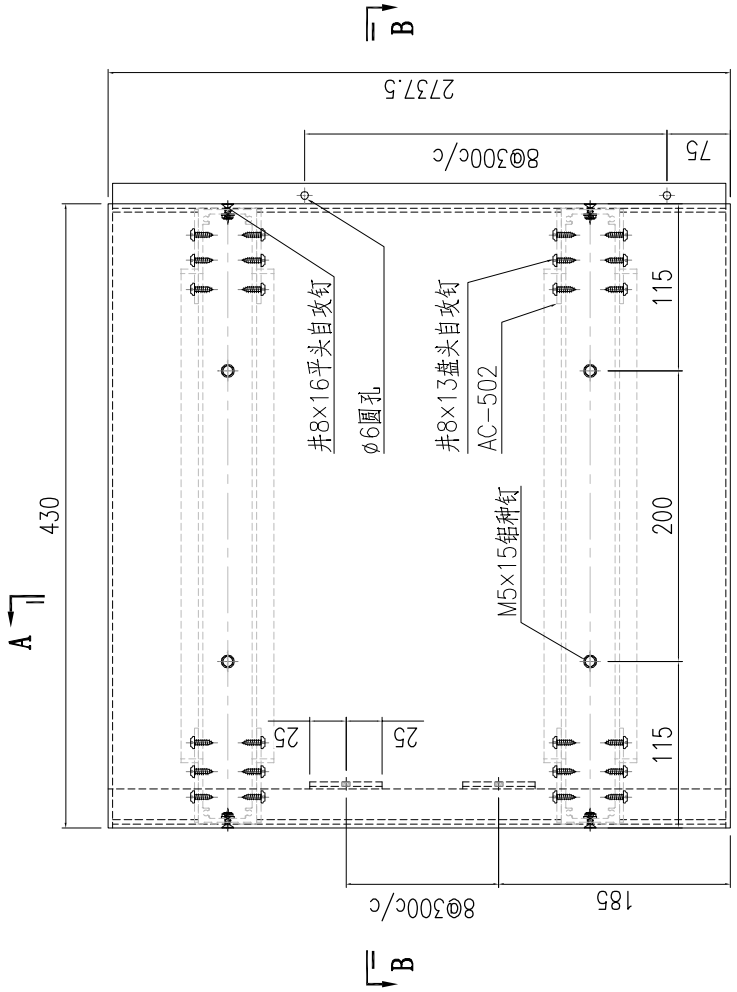

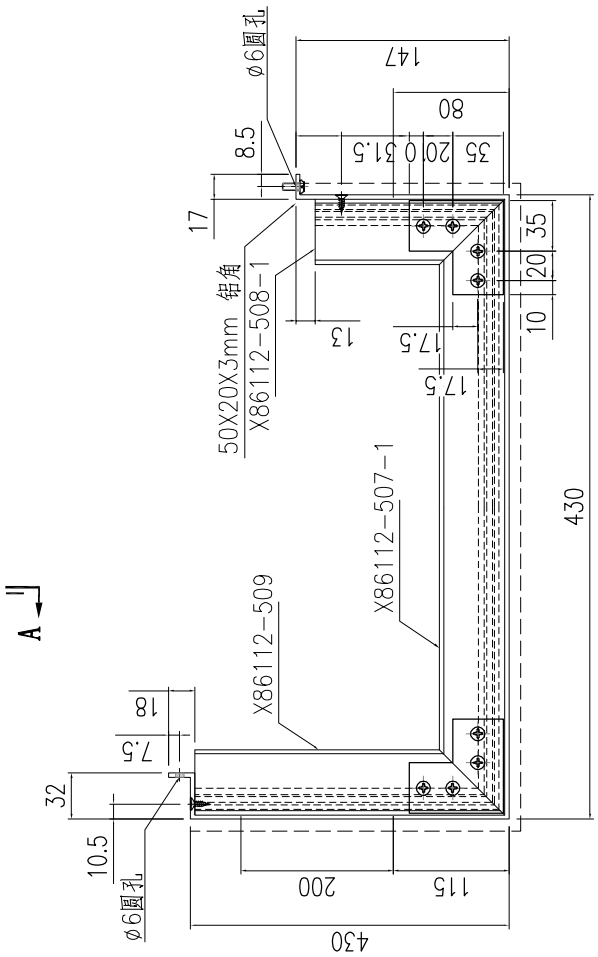



SECTION B-B




SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-904		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1		
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

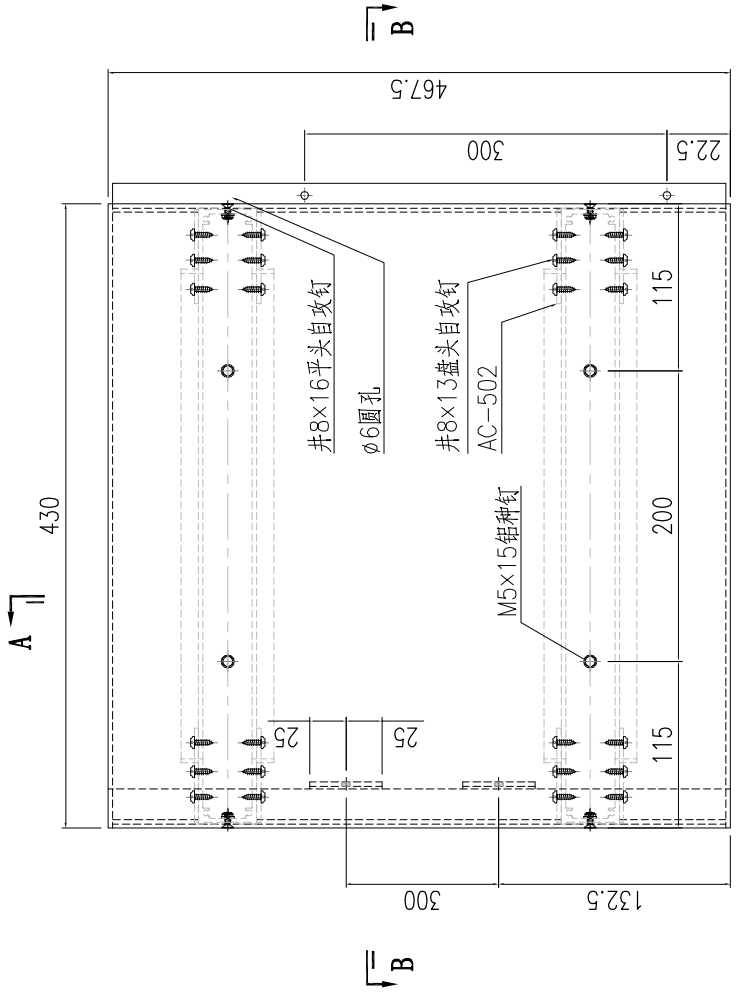

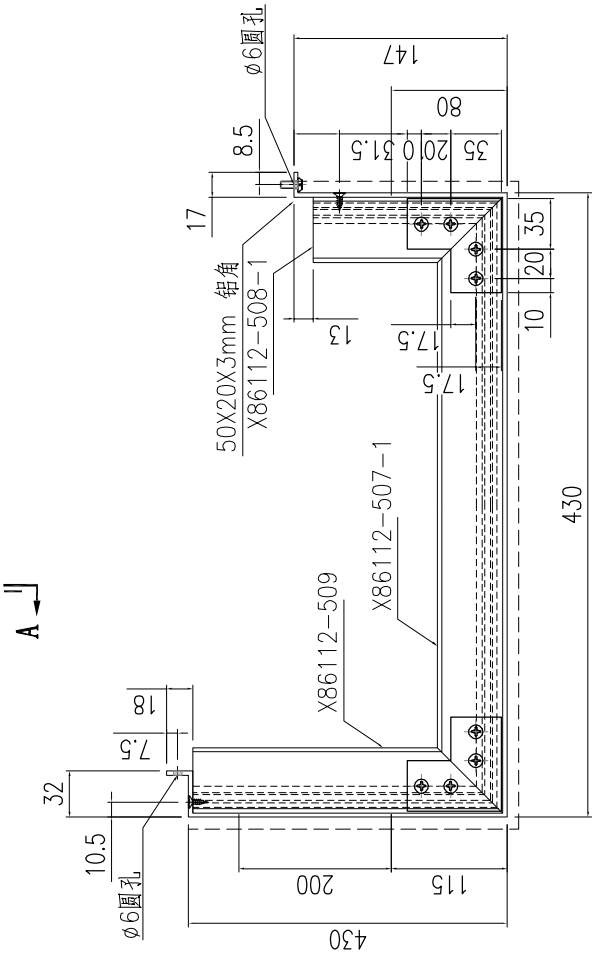



SECTION B-B

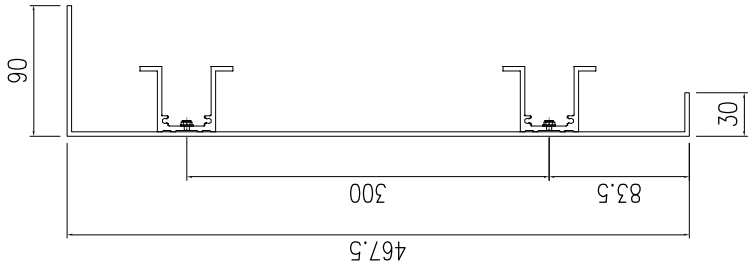


SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-905		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	2		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

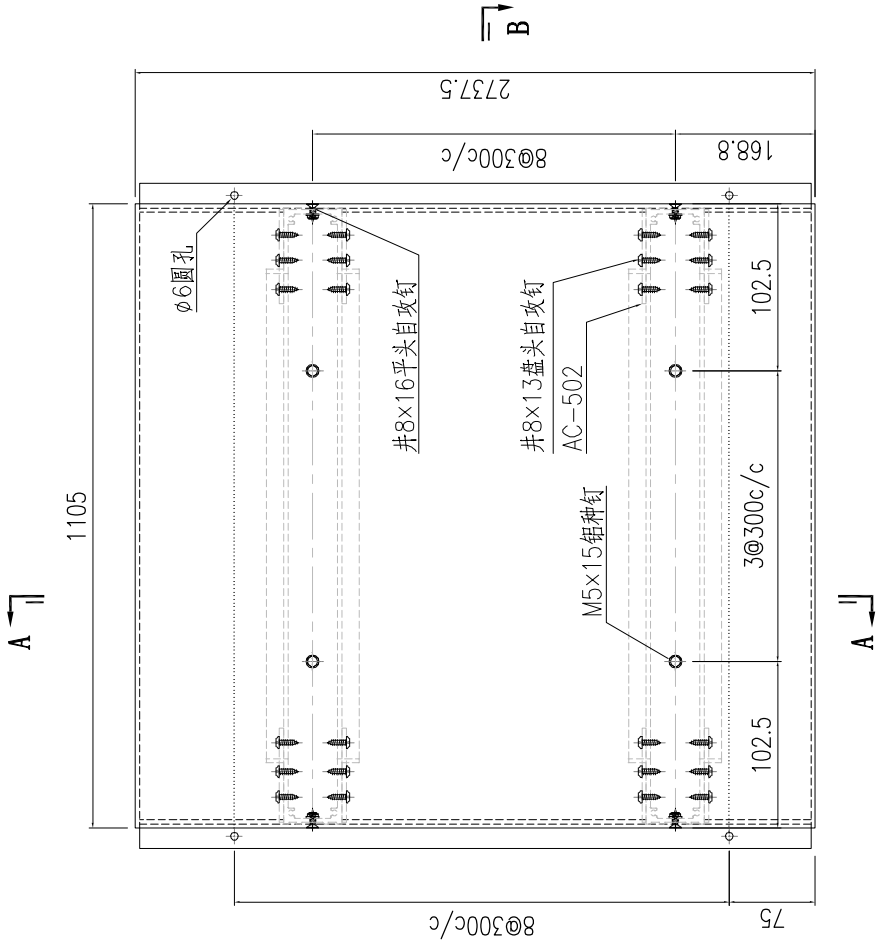


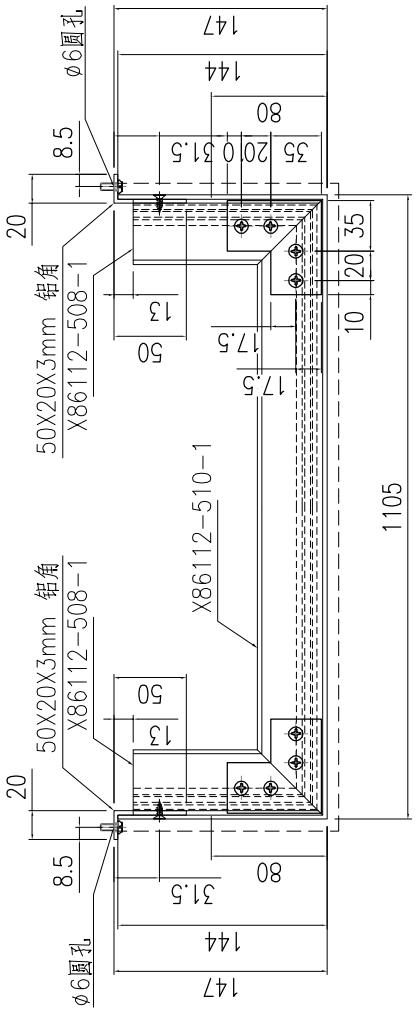




SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
修改	-	-	-	採用	工廠	-	地盤	✓	工程號	J857	類別		物料號	-			
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				地盤	啟德6552	制圖	陈梓豪	20221206	圖號	AC-906		
									图纸名称	鋁板加工圖	復核	練松文	20221209	數量	2		
									材料	3mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

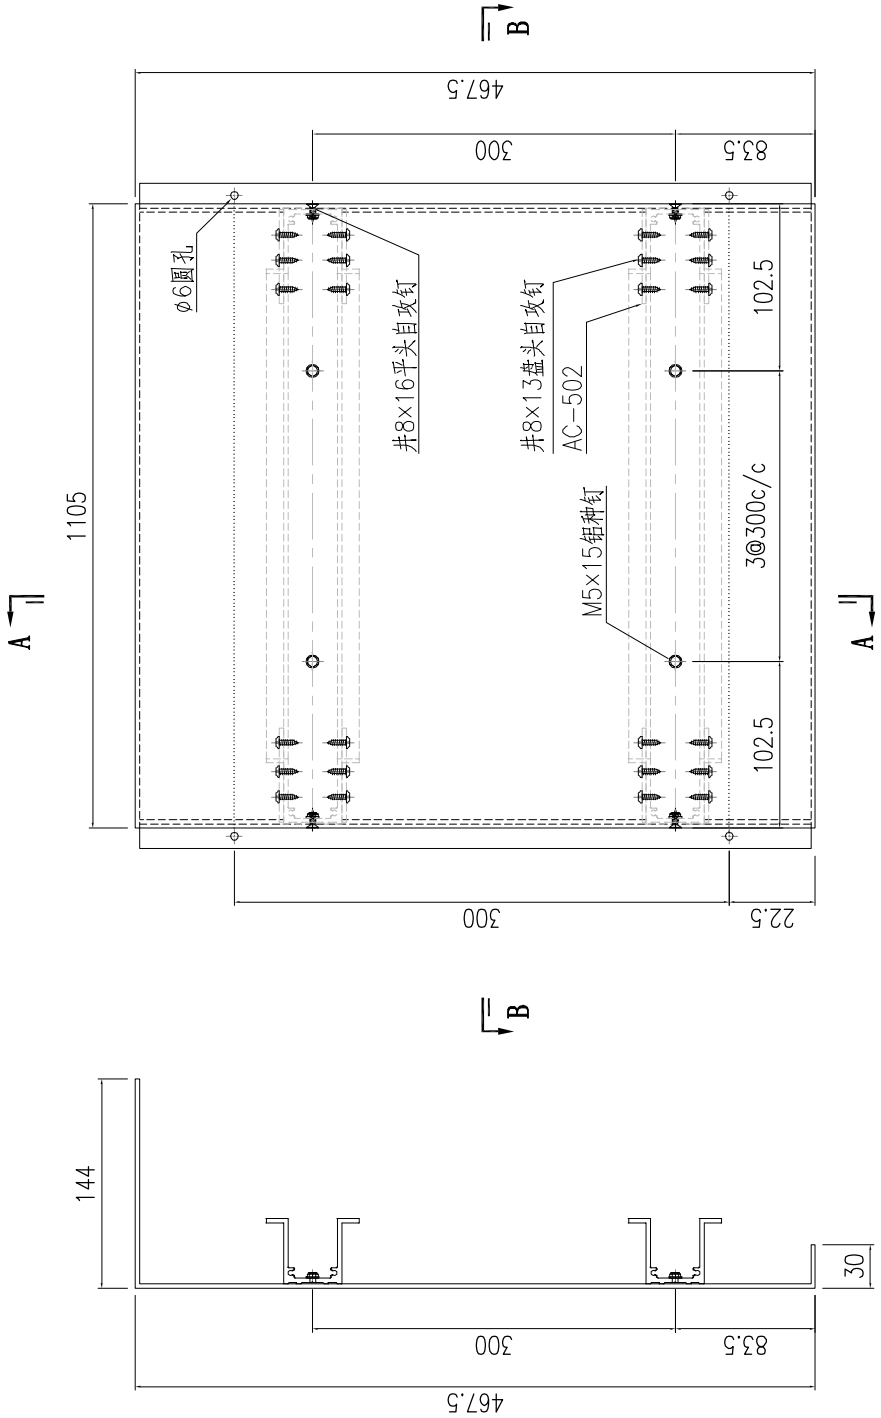



SECTION A-A

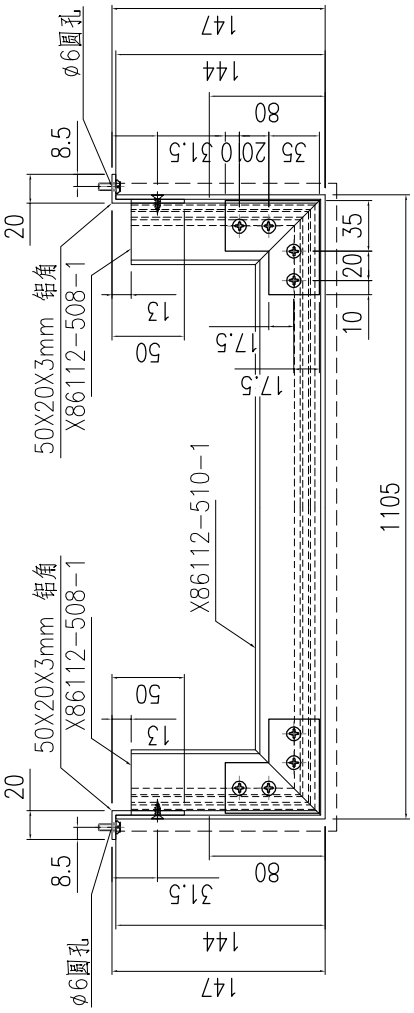


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-907		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

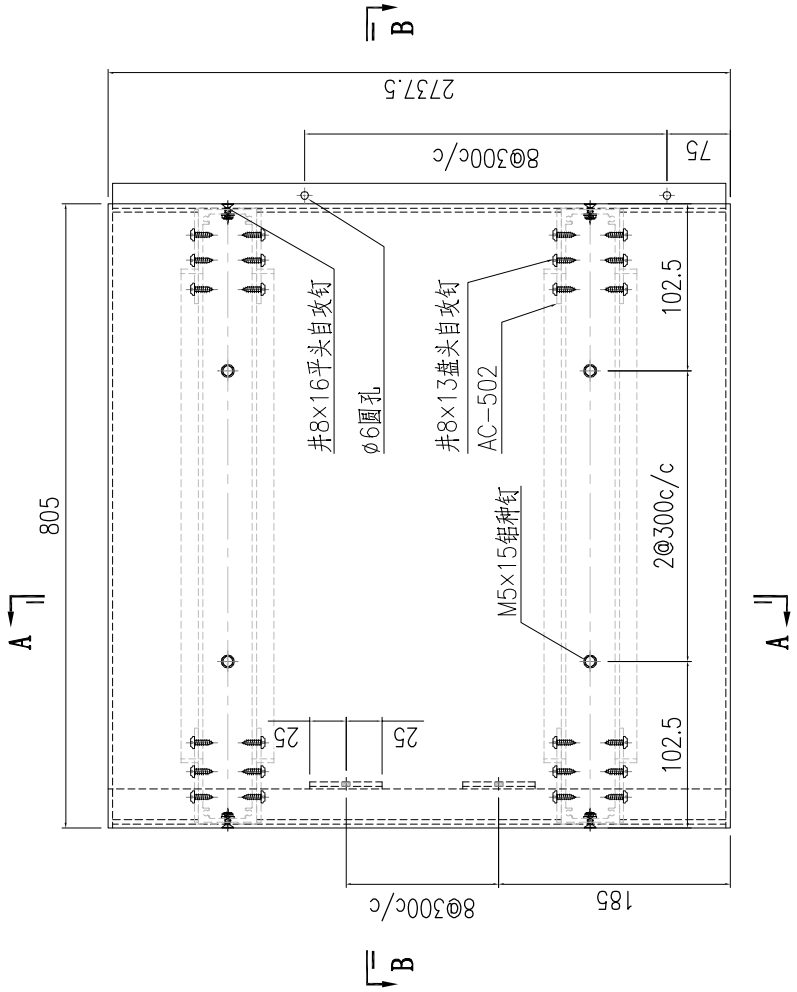

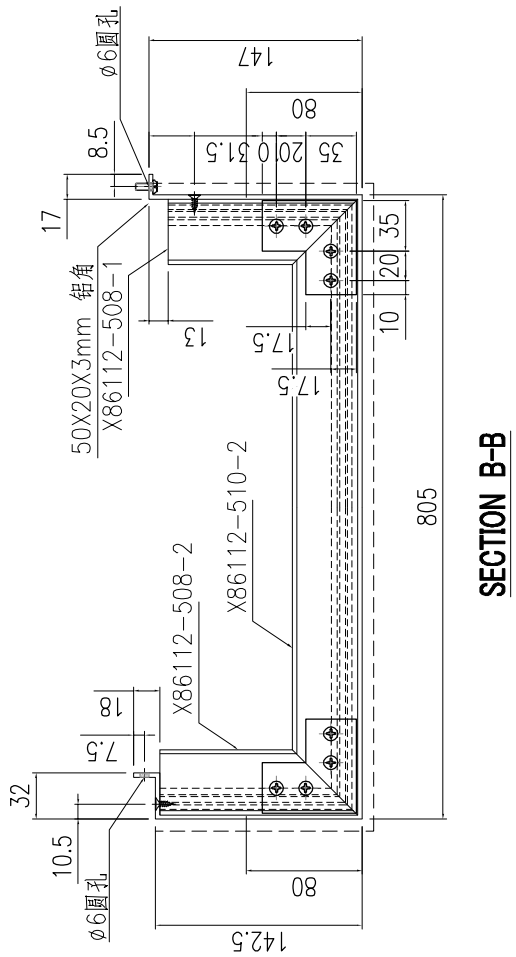



SECTION B-B




SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-908	
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文	20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安	20221210	單件重量	-	(KG)

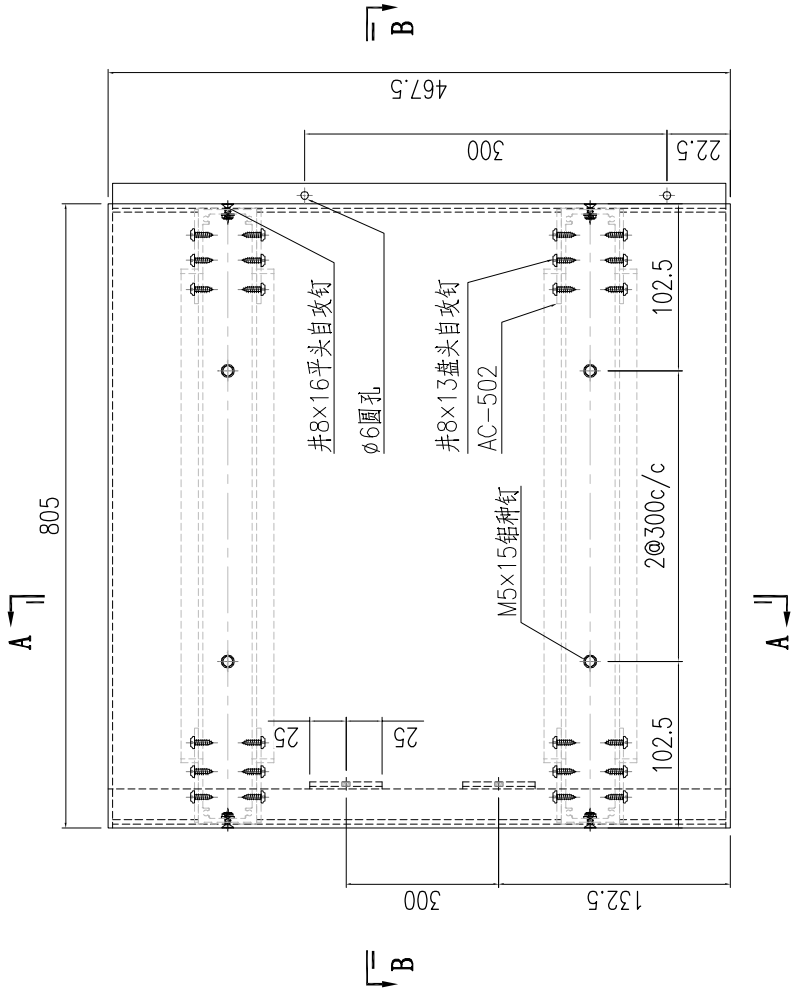

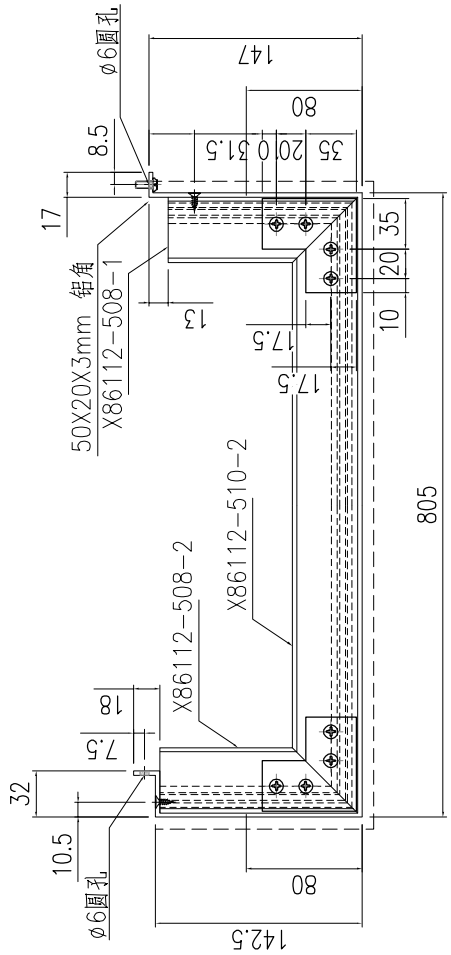



SECTION B-B

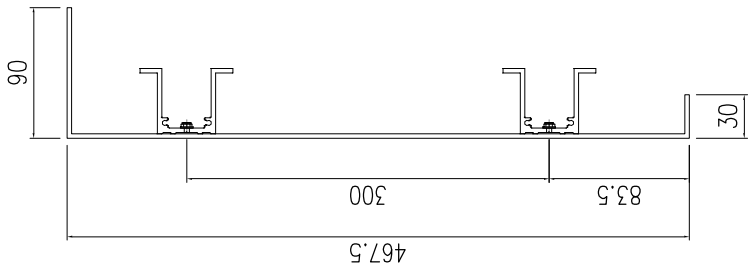


SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-909	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

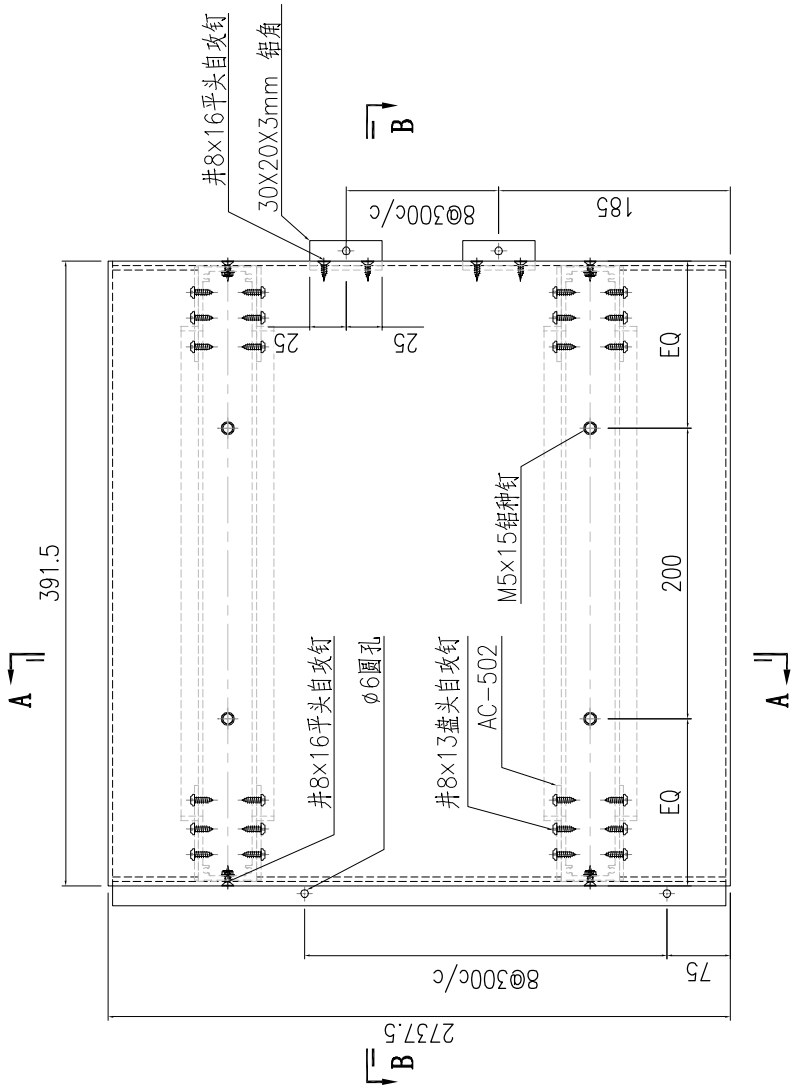

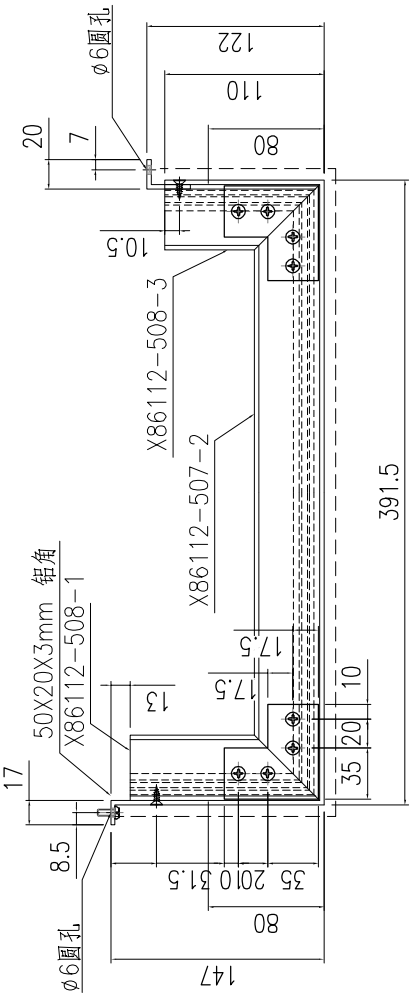



SECTION B-B




SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
								工程號	J857	類別		物料號	-		
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-910		
修改	-	-	-	採用	工廠	-	地盤	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1		
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1			材料	3mm 铝板	批准	林仁安 20221210	單件重量	-		(KG)

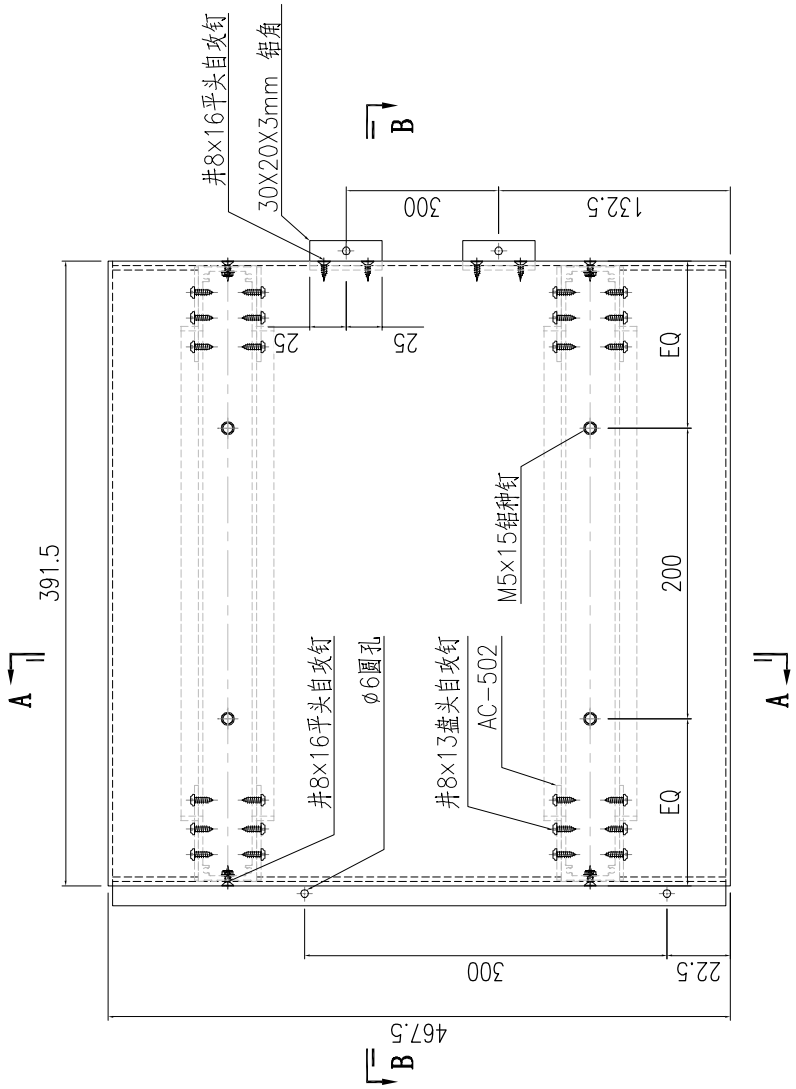

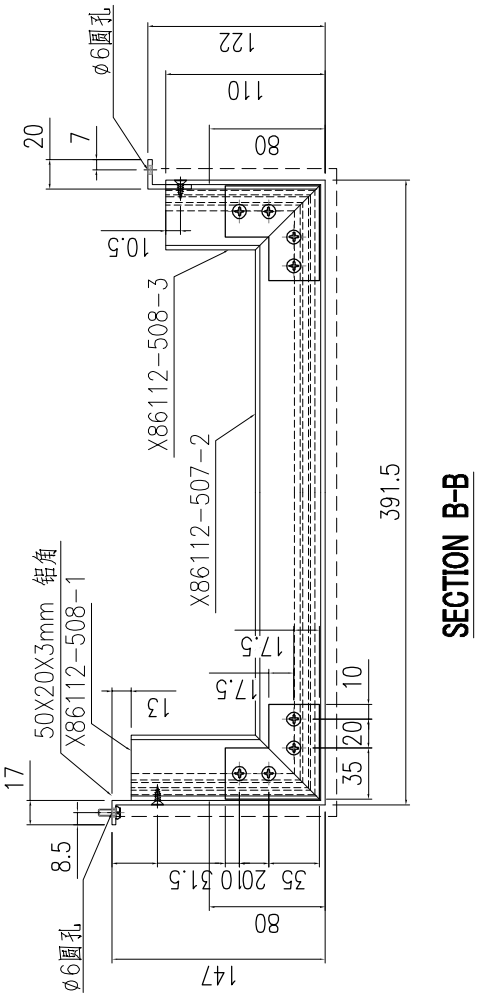



SECTION B-B

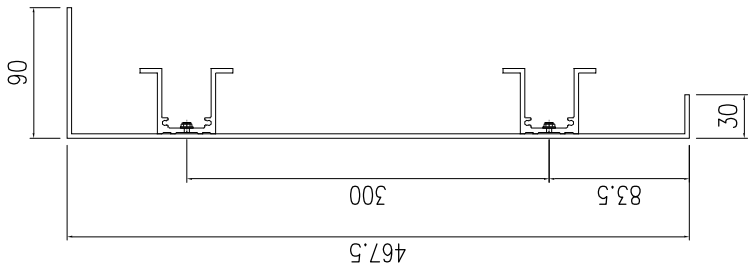

SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																
									工程號	J857	類別		物料號	-		
									地盘	啟德6552	制圖	陈梓豪 20221206		圖號	AC-911	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209		數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210		單件重量	-	(KG)

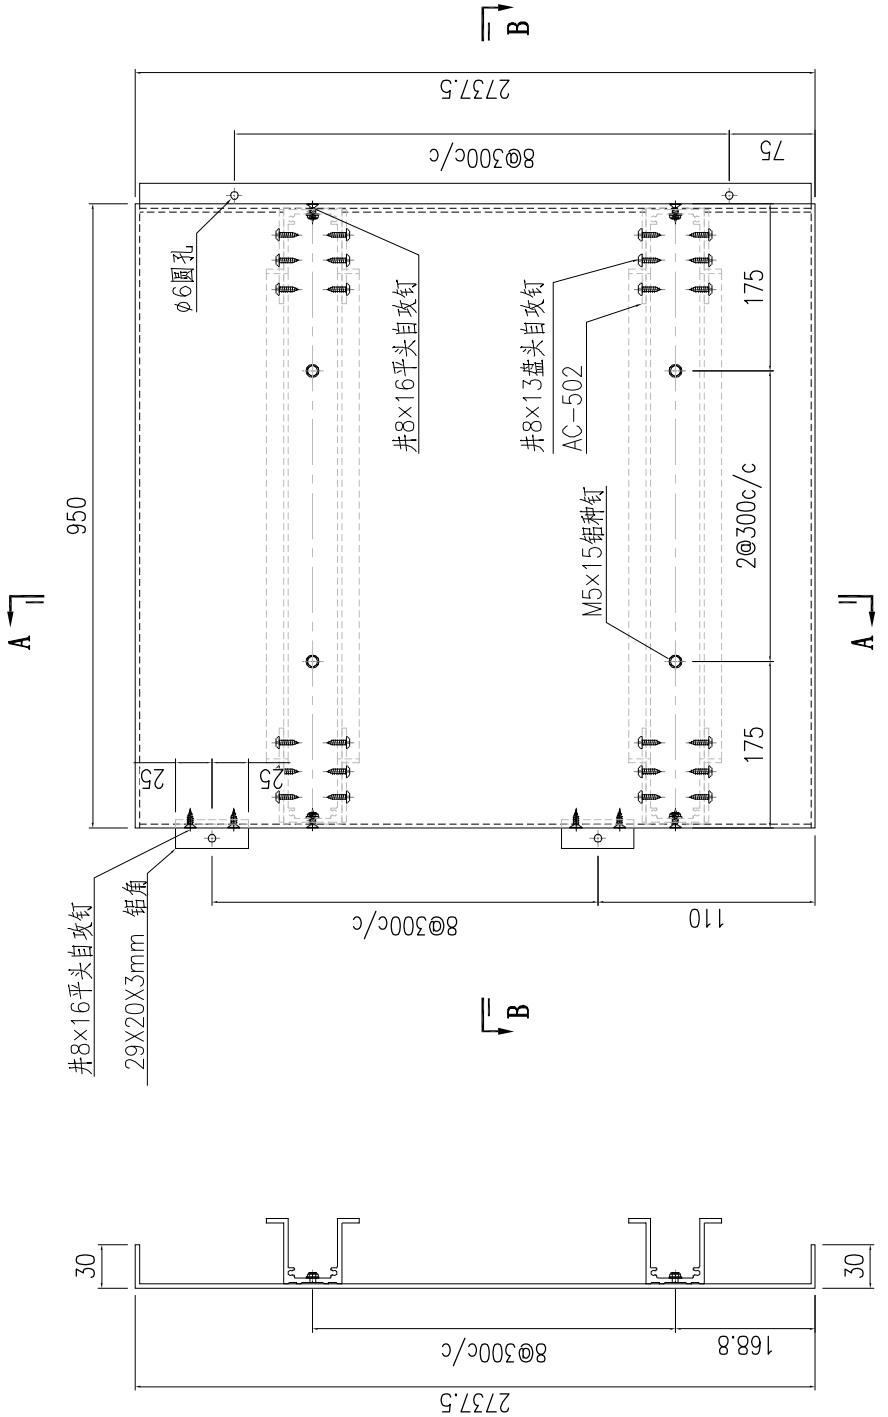


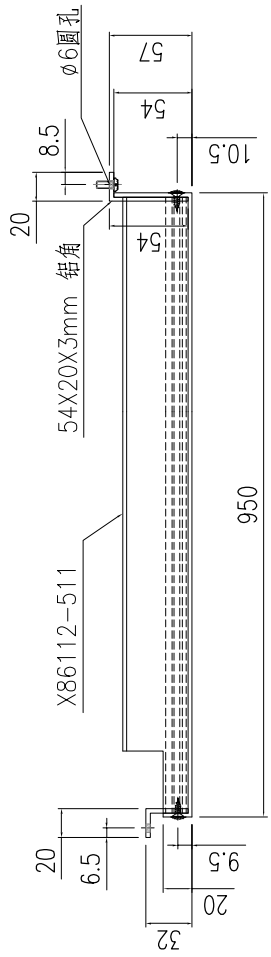


SECTION B-B

SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.																	
									工程號	J857	類別		物料號	-			
									地盘	啟德6552	制圖	陈梓豪	20221206	圖號	AC-912		
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文	20221209	數量	1		
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安	20221210	單件重量	-		(KG)

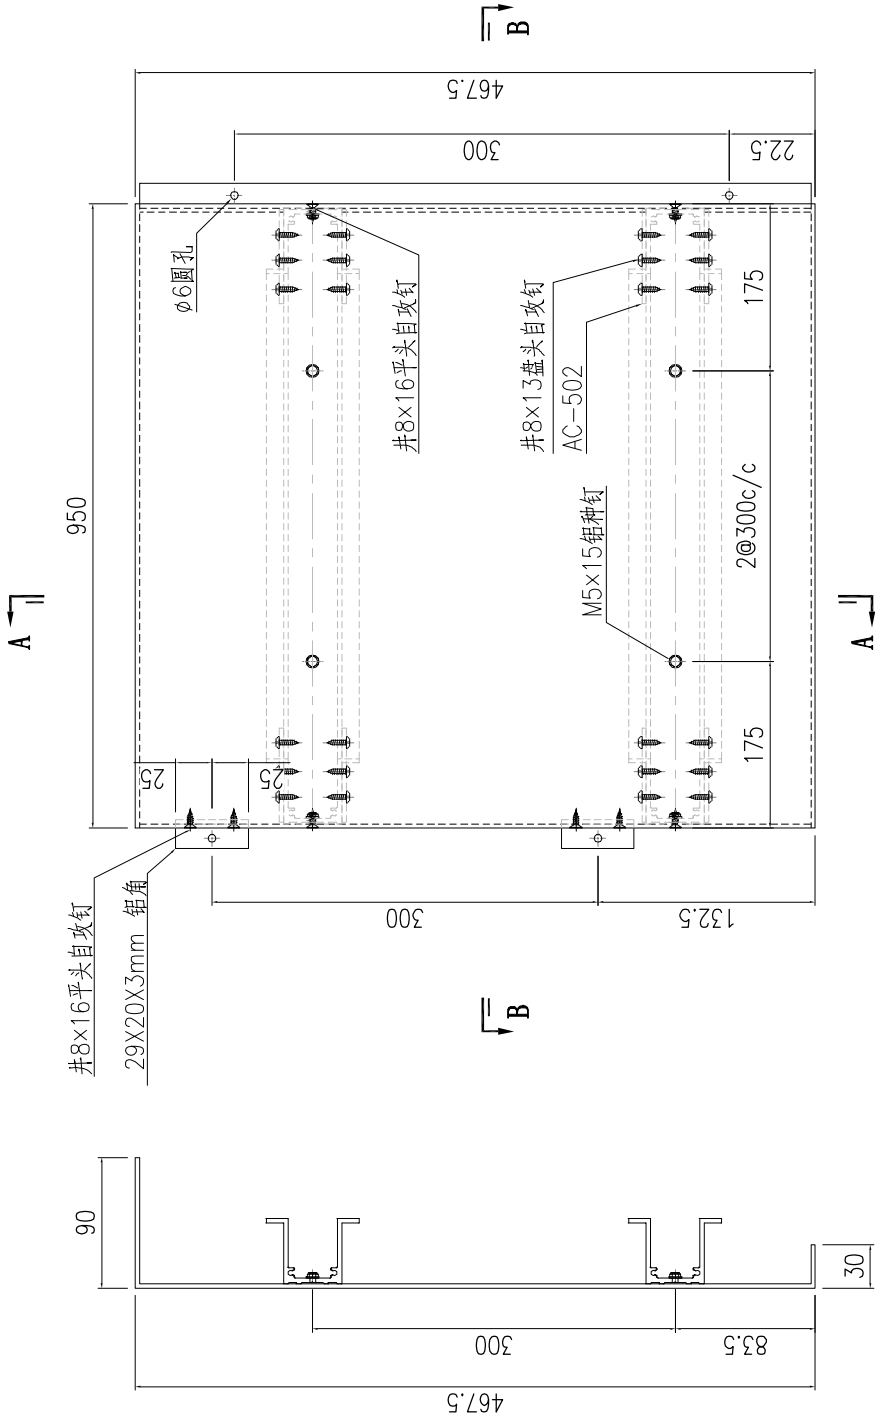


SECTION A-A

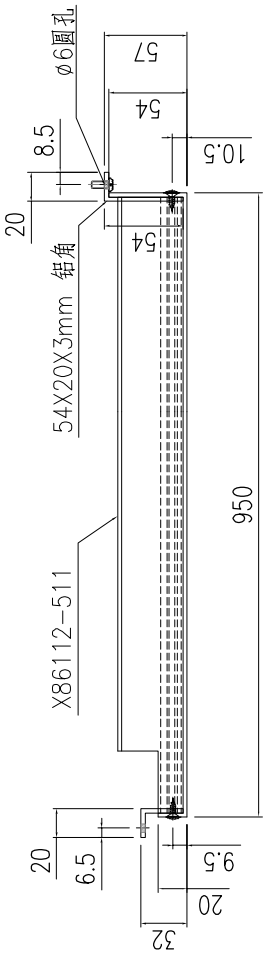


SECTION B-B


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盤	啟德6552	制圖	陈梓豪 20221206	圖號	AC-822	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 鋁板	批准	林仁安 20221210	單件重量	-	(KG)

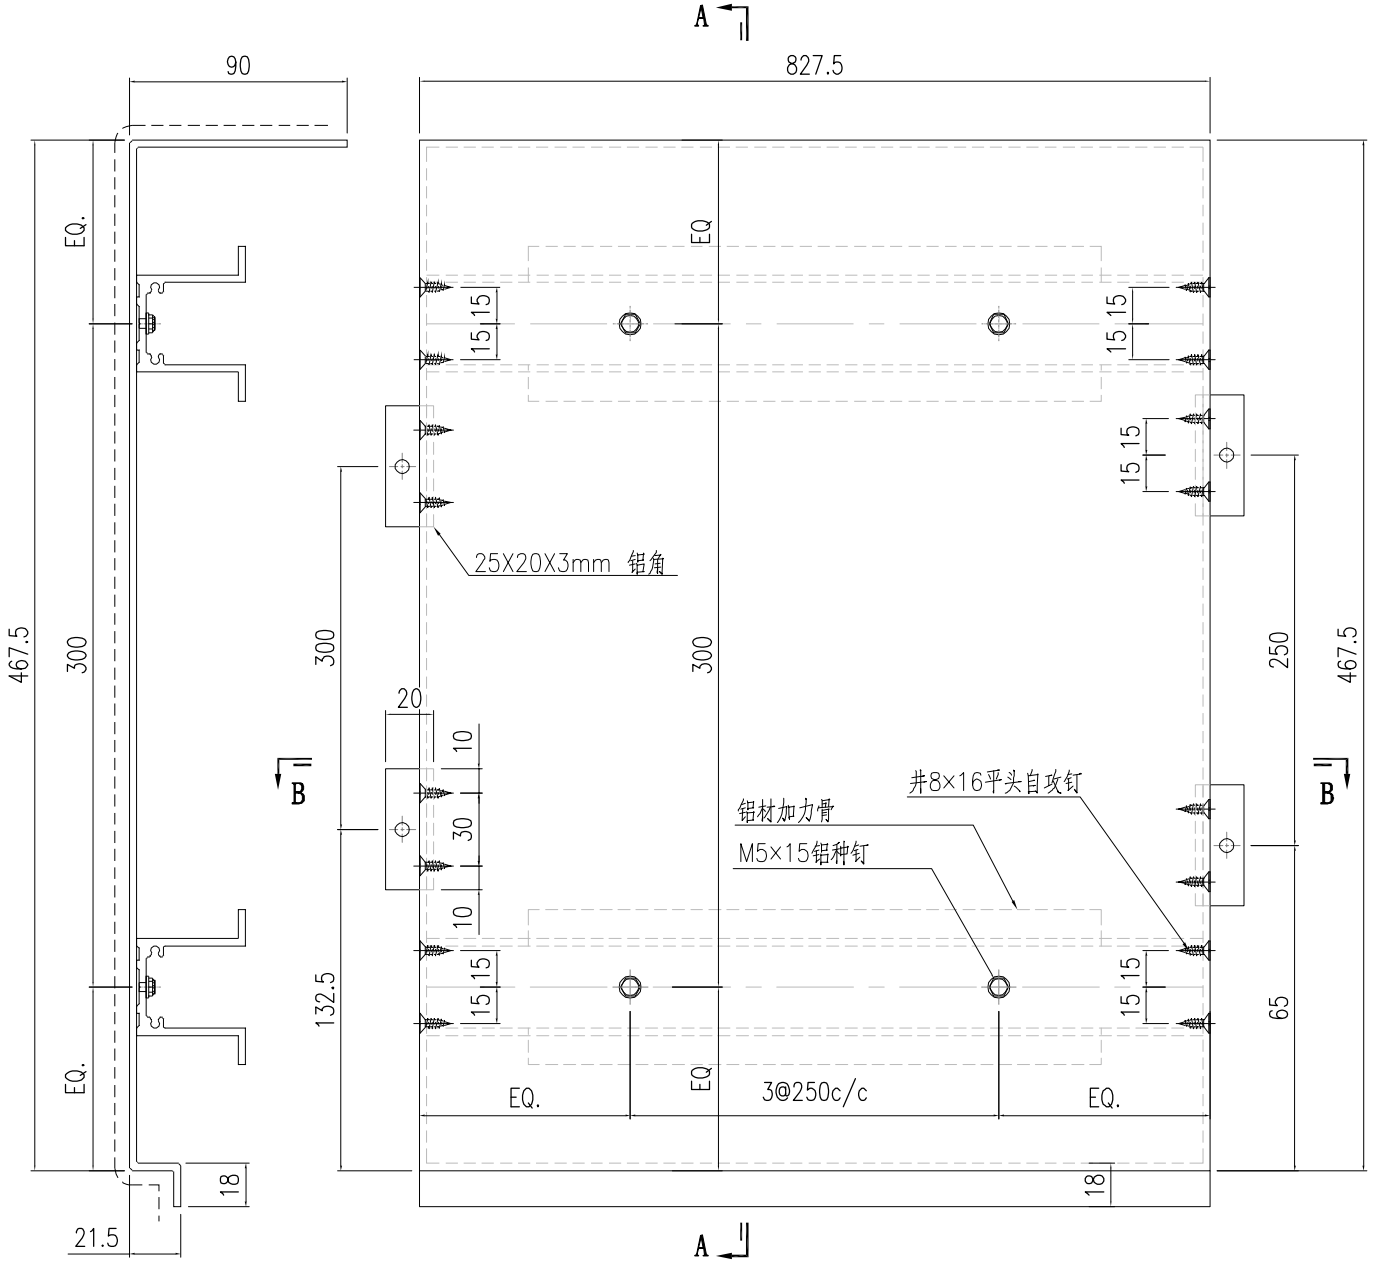

SECTION A-A

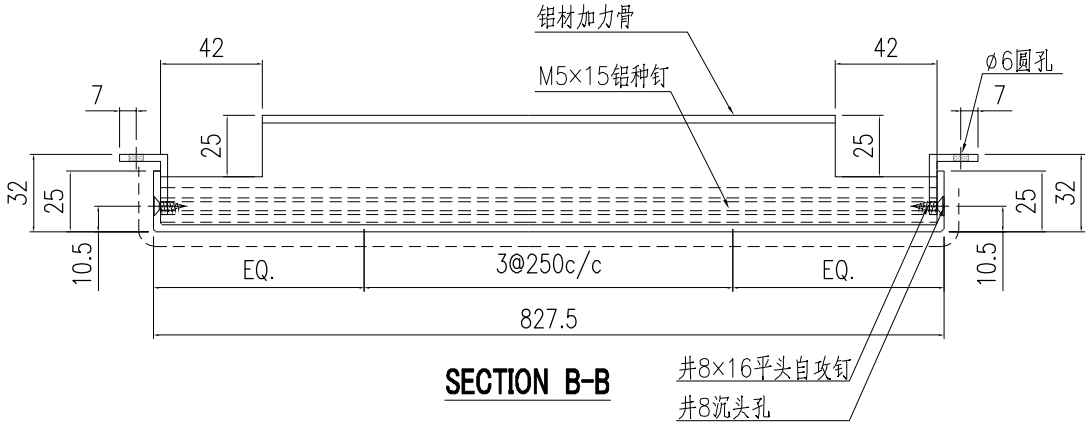


SECTION B-B



铝角码仔孔位示意


铝板长宽数据見AC-822a

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-951
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-
日期	-	-	-	材料颜色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

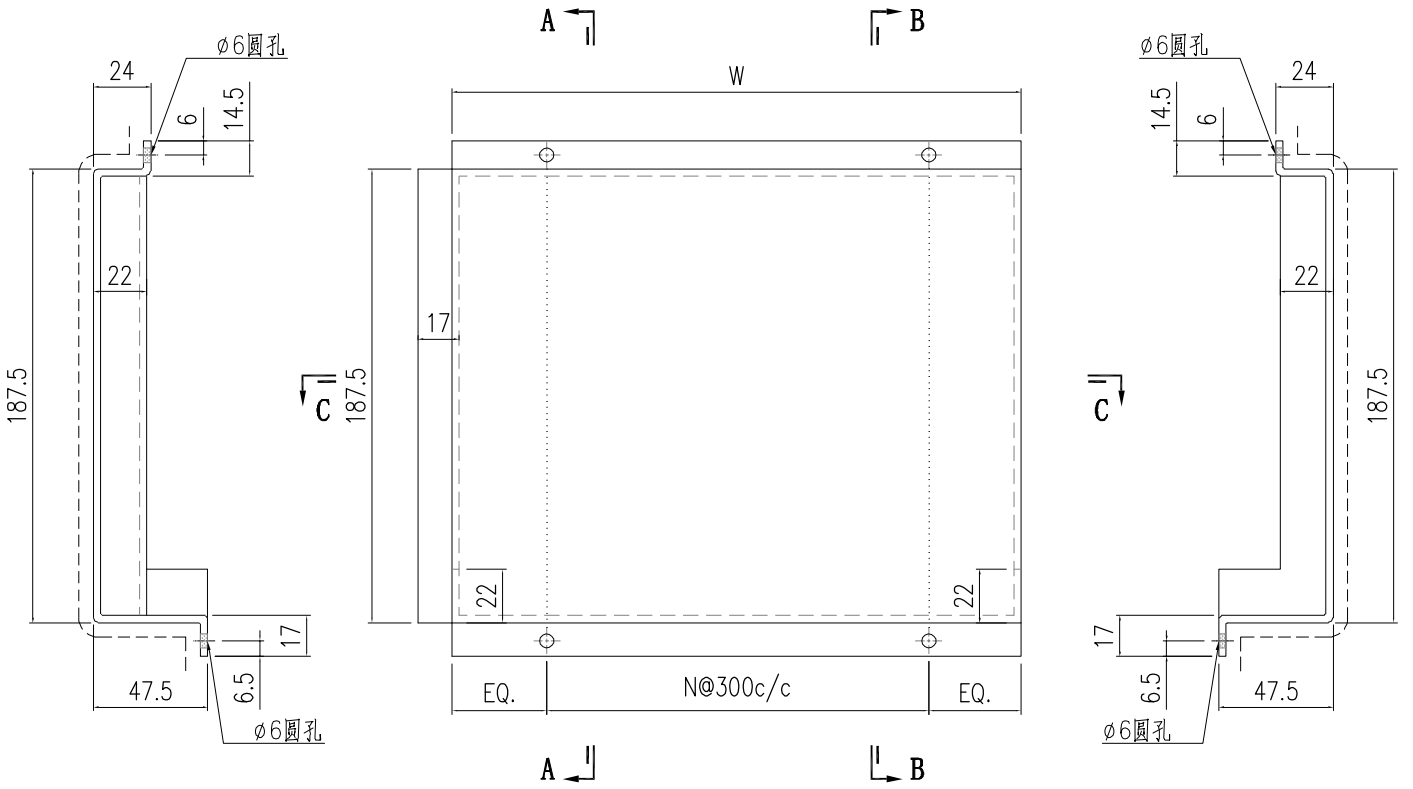

SECTION A-A

SECTION B-B

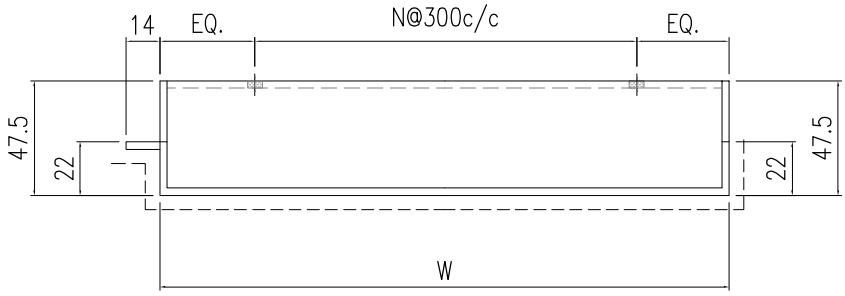


SECTION C-C


14	AC-951-14	1	760	7
13	AC-951-13	1	1135.5	3
12	AC-951-12	1	842	4
11	AC-951-11	1	997	1
S/N	部件编号	部件数量	W	N


10	AC-951-10	2	870.5	2
9	AC-951-9	3	2232	7
8	AC-951-8	2	536	1
7	AC-951-7	2	718	2
6	AC-951-6	2	1450.5	4
5	AC-951-5	2	842	2
4	AC-951-4	1	2170.5	7
3	AC-951-3	1	957	3
2	AC-951-2	1	1345.5	4
1	AC-951-1	4	632	1
S/N	部件编号	部件数量	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-952	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	-	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

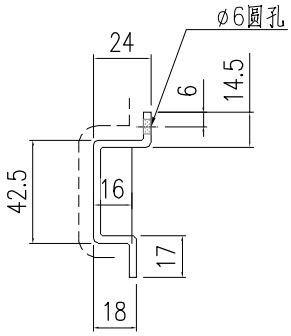

SECTION A-A

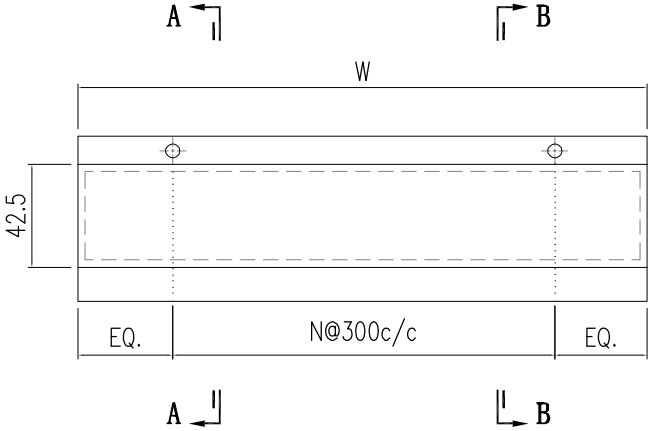


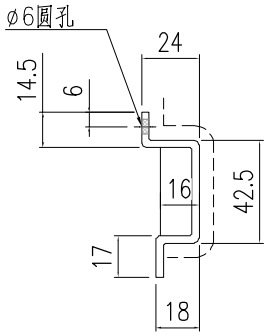

SECTION B-B

S/N	部件编号	部件数量	W	N
6	AC-952-6	1	1270.5	4
5	AC-952-5	1	1345.5	4
4	AC-952-4	4	1170.5	3
3	AC-952-3	1	1583	5
2	AC-952-2	1	1408	4
1	AC-952-1	8	632	1

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
									工程號	J857	類別		物料號	-	
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-953	
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1	
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

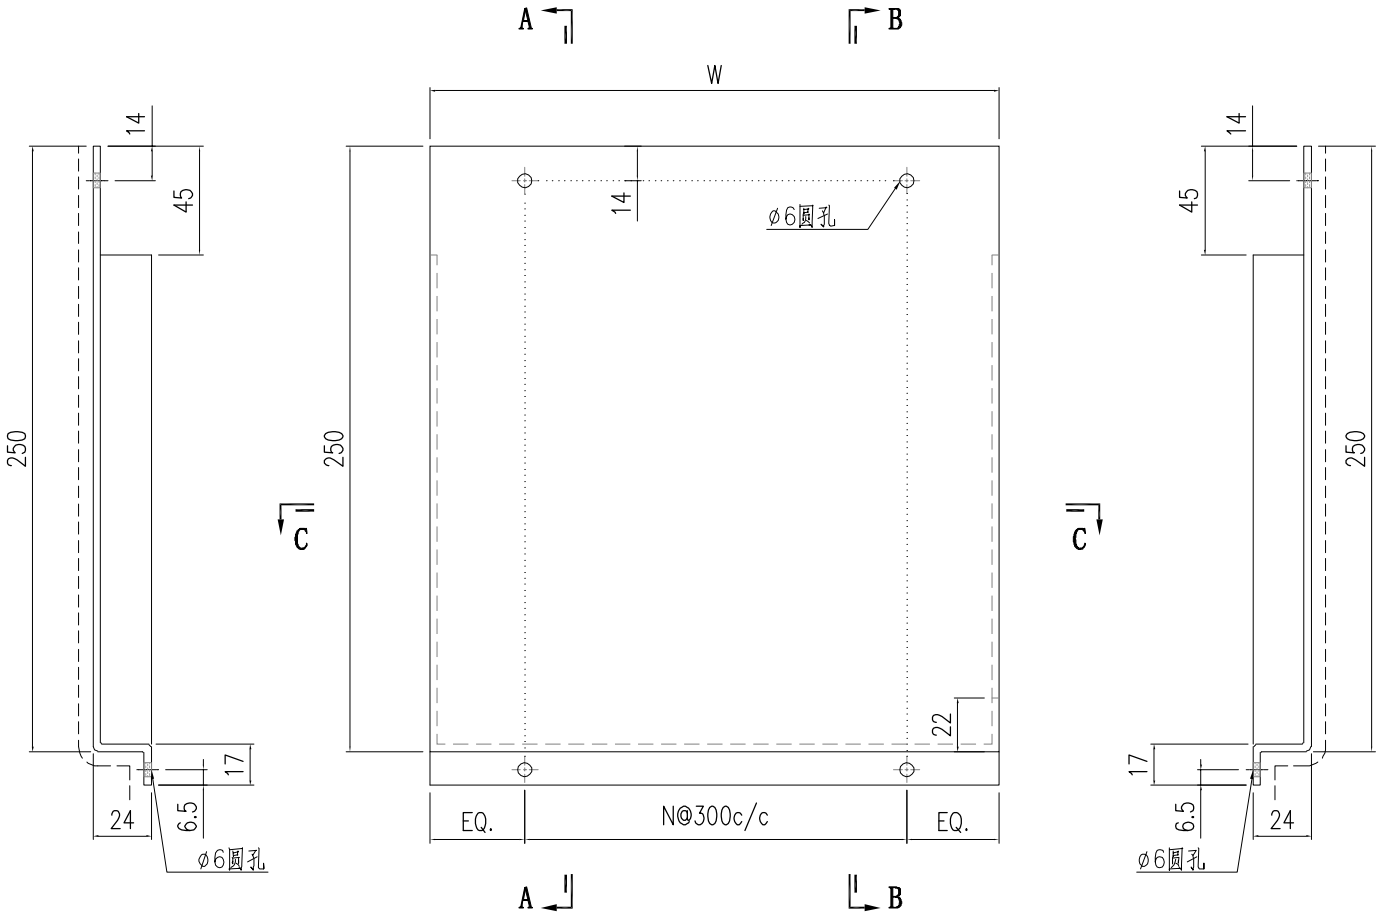


SECTION A-A

SECTION B-B


1	AC-951-1	3000	9
S/N	部件编号	W	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
									工程號	J857	類別		物料號	-
									地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-954
修改	-	-	-	採用	工廠	-	地盤	✓	图纸名称	鋁板加工圖	復核	練松文 20221209	數量	1
日期	-	-	-	材料顏色	AL2: ECK3M96295S-ZD1				材料	3mm 铝板	批准	林仁安 20221210	單件重量	- (KG)

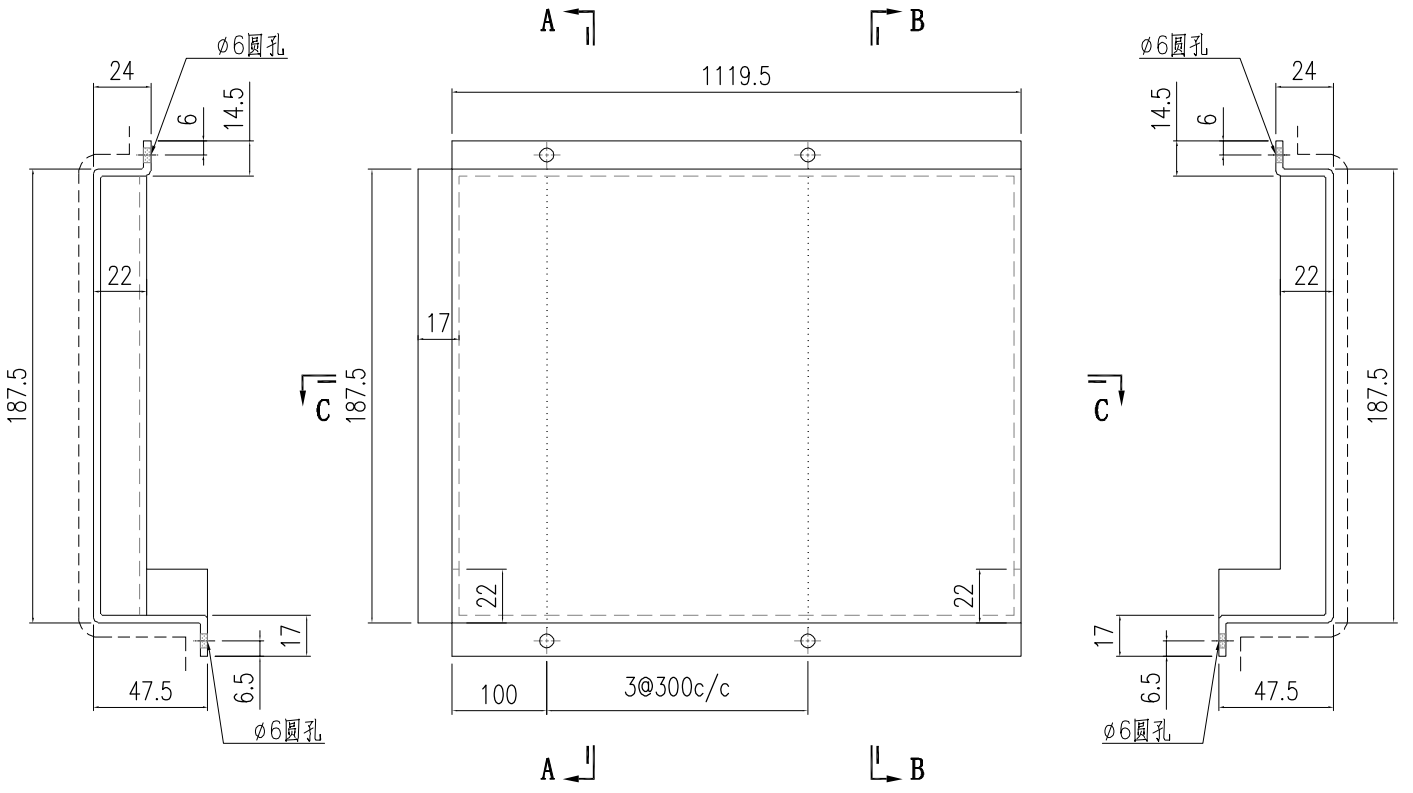


SECTION A-A


SECTION B-B

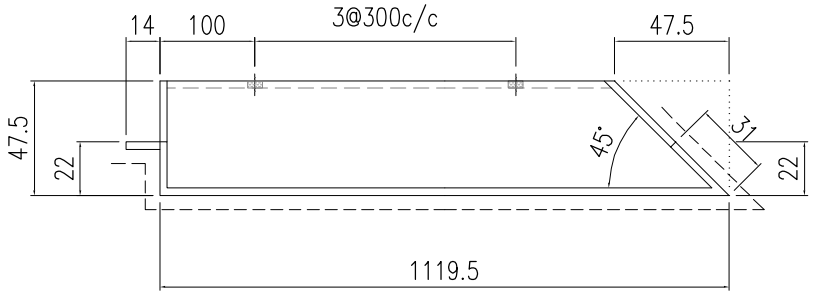

SECTION C-C

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.												
					工程號	J857	類別		物料號	-		
					地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-501	
修改	-	-	-	採用 工廠 ✓ 地盤 -	图纸名称	铝料加工图	復核	練松文	20221209	數量	-	
日期	-	-	-	材料颜色 鋯化	材料	X86112	批准	林仁安	20221210	單件重量	-	(KG)

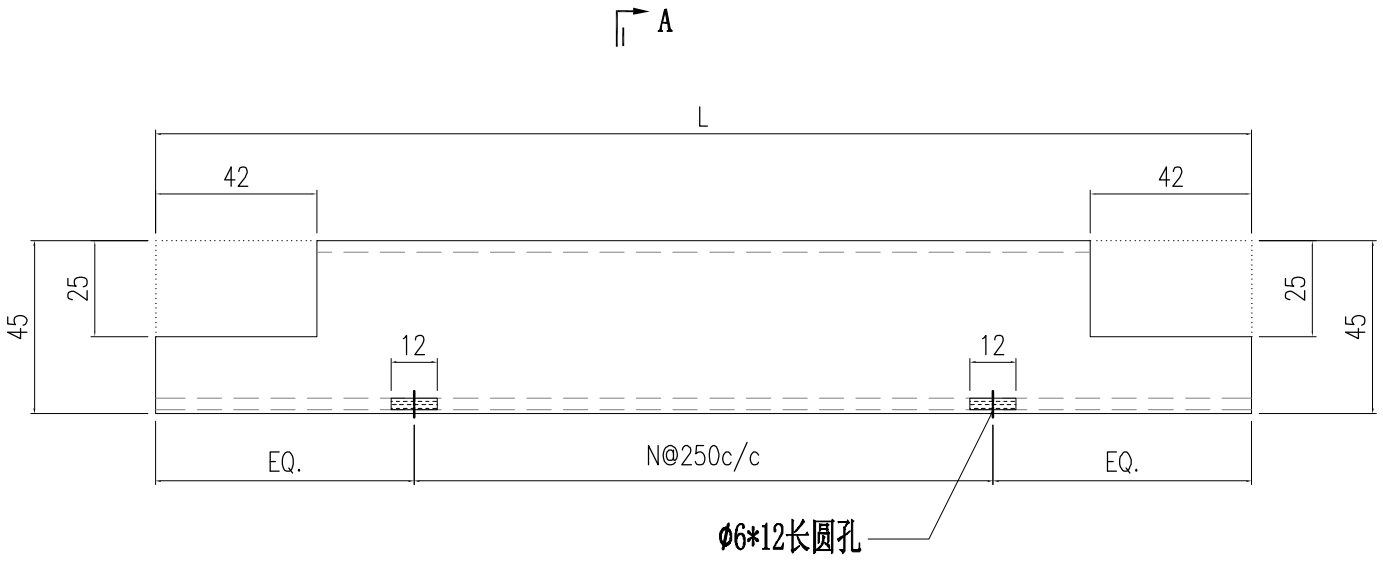


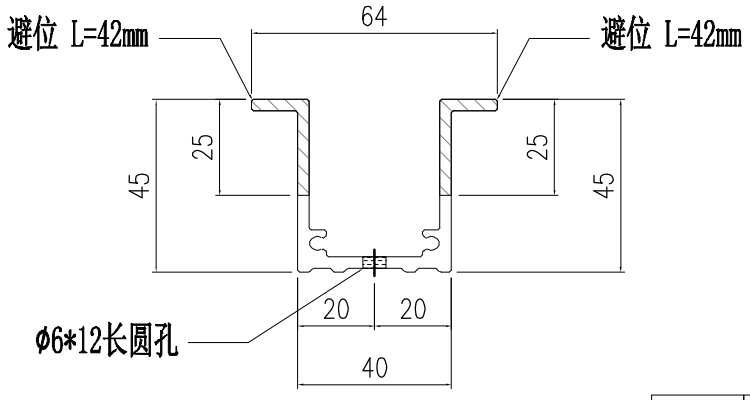


SECTION A-A


S/N	部件编号	L	N
12	X86112-501-12	818	3
11	X86112-501-11	1234	4
10	X86112-501-10	819	3
9	X86112-501-9	1234	4
8	X86112-501-8	1094	3
7	X86112-501-7	939	3
6	X86112-501-6	942	3
5	X86112-501-5	967	3
4	X86112-501-4	594	2
3	X86112-501-3	719	2
2	X86112-501-2	722	2
1	X86112-501-1	752	2

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
					工程號	J857	類別		物料號	-			
					地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-502		
修改	A	-	-	採用 工廠 ✓ 地盤 -	图纸名称	铝料加工图	復核	練松文	20221209	數量	-		
日期	9.15	-	-	材料颜色 鉻化	材料	X86112	批准	林仁安	20221210	單件重量	-		(KG)

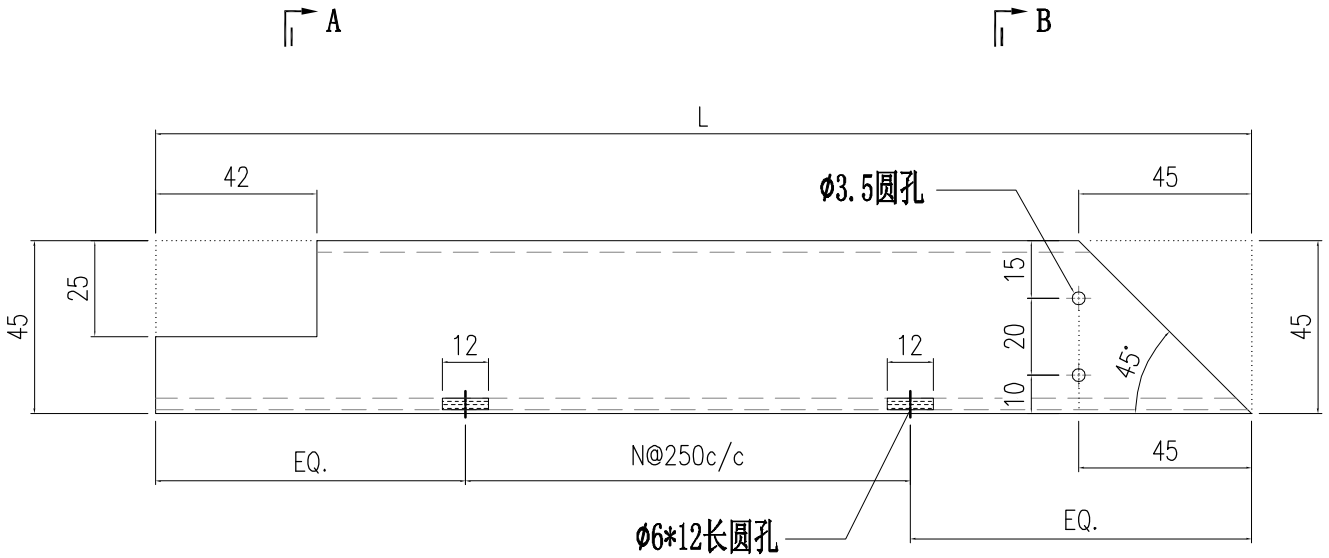

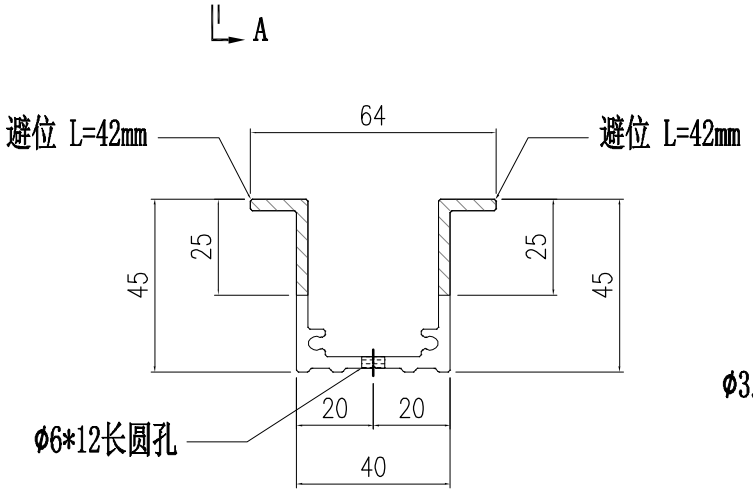


SECTION A-A

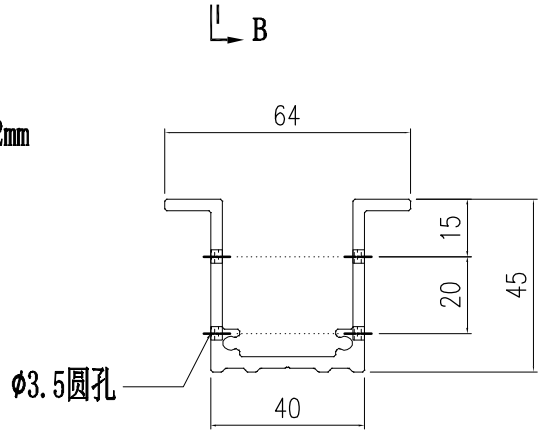


SECTION B-B

S/N	部件编号	L	N
8	X86112-502-8	767	2
7	X86112-502-7	752	2
6	X86112-502-6	477	1
5	X86112-502-5	677	2
4	X86112-502-4	542	1
3	X86112-502-3	517	1
2	X86112-502-2	549	1
1	X86112-502-1	674	2

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-503
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20221209	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20221210	單件重量	- (KG)

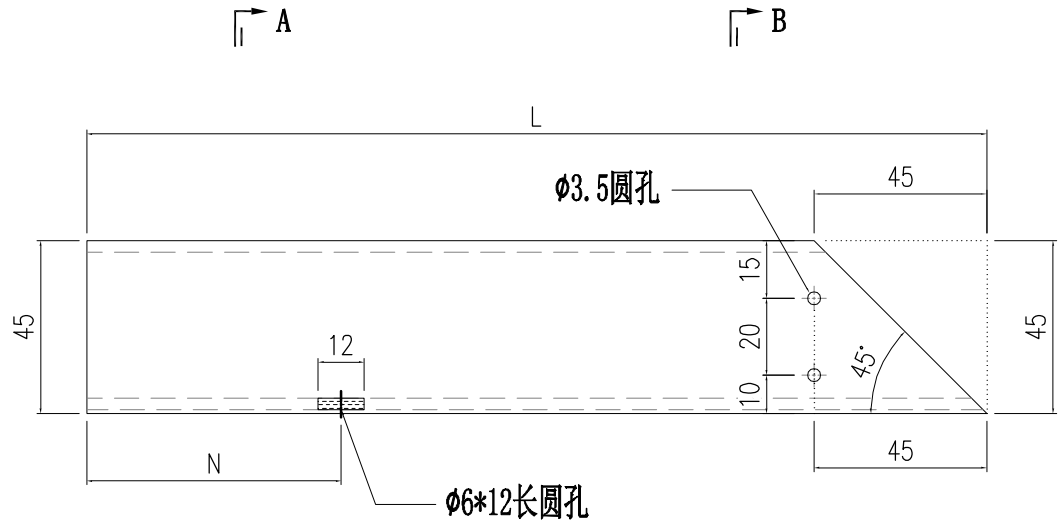

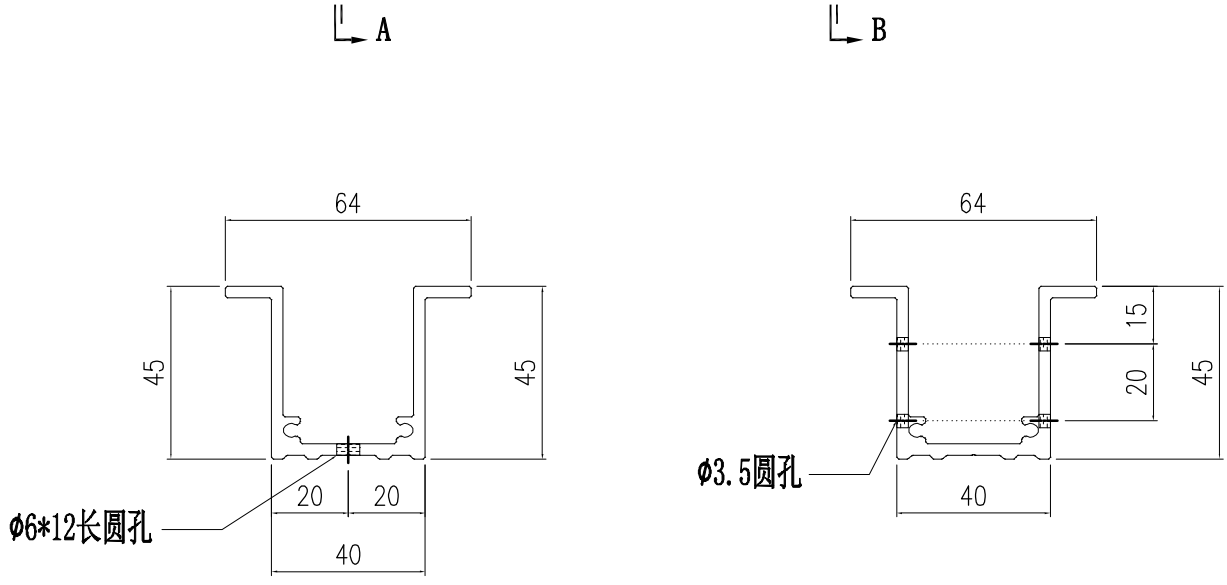



SECTION A-A

SECTION B-B


2	X86112-503-2	125	56
1	X86112-503-1	83	18
S/N	部件编号	L	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.												
							工程號	J857	類別		物料號	-		
							地盘	啟德6552	制圖	陈梓豪	20220915	圖號	X86112-504
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20220915	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20220915	單件重量	- (KG)

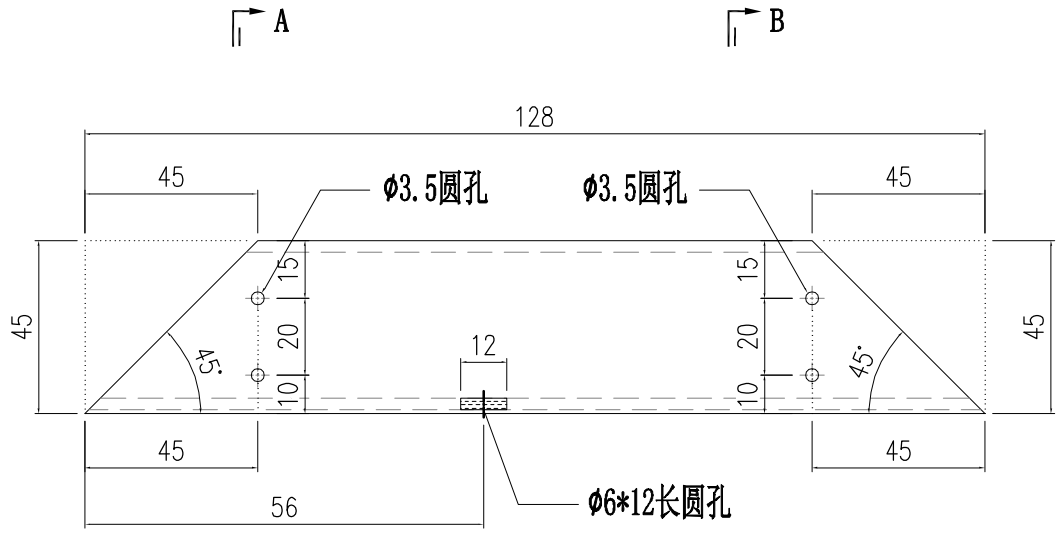

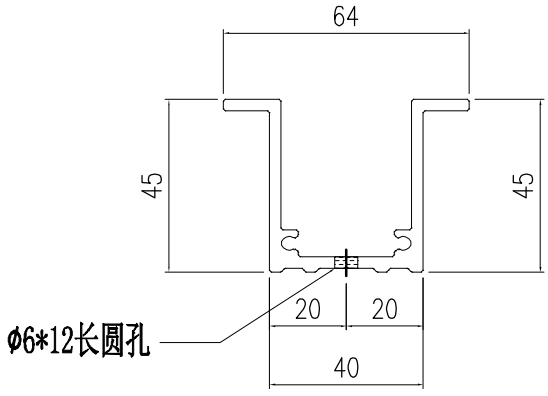



SECTION A-A

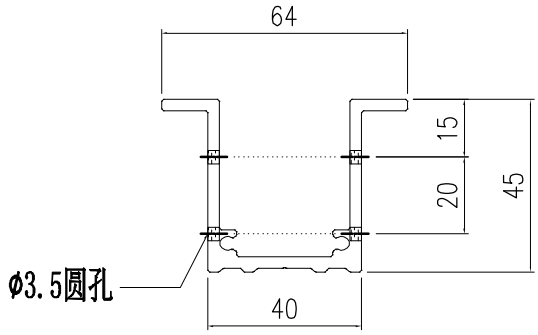

SECTION B-B


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20220915	圖號	X86112-505
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20220915	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20220915	單件重量	- (KG)

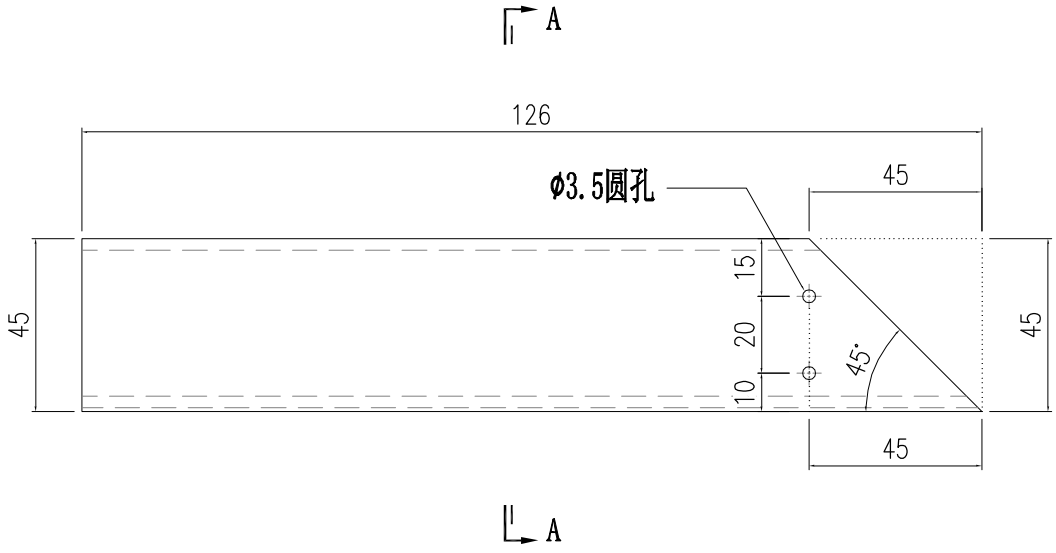


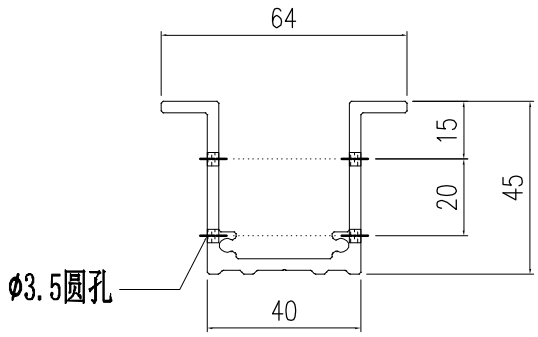

SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.											
				工程號	J857	類別		物料號	-		
				地盘	啟德6552	制圖	陈梓豪	20220915	圖號	X86112-506	
修改	A	-	-	採用	工廠 ✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20220915	數量	-	
日期	9.15	-	-	材料颜色	鉻化			材料	X86112	批准	林仁安	20220915	單件重量	-	(KG)

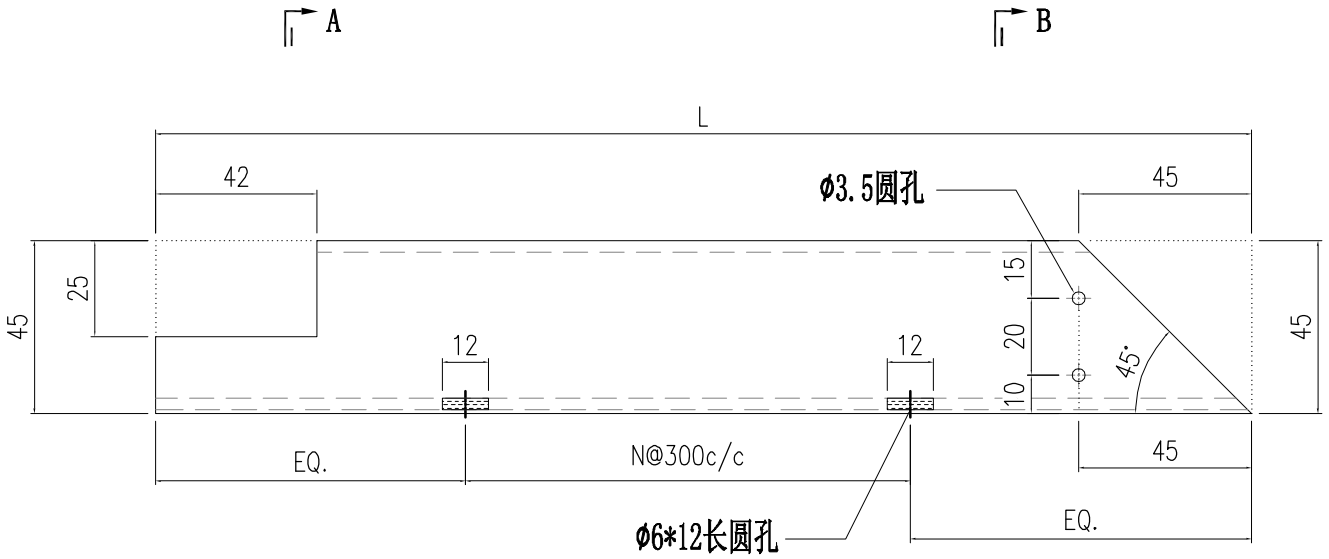

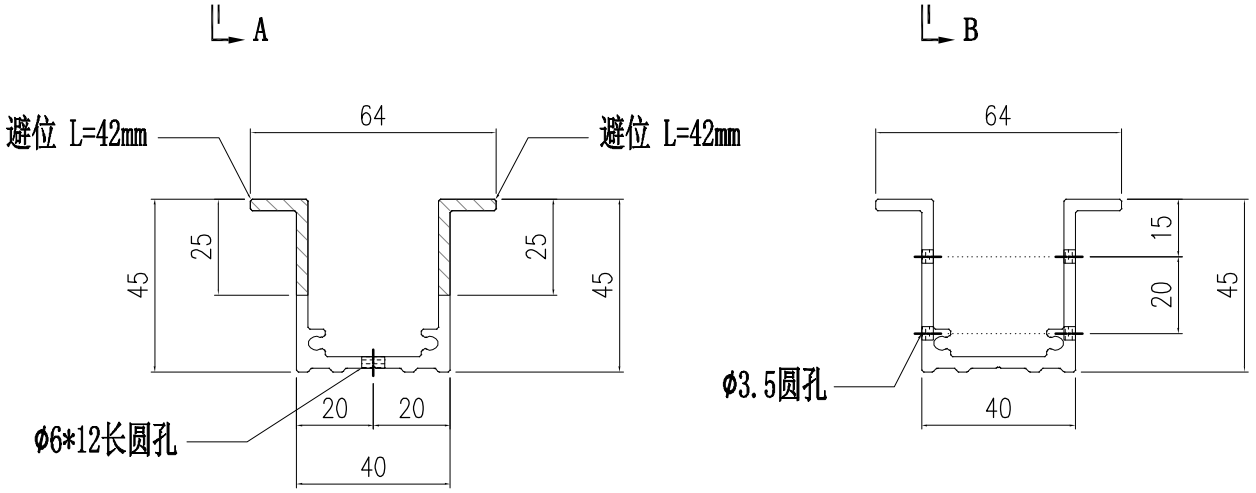



SECTION A-A

SECTION B-B


7	X86112-506-7	1209	3
6	X86112-506-6	1049	3
5	X86112-506-5	1024	3
4	X86112-506-4	932	2
3	X86112-506-3	842	2
2	X86112-506-2	827	2
1	X86112-506-1	552	1
S/N	部件编号	L	N

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20220915	圖號	X86112-507
修改	-	-	-	採用	工廠	✓	地盤	-	复核	練松文	20220915	數量	-
日期	-	-	-	材料颜色	鉻化		材料	X86112	批准	林仁安	20220915	單件重量	- (KG)

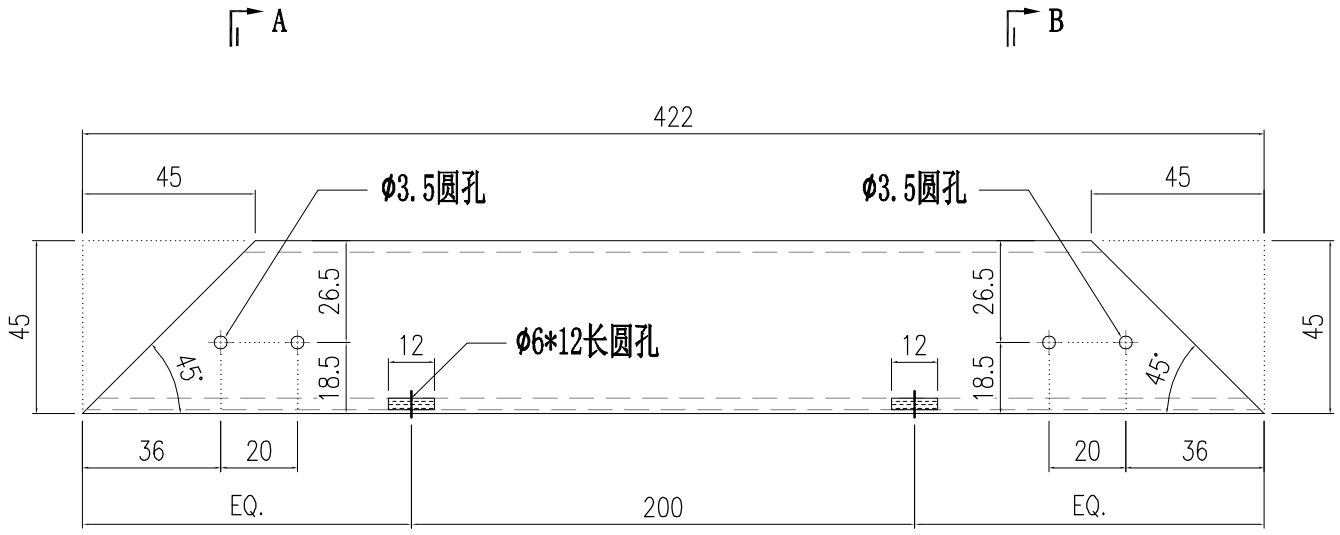

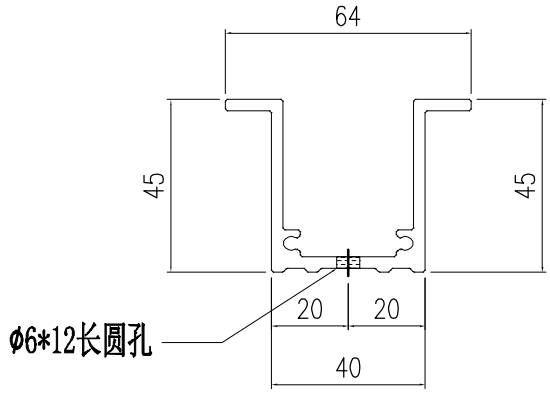


SECTION A-A

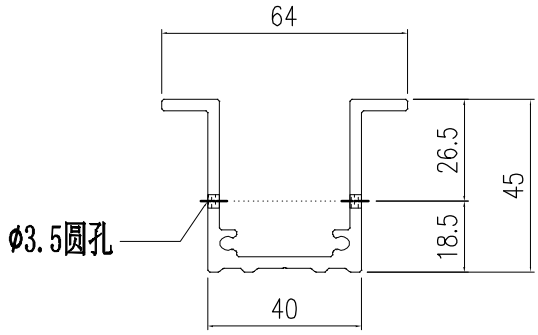


SECTION B-B

2	X86112-507-2	383
1	X86112-507-1	422
S/N	部件编号	L

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-508
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20221209	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20221210	單件重量	- (KG)

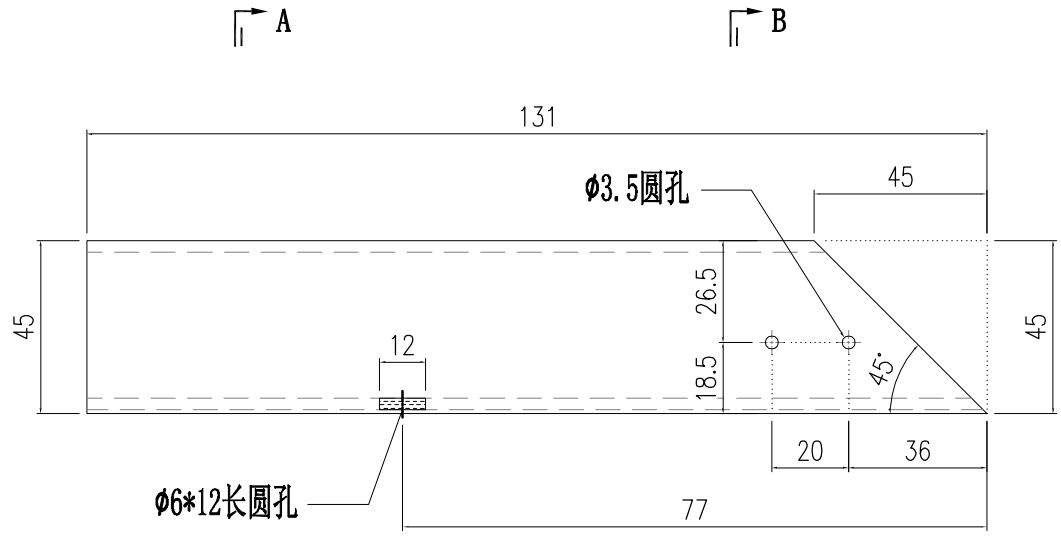

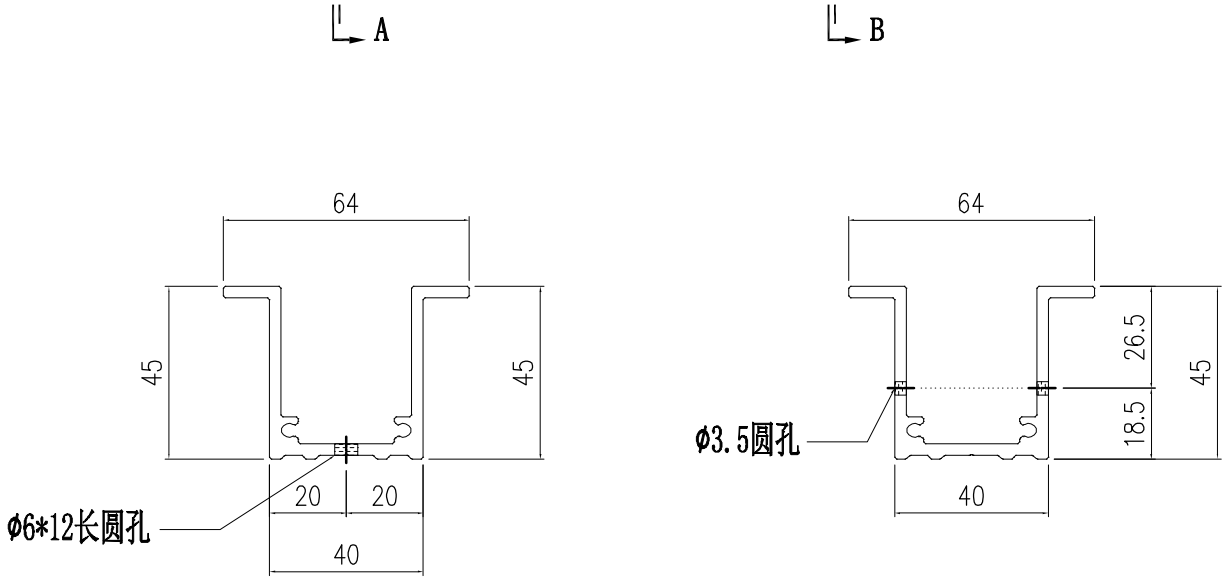



SECTION A-A

SECTION B-B


2	X86112-508-3	107
2	X86112-508-2	134
1	X86112-508-1	131
S/N	部件编号	L

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-509
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20221209	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20221210	單件重量	- (KG)

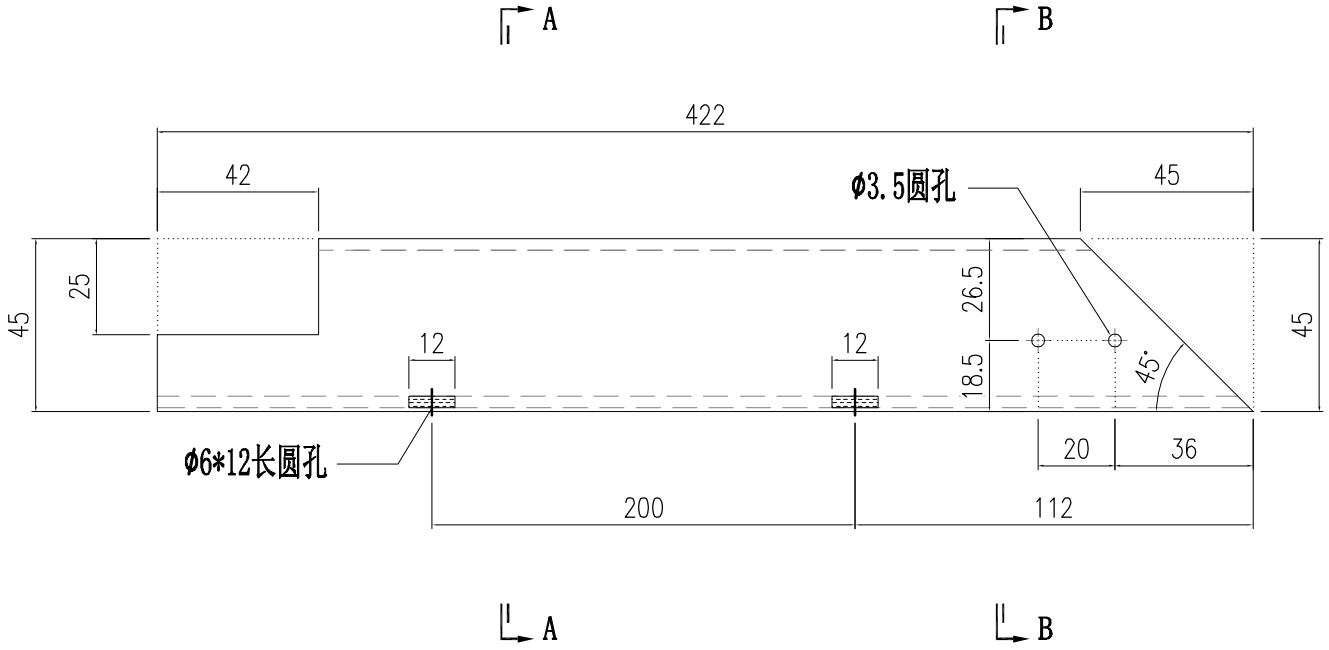

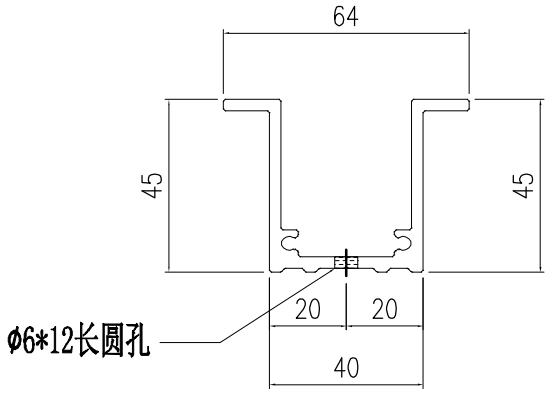



SECTION A-A

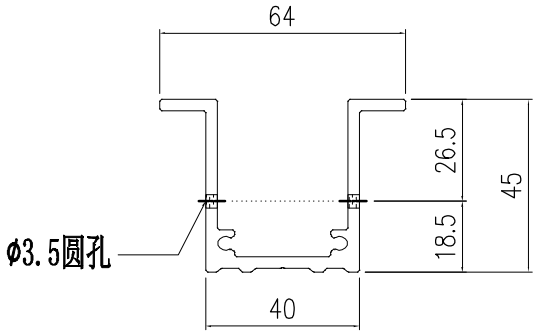


SECTION B-B

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20220915	圖號	X86112-510
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20220915	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20220915	單件重量	- (KG)

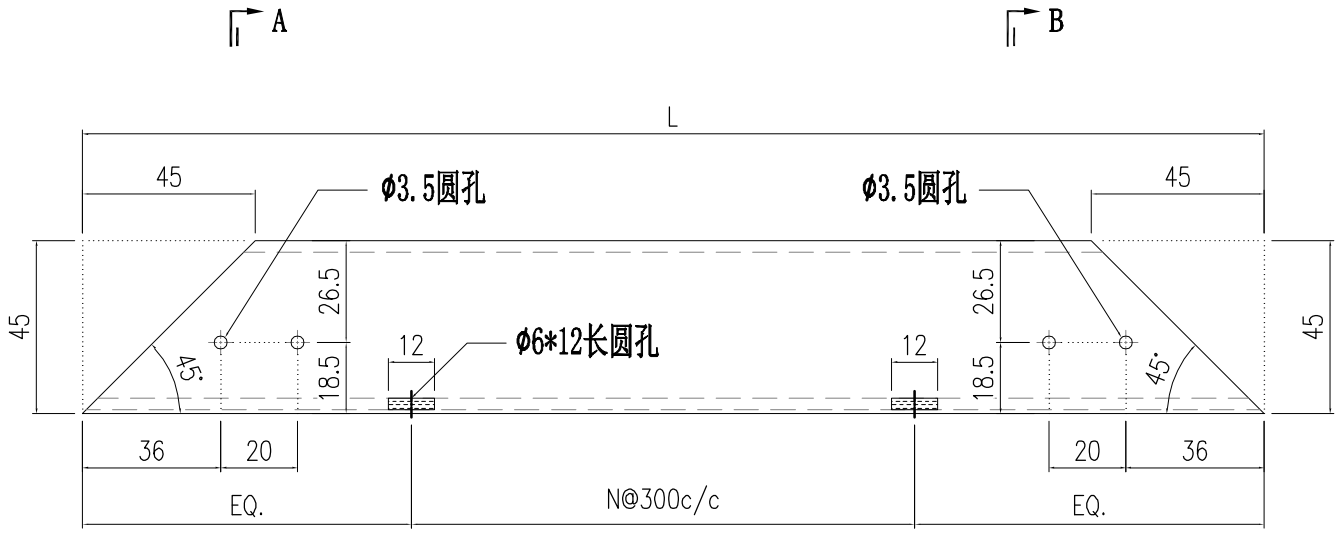

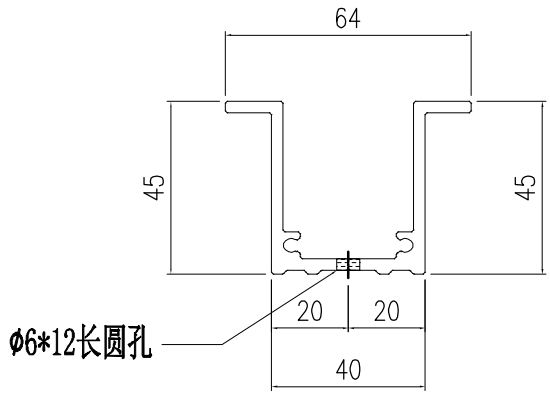


SECTION A-A

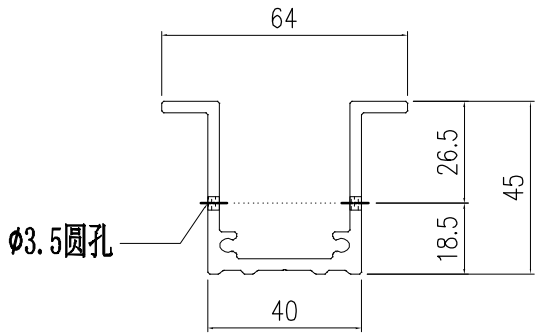


SECTION B-B

2	X86112-510-2	797	2
1	X86112-510-1	1097	3
S/N	部件编号	L	N


美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.													
							工程號	J857	類別		物料號	-	
							地盘	啟德6552	制圖	陈梓豪	20221206	圖號	X86112-511
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	铝料加工图	復核	練松文	20221209	數量	-
日期	-	-	-	材料颜色	鉻化				材料	X86112	批准	林仁安	20221210	單件重量	- (KG)

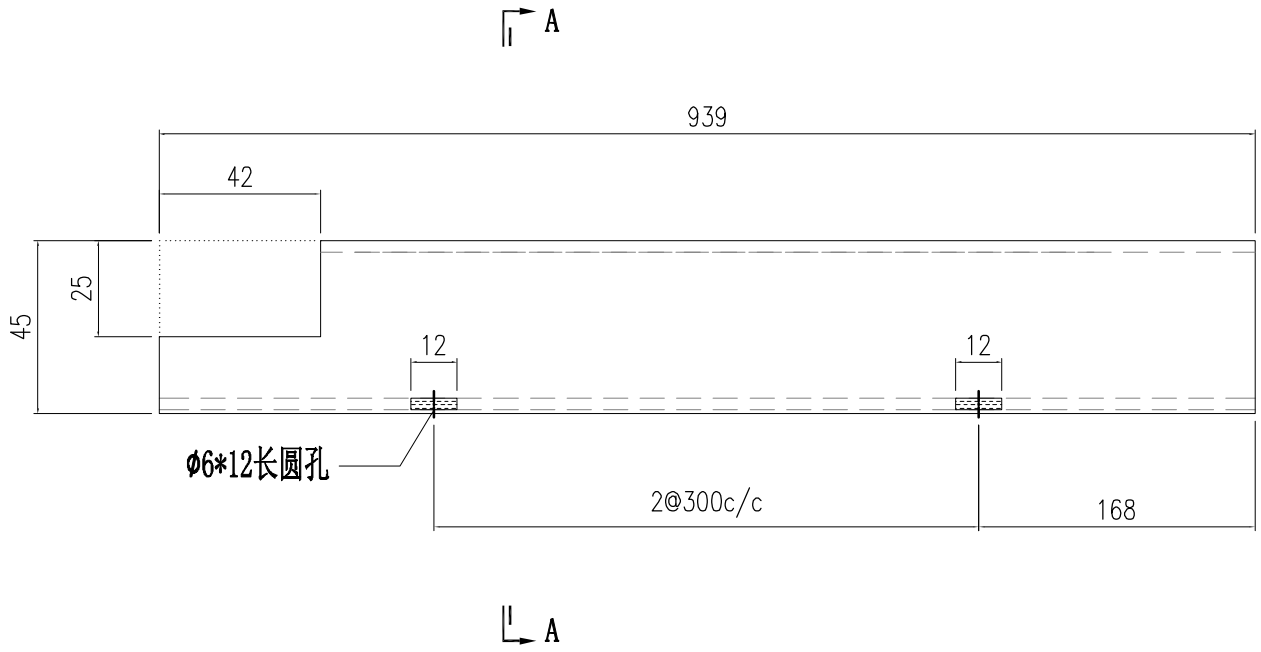

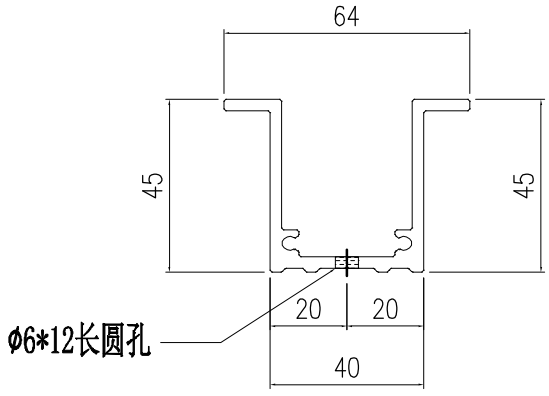



SECTION A-A

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.															
修改	-	-	-	採用	工廠	✓	地盤	-	工程號	J857	類別		物料號	-	
日期	-	-	-	材料顏色	鉻化				地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-501	
									图纸名称	收边铝板	復核	練松文 20221209	數量	-	
									材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

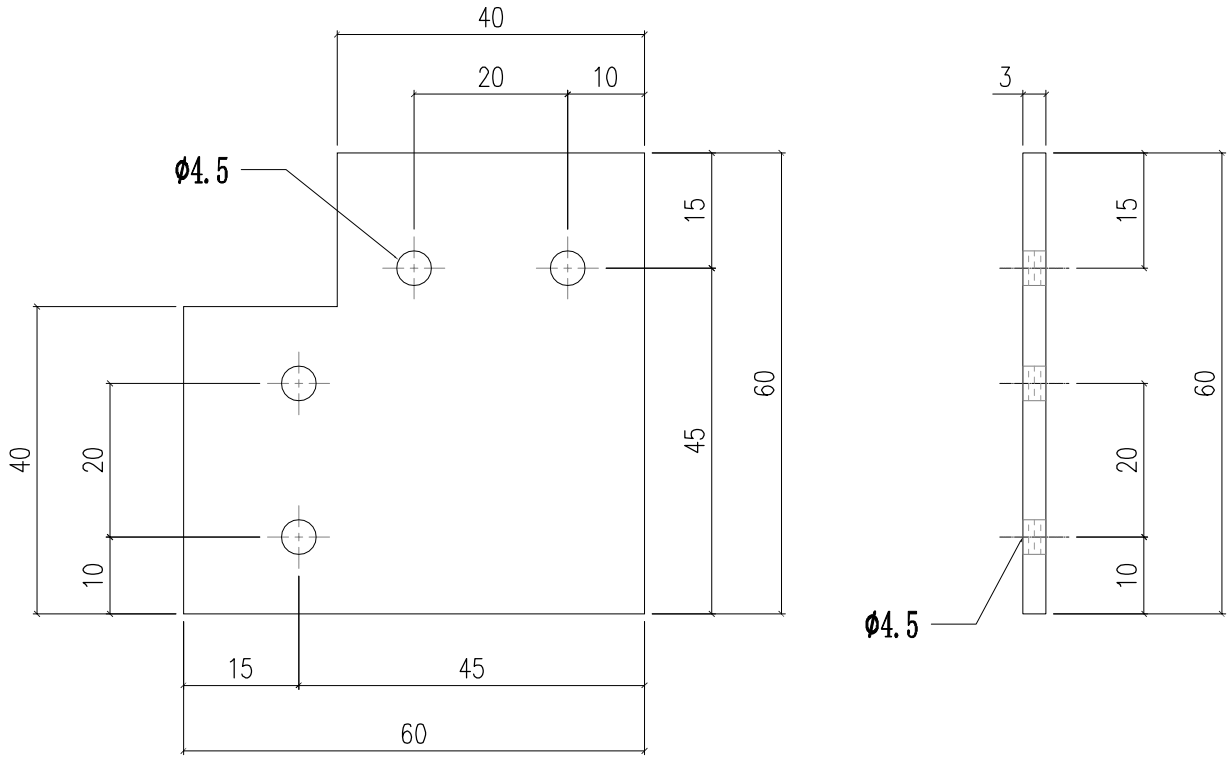

美特鋁質有限公司 MIDI Aluminium Fabricator Ltd.														
								工程號	J857	類別		物料號	-	
								地盘	啟德6552	制圖	陈梓豪 20221206	圖號	AC-502	
修改	-	-	-	採用	工廠	✓	地盤	-	图纸名称	收边铝板	復核	練松文 20221209	數量	-	
日期	-	-	-	材料顏色	鉻化				材料	3mm 铝板	批准	林仁安 20221210	單件重量	-	(KG)

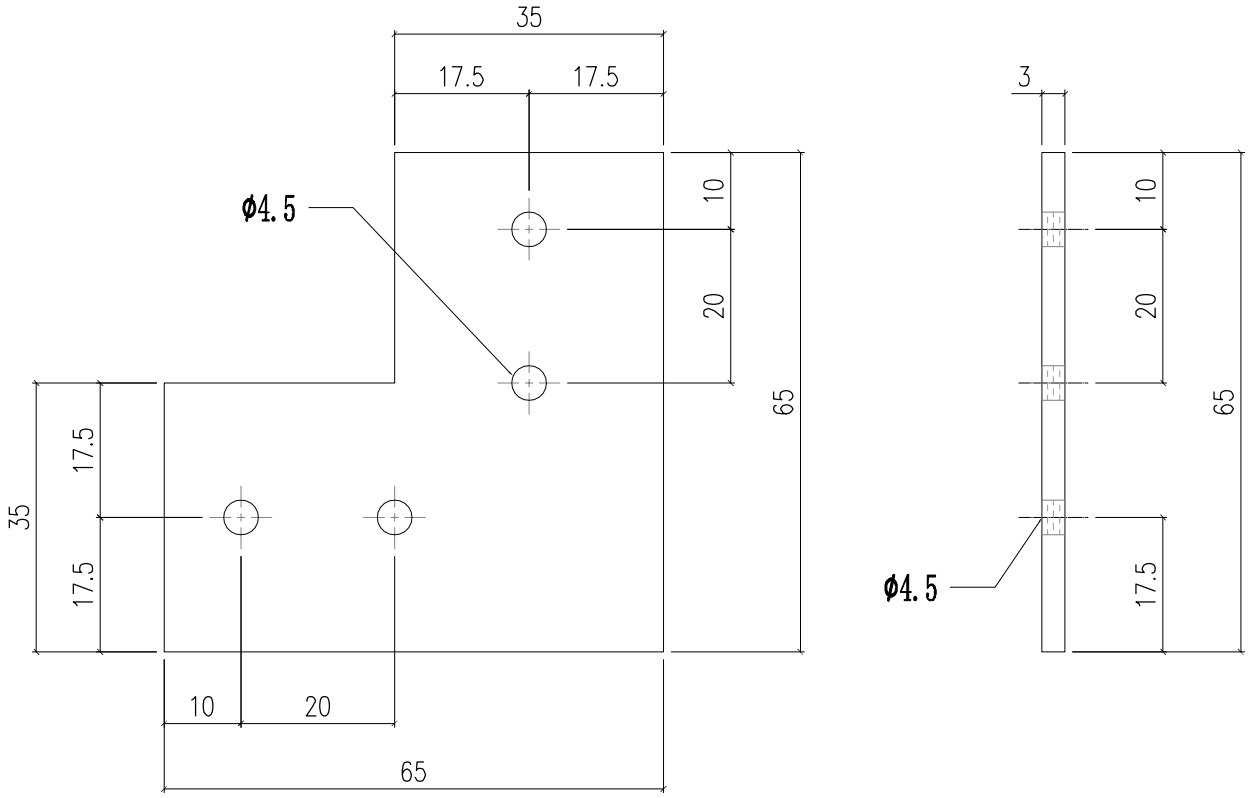

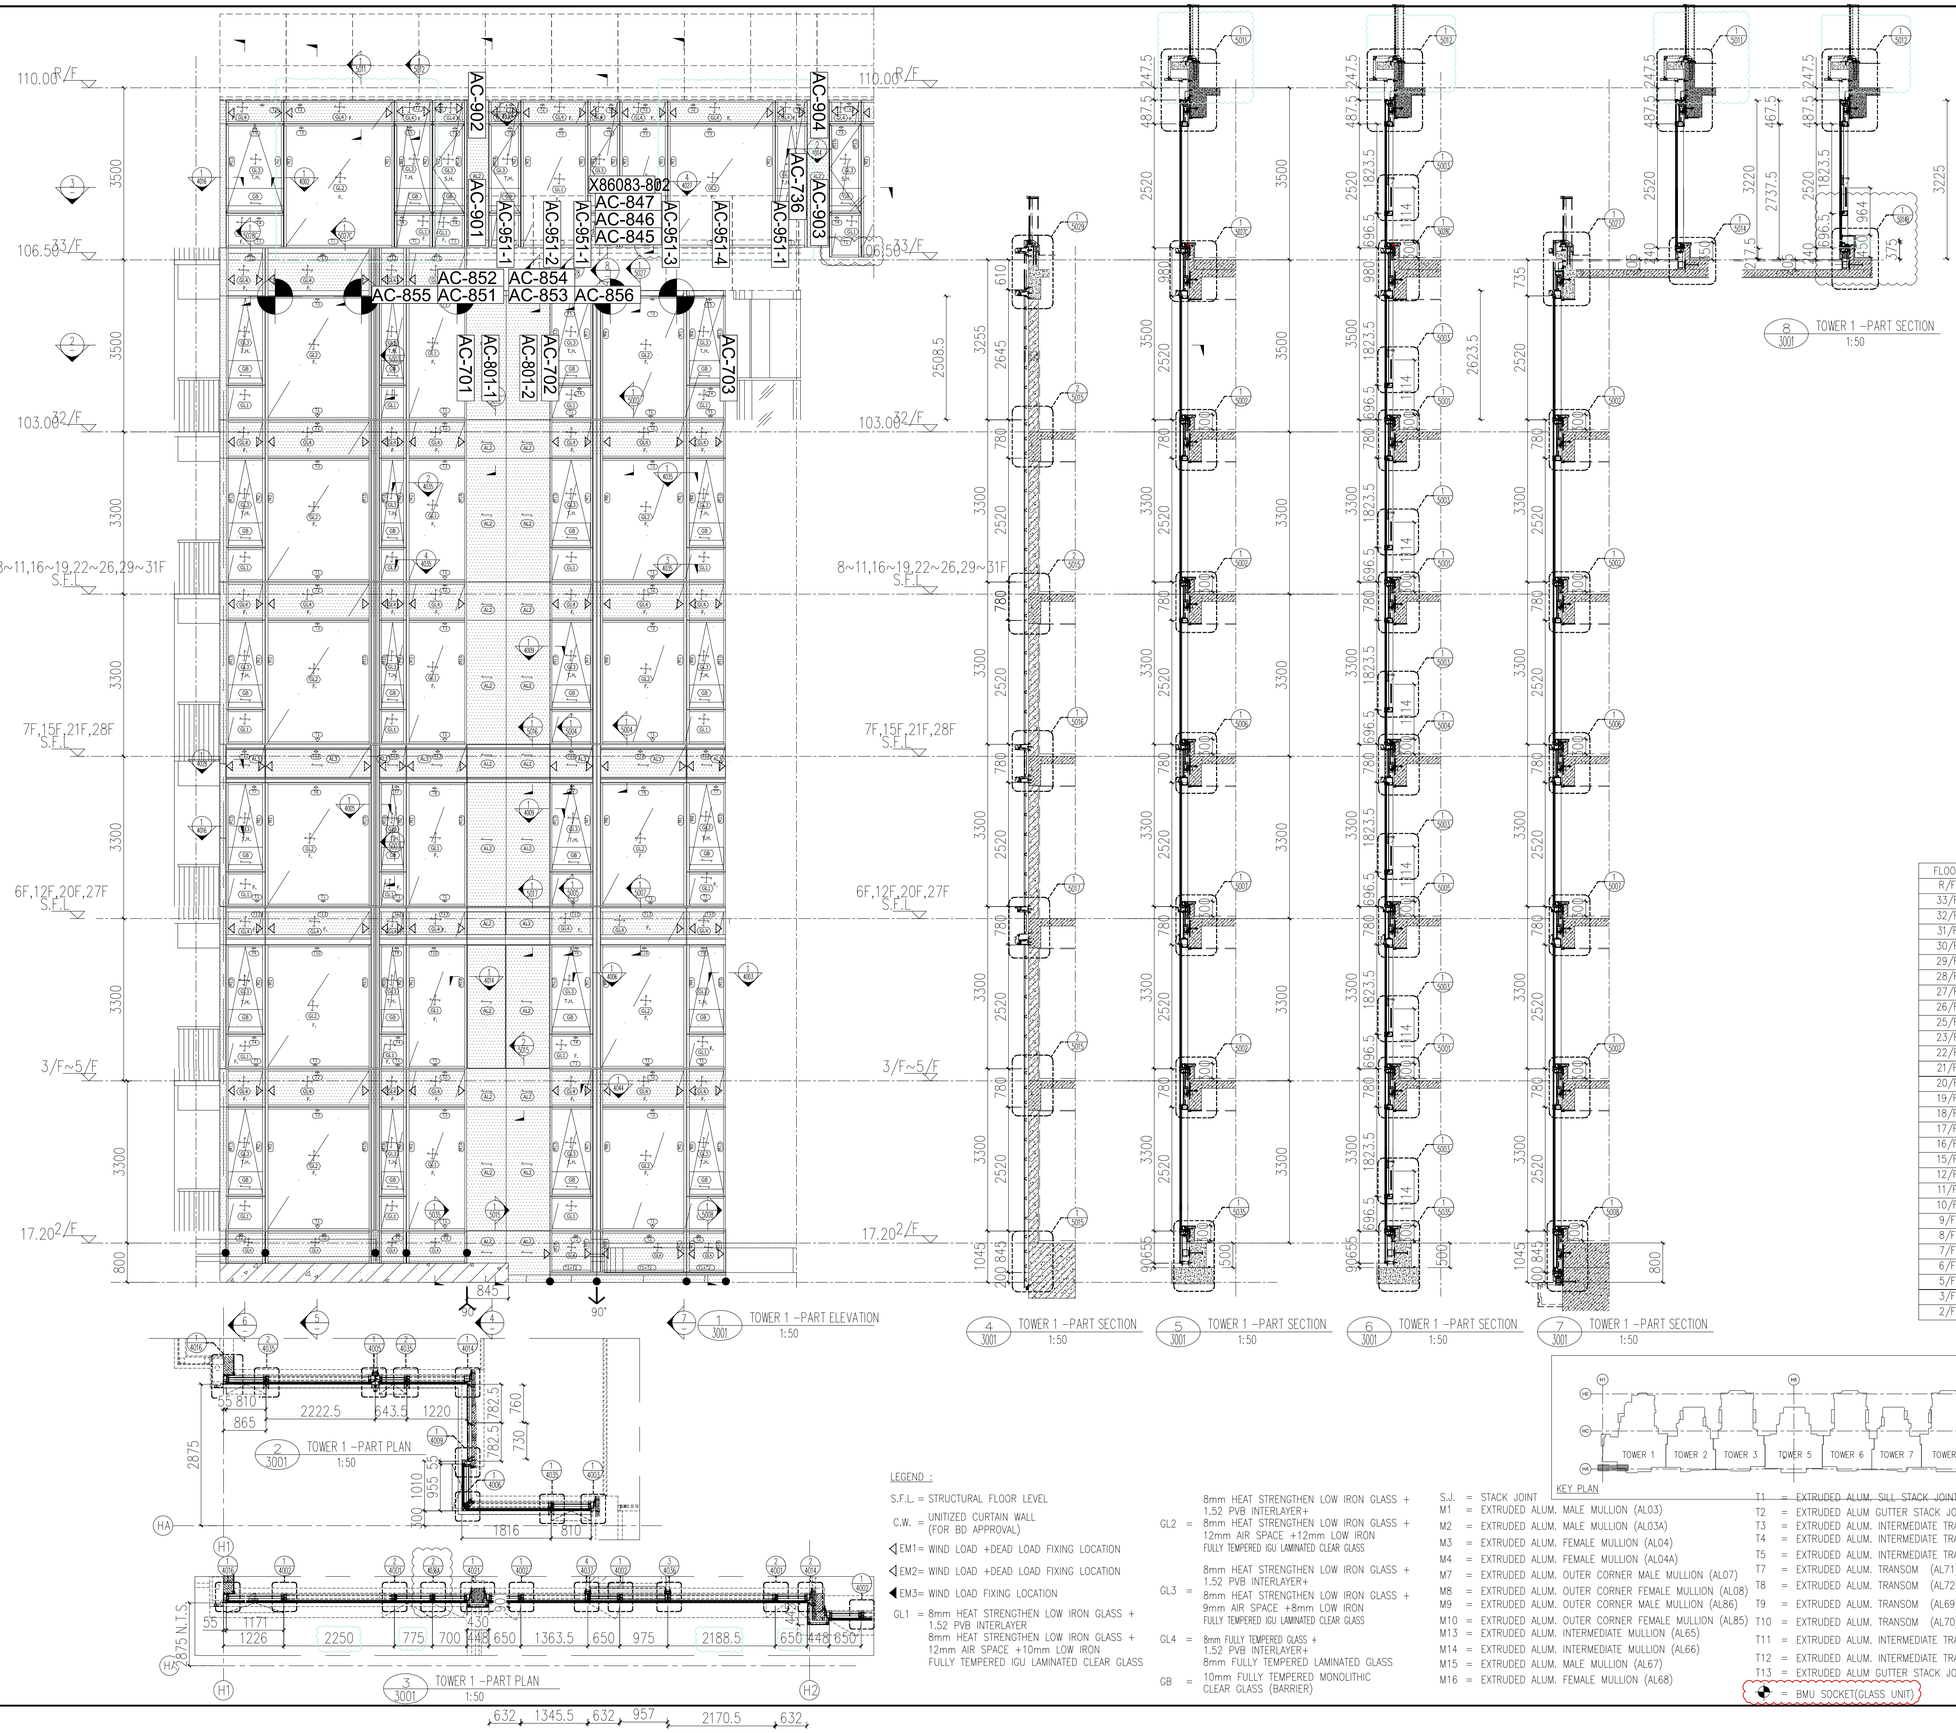

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3 = WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER + 12mm AIR SPACE +10mm LOW IRON + 8mm HEAT STRENGTHEN LOW IRON GLASS FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS


GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
= BMU SOCKET(GLASS UNIT)

KEY PLAN



B.D. REF :

F.S.D. REF :

Note :
1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
Email: cmwa@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 1

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :

SCALE A1: 1:50 A3:

DWG. NO. : SD-PE-3001

REV. : B

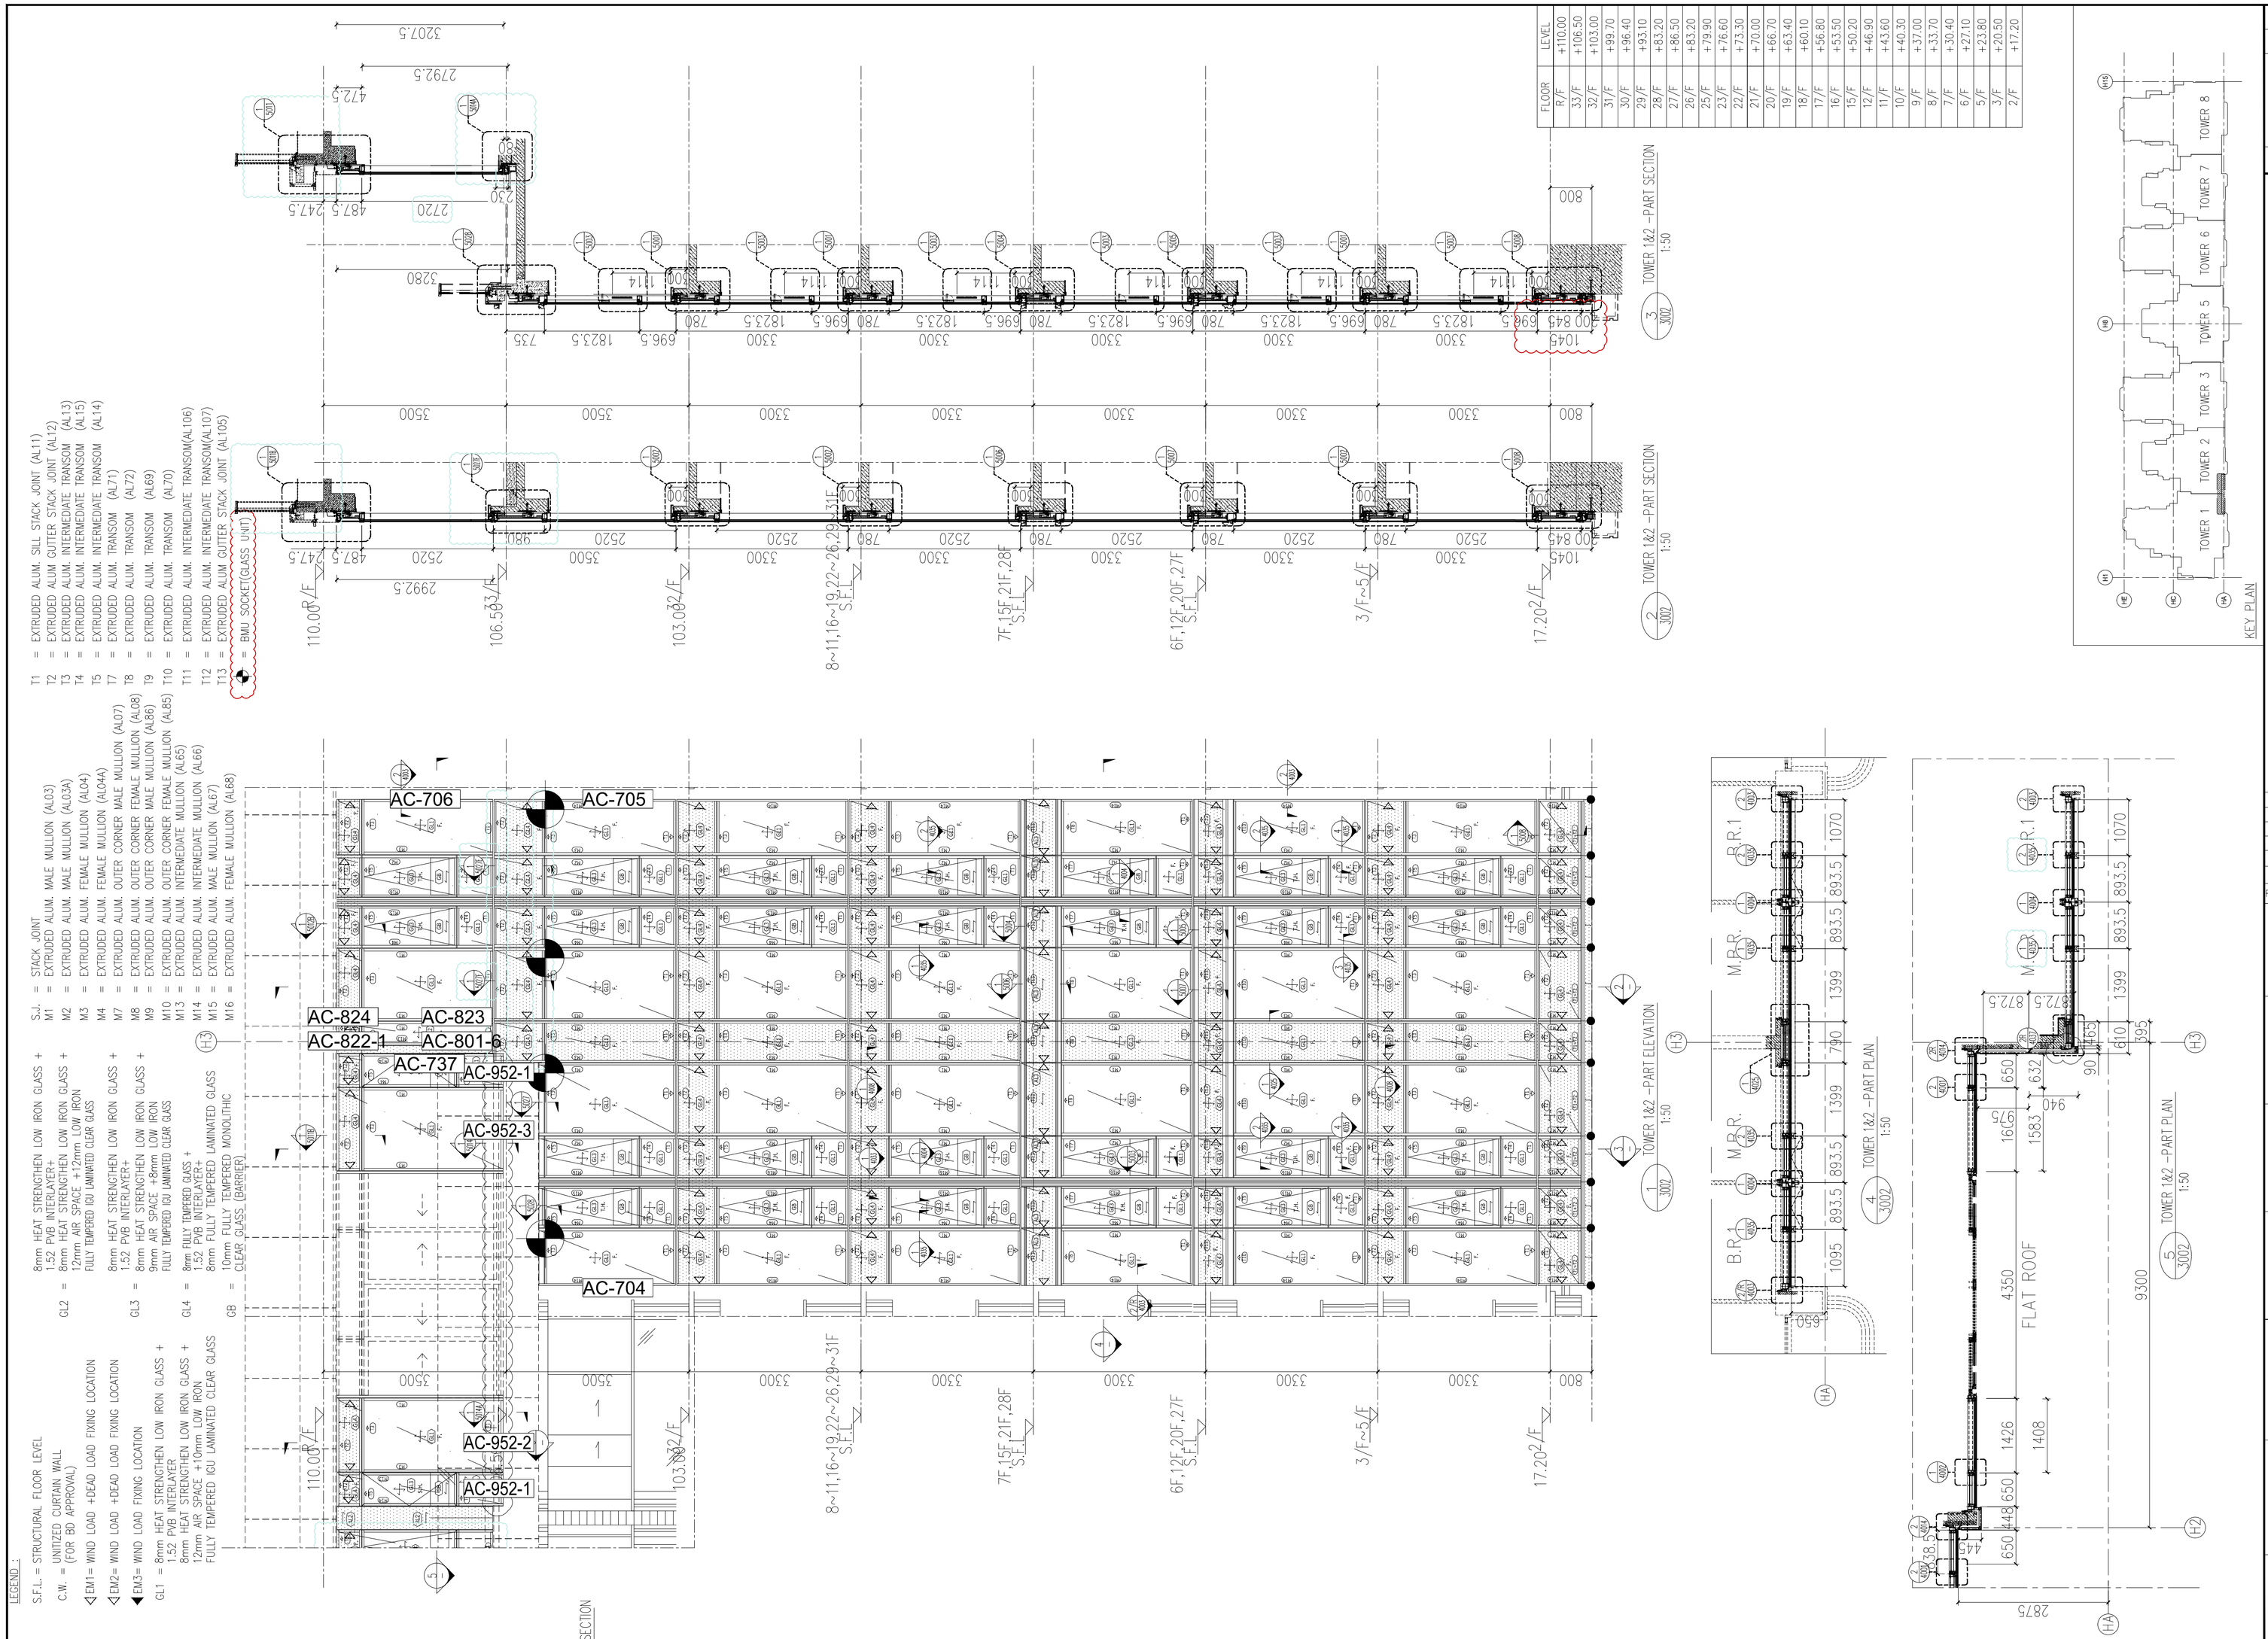

B.D. REF :

F.S.D. REF :

Note :

1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
G	16.Nov.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwa@cmwadi.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 1&2

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :

SCALE A1: 1:50
A3:

DWG. NO. : SD-PE-3002

REV. : B

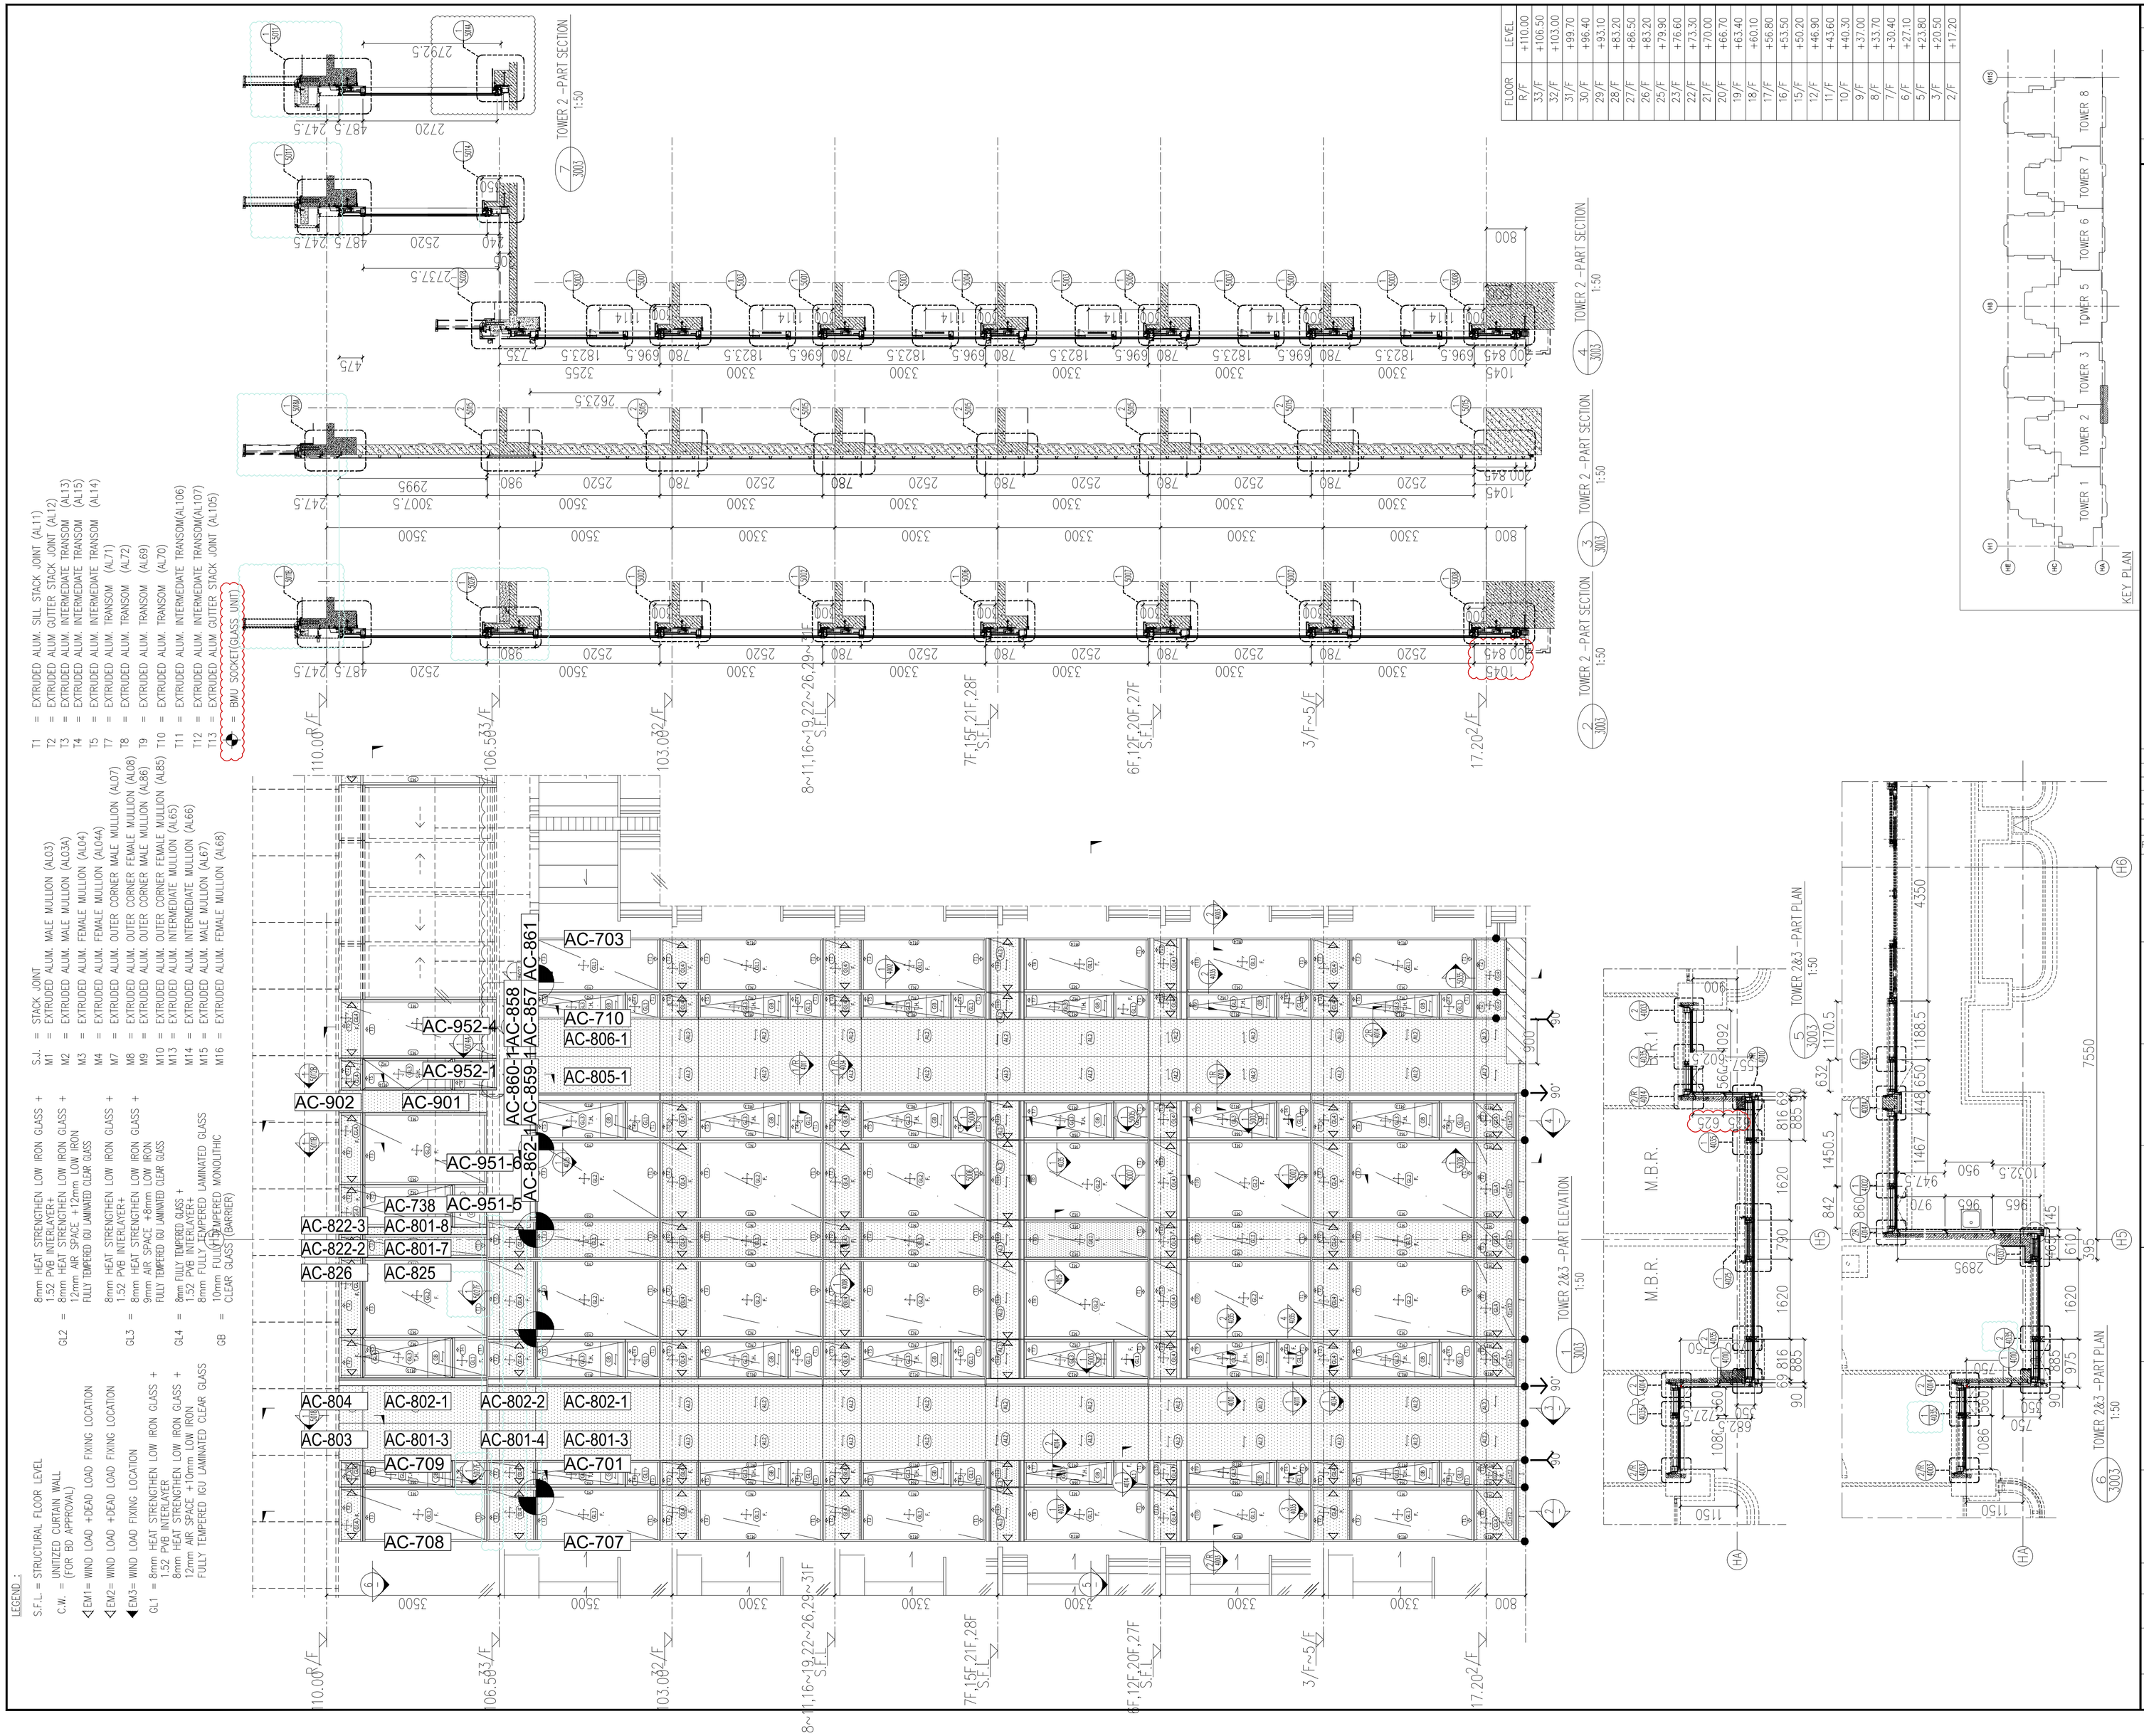

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
Tel: (852) 2522 1068
Email: cmwa@cmwa.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :


PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2

JOB NO. : J-857


DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:50 A3:


DWG. NO. : SD-PE-3003 | REV. : B

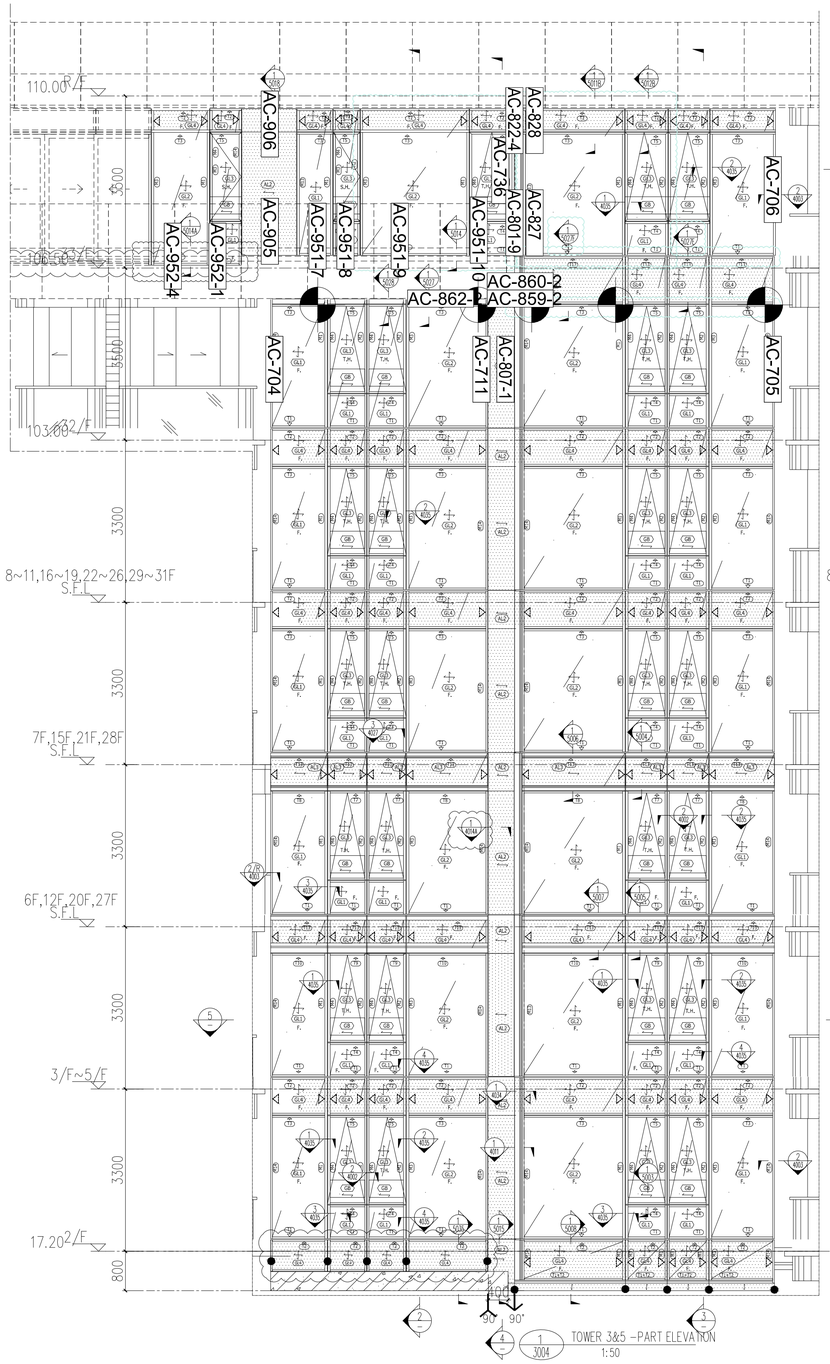


1 / 3004 TOWER 3&5 –PART ELEVATION 1:50

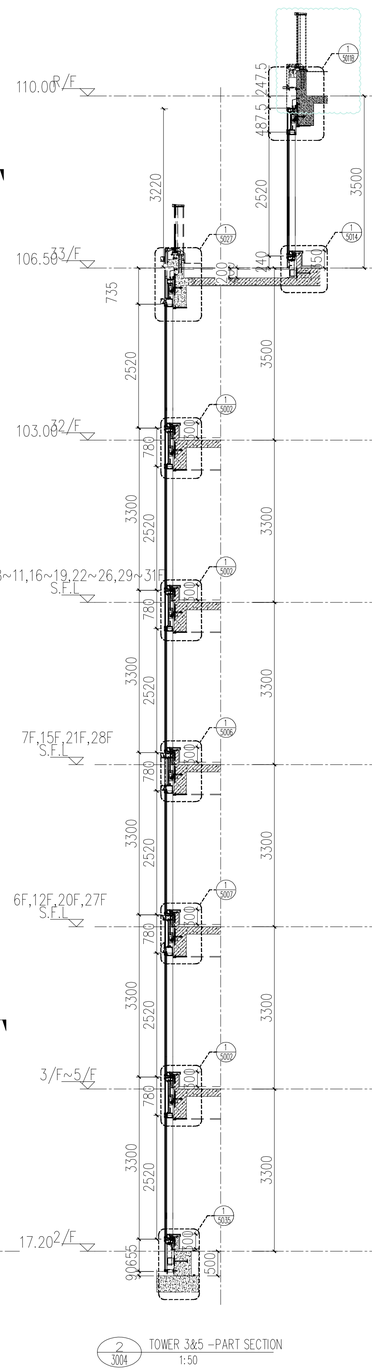


2 / 3004 TOWER 3&5 –PART SECTION 1:50

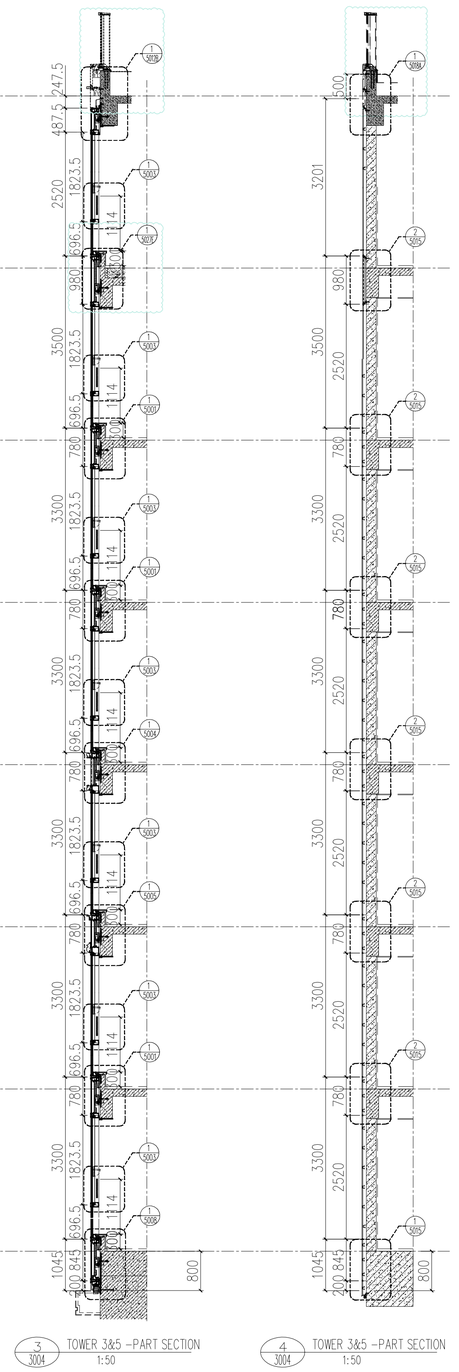


3 / 3004 TOWER 3&5 –PART SECTION 1:50

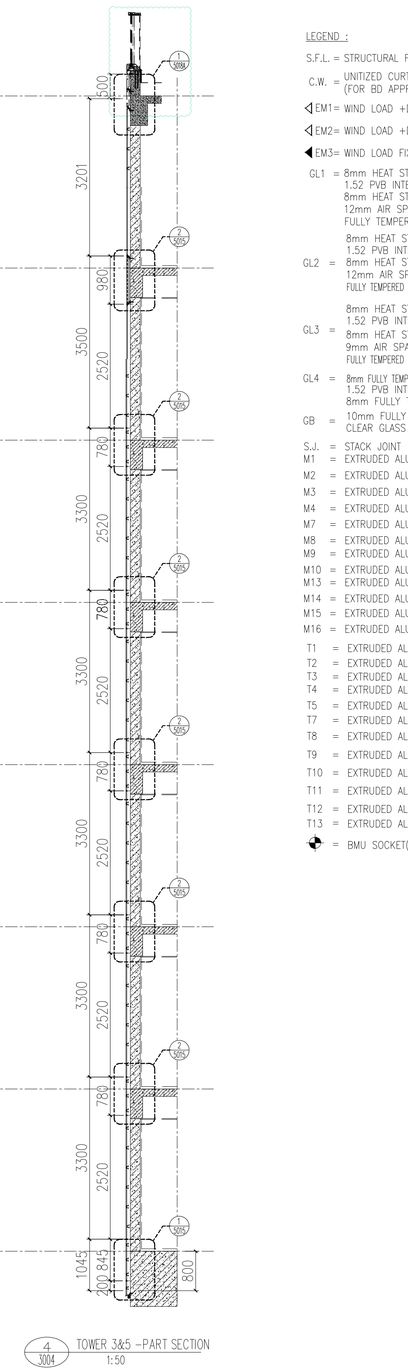

4 / 3004 TOWER 3&5 –PART SECTION 1:50

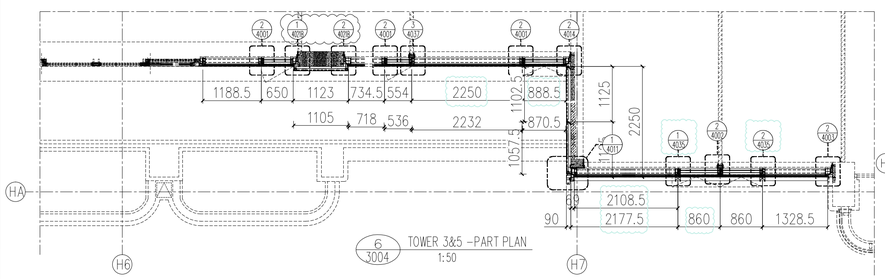

6 / 3004 TOWER 3&5 –PART PLAN 1:50



5 / 3004 TOWER 3&5 –PART PLAN 1:50

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3 = WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)

T10 = EXTRUDED ALUM. TRANSOM (AL70)


T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20



B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

A C M WONG & ASSOCIATES LTD
TEL: (852) 2521 1068
E-mail: cmwal@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :


SCALE A1: 1:50
A3:

DWG. NO. : SD-PE-3004

REV. : B

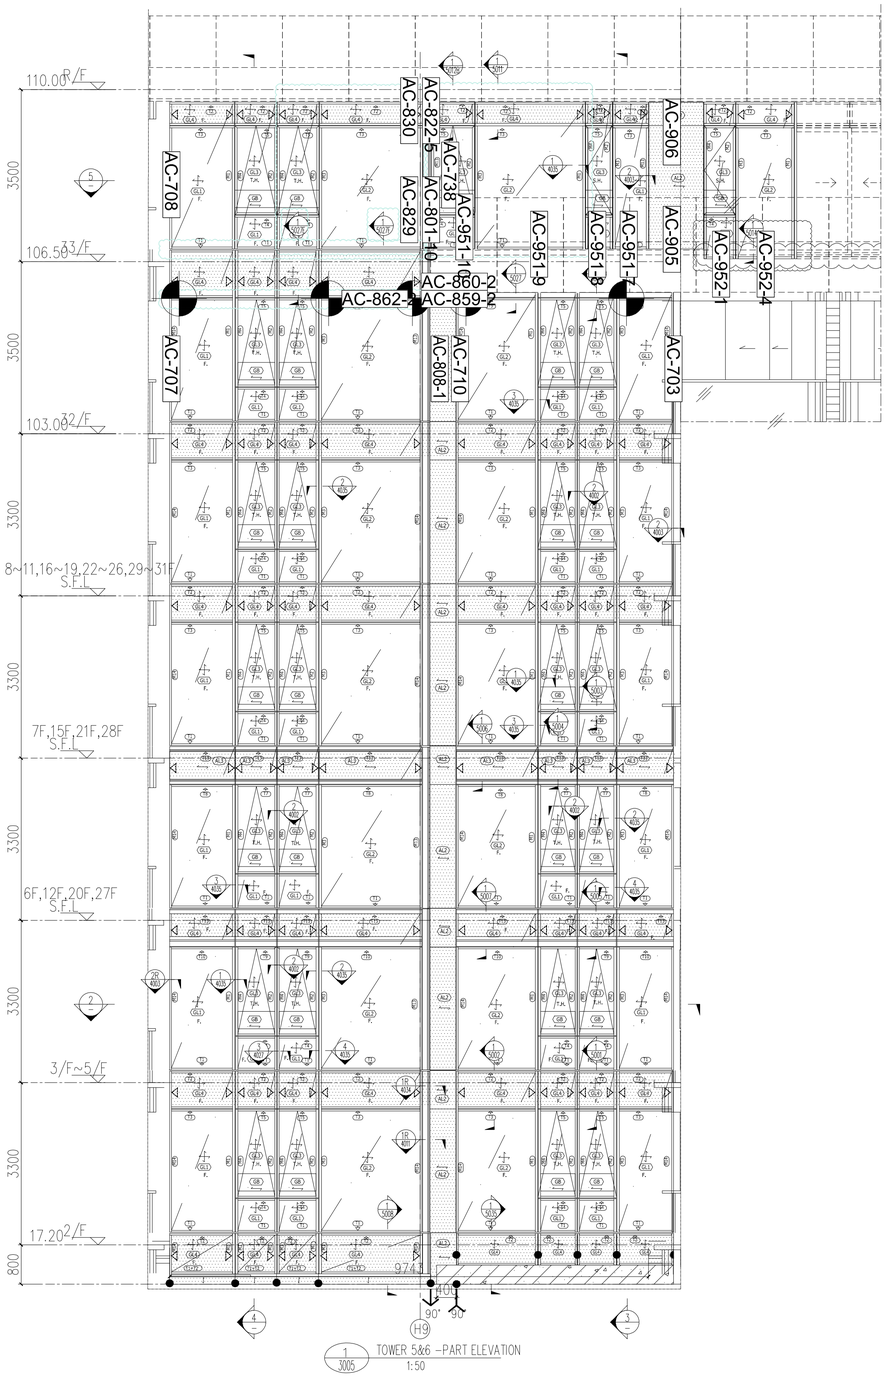


1 3005 TOWER 5&6 –PART ELEVATION 1:50

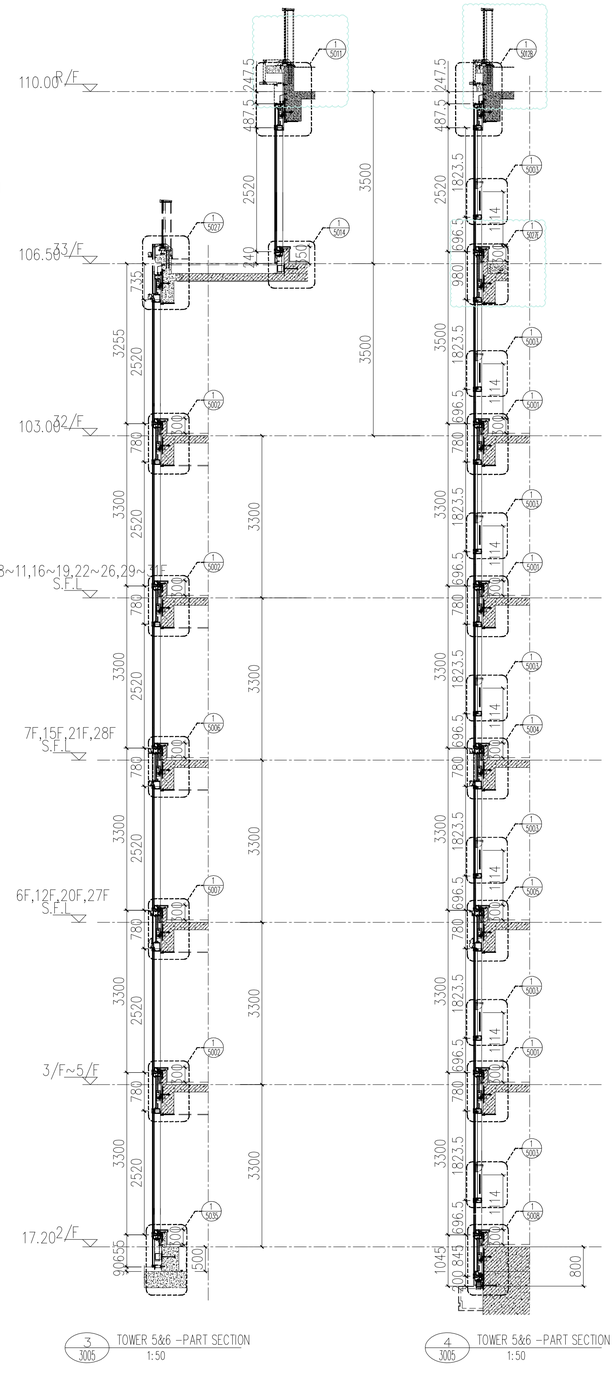


3 3005 TOWER 5&6 –PART SECTION 1:50

4 3005 TOWER 5&6 –PART SECTION 1:50

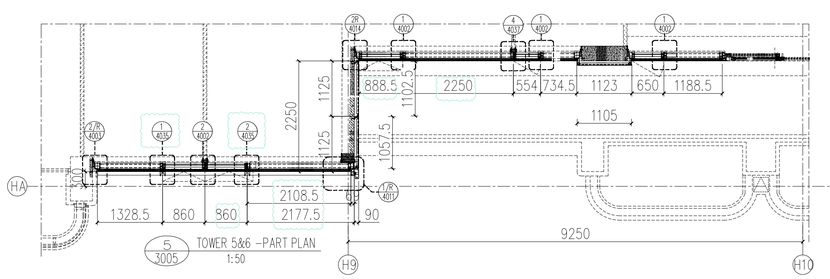

5 3005 TOWER 5&6 –PART PLAN 1:50



2 3005 TOWER 5&6 –PART PLAN 1:50

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3 = WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)

T10 = EXTRUDED ALUM. TRANSOM (AL70)


T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20



KEY PLAN

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. (/R) -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
	13.Nov.2021	GENERAL REVISION	
	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
B
A C M WONG & ASSOCIATES LTD
TEL:(852) 2522 1068
E-mail: cmwa@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :


PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2


JOB NO. : J-857

DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:50 A3:

DWG. NO. : SD-PE-3005 | REV. : B

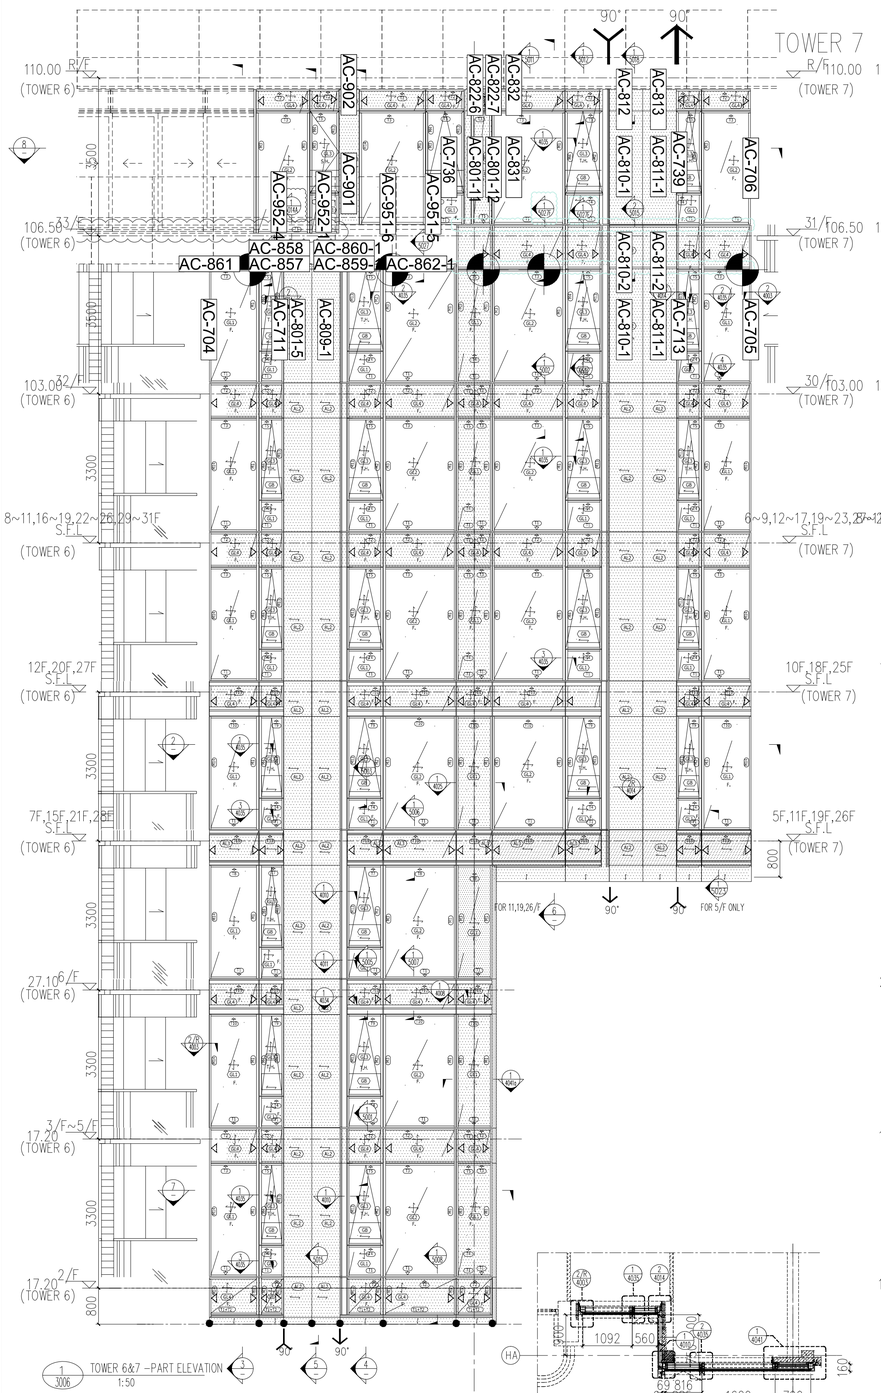

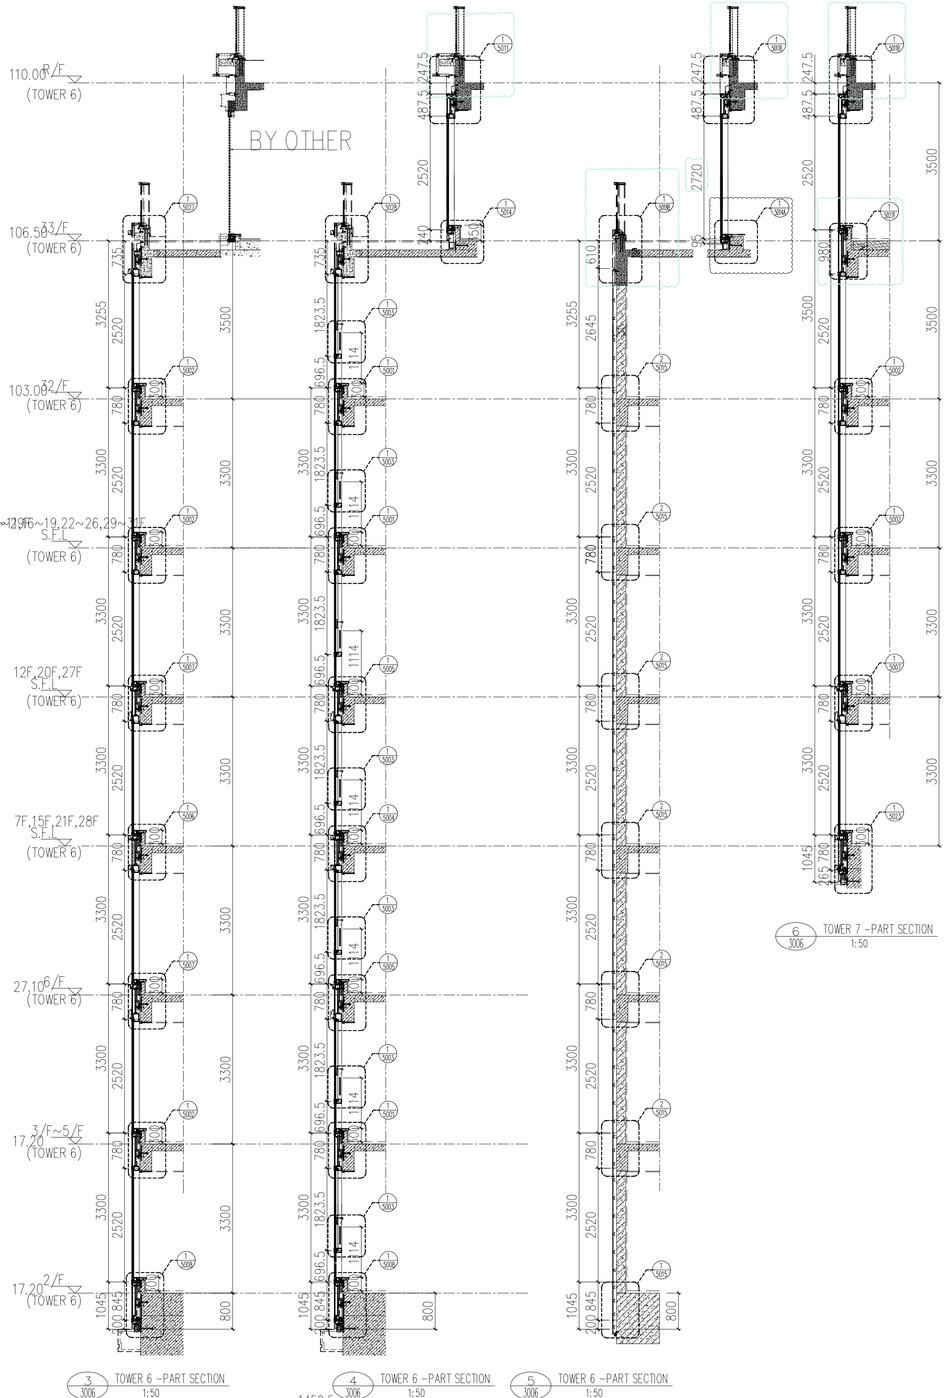

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)


S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

LEVEL	FLOOR	LEVEL	FLOOR
+110.00	R/F	+110.00	R/F
+106.50	31/F	+106.50	33/F
+103.00	30/F	+103.00	32/F
+99.70	29/F	+99.70	31/F
+96.40	28/F	+96.40	30/F
+93.10	27/F	+93.10	29/F
+83.20	26/F	+83.20	28/F
+86.50	25/F	+86.50	27/F
+83.20	23/F	+83.20	26/F
+79.90	22/F	+79.90	25/F
+76.60	21/F	+76.60	23/F
+73.30	20/F	+73.30	22/F
+70.00	19/F	+70.00	21/F
+66.70	18/F	+66.70	20/F
+63.40	17/F	+63.40	19/F
+60.10	16/F	+60.10	18/F
+56.80	15/F	+56.80	17/F
+53.50	12/F	+53.50	16/F
+50.20	11/F	+50.20	15/F
+46.90	10/F	+46.90	12/F
+43.60	9/F	+43.60	11/F
+40.30	8/F	+40.30	10/F
+37.00	7/F	+37.00	9/F
+33.70	6/F	+33.70	8/F
+30.40	5/F	+30.40	7/F
		+27.10	6/F
		+23.80	5/F
		+20.50	3/F
		+17.20	2/F



KEY PLAN

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. (/R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwa@cmwa.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6~8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :


PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2

JOB NO. : J-857


DRAWN BY : AN | DATE : 18.Oct.2021


CHKD BY : | SCALE A1: 1:50 A3:


DWG. NO. : SD-PE-3006 | REV. : B

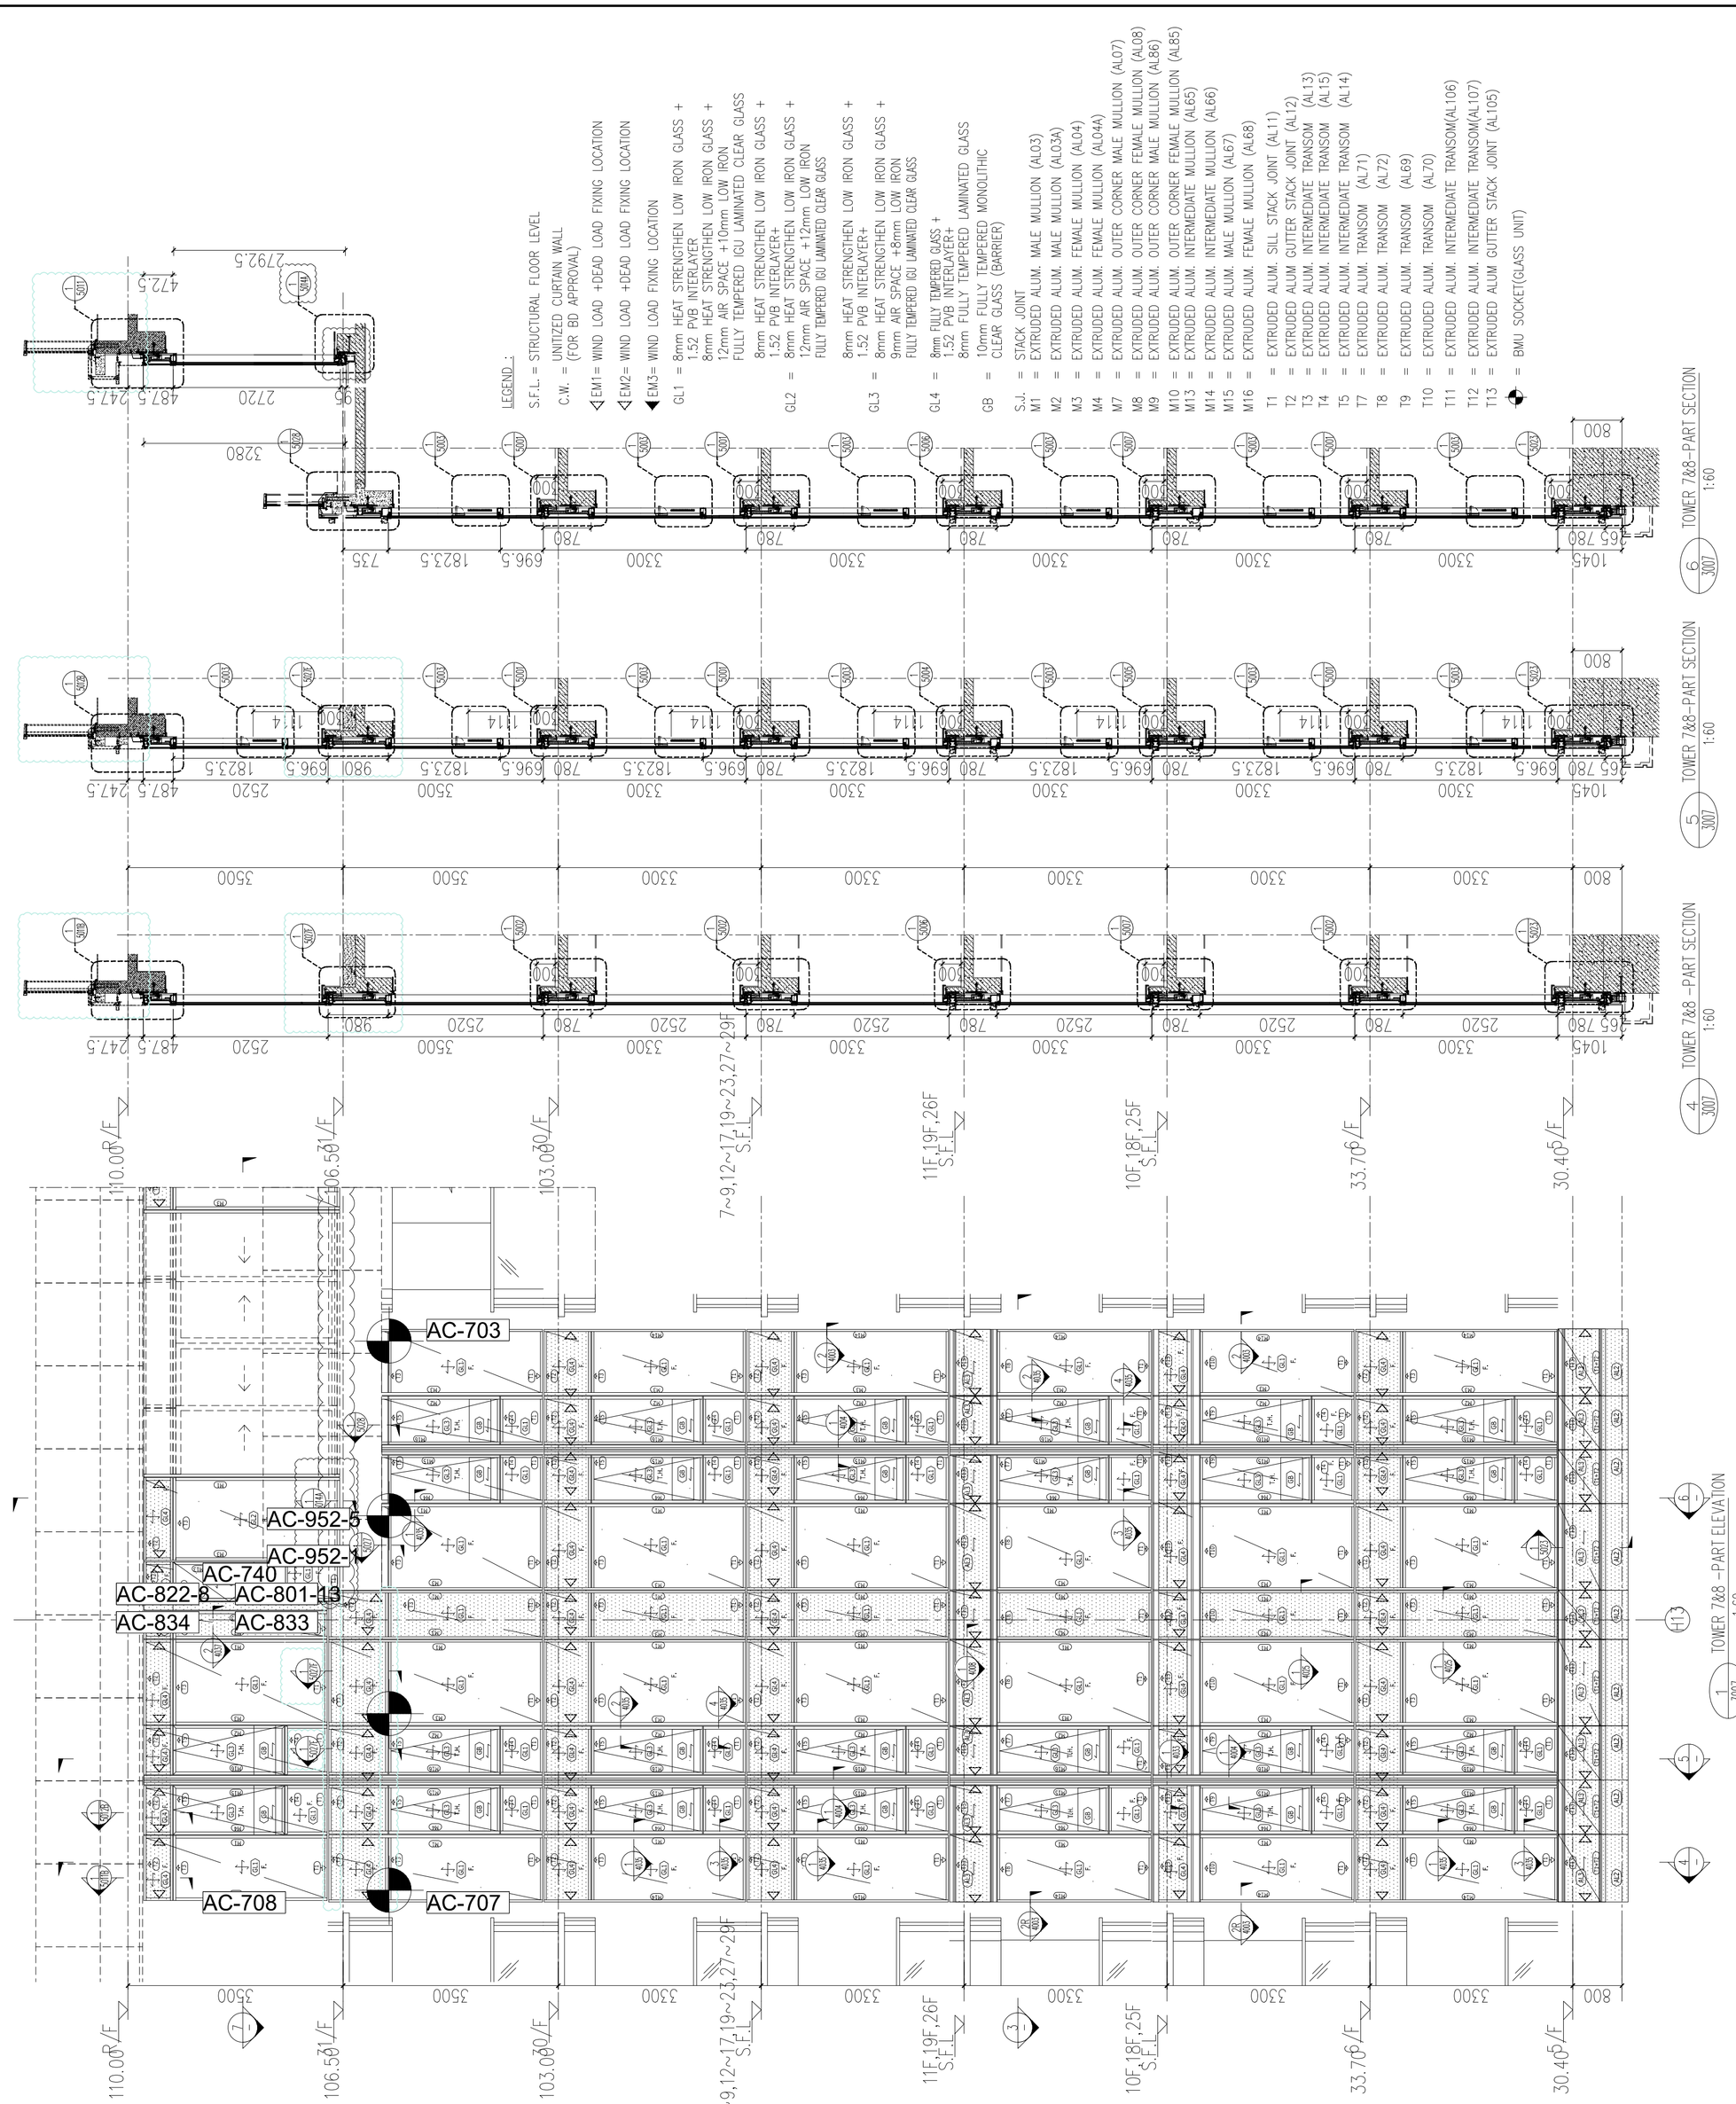

FLOOR	LEVEL
R/F	+110.00
31/F	+106.50
30/F	+103.00
29/F	+99.70
28/F	+96.40
27/F	+93.10
26/F	+83.20
25/F	+86.50
23/F	+83.20
22/F	+79.90
21/F	+76.60
20/F	+73.30
19/F	+70.00
18/F	+66.70
17/F	+63.40
16/F	+60.10
15/F	+56.80
12/F	+53.50
11/F	+50.20
10/F	+46.90
9/F	+43.60
8/F	+40.30
7/F	+37.00
6/F	+33.70
5/F	+30.40

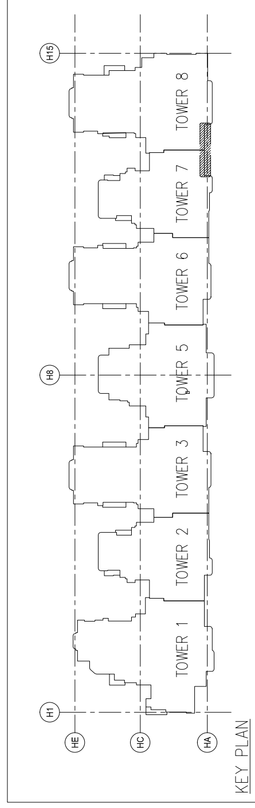

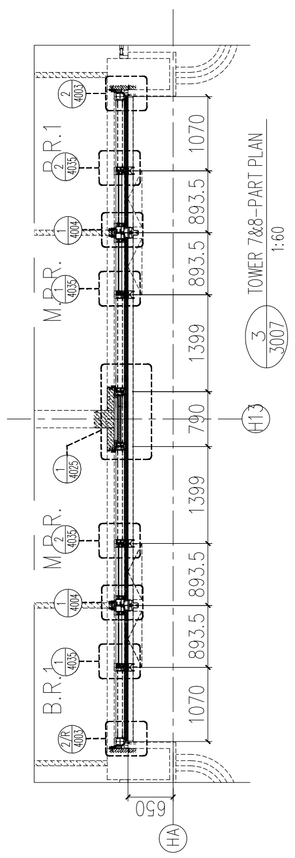

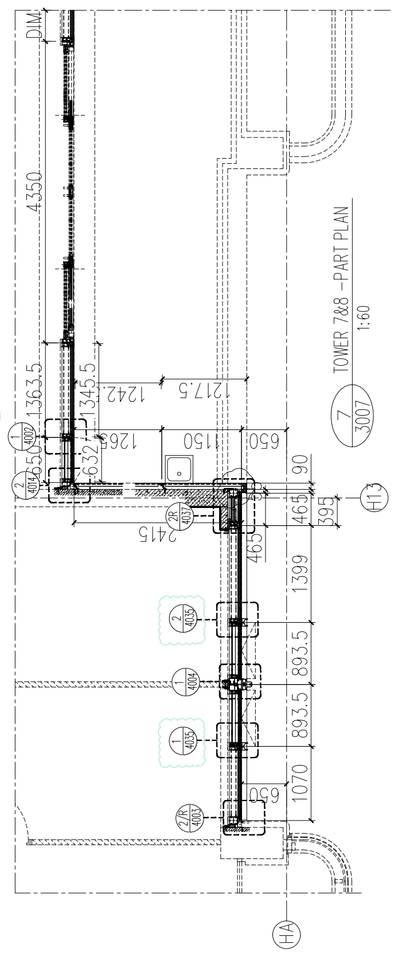

B.D. REF :

F.S.D. REF :

Note :

1.All dimensions are in mm.

2.All elevations are viewed from outside.

3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.

X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2552 1968
E-mail: cmwa@cmwa.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666


PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 7

JOB NO. : J-857	
DRAWN BY : AN	DATE : 18.Oct.2021
CHKD BY :	SCALE A1: 1:60 A3:
DWG. NO. : SD-PE-3007	REV. : B

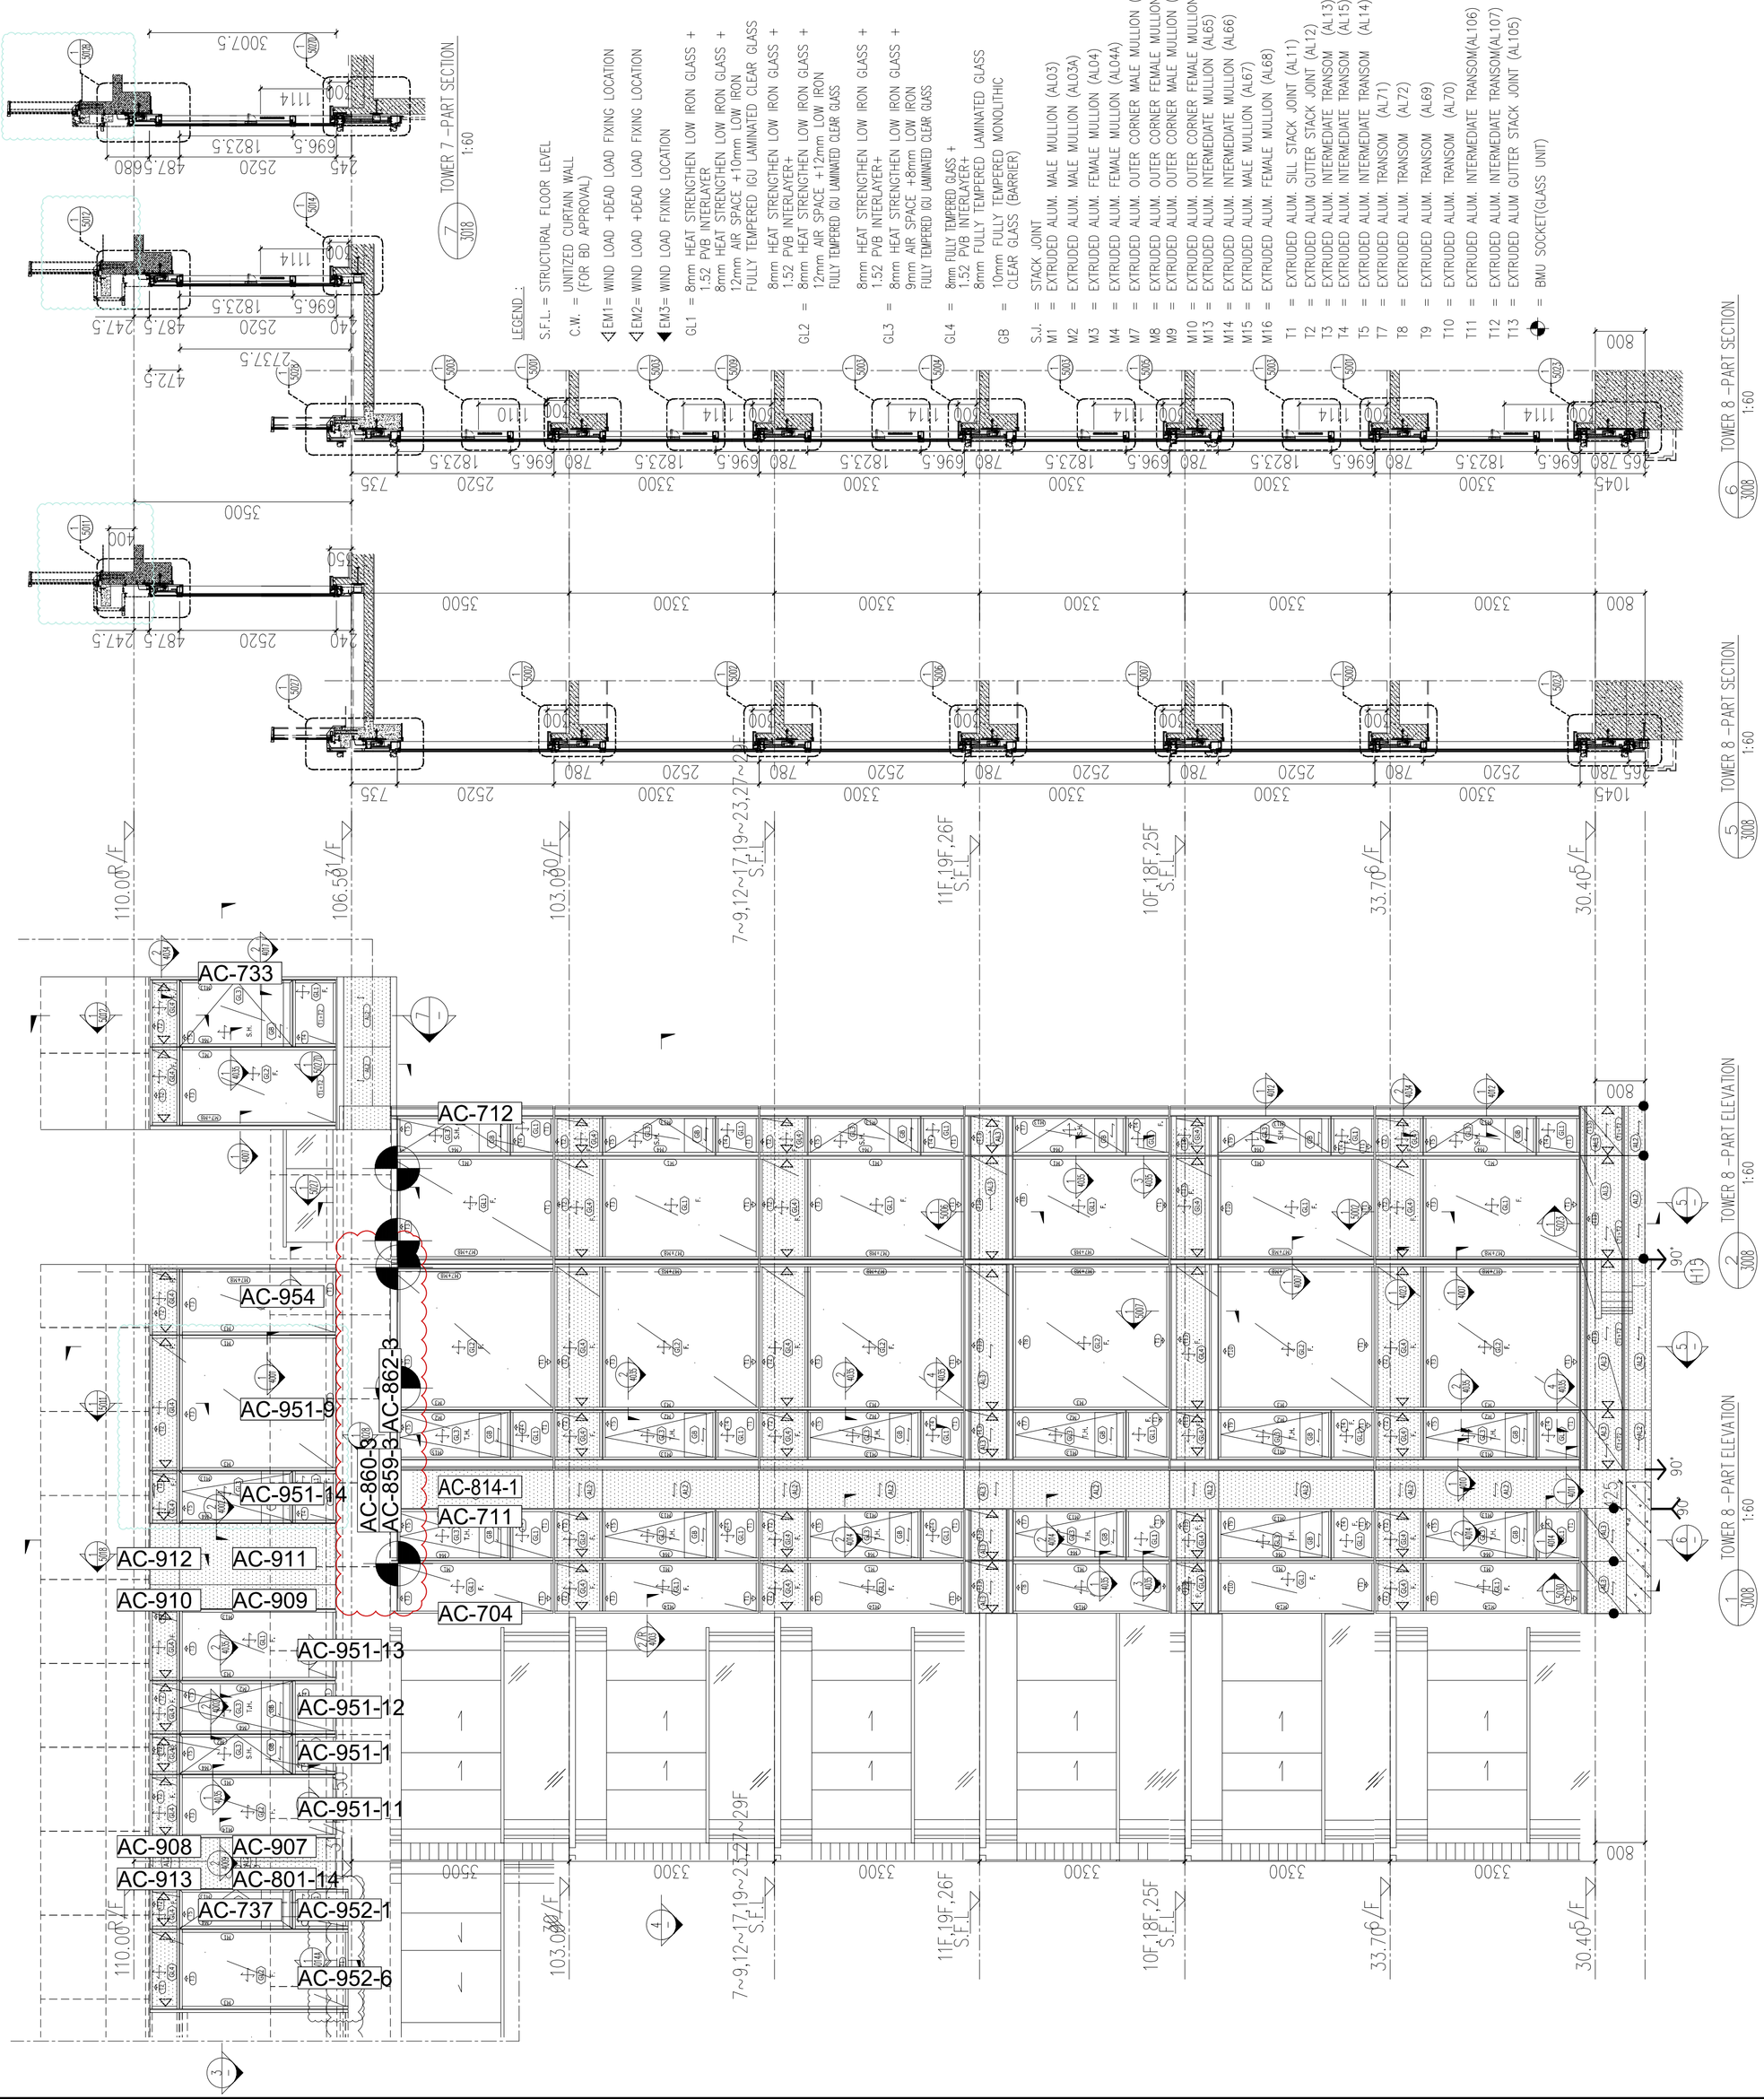

FLOOR	LEVEL
R/F	+110.00
31/F	+106.50
30/F	+103.00
29/F	+99.70
28/F	+96.40
27/F	+93.10
26/F	+83.20
25/F	+86.50
23/F	+83.20
22/F	+79.90
21/F	+76.60
20/F	+73.30
19/F	+70.00
18/F	+66.70
17/F	+63.40
16/F	+60.10
15/F	+56.80
12/F	+53.50
11/F	+50.20
10/F	+46.90
9/F	+43.60
8/F	+40.30
7/F	+37.00
6/F	+33.70
5/F	+30.40

B.D. REF :

F.S.D. REF :

Note :

1.All dimensions are in mm.

2.All elevations are viewed from outside.

3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666


PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 8

JOB NO. : J-857	
DRAWN BY : AN	DATE : 18.Oct.2021
CHKD BY :	SCALE A1: 1:60 A3:
DWG. NO. : SD-PE-3008	REV. : B

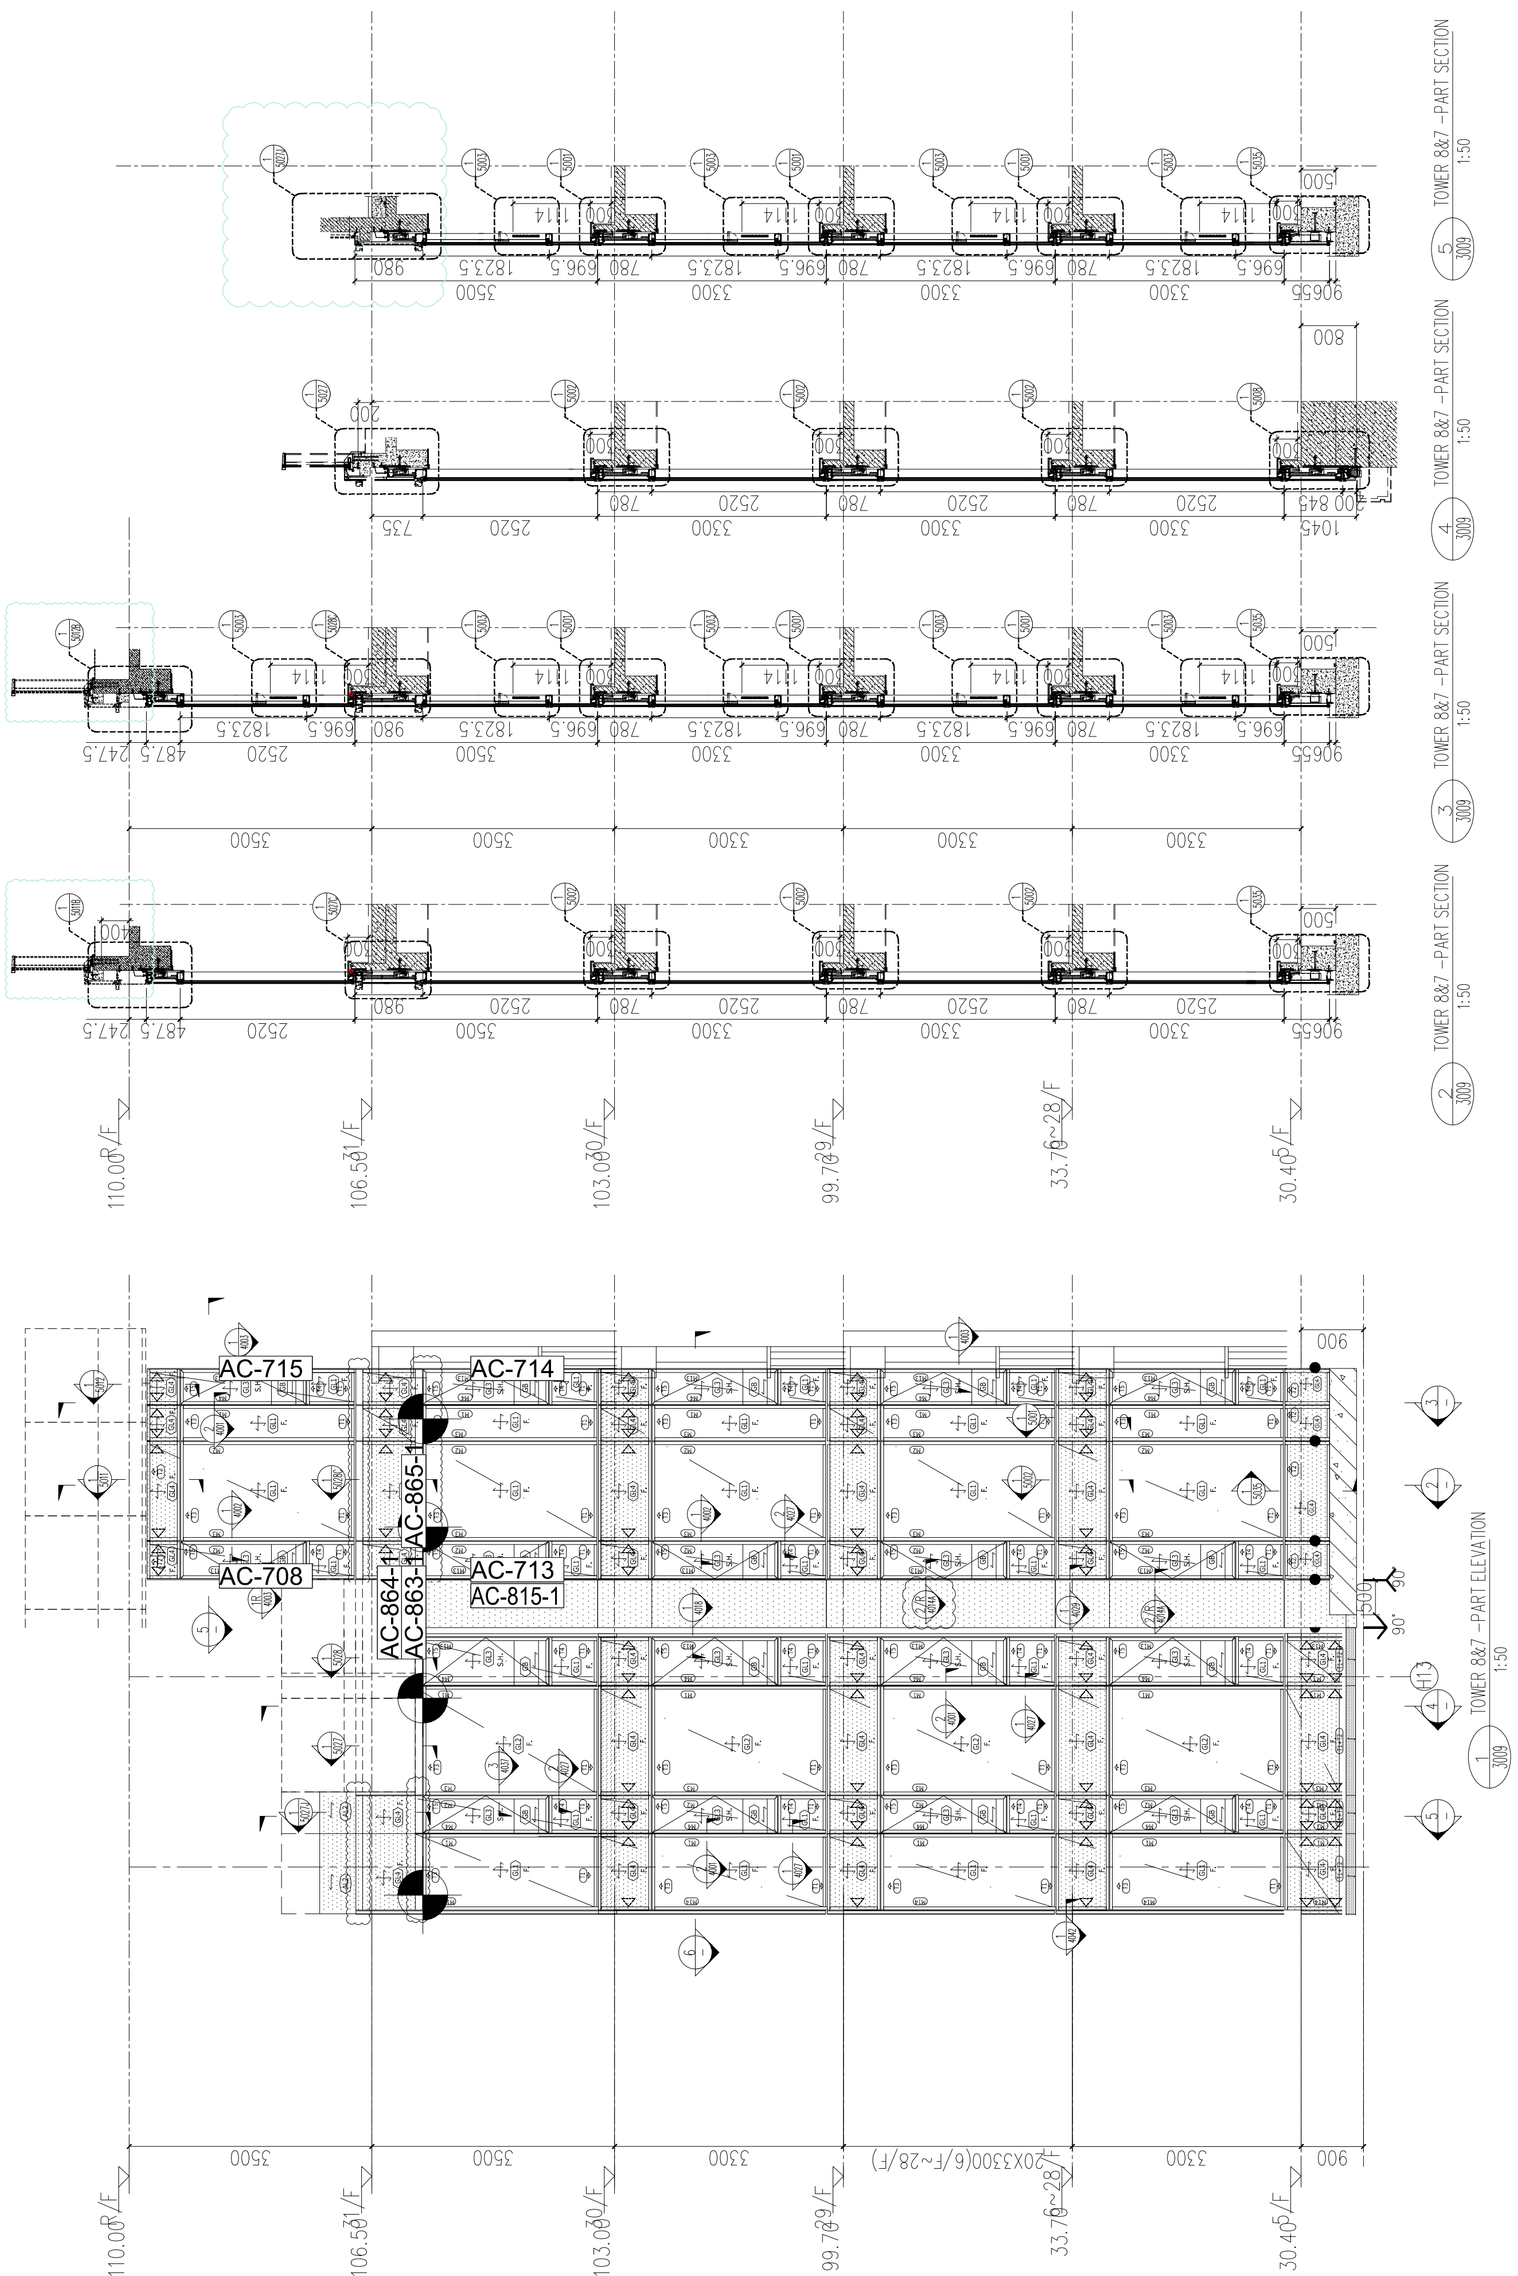

FLOOR	LEVEL
R/F	+110.00
31/F	+106.50
30/F	+103.00
29/F	+99.70
28/F	+96.40
27/F	+93.10
26/F	+83.20
25/F	+86.50
24/F	+83.20
23/F	+79.90
22/F	+76.60
21/F	+73.30
20/F	+70.00
19/F	+66.70
18/F	+63.40
17/F	+60.10
16/F	+56.80
15/F	+53.50
12/F	+50.20
11/F	+46.90
10/F	+43.60
9/F	+40.30
8/F	+37.00
7/F	+33.70
6/F	+30.40
5/F	

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
BMU SOCKET(GLASS UNIT)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS
GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.F.L. = STRUCTURAL FLOOR LEVEL
C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)
EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION
EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION
EM3 = WIND LOAD FIXING LOCATION
GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

B.D. REF :

F.S.D. REF :

Note :
1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 / X001 — DETAIL MARK NO. / REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwk@cmwk.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666


PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 8&7


JOB NO. : J-857	
DRAWN BY : AN	DATE : 18.Oct.2021
CHKD BY :	SCALE A1: 1:60 A3:
DWG. NO. : SD-PE-3009	REV. : B

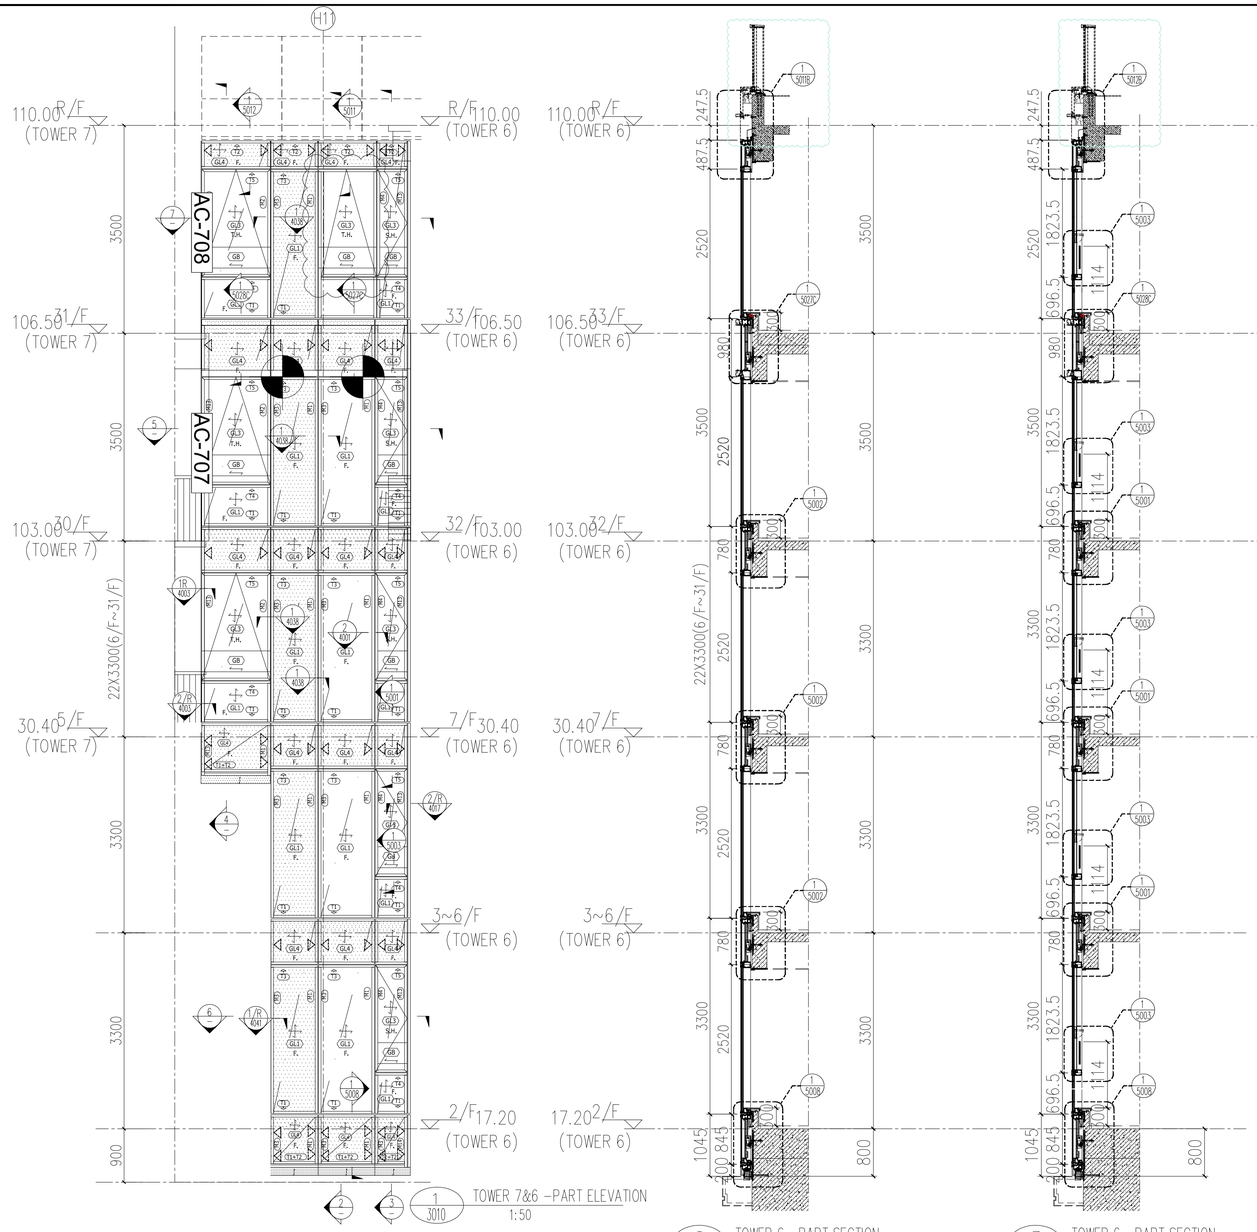


1 3010 TOWER 7&6 –PART ELEVATION 1:50

2 3010 TOWER 6 –PART SECTION 1:50


3 3010 TOWER 6 –PART SECTION 1:50

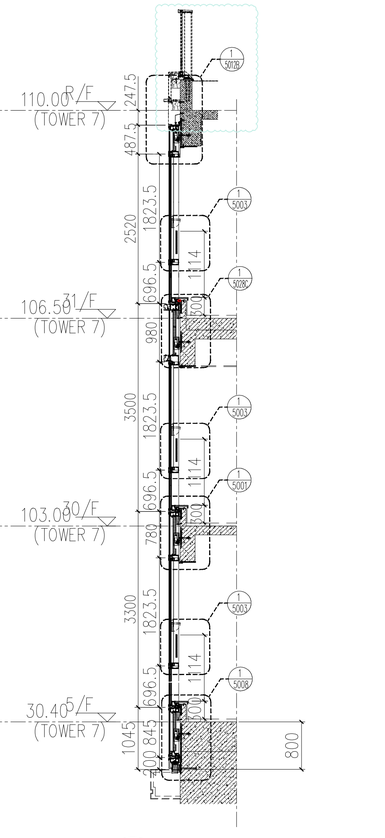


4 3010 TOWER 7 –PART SECTION 1:50

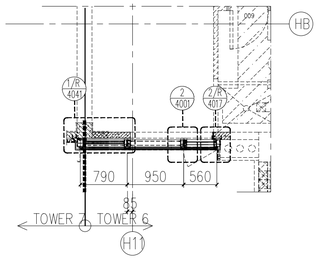


6 3010 TOWER 7&6 –PART PLAN 1:50



5 3010 TOWER 7&6 –PART PLAN 1:50

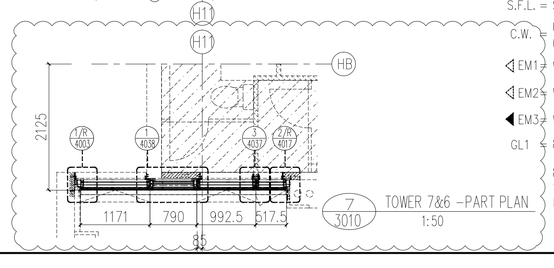

7 3010 TOWER 7&6 –PART PLAN 1:50



KEY PLAN

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

EM3 = WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER + 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
= BMU SOCKET(GLASS UNIT)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

A

B.D. REF :

F.S.D. REF :

Note :
1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
I	16.Nov.2022	GENERAL REVISION	
H	16.Ari.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
C M WONG & ASSOCIATES LTD
TEL: (852) 2502 7080
E-mail: cmwall@cmwall.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 7&6

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :


SCALE A1:1:50.000000 A3:

DWG. NO. : SD-PE-3010

REV. : B

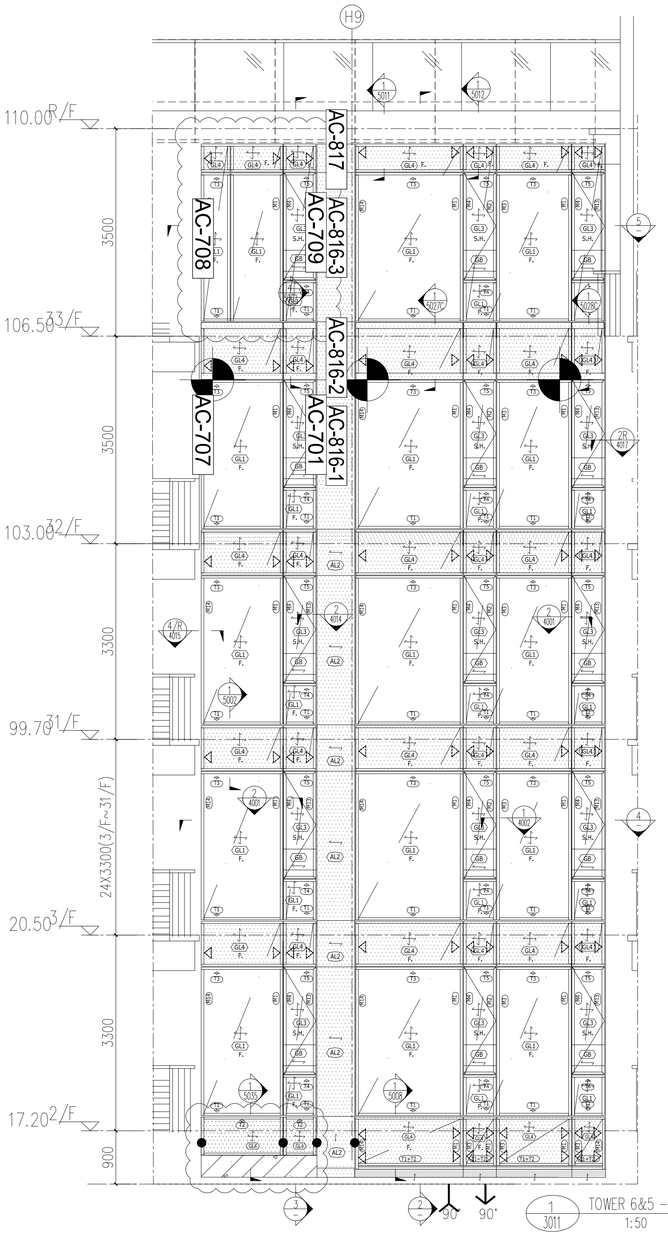

1 3011 TOWER 6&5 –PART ELEVATION
1:50

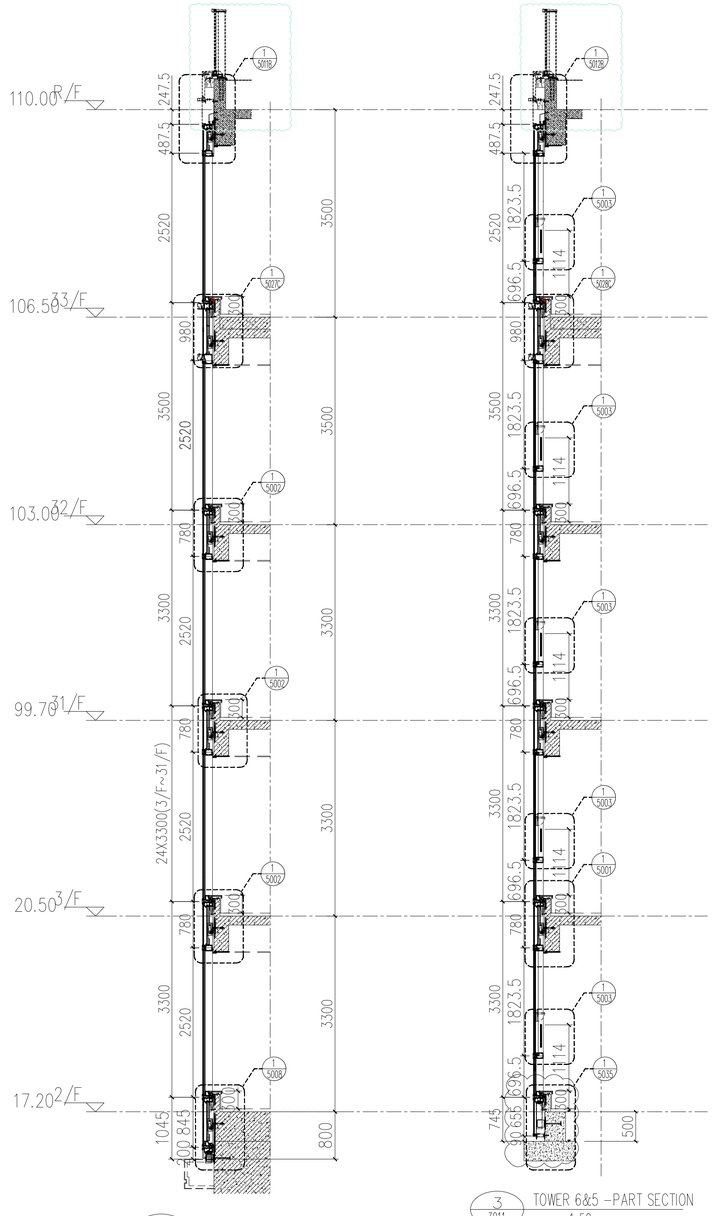


2 3011 TOWER 6&5 –PART SECTION
1:50


3 3011 TOWER 6&5 –PART SECTION
1:50

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

A



4 3011 TOWER 6&5 –PART PLAN
H9 1:50



5 3011 TOWER 6&5 –PART PLAN
H9 1:50

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁ EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

◁ EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

◀ EM3 = WIND LOAD FIXING LOCATION


GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER + 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)



KEY PLAN

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)

T10 = EXTRUDED ALUM. TRANSOM (AL70)

T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

B.D. REF :

F.S.D. REF :

Note :

1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. (R) -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
G	16.Nov.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL:(852) 2522 1068
E-mail: cmwa@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666


PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 6

JOB NO. :	J-857
DRAWN BY : AN	DATE : 18.Oct.2021
CHKD BY :	SCALE A1:50.000000 A3:
DWG. NO. : SD-PE-3011	REV. : B

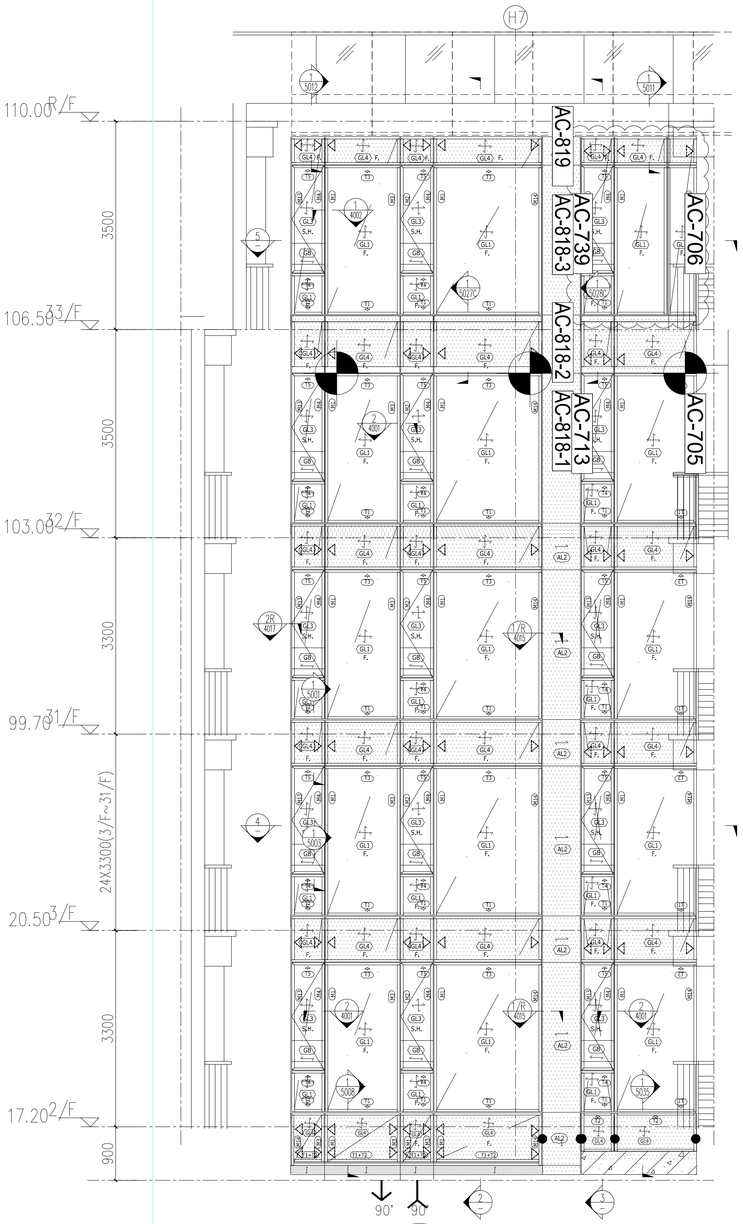


1 3012 TOWER 5&3 –PART ELEVATION 1:50

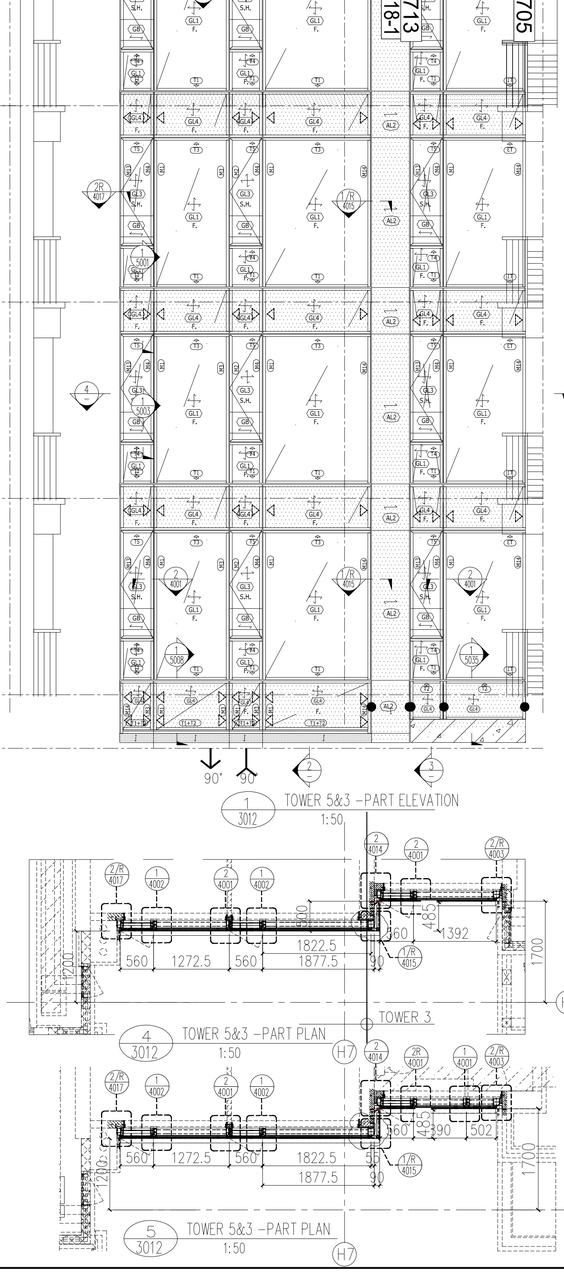

4 3012 TOWER 5&3 –PART PLAN 1:50

5 3012 TOWER 5&3 –PART PLAN 1:50

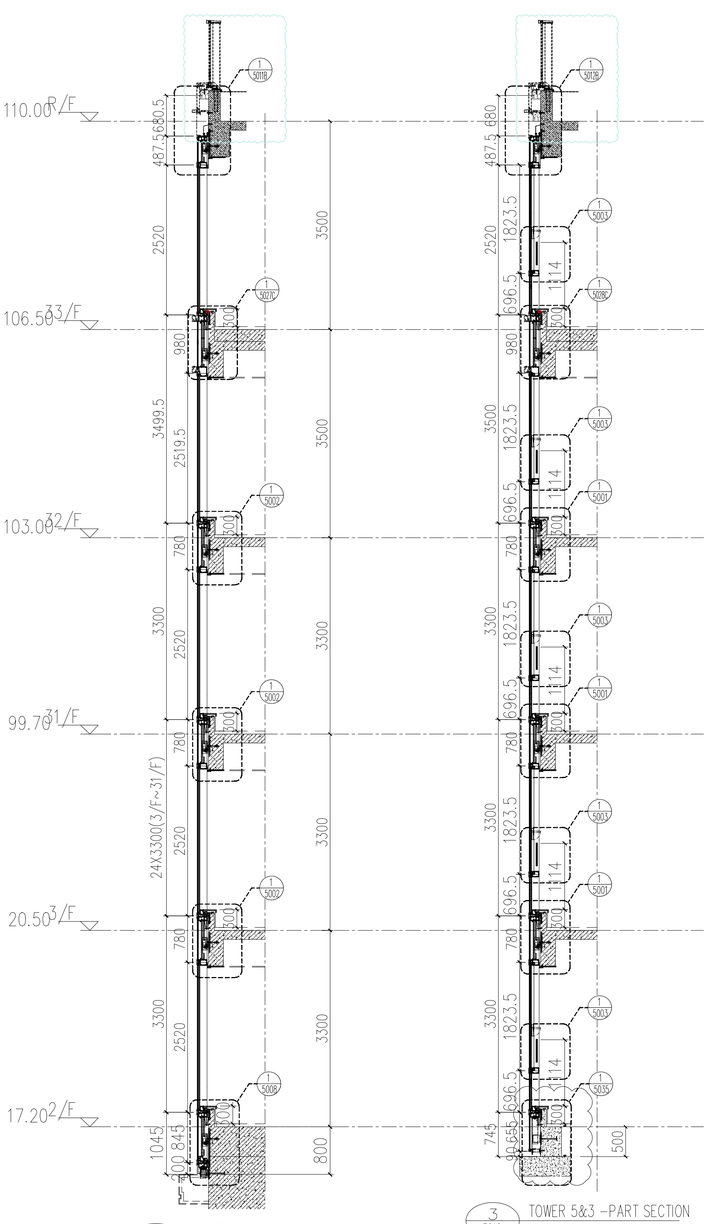

2 3012 TOWER 5&3 –PART SECTION 1:50

3 3012 TOWER 5&3 –PART SECTION 1:50

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)


T10 = EXTRUDED ALUM. TRANSOM (AL70)

T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)



KEY PLAN

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

B.D. REF :

F.S.D. REF :

Note :

1.All dimensions are in mm.

2.All elevations are viewed from outside.

3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.

X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
G	16.Nov.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

CMA C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwk@cmwk.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁貿有限公司
MIDI ALUMINIUM FABRICATOR LTD.

Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 5&3

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :


SCALE A1:50.000000 A3:

DWG. NO. : SD-PE-3012

REV. : B

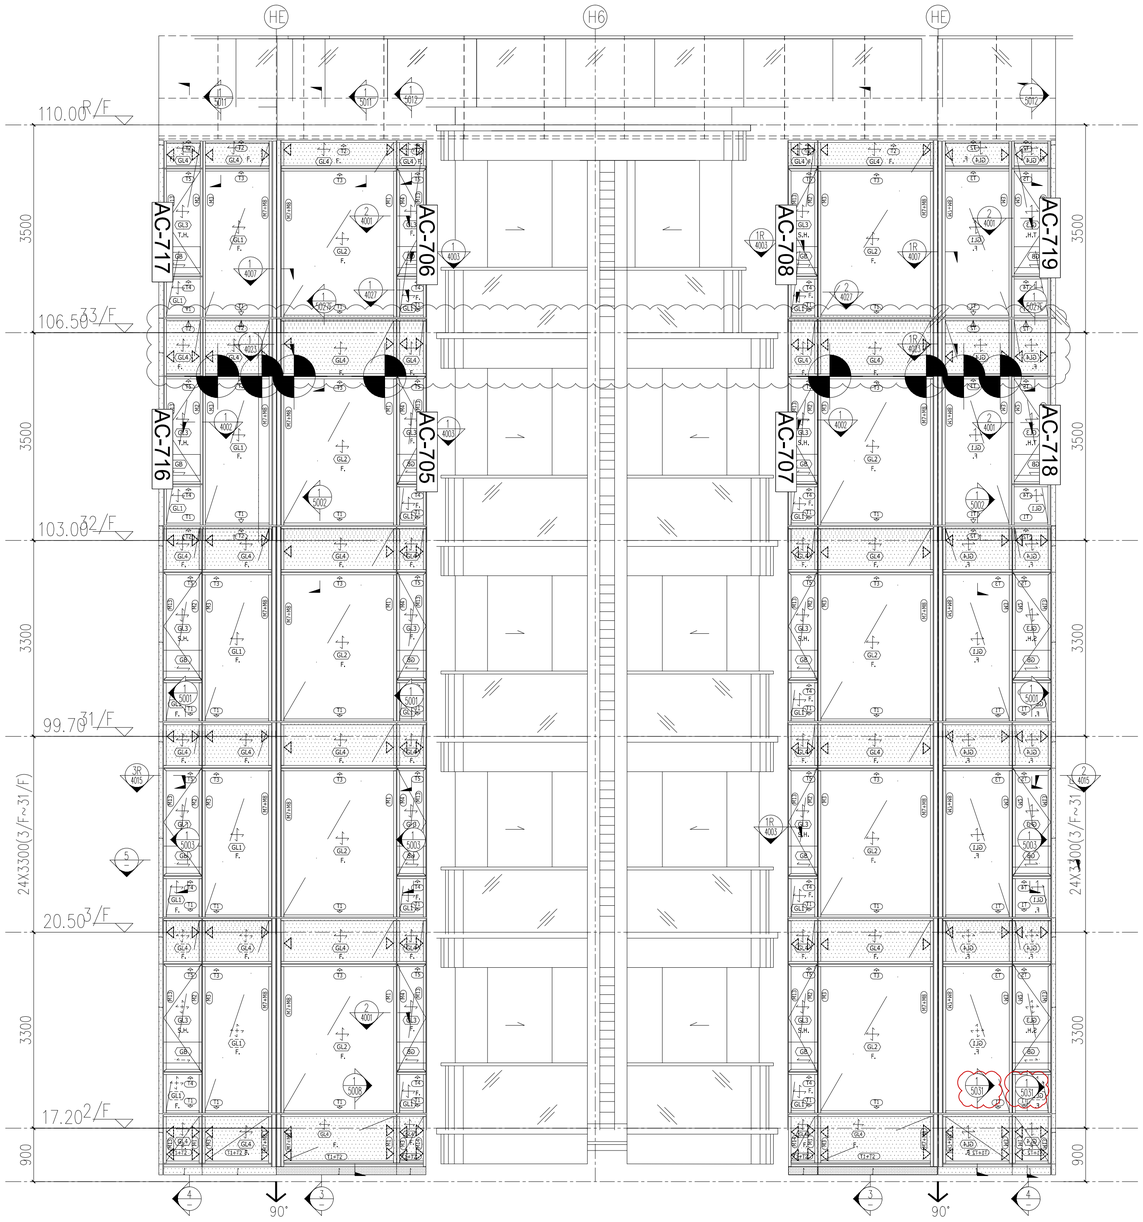


1 / 3013 TOWER 3 -PART ELEVATION 1:50

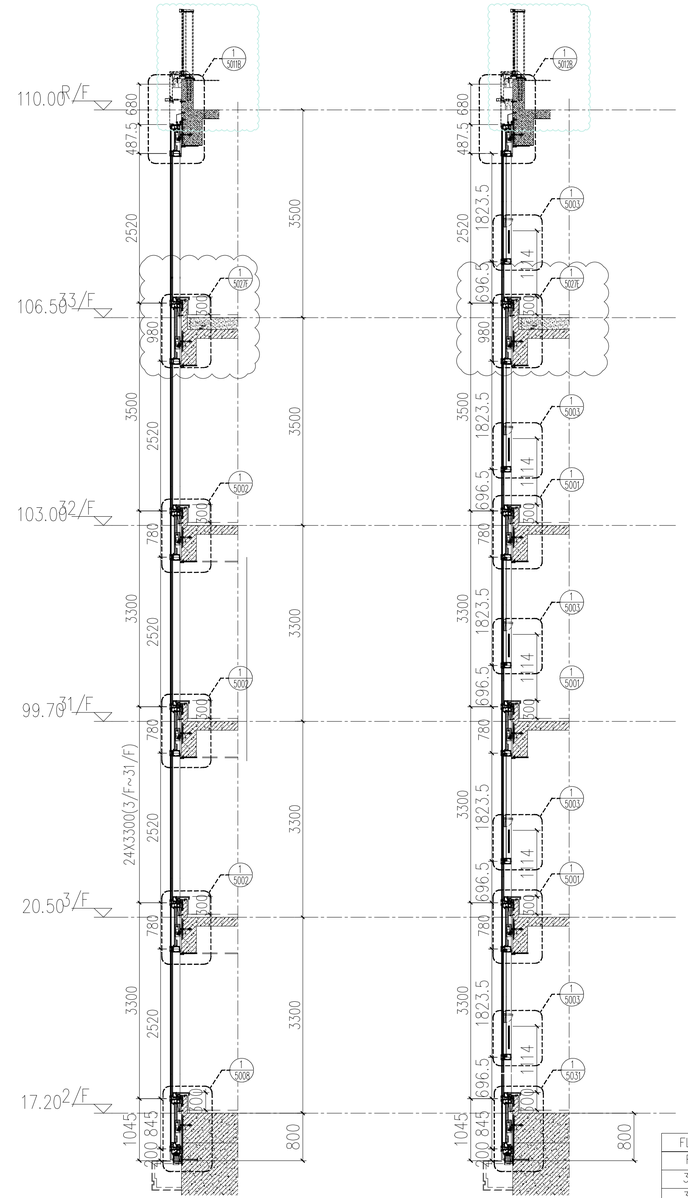


2 / 3013 TOWER 3 -PART ELEVATION 1:50

3 / 3013 TOWER 3 -PART SECTION 1:50

4 / 3013 TOWER 3 -PART SECTION 1:50

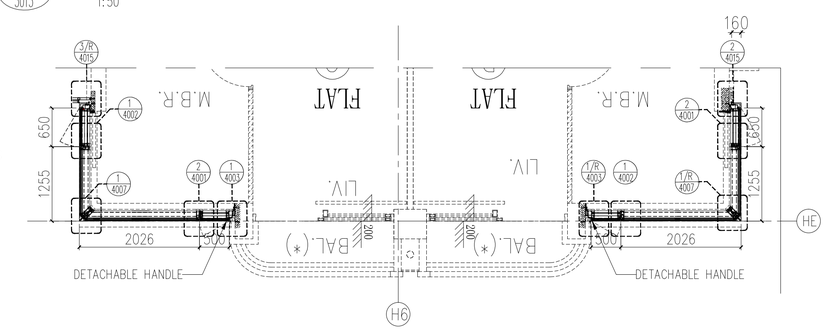

5 / 3013 TOWER 3 -PART PLAN 1:50



LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁ EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

◁ EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

◀ EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

B.D. REF :

F.S.D. REF :

Note :
1. All dimensions are in mm.
2. All elevations are viewed from outside.
3. All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
I	16.Nov.2022	GENERAL REVISION	
H	16.Ari.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
CMA C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwa@cmwa.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2&3

JOB NO. : J-857


DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:50 A3:

DWG. NO. : SD-PE-3013 | REV. : B

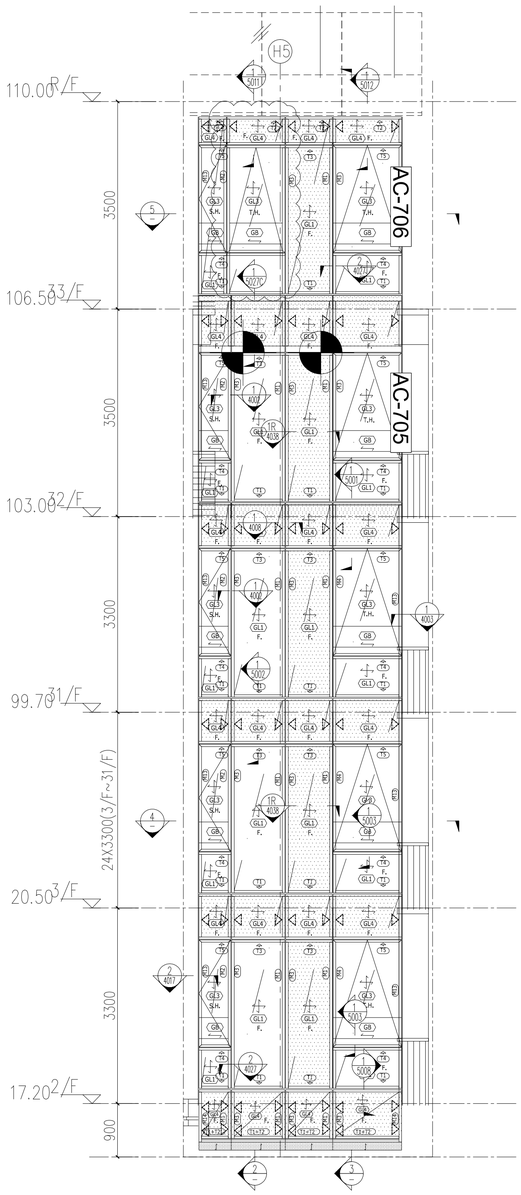


1 / 3014 TOWER 2&3 -PART ELEVATION
1:50

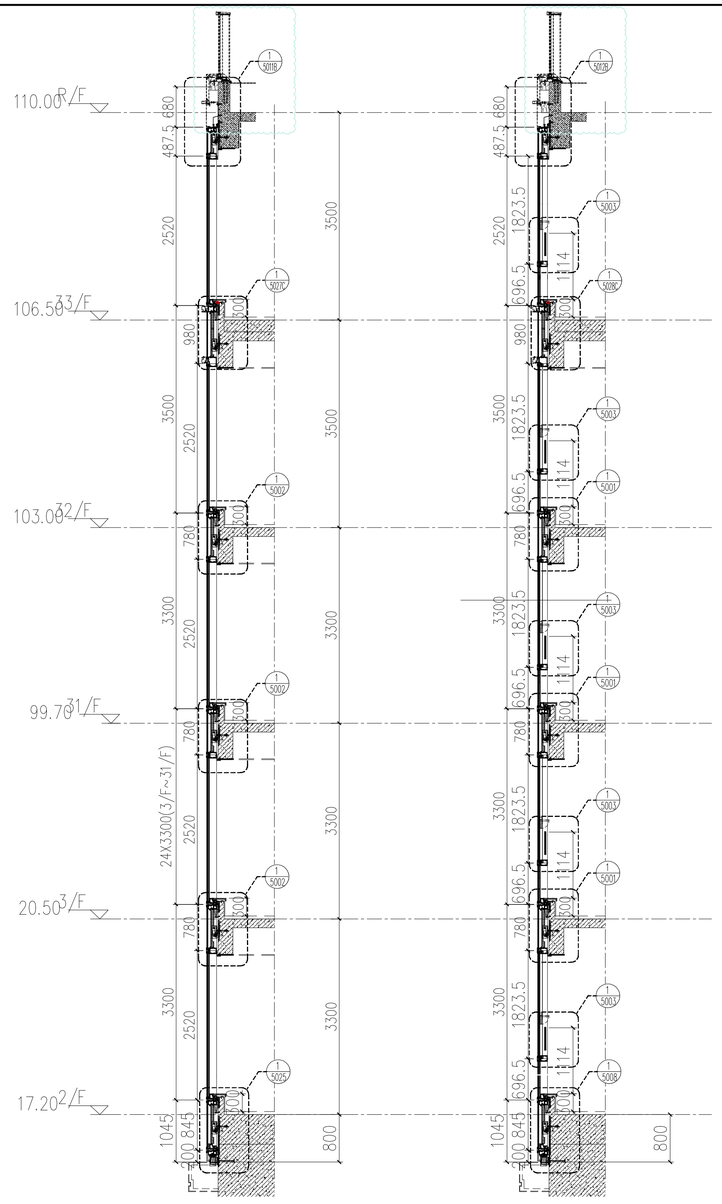


2 / 3014 TOWER 2&3 -PART SECTION
1:50

3 / 3014 TOWER 2&3 -PART SECTION
1:50



4 / 3014 TOWER 2&3 -PART PLAN
1:50



5 / 3014 TOWER 2&3 -PART PLAN
1:50


LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL
C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)
EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION
EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION
EM3 = WIND LOAD FIXING LOCATION
GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS
GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
= BMU SOCKET(GLASS UNIT)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20



KEY PLAN

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
G	16.Nov.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1066
Email: cmwa@cmwal.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2&3

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :


SCALE A1: 1:50
A3:

DWG. NO. : SD-PE-3014

REV. : B

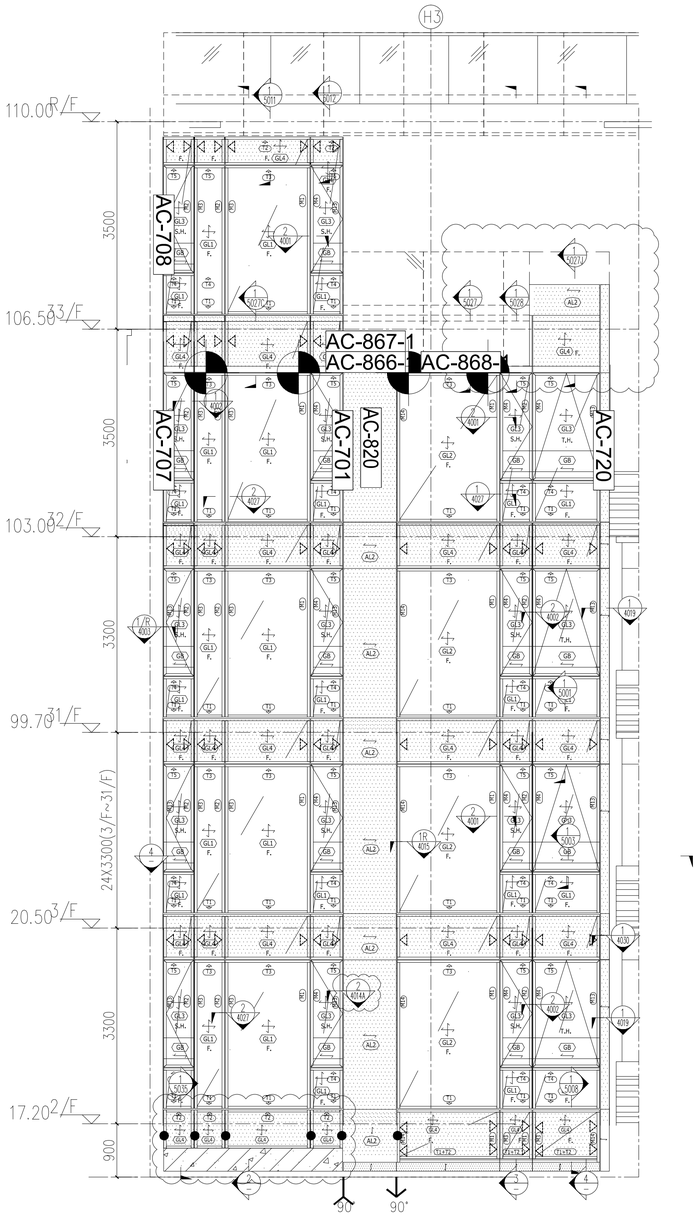


1 / 3015 TOWER 2&1 -PART ELEVATION
1:50

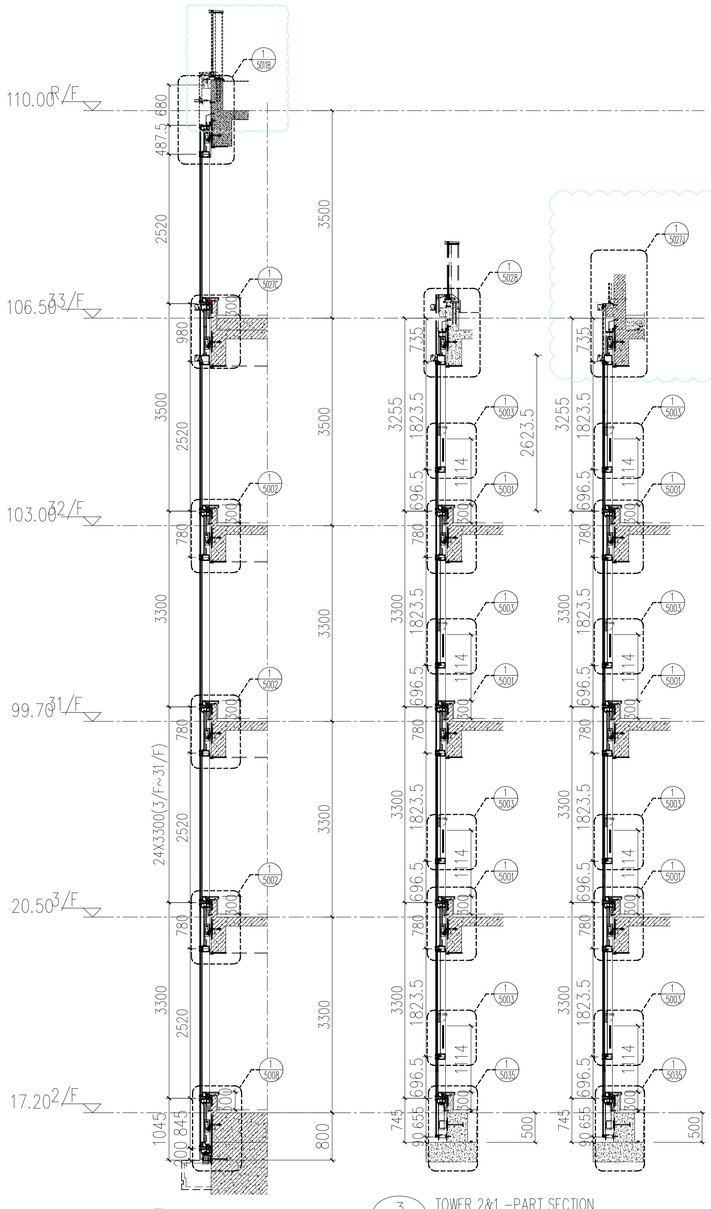


2 / 3015 TOWER 2&1 -PART SECTION
1:50

3 / 3015 TOWER 2&1 -PART SECTION
1:50

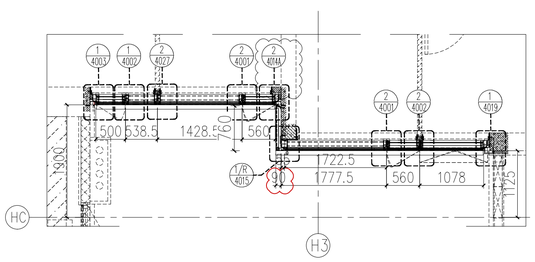

4 / 3015 TOWER 2&1 -PART PLAN
1:50

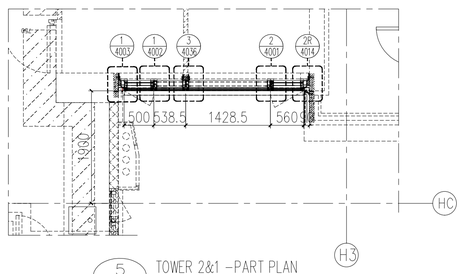

5 / 3015 TOWER 2&1 -PART PLAN
1:50

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)

T10 = EXTRUDED ALUM. TRANSOM (AL70)


T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20



KEY PLAN

B.D. REF :

F.S.D. REF :

Note :

1.All dimensions are in mm.

2.All elevations are viewed from outside.

3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwal@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666


PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 2&1

JOB NO. : J-857	
DRAWN BY : AN	DATE : 18.Oct.2021
CHKD BY :	SCALE A1: 1:50 A3:
DWG. NO. : SD-PE-3015	REV. : B

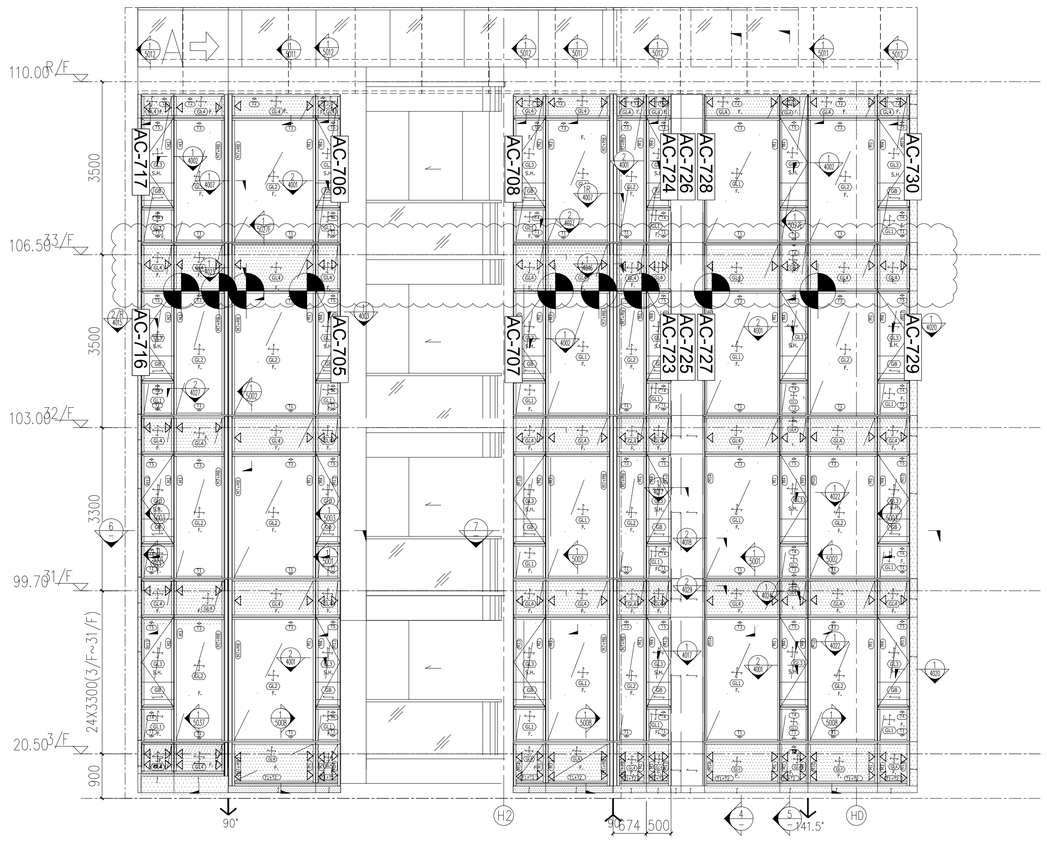

1 3016 TOWER 1 –PART ELEVATION 1:50

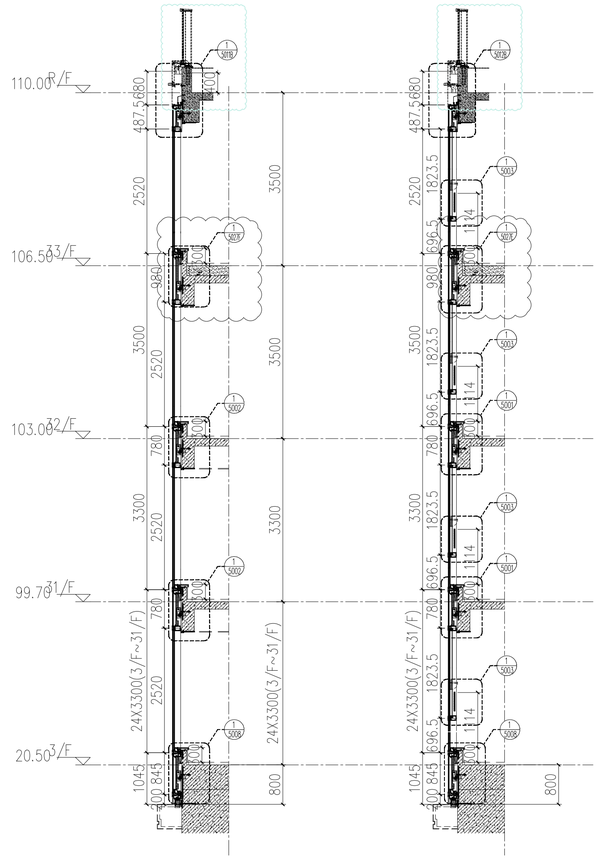


4 3016 TOWER 1 –PART SECTION 1:50


5 3016 TOWER 1 –PART SECTION 1:50

2 3016 TOWER 1 –PART ELEVATION 1:50

3 3016 TOWER 1 –PART ELEVATION 1:50

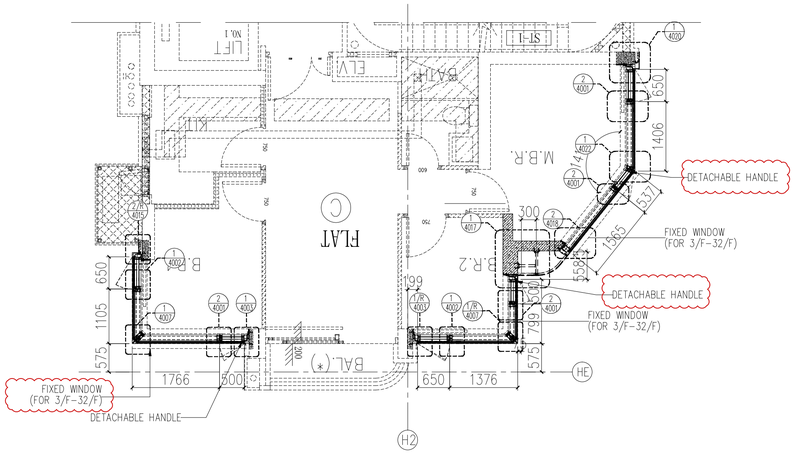

6 3016 TOWER 1–PART PLAN 1:50



KEY PLAN

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁ EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

◁ EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

◀ EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT

M1 = EXTRUDED ALUM. MALE MULLION (AL03)

M2 = EXTRUDED ALUM. MALE MULLION (AL03A)

M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)

M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)

M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)

M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)

M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)

M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)

M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)

M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)

M15 = EXTRUDED ALUM. MALE MULLION (AL67)

M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)

T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)

T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)

T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)

T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)

T7 = EXTRUDED ALUM. TRANSOM (AL71)

T8 = EXTRUDED ALUM. TRANSOM (AL72)

T9 = EXTRUDED ALUM. TRANSOM (AL69)

T10 = EXTRUDED ALUM. TRANSOM (AL70)

T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)

T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)

T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

B.D. REF :

F.S.D. REF :

Note :

1.All dimensions are in mm.

2.All elevations are viewed from outside.

3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :

1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
I	16.Nov.2022	GENERAL REVISION	
H	16.Ari.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :

MARBLE EDGE INVESTMENT LTD.

ARCHITECT :

RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :

C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1068
E-mail: cmwa@cmwal.com

MAIN CONTRACTOR :

裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :

PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :

PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 1

JOB NO. : J-857

DRAWN BY : AN


DATE : 18.Oct.2021

CHKD BY :


SCALE A1: 1:60 A3:

DWG. NO. : SD-PE-3016

REV. : B

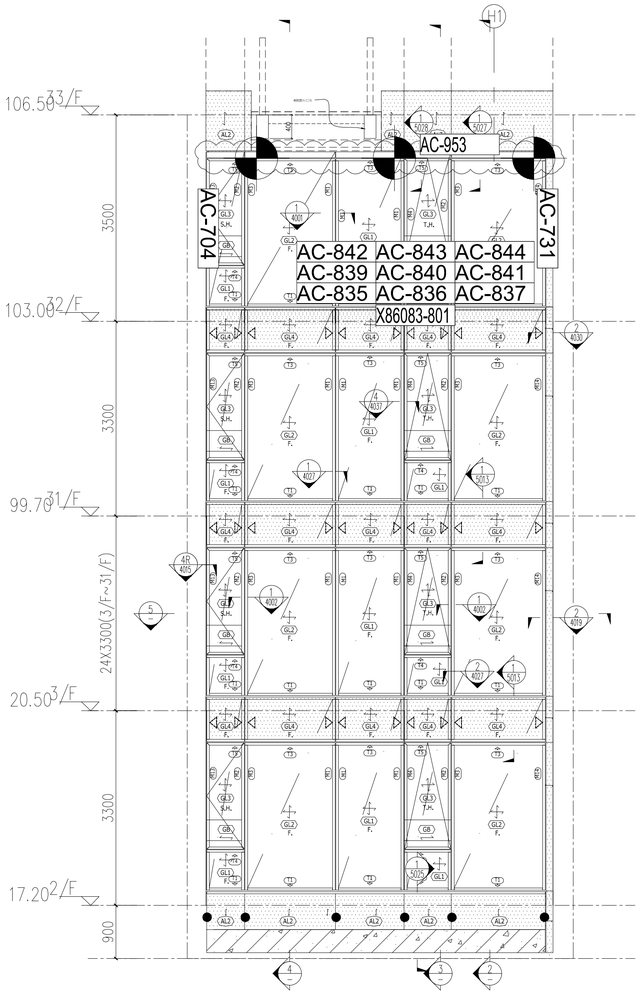


1 / 3017 TOWER 1 –PART ELEVATION
1:50

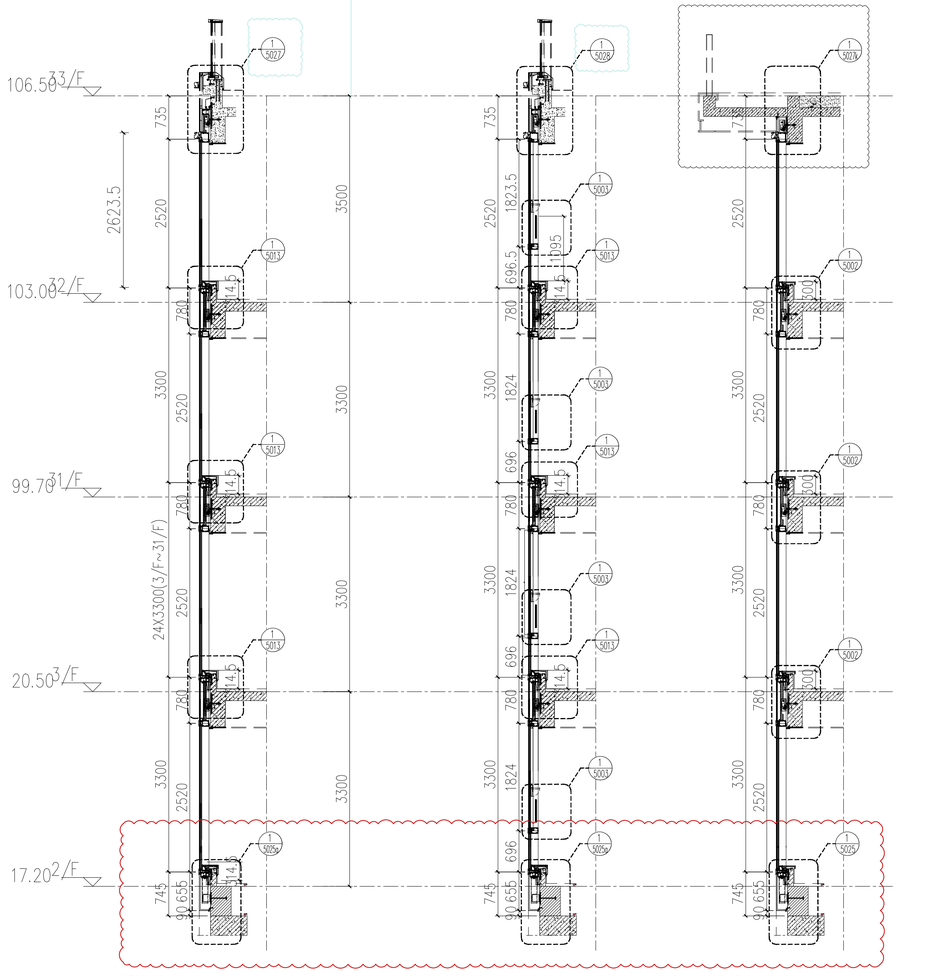

2 / 3017 TOWER 1 –PART SECTION
1:50


3 / 3017 TOWER 1 –PART SECTION
1:50

4 / 3017 TOWER 1 –PART SECTION
1:50

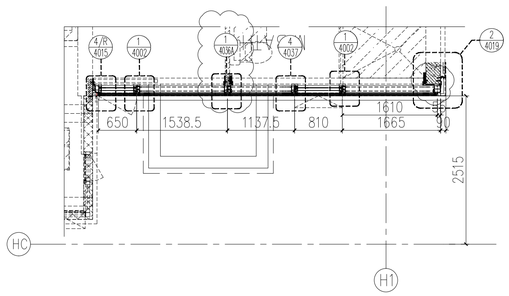

5 / 3017 TOWER 1 –PART PLAN
1:50

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20



KEY PLAN

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁EM1 = WIND LOAD +DEAD LOAD FIXING LOCATION

◁EM2 = WIND LOAD +DEAD LOAD FIXING LOCATION

◀EM3 = WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)

= BMU SOCKET(GLASS UNIT)

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
C M WONG & ASSOCIATES LTD
TEL:(852) 2522 1068
E-mail: cmwad@cmwal.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 1

JOB NO. : J-857

DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:50 A3:


DWG. NO. : SD-PE-3017 | REV. : B

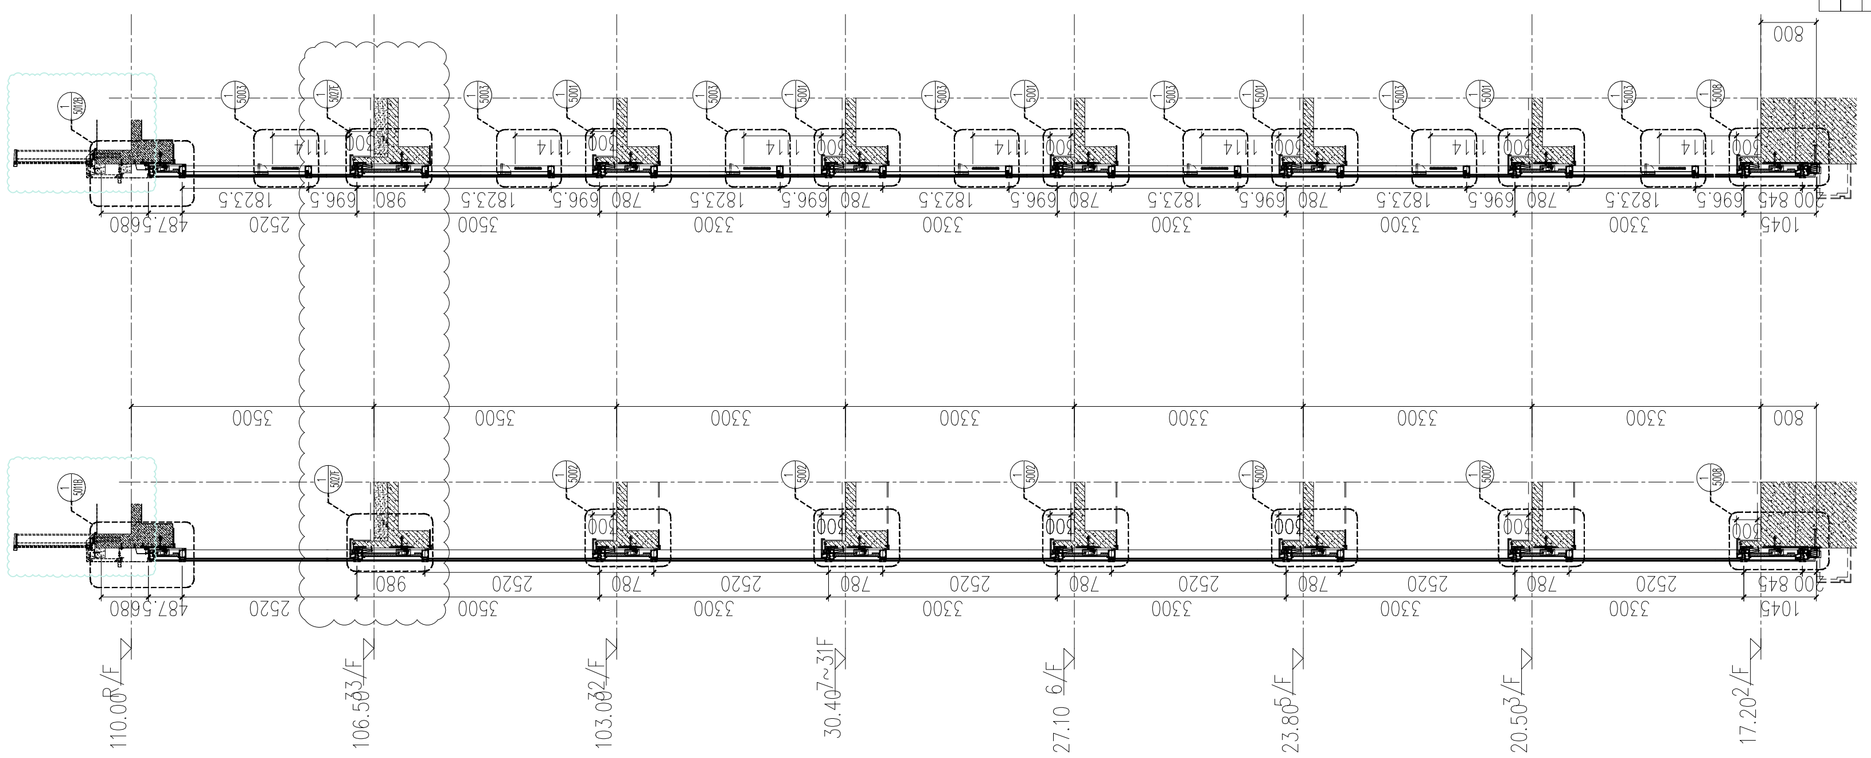

3 TOWER 6 -PART SECTION 1:50

2 TOWER 6 -PART SECTION 1:50

FLOOR	LEVEL
R/F	+110.00
33/F	+106.50
32/F	+103.00
31/F	+99.70
30/F	+96.40
29/F	+93.10
28/F	+83.20
27/F	+86.50
26/F	+83.20
25/F	+79.90
23/F	+76.60
22/F	+73.30
21/F	+70.00
20/F	+66.70
19/F	+63.40
18/F	+60.10
17/F	+56.80
16/F	+53.50
15/F	+50.20
12/F	+46.90
11/F	+43.60
10/F	+40.30
9/F	+37.00
8/F	+33.70
7/F	+30.40
6/F	+27.10
5/F	+23.80
3/F	+20.50
2/F	+17.20

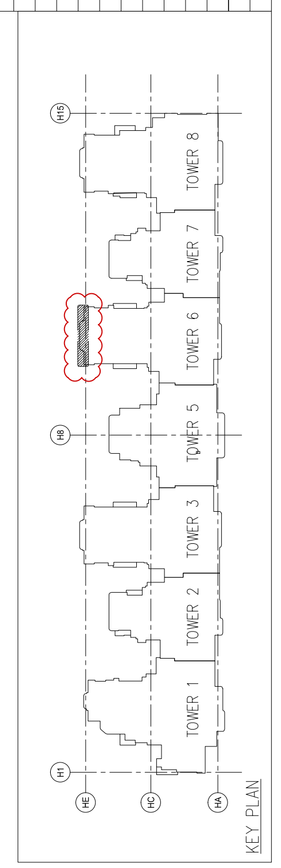


T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM. GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
T14 = BMU SOCKET(GLASS UNIT)


S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS
GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

LEGEND :
S.F.L. = STRUCTURAL FLOOR LEVEL
C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)
EM1= WIND LOAD +DEAD LOAD FIXING LOCATION
EM2= WIND LOAD +DEAD LOAD FIXING LOCATION
EM3= WIND LOAD FIXING LOCATION
GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

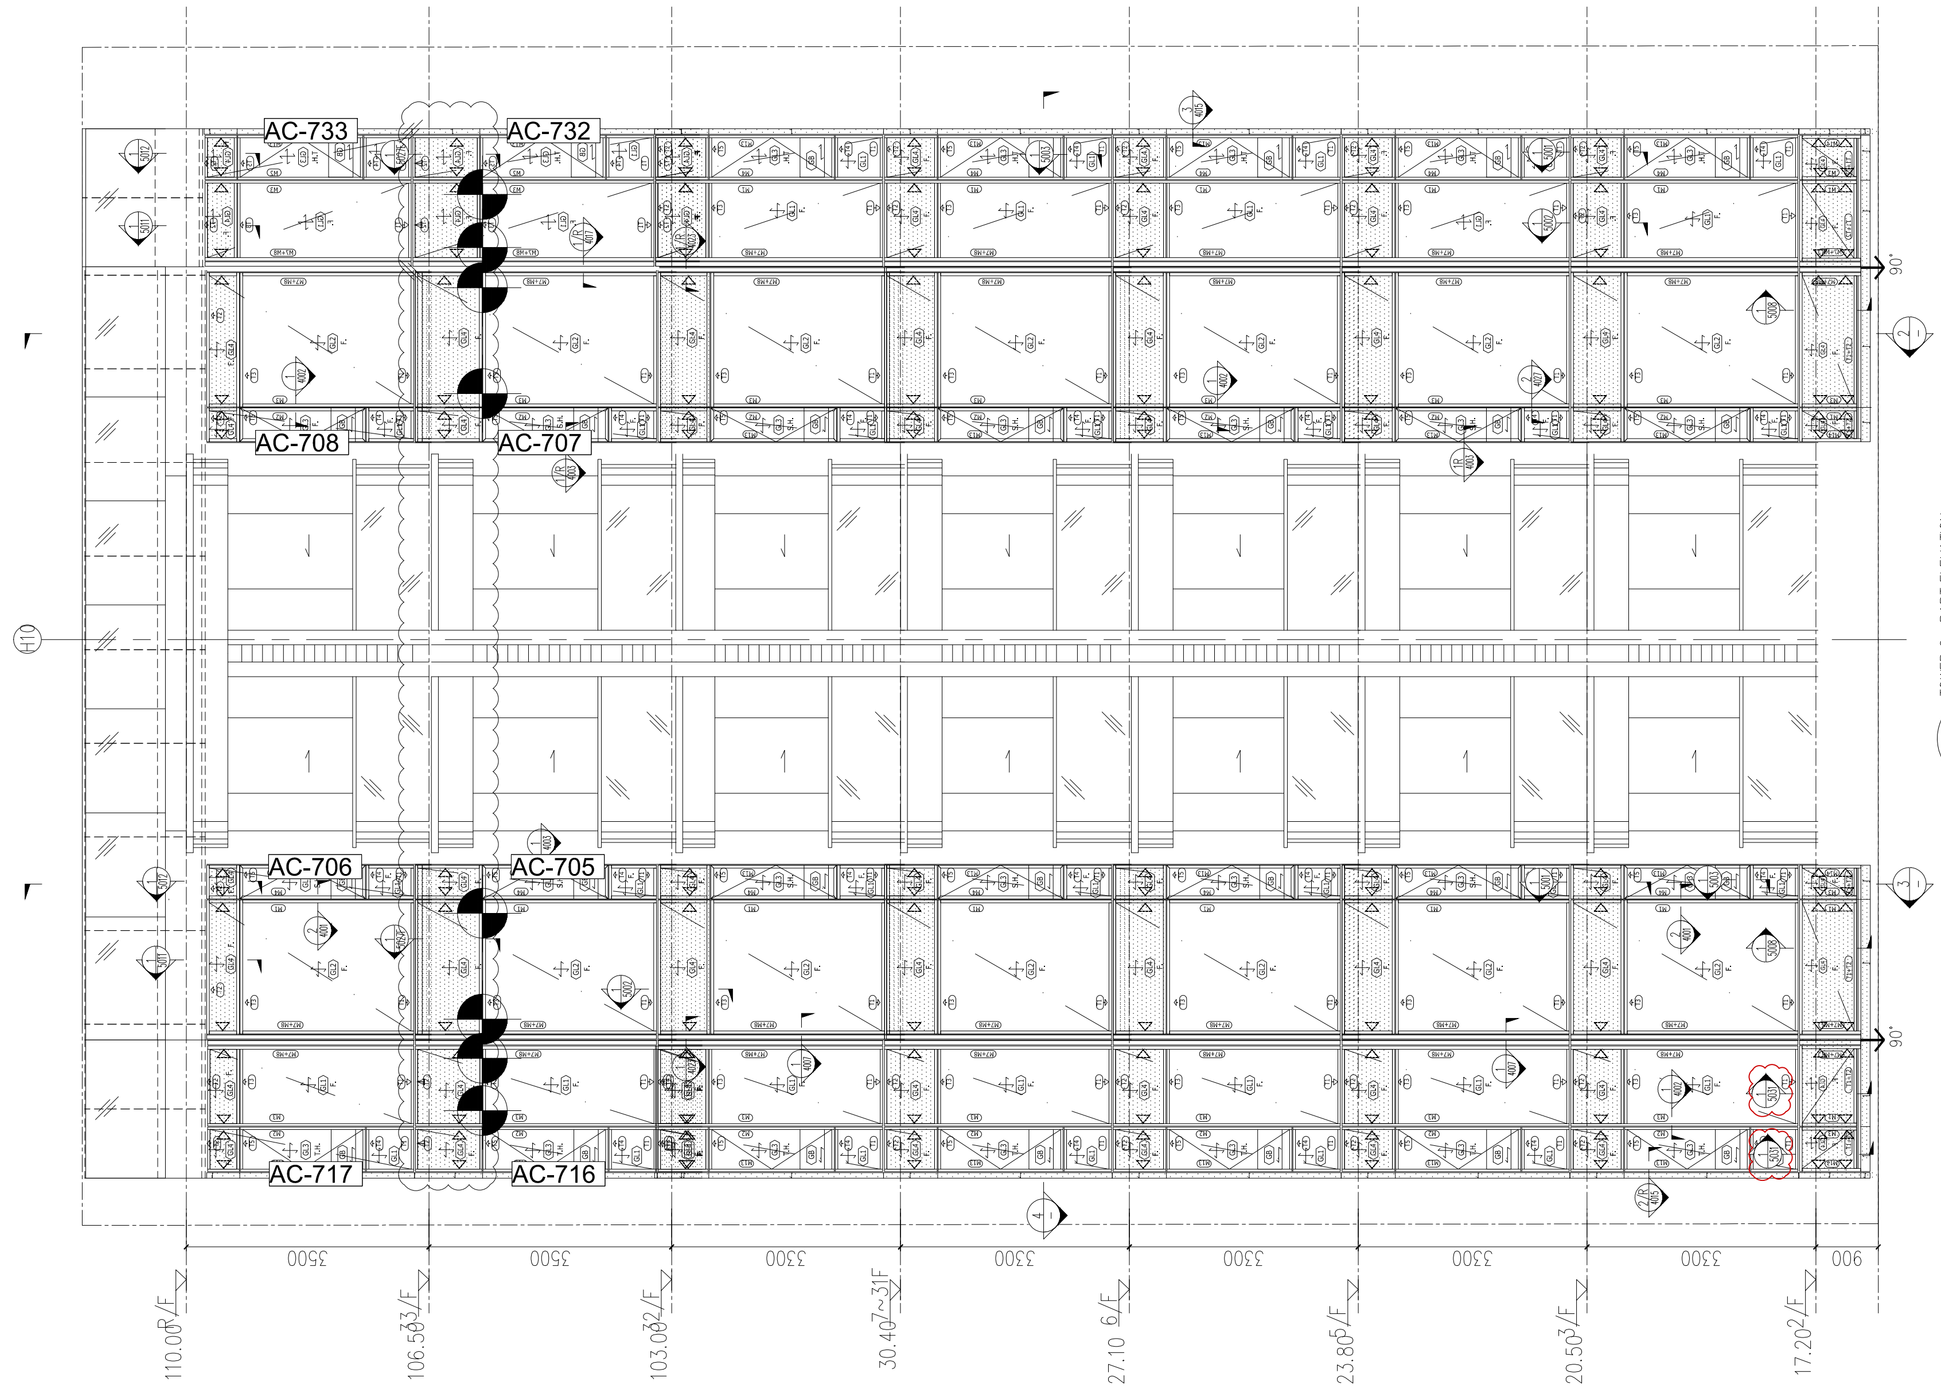

1 TOWER 6 -PART ELEVATION 1:50

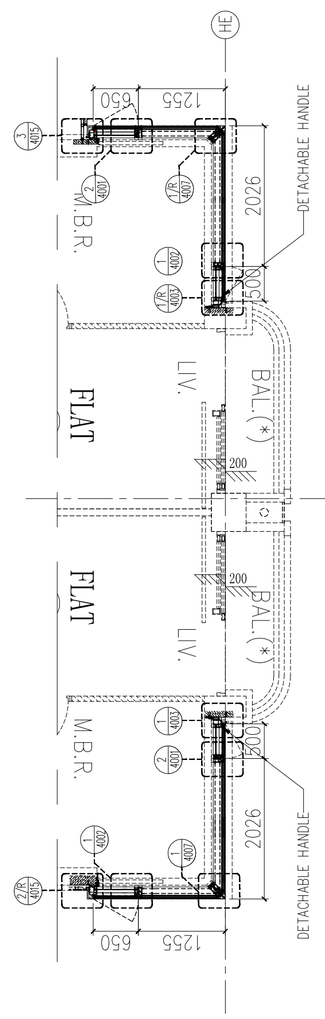

4 TOWER 6 -PART PLAN 1:50

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
I	16.Nov.2022	GENERAL REVISION	
H	16.Ari.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
CMA C M WONG & ASSOCIATES LTD
TEL: (852) 2522 7092
E-mail: cmwk@cmwk.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 6

JOB NO. : J-857

DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:50 A3:

DWG. NO. : SD-PE-3019 | REV. : B

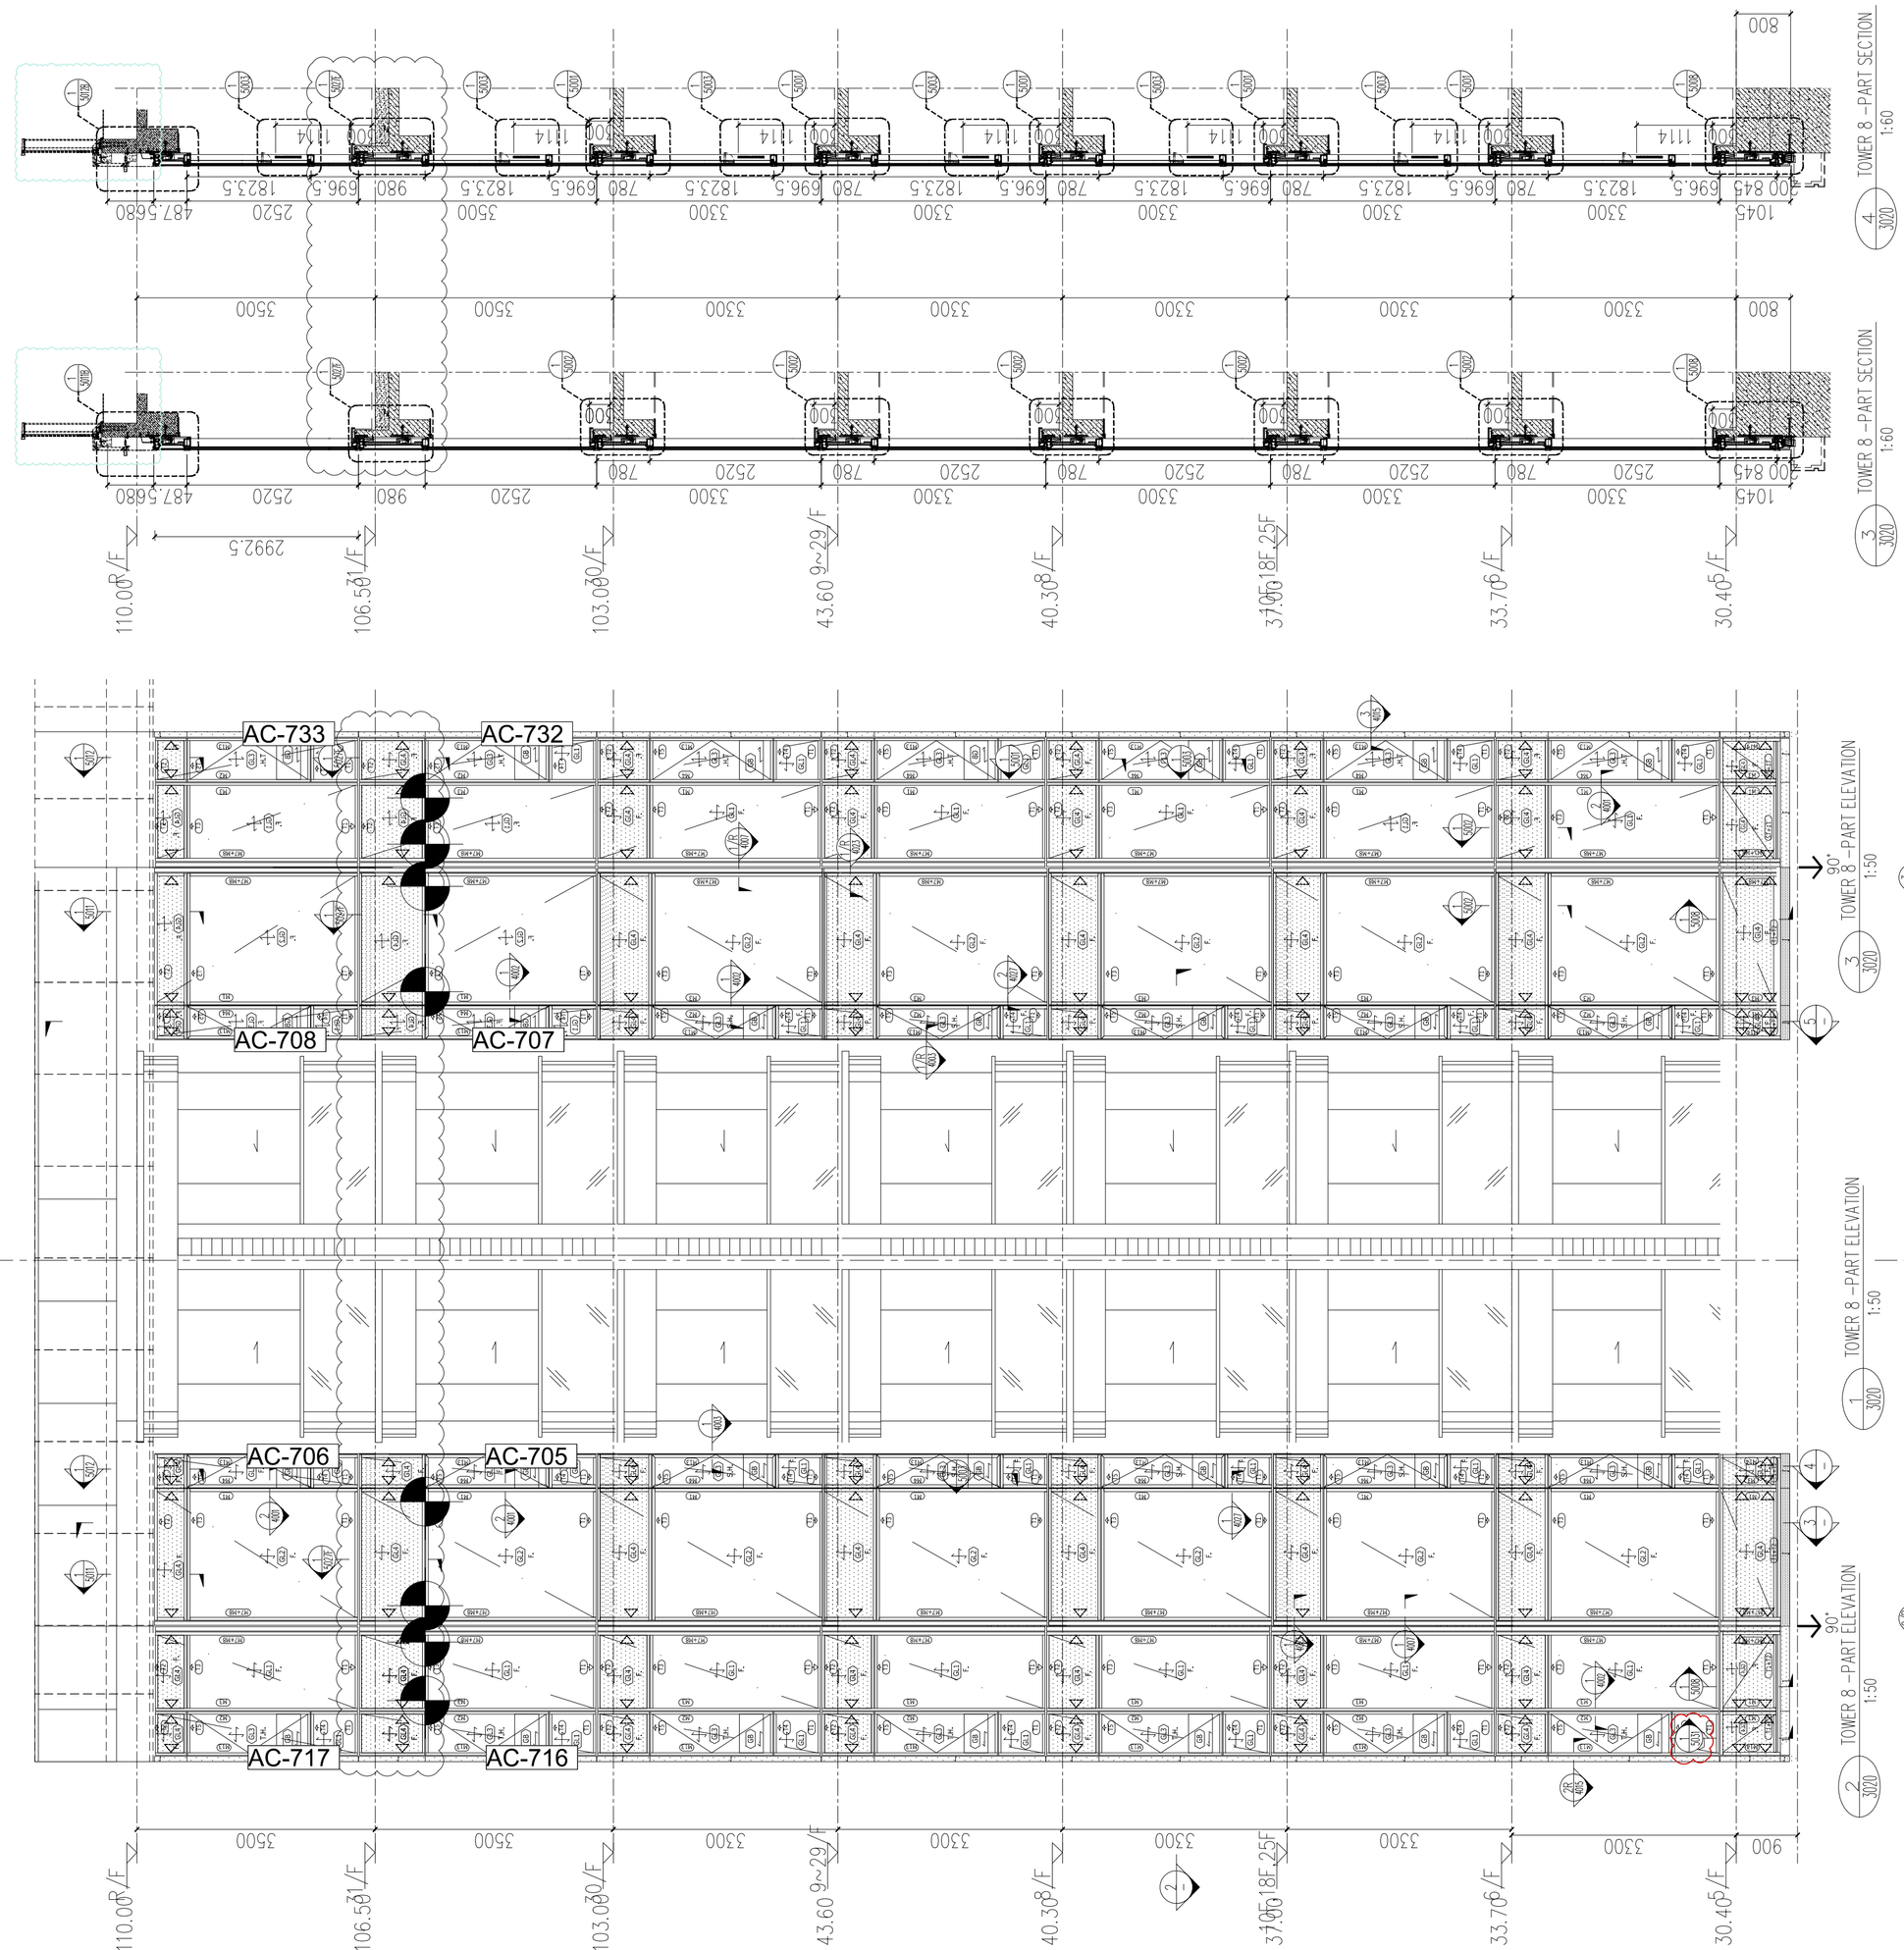

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM. GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM. GUTTER STACK JOINT (AL105)
BMU SOCKET(GLASS UNIT)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS
GB = 10mm FULLY TEMPERED CLEAR GLASS (BARRIER)

LEGEND :
S.F.L. = STRUCTURAL FLOOR LEVEL
C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)
WM1= WIND LOAD +DEAD LOAD FIXING LOCATION
WM2= WIND LOAD +DEAD LOAD FIXING LOCATION
WM3= WIND LOAD FIXING LOCATION
GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

FLOOR	LEVEL
R/F	+110.00
31/F	+106.50
30/F	+103.00
29/F	+99.70
28/F	+96.40
27/F	+93.10
26/F	+83.20
25/F	+86.50
23/F	+83.20
22/F	+79.90
21/F	+76.60
20/F	+73.30
19/F	+70.00
18/F	+66.70
17/F	+63.40
16/F	+60.10
15/F	+56.80
12/F	+53.50
11/F	+50.20
10/F	+46.90
9/F	+43.60
8/F	+40.30
7/F	+37.00
6/F	+33.70
5/F	+30.40

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 — DETAIL MARK NO.
X001 — REFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
CMA C M WONG & ASSOCIATES LTD
TEL: (852) 2522 1066
E-mail: cmwa@cmwa.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552


TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 8

JOB NO. : J-857


DRAWN BY : AN | DATE : 18.Oct.2021

CHKD BY : | SCALE A1: 1:60 A3:


DWG. NO. : SD-PE-3020 | REV. : B

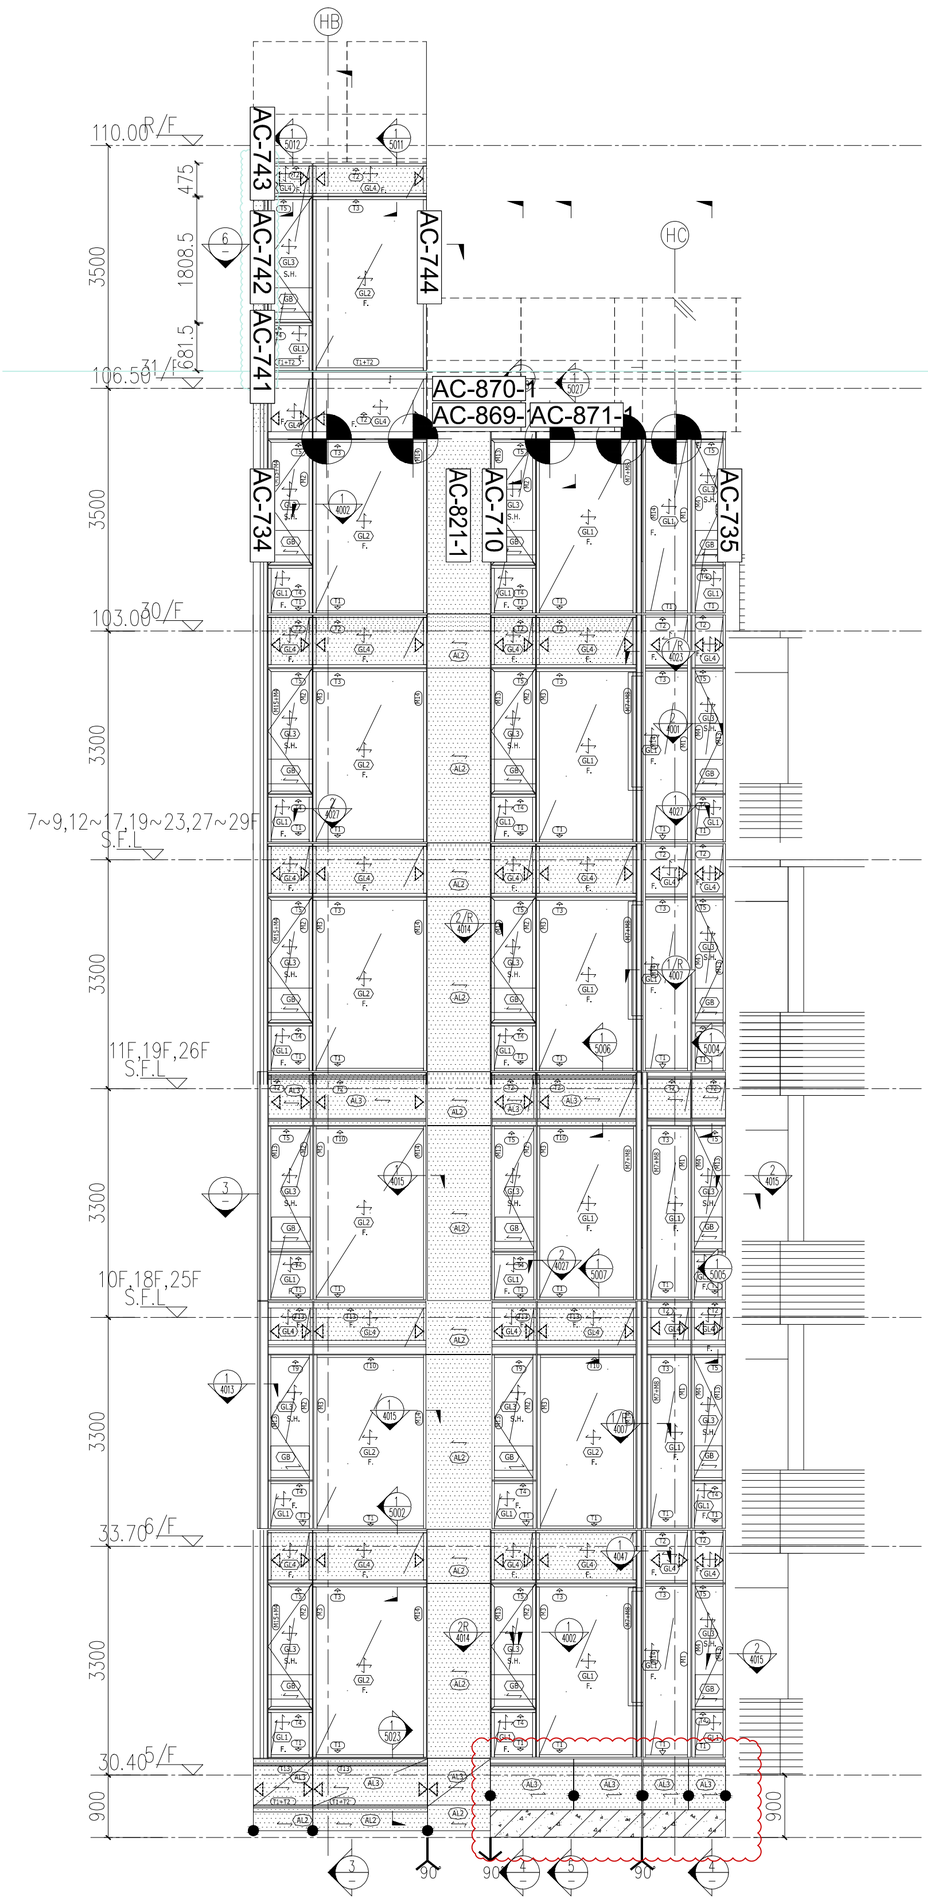


1 3021 TOWER 8 –PART ELEVATION 1:60

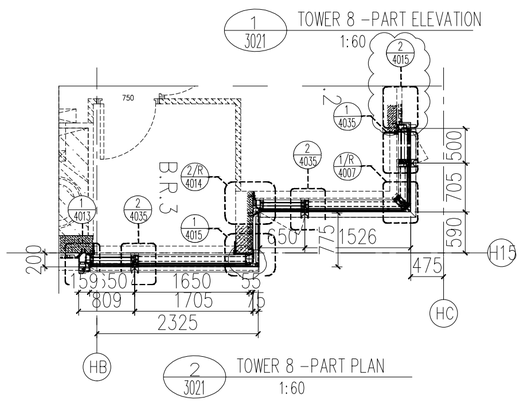


2 3021 TOWER 8 –PART PLAN 1:60




6 3021 TOWER 8 –PART PLAN 1:60

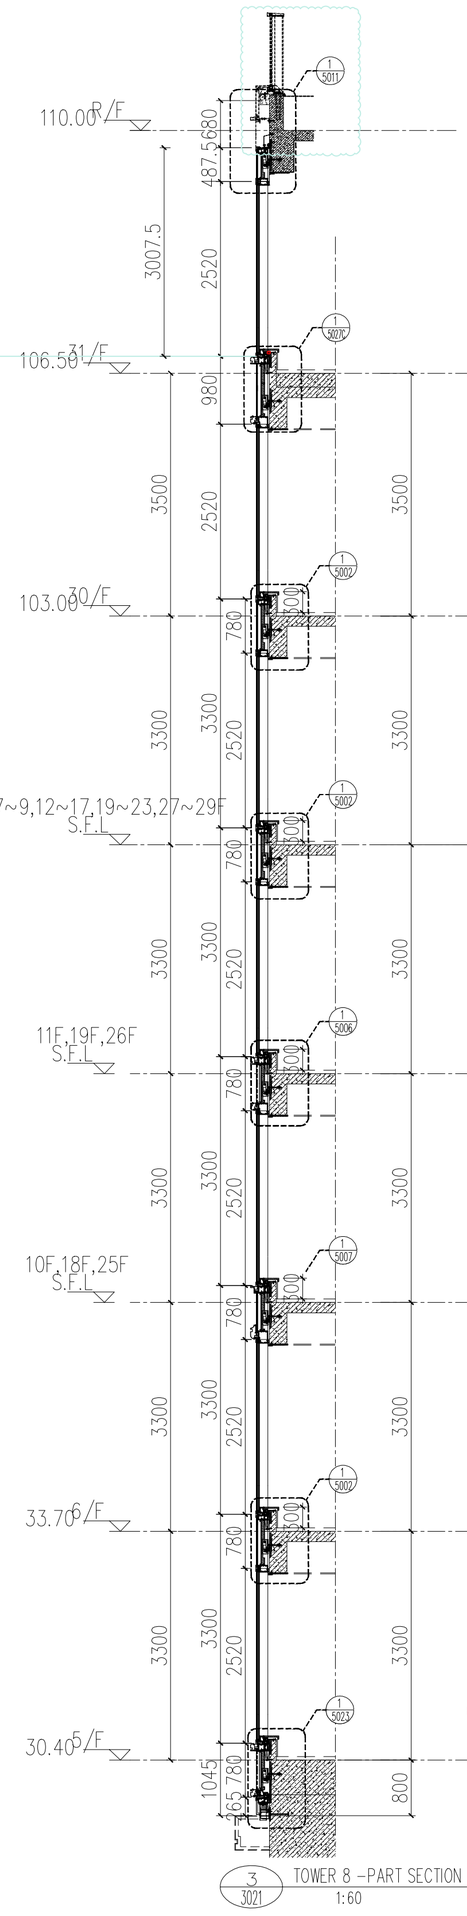

3 3021 TOWER 8 –PART SECTION 1:60

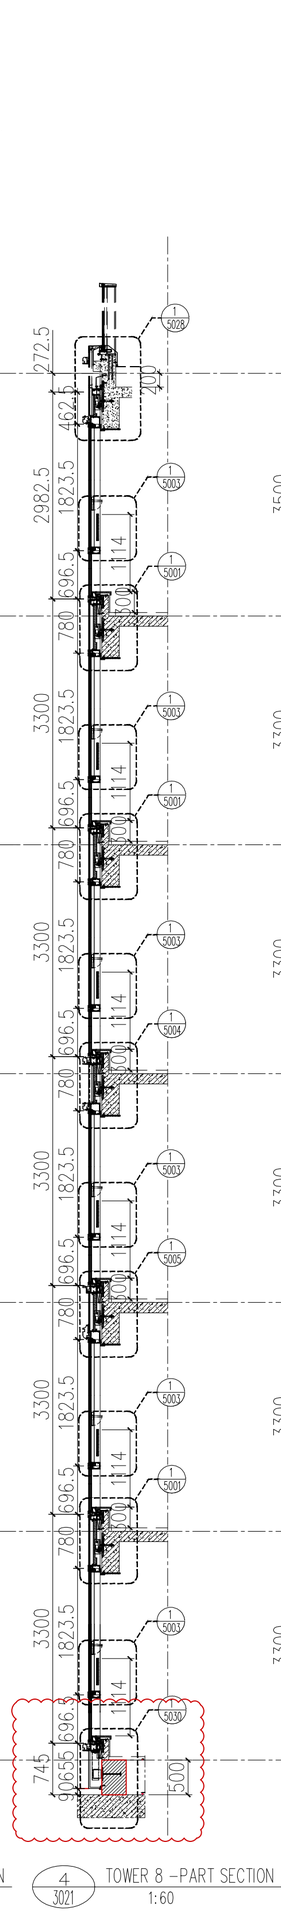


4 3021 TOWER 8 –PART SECTION 1:60

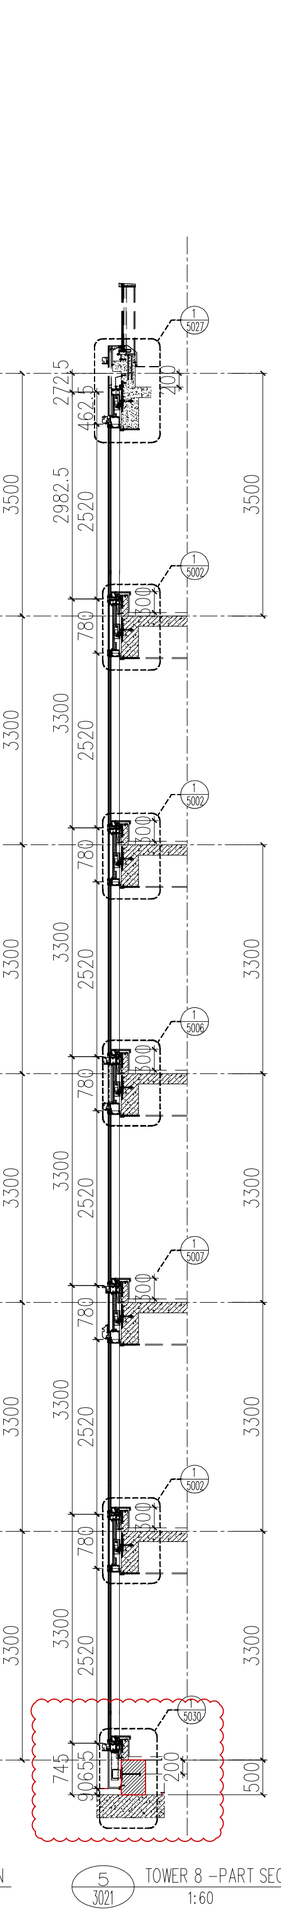

5 3021 TOWER 8 –PART SECTION 1:60

FLOOR	LEVEL
R/F	+110.00
31/F	+106.50
30/F	+103.00
29/F	+99.70
28/F	+96.40
27/F	+93.10
26/F	+83.20
25/F	+86.50
23/F	+83.20
22/F	+79.90
21/F	+76.60
20/F	+73.30
19/F	+70.00
18/F	+66.70
17/F	+63.40
16/F	+60.10
15/F	+56.80
12/F	+53.50
11/F	+50.20
10/F	+46.90
9/F	+43.60
8/F	+40.30
7/F	+37.00
6/F	+33.70
5/F	+30.40

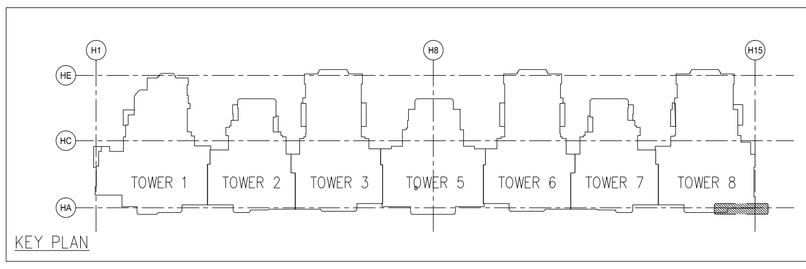

LEGEND :

S.F.L. = STRUCTURAL FLOOR LEVEL

C.W. = UNITIZED CURTAIN WALL (FOR BD APPROVAL)

◁ EM1= WIND LOAD +DEAD LOAD FIXING LOCATION

◁ EM2= WIND LOAD +DEAD LOAD FIXING LOCATION

◀ EM3= WIND LOAD FIXING LOCATION

GL1 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +10mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL2 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 12mm AIR SPACE +12mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL3 = 8mm HEAT STRENGTHEN LOW IRON GLASS + 1.52 PVB INTERLAYER+ 8mm HEAT STRENGTHEN LOW IRON GLASS + 9mm AIR SPACE +8mm LOW IRON FULLY TEMPERED IGU LAMINATED CLEAR GLASS

GL4 = 8mm FULLY TEMPERED GLASS + 1.52 PVB INTERLAYER+ 8mm FULLY TEMPERED LAMINATED GLASS

GB = 10mm FULLY TEMPERED MONOLITHIC CLEAR GLASS (BARRIER)

S.J. = STACK JOINT
M1 = EXTRUDED ALUM. MALE MULLION (AL03)
M2 = EXTRUDED ALUM. MALE MULLION (AL03A)
M3 = EXTRUDED ALUM. FEMALE MULLION (AL04)
M4 = EXTRUDED ALUM. FEMALE MULLION (AL04A)
M7 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL07)
M8 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL08)
M9 = EXTRUDED ALUM. OUTER CORNER MALE MULLION (AL86)
M10 = EXTRUDED ALUM. OUTER CORNER FEMALE MULLION (AL85)
M13 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL65)
M14 = EXTRUDED ALUM. INTERMEDIATE MULLION (AL66)
M15 = EXTRUDED ALUM. MALE MULLION (AL67)
M16 = EXTRUDED ALUM. FEMALE MULLION (AL68)

T1 = EXTRUDED ALUM. SILL STACK JOINT (AL11)
T2 = EXTRUDED ALUM GUTTER STACK JOINT (AL12)
T3 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL13)
T4 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL15)
T5 = EXTRUDED ALUM. INTERMEDIATE TRANSOM (AL14)
T7 = EXTRUDED ALUM. TRANSOM (AL71)
T8 = EXTRUDED ALUM. TRANSOM (AL72)
T9 = EXTRUDED ALUM. TRANSOM (AL69)
T10 = EXTRUDED ALUM. TRANSOM (AL70)
T11 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL106)
T12 = EXTRUDED ALUM. INTERMEDIATE TRANSOM(AL107)
T13 = EXTRUDED ALUM GUTTER STACK JOINT (AL105)
= BMU SOCKET(GLASS UNIT)

B.D. REF :

F.S.D. REF :

Note :
1.All dimensions are in mm.
2.All elevations are viewed from outside.
3.All dimensions to be verified on site before fabrication.

GENERAL NOTES

Legend :
1. F.F.L.-- Finished Floor Level
2. S.F.L.-- Structural Floor Level
3. /R -- Reversed Detail

X1 → DETAIL MARK NO.
X001 → REFFER SHEET NO.

REV.	DATE	DESCRIPTION	BY
H	16.Nov.2022	GENERAL REVISION	
G	01.Mar.2022	GENERAL REVISION	
F	04.JAN.2022	GENERAL REVISION	
E	25.Nov.2021	GENERAL REVISION	
D	22.Nov.2021	GENERAL REVISION	
C	13.Nov.2021	GENERAL REVISION	
B	10.Nov.2021	GENERAL REVISION	
A	18.Oct.2021	GENERAL REVISION	

CLIENT :
MARBLE EDGE INVESTMENT LTD.

ARCHITECT :
RONALD LU & PARTNERS
ARCHITECTS | PLANNERS | INTERIOR DESIGNERS

STRUCTURAL ENGINEER :
C M WONG & ASSOCIATES LTD
TEL:(852)2522 4180 E-mail:cmwa@cmwal.com

MAIN CONTRACTOR :
裕民建築有限公司

美特鋁質有限公司
MIDI ALUMINIUM FABRICATOR LTD.
Units 6-8, Sunray Industrial Centre, 1/F
610 Cha Kwo Ling Road, Kowloon
Tel:23489211-4 Fax:(852)27727666

PROJECT :
PROPOSED RESIDENTIAL DEVELOPMENT AT NEW KOWLOON INLAND LOT. NO.6552

TITLE :
PARTIAL ELEVATION, PLAN, SECTION FOR TOWER 8

JOB NO. : J-857
DRAWN BY : AN
DATE : 18.Oct.2021
CHKD BY :
SCALE A1:60.000000 A3:
DWG. NO. : SD-PE-3021
REV. : B
